





BROAD STATUS REPORT OF UNDER CONSTRUCTION THERMAL POWER PROJECTS (JULY, 2022)

Monthly Thermal Capacity addition achievement (MW) during FY : 2022-23

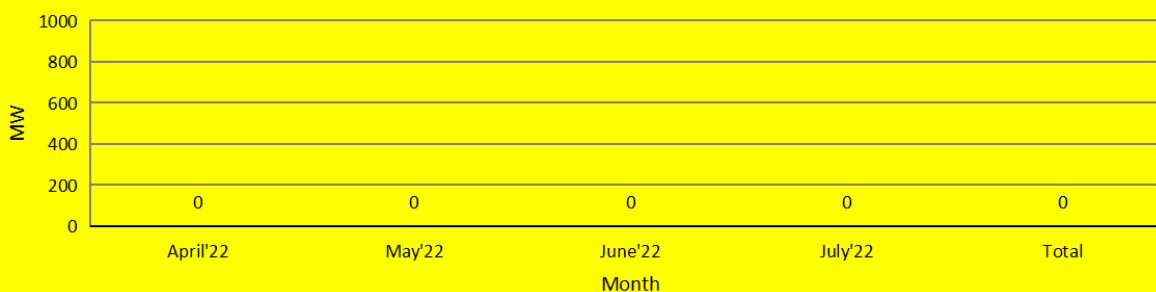

Tentative Thermal Capacity Addition Program for FY 2022-23

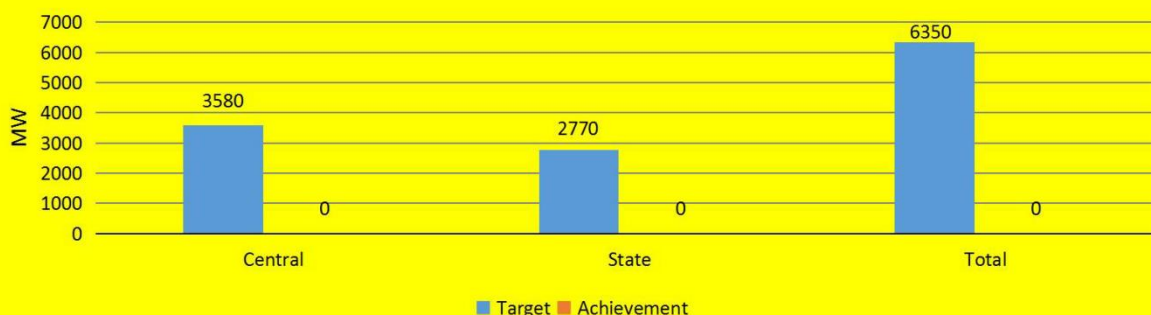

Thermal Project Monitoring Division
Central Electricity Authority
New Delhi

Ministry of Power
Government of India

www.cea.nic.in

(In fulfillment of CEA's obligation under section 73(f) of Electricity Act, 2003)

FOREWORD

As per clause 73(f) of the Electricity Act 2003, Central Electricity Authority is to “promote and assist in the timely completion of schemes and projects”. The Thermal Project Monitoring (TPM) Division of CEA is entrusted with the responsibility of monitoring the progress of construction/erection activities of all the thermal power projects in the country till the units are commissioned. Visits are also made by CEA officers to the sites for assessing the on the spot progress of works and rendering the advice/assistance in solving the problems being faced by the project authorities, thereby helping the project authorities to avoid / minimize the time and cost overruns of the thermal power projects.

In this context, Thermal Project Monitoring Division, Central Electricity Authority has been bringing out the monthly report titled “Broad Status of Thermal Power Projects in the Country”. This report gives year-wise details of thermal power projects commissioned during the 12th plan and onwards. Further, the Report includes up-to-date information on thermal power projects under construction in the country wherein the details regarding name of the Project, capacity, location, implementing agency, commissioning schedule, type of fuel, estimated cost, physical and financial progress, the milestones achieved as on date etc. are available. The critical issues requiring immediate attention of concerned authorities in the implementation of these thermal power projects have also been highlighted.

The Broad Status Report is being brought out regularly by TPM Division on the basis of the data forwarded by various project authorities, visits made by CEA officers to various power projects, discussions held with the executing agencies and suppliers of equipment from time to time.

CEA welcomes feedback for further improvement in the Broad Status Report.

Chief Engineer (TPM)

This report is based on the details received from various project authorities & other organizations / agencies associated with the projects and is for information and non-commercial use only. CEA is not responsible for the contents or reliability of other websites to which CEA provides a link and do not necessarily endorse the views expressed by them.

CONTENTS

Sl. No.	Description	Page No.
	Executive Summary	3-4
1.1	Tentative Thermal Capacity Addition Program for FY 2022-23	5
1.2	Thermal Power Projects under construction in the country	6
1.3	Under construction TPPs where work is on hold / not likely to be commissioned	7-8
BROAD STATUS OF CENTRAL SECTOR PROJECTS		
A	NATIONAL THERMAL POWER CORPORATION LTD. (NTPC Ltd.)	
	Barh STPP St-I, Distt.- Patna, Bihar	9-10
	North Karanpura STPP, Distt.- Chatra, Jharkhand	11-12
	Telangana TPP (Ph-I), Distt.- Karim Nagar, Telangana	13-14
	Patratu TPS, Distt.- Ramgarh, Jharkhand. [PVUNL (JV of NTPC & Govt. of Jharkhand)]	15-16
B	NEYVELI LIGNITE CORPORATION LIMITED (NLC Ltd.)	
	Ghatampur TPP, Distt. -Kanpur [NUPPL (JV of NLC & UPRVUNL)]	17-18
C	TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED (THDC Ltd.)	
	Khurja STPP, Distt. -Bulandshahr, U.P.	19-20
D	SATLAJ JAL VIDHUT NIGAM LIMITED (SJVN Ltd)	
	Buxar TPP, Distt. -Buxar, Bihar.	21-22
BROAD STATUS OF STATE & PRIVATE SECTOR PROJECTS		
Northern Region		
E	Uttar Pradesh	
	Obra-C TPP, Distt.- Sonebhadra, [UPRVUNL]	23-24
	Jawaharpur STPP, Distt.- Etah, [JVUNL (A 100% subsidiary of UPRVUNL)].	25-26
	Panki TPS Ext, Distt. -Kanpur, [UPRVUNL]	27-28
Western Region		
F	Maharashtra	
	Bhusawal TPP, Distt. -Jalgaon, [MAHAGENCO]	29-30
Southern Region		
G	Andhra Pradesh	
	Sri Damodaram Sanjeevaiah TPP St-II (Krishnapatnam), Distt.-Nellore, [APPDCL]	31-32
	Dr. Narla Tata Rao TPP, Distt.- Vijayawada, [APGENCO]	33-34
H	Telangana	
	Yadadri TPS (TSGENCO), Distt.- Nalgonda, [TSGENCO]	35-37
I	Karnataka	
	Yelahanka Combined Cycle Power plant, Distt.- Bangalore, [KPCL].	38-39
J	Tamil Nadu	
	Ennore SEZ SCTPP, Distt. -Thiruvallur, [TANGEDCO]	40-41
	Uppur SCTPP, Distt. -Ramanathapuram, [TANGEDCO]	42-43
	North Chennai TPP St-III, Distt.-Thiruvallur, [TANGEDCO]	44-45
	Udangudi STPP, Distt.-Thoothukudi, [TANGEDCO]	46-47
Eastern Region		
K	West Bengal	
	Sagardighi Thermal Power Project, Distt.-Murshidabad, [WBPDC]	48-49
	Abbreviations	50

EXECUTIVE SUMMARY

I. All India Installed Capacity (MW)*

Sector	Thermal					Nuclear	Hydro	RES	Grand total
	Coal	Lignite	Gas	Diesel	Total				
State	66831.50	1150.00	7044.05	236.01	75261.56	0.00	27254.45	2453.31	104969.33
Private	73198.00	1830.00	10574.24	273.70	85875.95	0.00	3931.00	110351.75	200158.70
Central	64050.00	3640.00	7237.91	0.00	74927.91	6780.00	15664.72	1632.30	99004.93
Total	204079.50	6620.00	24856.21	509.71	236065.42	6780.00	46850.17	114437.37	404132.95
% of Grand Total	50.50%	1.64%	6.15%	0.13%	58.41%	1.68%	11.59%	28.32%	100.00%

*Compiled from Installed Capacity Report on NPP site.

II. Tentative Year-wise Thermal Capacity likely to be included into National Capacity :

(as on 31.07.2022)

FY	2022-23	2023-24	2024-25	2025-26	Total (MW)
Central	2920	5940	2260	800	11920
State	2770	7680	3580	1600	15630
Private	0	0	0	0	0
Total	5690	13620	5840	2400	27550

III. Details of Technology wise Under Construction TPPs (excluding TPPs on hold) in the country:

(as on 31.07.2022)


Sector	Super Critical #		Sub-Critical		Total	
	No. of Projects	Capacity	No. of Projects	Capacity	No. of Projects	Capacity
	[Units]	(MW)	[Units]	(MW)	[Units]	(MW)
Central	7 [17]	11920	0	0	7 [17]	11920
State	12 [21]	15260	1 [1]	370	13 [22]	15630
Private	0	0	0	0	0	0
Total	19 [38]	27180	1 [1]	370	20 [39]	27550

Out of the 19 Supercritical TPPs, 6 projects (14 units) totaling to 9940 MW [4 projects (10 units) in central sector totaling 7300 MW and 2 projects (4 units) in state sector totaling 2640 MW] are based on Ultra Super critical technology. The details of these projects are given in Table 1.2


IV. Sector-wise Thermal Capacity Addition during last five years :

Thermal capacity addition (MW) after 12th Plan (from 01.04.2017 onwards)										
Sector	FY:2017-18		FY:2018-19		FY:2019-20		FY:2020-21		FY:2021-22	
	Target	Achievement	Target	Achievement	Target	Achievement	Target	Achievement	Target	Achievement
Central	4880	3170	2760	1960	6040	3940	5790	4080	5400	2370
State	3546	1760	4506	2850	4256	2780	4276	846	4360	1590
Private	2940	3780	Nil	972	Nil	45	525	0	525	525
Total	11366	8710	7266	5782	10296	6765	10591	4926	10285	4485

V.(a) Tentative Thermal Capacity Addition Program for FY 2022-23:

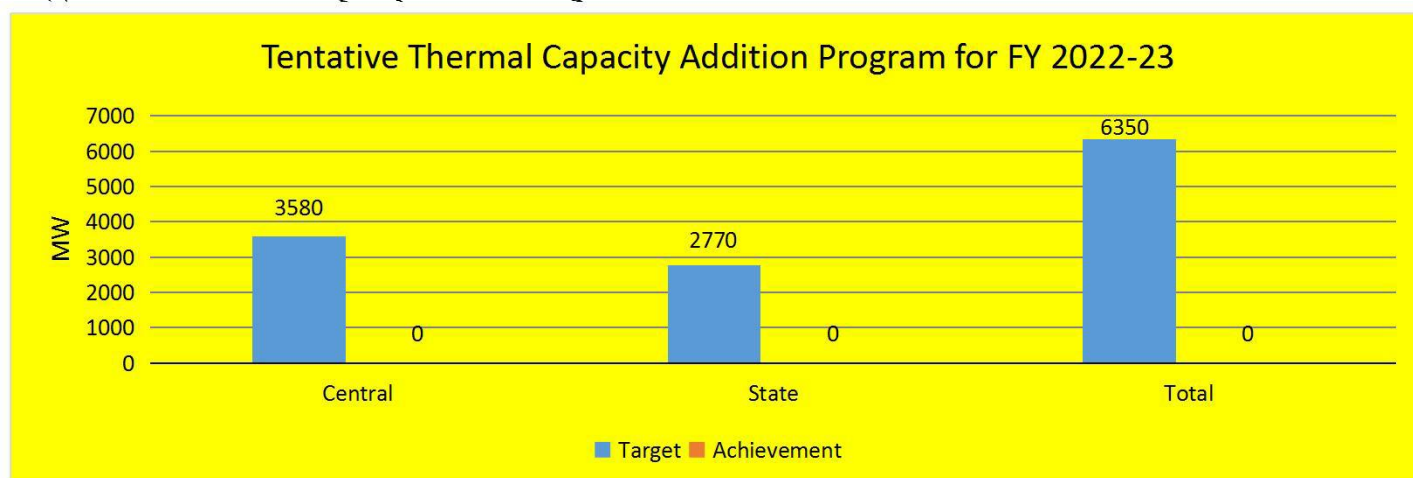

V.(b) Monthly Thermal Capacity Addition Achievement during FY 2022-23:

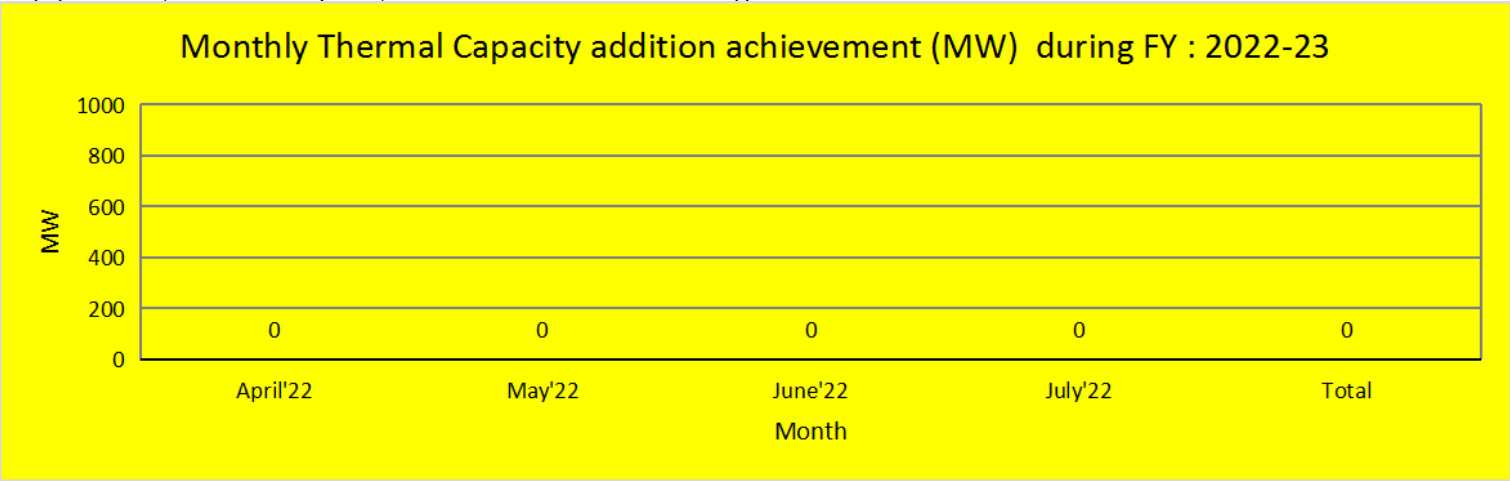

1.1 Tentative Thermal Capacity Addition Program and Actual Achievement for FY 2022-23 :

(as on 31.07.2022)

(as on 31.07.2022)										
S. No	Project Name	Implementing Agency	State	Boiler & Turbine Make	Unit No	Capacity (MW)	Trial Run anticipated at the Beginning of the year	Trial Run Assessment as per latest Review by CEA	Capacity Achieved (MW)	Actual Date of Capacity Addition
CENTRAL SECTOR										
1	Barh STPP-I	NTPC	Bihar	Boiler: DPSI, TG: Power Machine, Russia	U-2	660	Dec-22	Dec-22		
2	North Karanpura STPP	NTPC	Jharkhand	BTG: BHEL	U-1	660	May-22	Oct-22		
3	Ghatampur TPP	NUPPL	Uttar Pradesh	Boiler : MHPS, TG : Alstom & Bharat Forge	U-1	660	Dec-22	May-23		
4	Telangana STPP St- I	NTPC	Telangana	Boiler :MHPS, TG: Alstom & Bharat Forge	U-1	800	Aug-22	Nov-22		
					U-2	800	Feb-23	Feb-23		
Total Central Sector						3580				
STATE SECTOR										
5	Dr. Narla Tata Rao TPS St-V	APGENCO	Andhra Pradesh	BTG: BHEL	U-1	800	Jul-22	Aug-23		
6	North Chennai TPP St-III	TANGEDCO	Tamil Nadu	Boiler : BHEL(Alstom), TG: BHEL(Siemens)	U-1	800	Oct-22	Oct-22		
7	Yelahanka CCPP	KPCL	Karnataka	EPC: BHEL	GT+ST	370	Sep-22	Jan-23		
8	Sri Damodaran Sanjeevaiah TPP St-II	APPDCL	Andhra Pradesh	EPC: BHEL	U-1	800	Apr-22	Oct-22		
Total State Sector						2770				
Total Targeted Capacity						6350				

1.2 Thermal Power projects under construction in the country:

(as on 31.07.2022)

S.No.	Project Name	State	Implementing Agency	Boiler	Turbine	Technology	LOA Date	Unit No	Cap. (MW)	Org Trial Run	Anticipated Trial Run (as per CEA)	Original Cost (cr)	Latest Cost (cr)	Total Exp. (cr)	% Financial progress
CENTRAL SECTOR															
1	Barh STPP-I	Bihar	NTPC	Doosan	Power Machine, Russia	Supercritical	Mar-05	U-2	660	Dec-10	Dec-22	8693	21312	20056	94.1%
								U-3	660	Oct-11	Dec-23				
2	Buxar TPP	Bihar	SVVN	L&T	L&T	Supercritical	Jun-19	U-1	660	May-23	Jun-23	10439	10439	5768	55.3%
								U-2	660	Sep-23	Dec-23				
3	North Karanpura STPP	Jharkhand	NTPC	BHEL	BHEL	Ultra-Supercritical	Feb-14	U-1	660	Jun-18	Oct-22	14367	15389	13128	85.3%
								U-2	660	Dec-18	Oct-23				
								U-3	660	Jun-19	Jan-24				
4	Patratu STPP	Jharkhand	PVUNL	BHEL	BHEL	Ultra-Supercritical	Mar-18	U-1	800	Jan-22	Jun-24	17112	18668	6043	32.4%
								U-2	800	Jul-22	Dec-24				
								U-3	800	Jan-23	Jun-25				
5	Ghatampur TPP	Uttar Pradesh	NUPPL	L&T MHPS	GE Power system	Supercritical	Aug-16	U-1	660	May-20	May-23	17238	17238	13838	80.3%
								U-2	660	Nov-20	Aug-23				
								U-3	660	May-21	Nov-23				
6	Khurja SCTPP	Uttar Pradesh	THDC	L&T MHI	BHEL	Ultra-Supercritical	Aug-19	U-1	660	Jul-23	Feb-24	11089	11089	4806	43.3%
								U-2	660	Jan-24	Aug-24				
7	Telangana STPP St- I	Telangana	NTPC	BHEL	GE Power system	Ultra-Supercritical	Feb-16	U-1	800	May-20	Nov-22	10599	10998	9489	86.3%
								U-2	800	Nov-20	Feb-23				
Total Central Sector									11920			89537	105134	73128	
STATE SECTOR															
1	Dr.Narla Tata Rao TPS St-V	Andhra Pradesh	APGENCO	BHEL	BHEL	Supercritical	Dec-15	U-1	800	Apr-19	Aug-23	5287	7587	6977	92.0%
2	Sri Damodaram Sanjeevaiah TPP St-II	Andhra Pradesh	APPDCL	BHEL	BHEL	Supercritical	Nov-15	U-1	800	Jun-19	Oct-22	4276	7923	8204	103.5%
3	Jawaharpur STPP	Uttar Pradesh	UPRVUNL	Doosan	Doosan	Ultra-Supercritical	Dec-16	U-1	660	Dec-20	Jun-23	8079	10566	8889	84.1%
								U-2	660	Apr-21	Dec-23				
4	Obra-C STPP	Uttar Pradesh	UPRVUNL	Doosan India	Doosan India (GE)	Ultra-Supercritical	Dec-16	U-1	660	Dec-20	Jun-23	8778	10416	7573	72.7%
								U-2	660	Apr-21	Dec-23				
5	Panki TPS Extn.	Uttar Pradesh	UPRVUNL	BHEL	BHEL	Supercritical	Mar-18	U-1	660	Sep-21	Jan-24	5817	5817	4039	69.4%
6	Ennore SCTPP	Tamil Nadu	TANGEDCO	BHEL	BHEL	Supercritical	Sep-14	U-1	660	Nov-17	Mar-24	9800	9800	5748	58.7%
								U-2	660	Jan-18	May-24				
7	North Chennai TPP St-III	Tamil Nadu	TANGEDCO	BHEL	BHEL	Supercritical	Jan-16	U-1	800	Apr-19	Mar-23	6376	8723	7340	84.1%
8	Udangudi STPP Stage I	Tamil Nadu	TANGEDCO	BHEL	BHEL	Supercritical	Dec-17	U-1	660	Jan-21	Mar-24	13077	13077	6133	46.9%
								U-2	660	Mar-21	Jun-24				
9	Uppur Super Critical TPP	Tamil Nadu	TANGEDCO	BHEL	BHEL	Supercritical	Feb-16	U-1	800	Nov-20	On Hold	12778	12778	2298	18.0%
								U-2	800	Nov-20	On Hold				
10	Yadadri TPS	Telangana	TSGENCO	BHEL	BHEL	Supercritical	Oct-17	U-1	800	Oct-21	Jun-23	25099	29965	15844	52.9%
								U-2	800	Oct-21	Aug-23				
								U-3	800	Jun-22	Dec-23				
								U-4	800	Jun-22	Apr-24				
								U-5	800	Oct-22	Aug-24				
11	Yelahanka CCPP	Karnataka	KPCL	BHEL	BHEL	Sub critical	Nov-15	GT+ST	370	Feb-18	Jan-23	1571	2055	2283	111.1%
12	Bhusawal TPS	Maharashtra	MAHAGENCO	BHEL	BHEL	Supercritical	Jan-18	U-6	660	May-22	Jun-23	4548	4551	3630	79.8%
13	Sagardighi Thermal Power Plant Ph-III	West bengal	WBPDCL	BHEL	BHEL	Supercritical	Dec-18	U-1	660	Jan-24	Apr-24	3863	4567	843	18.4%
Total State Sector									15630			109347	127825	79800	
Grand Total									27550			198885	232958	152928	

1.3 Under construction TPPs where work is on hold / not likely to be commissioned:

(as on 31.07.2022)

S. No	State	Project Name / Impl. Agency/ EPC or BTG	LOA Date/ ordered date	Unit No	Cap. (MW)	Org. Comm. Sched.	Present Status/Remarks	Original Cost	Latest Cost (cr)	Exp. (cr)	Exp Till Date
CENTRAL SECTOR											
1	Rajasthan	Barsingar TPP ext/NLC/Reliance Infra/Chinese	Nov-16	U-1	250	May-20	Project put on hold due to withdrawal of PPA by DISCOM	2112.59	2112.59	158.25	Jan- 21
2	Rajasthan	Bithnok TPP /NLC/Reliance Infra/ Chinese	Nov-16	U-1	250	May-20	Project put on hold due to withdrawal of PPA by DISCOM	2196.3	2196.3	173.82	Jan- 21
TOTAL CENTRAL SECTOR [No. of Projects: 2, No. of Units: 2]					500						
STATE SECTOR											
1	Tamil Nadu	Ennore Exp. SCTPP/ Tangedco/ BTG Lanco (DEC-CHINA)	May-14	U-1	660	Jan-18	Based on the Board decision, fresh LoI has been issued to M/s BGR in June,2022.	4956	5421.38	791.4	Dec- 17
TOTAL STATE SECTOR [No. of Projects: 1, No. of Units: 1]					660						
PRIVATE SECTOR											
1	Andhra Pradesh	Bhavanapadu TPP Ph-I / East Coast Energy Ltd. / BTG DEC china	Sep-09	U-1	660	Oct-13	Liquidation Order date 22/04/2019 the Liquidator has partially sold the assets of the company on a standalone basis through e-auction. Regarding the remaining, advertisement has been published.	6571.94	9343.15	3785.6	Jan- 16
			Sep-09	U-2	660	Mar-14					
2	Andhra Pradesh	Thamminapatnam TPP stage –II / Meenakshi Energy Pvt. Ltd. SG-Cether vessels TG- Chinese	Dec-09	U-3	350	May-12	Admitted to NCLT on 07.11.2019. Resolution Plans have been received. RP is coordinating with PRAs for completing their due diligence and upon submission of the plan further steps under CIRP process would be taken up.	5005	5414.4	5414.4	Feb- 19
			Dec-09	U-4	350	Aug-12					
3	Bihar	Siriyi TPP (Jas Infra. TPP) / JICPL BTG-DEC China	Mar-11	U-1	660	Aug-14	Liquidation Order date 17.07.2020; The liquidator is unable to sell, alienate, transfer or create third party encumbrance on the property of the Corporate Debtor owing to NCLAT Directions. Liquidator is awaiting further directions from NCLAT for completion of the Liquidation process.	11120	11120	NA	NA
			Mar-11	U-2	660	Dec-14					
			Mar-11	U-3	660	Apr-15					
			Mar-11	U-4	660	Aug-15					
4	Chhattisgarh	Akaltara TPP (Naiyara) / KSK Mahandi Power Company Ltd., Boiler- SEPCO CHINA (Shanghai china) / TG- SEPCO (Dongfong china)	Apr-09	U-4	600	Apr-13	Admitted to NCLT on 03.10.2019. CIRP commenced on 03-10-2019EoI have been received from PRAs and the process for resolving the corporate debtor was progressing. However, NCLT ,Hyderabad vide its interim order dt 07-06-2022 stayed the CIRP.	16190	27080	18730	Dec- 16
			Apr-09	U-5	600	Aug-13					
			Apr-09	U-6	600	Dec-13					
5	Chhattisgarh	Binjkote TPP/ SKS Power Generation (Chhattisgarh) Ltd. Boiler-Cethar Vessels /Turbine-Harbin China	Mar-11	U-3	300	Mar-14	Due to non-availability of Long – Term PPA'S , lenders are not sanctioning any fresh loans. Due to funds constraint developer is not in a position to implement balance 2*300 MW BTG at this point of time.	5058	7940	3828	Jun- 15
			Mar-11	U-4	300	Jun-14					
6	Chhattisgarh	Lanco Amarkantak TPP- II/ LAP Pvt. Ltd. BTG-DEC china	Nov-09	U-3	660	Jan-12	Admitted to NCLT on 05.09.2019. CIRP is at advanced stage and is ongoing .	6886	10815.24	9537.79	Dec- 16
			Nov-09	U-4	660	Mar-12					
7	Chhattisgarh	Singhitarai TPP / Athena Chhattisgarh Power Ltd. BTG –DEC china	Dec-09	U-1	600	Nov-14	Admitted to NCLT on 15.05.2019 The Liquidator is underprocess and making efforts for Sale as a going concern.	6200	8443.79	6408.47	May- 17
			Dec-09	U-2	600	Feb-15					
8	Chhattisgarh	Salora TPP / Vandana Vidyut/ Boiler- Cether Vessels /TG Harbin China	Sep-09	U-2	135	Sep-11	Liquidation Order date 16.12.2019 The Liquidator is underprocess and making efforts for sale of the Thermal Power Plant.	1458.44	2386.89	2386.89	Mar- 15
9	Chhattisgarh	Deveri (Visa) TPP / Visa Power Ltd. BTG-BHEL	Jun-10	U-1	600	Aug-13	Liquidation Order date 11.10.2018 The liquidator has started the process of liquidating the company by selling the assets of the Corporate Debtor on piecemeal basis.BHEL claims certain unpaid lien on the assets available at the site of the Corporate Debtor and in this regard matter is still pending before the Supreme Court of India.	2618.7	3930	2077.23	Nov- 15
10	Jharkhand	Matrishri Usha TPP Ph-I / CorporatePower Ltd. EPC- BHEL	Dec-09	U-1	270	Apr-12	Admitted to NCLT on 19.02.2020 No compliant resolution plan were received, hence no resolution has been implemented. The liquidator may explore for sale of company as a going concern under the liquidation process after receipt of the liquidation order from the NCLT.	2900	3120	3120	Nov- 12
			Dec-09	U-2	270	May-12					
11	Jharkhand	Matrishri Usha TPP Ph-II / CorporatePower Ltd. EPC- BHEL	Mar-11	U-3	270	Oct-12		3182	3182	2207	Sep- 12
			Mar-11	U-4	270	Jan-13					
12	Jharkhand	Tori TPP Ph-I / Essar Power Ltd. BTG- Harbin China	Aug-08	U-1	600	Jul-12	Liquidation Order date 18.12.2019 The Liquidator has initiated the e-auction process for realizing the assets of the Corporate Debtor and till date has sold around 15,000 MT of Fabricated Steel Structure from the power plant	5700	5700	4757.92	Jun- 17
			Aug-08	U-2	600	Sep-12					
13	Jharkhand	Tori TPP Ph-II / Essar Power Ltd./ BTG- Harbin China	Feb-10	U-3	600	Dec-15		2500	2500	246.65	Mar- 15

14	Maharashtra	Amravati TPP Ph-II / Ratan India Power Pvt. Ltd. BTG-BHEL	Oct-10	U-1	270	Jul-14	Company has decided to drop Phase II due to following reasons: a) no new Bids for Long Term PPAs have been coming up in the Market since the last 5 years. b) the revised emission norms under the Environment (Protection) Amendment Rules, 2015 revising, inter alia, emission norms for thermal power plants., drastic changes in the design and equipment of Phase II was required to be carried out. c) Central Electricity Authority has stated in the National Electricity Plan that “No coal based capacity addition is required under any scenario irrespective of RE capacity addition”. Due to aforesaid reasons and non-availability of New PPAs, Lenders were reluctant to release funds for further construction of Phase II; hence, construction of Phase II had been stalled indefinitely. d) As per CEA small capacity plants are only for captive purpose and new capacity addition will be through super critical units only. Accordingly the entire contact awarded needs to be changed to super critical based technology of 660 MW and above and scrap the present capacity of 270 MW sub critical.	6646	6646	763.8	Mar- 15
			Oct-10	U-2	270	Sep-14					
			Oct-10	U-3	270	Nov-14					
			Oct-10	U-4	270	Jan-15					
			Oct-10	U-5	270	Mar-15					
15	Maharashtra	Nasik TPP Ph-II / Ratan India Nasik Power Pvt. Ltd. BTG-BHEL	Nov-09	U-1	270	Apr-13	Liquidation Order date 30.06.2021 The Liquidator has initiated for E- Auction Sale as a going concern.	6789	6789	711.81	Mar- 15
			Nov-09	U-2	270	Jun-13					
			Nov-09	U-3	270	Aug-13					
			Nov-09	U-4	270	Oct-13					
			Nov-09	U-5	270	Dec-13					
16	Maharashtra	Lanco Vidarbha TPP / LVP Pvt. Ltd. EPC- LANCO/ Boiler- Dongfong China / Turbine- Harbin china	Nov-09	U-1	660	Jul-14	Liquidation Order date 10.03.2021 7th e-Auction of the company on Slump Sale basis is currently underway	6936	10433	5338	Apr- 17
			Nov-09	U-2	660	Nov-14					
17	Maharashtra	Bijora Ghanmukh TPP / Jinbhuvish Power Generation Pvt. Ltd.	Sep-11	U-1	300	Dec-16	Work held up due to financial constraints.	3189	3450	422.27	Mar- 15
			Sep-11	U-2	300	Mar-17					
18	Maharashtra	Shirpur TPP ,Shirpur Power Pvt. Ltd./BTG- BHEL	Nov-11	U-2	150	Apr-15	Liquidation Order date 10.03.2021 7th e-Auction of the company on Slump Sale basis is currently underway	2413	2413	2277.94	Apr- 17
19	Madhya Pradesh	Gorgi TPP / D.B. Power (MP) Ltd. BTG- BHEL	Mar-11	U-1	660	Jun-13	Work is on hold at site due to Financial crunch being faced by the developer. Given the current status of Thermal Power Industry, company is exploring alternate options	3941	3941	475.79	Sep- 15
20	Odisha	Ind Barath TPP (Odisha) / Ind Barath/BTG-Cethar Vessels	May-09	U-2	350	Dec-11	Admitted to NCLT on 29.08.2018.	3150	4254	4254	Apr- 17
21	Odisha	KVK Nilanchal TPP/ KVK Nilanchal / BTG-Harbin China	Nov-09	U-1	350	Dec-11	Liquidation Order date 17.12.2020 The Liquidator has initiated for E- Auction Sale as a going concern.	4990	6000	1708.36	Mar- 15
			Nov-09	U-2	350	Feb-12					
			Nov-09	U-3	350	Feb-12					
22	Odisha	Lanco Babandh TPP / LBP Ltd./ BTG- DEC Chinese	Nov-09	U-1	660	Apr-13	Liquidation Order date 27.11.2019 The Liquidator has partially sold the assets of the company on a standalone basis through e-auction	6930	10430	7615	Mar- 17
			Nov-09	U-2	660	Aug-13					
23	Odisha	Malibrahmani TPP / MPCL/ BTG-BHEL	Jun-10	U-1	525	Dec-12	Liquidation Order date 23.10.2019. Company is under liquidation, however, the liquidation is not complete. There is stay by Hon'ble NCLAT, which is sub judice now.	5093	6330	5329.75	Dec- 14
			Jun-10	U-2	525	Feb-13					
24	Tamil Nadu	Tuticorin TPP (Ind- Barath) / IBPIL / BTG- Shangdong China	May-10	U-1	660	May-12	Liquidation Order date 22.04.2019 Stay on Liquidation Order	3595	3595	2000	May- 15
25	West Bengal	Hiranmaye Energy Ltd (India Power corporation (Haldia) TPP / Haldia Energy Ltd/ EPC- MEIL /BTG-BHEL.	Sep-10	U-3	150	May-16	Project is currently under hold	2656	3307	3263.05	Oct- 17
TOTAL PRIVATE SECTOR [No. of Projects:25, No. of Units:52]					23205						
GRAND TOTAL [No. of Projects: 28, No. of Units: 55]					24365						

BARH STPP St-I, Unit# 1, 2 & 3 (3x660 MW) / NTPC (CENTRAL SECTOR)

NTPC Barh Super Thermal Power Station, Barh, Distt – Patna, Bihar – 803215

E-Gen Portal Registration No. (U#1 - 1200002610; U#2 - 1200002611; U#3 - 1200002612)

Project Developer / Implementing Agency - NTPC			Main Plant Vendor - Power Machines, Russia, M/s TPE, M/s DPSI		
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	Trial Run Date	
Unit#1	Mar-2005	Feb-2010	Oct-2021		
Unit#2		Dec-2010	Dec-2022		
Unit#3		Oct-2011	Dec-2023		
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Indigenous, Non-pit head		ORIGINAL ESTIMATED COST OF THE PROJECT		8693.00
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST		21312.11
APPROVAL DATE / NTP	Feb-2005		DATE OF FINANCIAL CLOSURE		21.02.2005
EPC/BTG/BoP Contractor Details (Package Wise)	TG: Power Machines, Russia on 14.03.2005. Boiler: Awarded to TPE on 14.03.2005, contract terminated on 14.01.2015; Balance work awarded to DPSI on 30.01.2016. Pressure Parts ordered partially (replacement of DI 59 coils) to GE Power on 15.01.2018.		YEAR WISE EXPENDITURE		
PPA	Bihar (incl. Home state share): 1025 MW, Jharkhand: 202 MW, Orissa: 418 MW, Sikkim: 38 MW and unallocated: 297MW.		2010-11	921.81	
COAL LINKAGE/FSA	Letter of Assurance dtd. 18.11.2010 from CCL, securing 10 MMTPA coal for 03 Units. FSA of Unit-1 (3.333 MTPA) already signed with CCL(all operative mines, G8-G10) as per MoC PD dtd. 17.07.2013. FSA of Unit-2 & 3 to be signed after commissioning in terms of para 1A(i)of SHAKTI-2017 policy.		2011-12	1286.25	
			2012-13	1384.43	
			2013-14	1581.22	
			2014-15	568.49	
			2015-16	1143.46	
START UP POWER AGREEMENT	Done with PGCIL on 27.01.2020 for 400 kV D/C LILO of Kahalgaon-Patna, Barh-Patna & Barh-Gorakhpur lines		2016-17	1410.21	
POWER EVACUATION SYSTEM	Tx Line Developer	PGCIL	2017-18	1389.43	
	Tx Line Name Tx Voltage Level	LILOing of Kahalgaon – Patna 400 kV D/C (Quad) line at Barh (NTPC) switchyard.	2018-19	1453.89	
	Configuration of Tx Line (S/C or D/C)	D/C	2019-20	1502.47	
LAND POSSESSION	Required – 3212 Acres, Under Possession – 3212 Acres		2020-21	1123.15	
WATER ALLOCATION	100 Cusec from River Ganges		2021-22	1185.00	
MOEF CLEARANCE	11.09.2001		EXPENDITURE OF JULY’2022	54.43	
CIVIL AVIATION CLEARANCE	09.08.2004		TOTAL EXPENDITURE (upto 31.07.2022)	20055.97	
CPCB CLEARANCE	Not Applicable				
SPCB CLEARANCE	Consent to Operate (Emission & Discharge) Granted by SPCB on 04.07.2017, For Unit#1, and is Valid upto 30.09.2021				
FOREST CLEARANCE	Not Applicable				

BARH STPP St-I, Unit# 1, 2 & 3 (3x660 MW)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)							
Sl.	MILESTONE	UNIT-01		UNIT-02		UNIT-03	
		Original Date of Completion	Actual / Anticipated Date of Completion	Original Date of Completion	Actual / Anticipated Date of Completion	Original Date of Completion	Actual / Anticipated Date of Completion
1	COMPLETION OF BOILER FOUNDATION	Complete		Complete		Complete	
2	START OF BOILER ERECTION	May-06	Mar-11	Mar-07	Jul-11	Jan-08	Jan-12
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA		NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	Complete		Complete		Complete	
5	CONDENSER ERECTION START	Jun-07	Nov-08	Apr-08	Jan-09	Feb-09	Nov-13
6	TG ERECTION START	Aug-07	Aug-11	Jun-08	Sep-11	Apr-09	Mar-12
7	HP PIPING ERECTION START						
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	Dec-07	Feb-13	Oct-08	Jan-21	Aug-09	Dec-22
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION		Feb-13		Jan-21	-	Dec-22
10	TG BOX UP	Aug-08	Dec-13	Jun-09	Jan-15	Apr-10	Aug-23
11	HP PIPING ERECTION COMPLETION						
12	START OF OIL FLUSHING						
13	BOILER LIGHT UP	Aug-08	Aug-19	Jun-09	May-22	Apr-10	Jun-23
14	CHEMICAL CLEANING COMPLETION						
15	STEAM BLOWING START						
16	STEAM BLOWING COMPLETION	Jan-09	Jan-20	Nov-09	Aug-22	Sep-10	Aug-23
17	ROLLING & SYNC.	Mar-09	Sep-20	Jan-10	Oct-22	Nov-10	Oct-23
18	FULL LOAD		Apr-21		Nov-22		Nov-23
19	TRIAL RUN	Feb-10	Oct-21	Dec-10	Dec-22	Oct-11	Dec-23
20	COD		Nov-21				

STATUS OF MAIN PLANT PACKAGE (BTG) / SG - DPSI, TG - Power Machine, Russia					
Sl.	Packages	AREA	UNIT-01	UNIT-02	UNIT-03
			% Completion	% Completion	% Completion
1	BOILER	CIVIL	100%	100%	98%
		STRUCTURE		94%	66%
		PRESSURE PARTS		100%	85%
2	TG	CIVIL	100%	100%	100%
		STRUCTURE		100%	97%
		TG ERECTION		88%	68%
3	ESP	UNDER PROGRESS	100%	96%	92%
4	FGD	CIVIL WORK	25%	12%	13%
		MATERIAL SUPPLY	25%	23%	18%
		ERECTION WORK	1%	Yet to start	Yet to start

STATUS OF BOPs								
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (DPSI)	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01	UNIT-02	UNIT-03
						% Completion	% Completion	% Completion
1	Chimney	NBCC	20.12.2005	19.07.2009		100%	100%	100 %
2	Coal Handling Plant	L&T (Conveyor package)	22.09.2005	21.07.2009		100%	100%	100%
		L&T (Wagon Tripler				100%	100 %	100 %
		L&T(Stacker Reclaimer)				100%	100 %	100 %
3	Ash Handling Plant	Melco	15.04.2016	14.01.2019	U2-Oct'22; U3-Sep'23	100%	75%	50%
4	Fuel Oil System	Techno	07.05.2006	05.07.2009	U3-Jan'23	100%	100 %	86%
5	Cooling Towers	Paharpur	28.12.2005	27.08.2009	U2-Sep'22; U3-Aug'23	100%	92%	78%
6	CW Pump house	KBL	17.07.2006	16.01.2014	U3-Dec'22	100%	100 %	82 %
7	WPT Plant	SPML	28.05.2007	27.11.2008	Completed	100%	100 %	100 %
8	DM Plant	Driplex	24.03.2006	23.09.2008	Completed	100%	100 %	100 %
9	Compressed Air System	Power Machines	24.03.2005	29.10.2014	Completed	100%	100%	100%
10	Fire Protection System	Minimax	24.03.2006	23.07.2008	U2-Sep'22; U3-Dec'22	100%	94%	86%
11	Switch Yard	BHEL	23.03.2006	06.11.2009	Completed	100%	100 %	100 %
12	Station Transformers	ABB	10.10.2005	11.09.2008	U3-Mar'23	100%	100%	76%
13	Unit Transformers	TRIL/BHEL/Kanohar	22.05.2006	21.01.2009	U3-Aug'23	100%	100%	78%
14	Railway Siding	RITES	28.06.2006	27.12.2007	Completed	100%	100 %	100 %
15	Power Evacuation Lines	PGCIL			Completed	100%	100%	100%

CRITICAL ISSUES

♦ DPSI has expressed inability in supply of balance main equipment as well as mandatory spares of SG Pkg ordered by them on TKZ, Russia due to risk of secondary sanctions affecting the progress of work. Process of award directly by NTPC in progress.

Readiness of railway line Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur route (250km) is required to ease the coal transportation and enable requisite quantity of coal transportation for Barh Project. NTPC has funded Rs 664 Crores to Railways for development of following works in envisaged Coal transportation route. Construction of Karnauti-Bakhtiyarpur flyover (Acquisition of ~6 Acre land by Railways is balance) and Construction of Manpur Flyover (ROR).

REASONS OF DELAY

♦ Inordinate delay by Main Plant (SG & Auxiliaries Package) vendor M/s TPE. Work started after 6 Years of award. Contract of M/s TPE was terminated in Jan'15 due to consistent failure of commitments and poor performance. Contract for balance works re-awarded after 1 year in Jan'2016.

♦ During Hydro Test of Boiler U#1, DI-59 Coils in PSH-IV, CSH & LPRH-II failed which were supplied by M/s TPE. Accordingly, change of material to SS304H was approved and contract was awarded to M/s GE on 15.01.2018 for supply, Dismantling & Installation of Coils. Delayed project by approx. 2 years.

♦ Due to unusual delay in project commissioning for Main plant vendors, revival of Balance Offsite Packages is taking considerable time.

♦ Due to US sanction on Power Machines, Russia, balance TG/SG supplies and works got delayed.

NORTH KARANPURA TPP, Unit# 1, 2 & 3 (3x660 MW) / NTPC (CENTRAL SECTOR)

NTPC North Karanpura, Tandwa, Sub division – Simaria, Distt–Chatra – Jharkhand-825321

E-Gen Portal Registration No. (U#1 - 1200002378; U#2 - 1200002379; U#3 - 1200002380)

Project Developer / Implementing Agency - NTPC			Main Plant Vendor - BHEL (EPC)		
Unit No.	LOA		Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Feb-2014		Jun-2018		Oct-2022
Unit#2			Dec-2018		Oct-2023
Unit#3			Jun-2019		Jan-2024
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Pithead		ORIGINAL ESTIMATED COST OF THE PROJECT		14367.00
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST		15389.42
APPROVAL DATE / NTP	Feb-2014		DATE OF FINANCIAL CLOSURE		28.01.2014
EPC/BTG/BoP Contractor Details (Package Wise)	BTG (EPC) – BHEL		YEAR WISE EXPENDITURE		
			2010-11	8.17	
PPA	Jharkhand: 500 MW; Odisha: 396 MW; Bihar: 688 MW; WB: 99 MW; Unallocated: 297 MW.		2011-12	4.88	
COAL LINKAGE/FSA	Letter of Assurance dtd. 24.03.2015 from CCL, securing 7.039 MTPA coal (G7-G11) for 03 Units. FSA to be signed after commissioning in terms of para 1A (i) of SHAKTI-2017 policy.		2012-13	5.75	
			2013-14	1362.18	
			2014-15	527.92	
START UP POWER AGREEMENT	Through ATS – 400 KV NK Chandwa line. Line is under construction. Agreement yet to be done.		2015-16	615.73	
POWER EVACUATION SYSTEM	Tx Line Developer	NKTL	2016-17	2199.92	
	Tx Line Name Tx Voltage Level	i) NKSTPP-Chandwa 400 KV, D/c line ii) NKSTPP-Gaya, 400 KV D/c line	2017-18	2044.46	
	Configuration of Tx Line (S/C or D/C)	D/C	2018-19	1747.91	
LAND POSSESSION	2263/ 2293 Acres. 30 Acres pending for acquisition.		2019-20	1762.62	
WATER ALLOCATION	20 Cusec from Garhi River – Raw water drawl agreement signed with DVC on 18.09.2020.		2020-21	1243.28	
MOEF CLEARANCE	29.11.2004		2021-22	1051.00	
CIVIL AVIATION CLEARANCE	13.02.2009		EXPENDITURE OF JULY'2022	127.00	
CPCB CLEARANCE	Not Applicable		TOTAL EXPENDITURE (upto 31.07.2022)		
SPCB CLEARANCE	Available. 31.12.2001 for Bihar. 11.12.2014 for Jharkhand		13128.00		
FOREST CLEARANCE	03.11.2015				

NORTH KARANPURA TPP, Unit# 1, 2 & 3 (3x660 MW) / NTPC (CENTRAL SECTOR)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)

Sl.	MILESTONE	UNIT-01		UNIT-02		UNIT-03	
		Original Date of Completion	Actual / Anticipated Date of Completion	Original Date of Completion	Actual / Anticipated Date of Completion	Original Date of Completion	Actual / Anticipated Date of Completion
1	COMPLETION OF BOILER FOUNDATION		Complete		Complete		Complete
2	START OF BOILER ERECTION	Aug-15	Apr-16	Feb-16	Jul-16	Aug-16	Jun-17
3	BOILER DRUM LIFTING (if sub-critical unit)		NA		NA		NA
4	BOILER CEILING GIRDER LIFTING COMPLETION		Complete		Complete		Complete
5	CONDENSER ERECTION START	May-16	Nov-18	Nov-16	Jan-20	May-17	Aug-22
6	TG ERECTION START	Jul-16	Nov-17	Jan-17	Jan-18	Jul-17	Mar-22
7	HP PIPING ERECTION START						
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	Jan-17	Dec-18	Jul-17	Oct-19	Jan-18	Nov-22
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION		Jan-19		Oct-19	-	Nov-22
10	TG BOX UP	Jun-17	Aug-19	Dec-17	Jan-22	Jun-18	Dec-22
11	HP PIPING ERECTION COMPLETION						
12	START OF OIL FLUSHING						
13	BOILER LIGHT UP	Aug-17	Dec-20	Feb-18	Nov-22	Aug-18	May-23
14	CHEMICAL CLEANING COMPLETION						
15	STEAM BLOWING START						
16	STEAM BLOWING COMPLETION	Oct-17	Feb-21	Apr-18	Jan-23	Oct-18	Jul-23
17	ROLLING & SYNC.	Dec-17	Mar-22	Jun-18	May-23	Dec-18	Dec-23
18	FULL LOAD	Feb-18	Jul-22	Aug-18	Jun-23	Feb-19	Jan-24
19	TRIAL RUN	Jun-18	Oct-22	Dec-18	Oct-23	Jun-19	Jan-24
20	COD						

STATUS OF MAIN PLANT PACKAGE (BTG) : BHEL

Sl.	Packages	AREA	UNIT-01	UNIT-02	UNIT-03
			% Completion	% Completion	% Completion
1	BOILER	CIVIL	100%	96%	79%
		STRUCTURE	100%	88%	62%
		PRESSURE PARTS	100%	99%	35%
2	TG	CIVIL	98%	99%	95%
		STRUCTURE	100%	99%	94%
		TG ERECTION	NA	NA	NA
3	ESP	UNDER PROGRESS	100%	95%	59%
4	FGD	CIVIL WORK	31%	31%	31%
		MATERIAL SUPPLY	17%	32%	8%
		ERECTION WORK	7%	0%	0%

STATUS OF BOPs

Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (DPSI)	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01	UNIT-02	UNIT-03
						% Completion	% Completion	% Completion
1	Chimney	M/s BHEL	Feb-14	U#1-Dec-18 U#2-Jun-19 U#3-Sep-20	U#2-Dec-22 U#3-Sep-23	100%	83%	78%
2	Coal Handling Plant	M/s BHEL (Conveyor package)	Feb-14	Dec-18	U#2-Sep-23 U#3-Dec-23	95%	43%	27%
		M/s BHEL (Wagon Tripler)	Feb-14	NA	NA	NA	NA	NA
		M/s BHEL (Stacker Reclaimer)	Feb-14	Dec-18	U#1-Nov-22 U#2&3-Sep-23	78%	48%	48%
3	Ash Handling Plant	M/s BHEL	Feb-14	Dec-18	U#1-Aug-22 U#2-Sep-23 U#3-Dec-23	93%	30%	0%
4	Fuel Oil System	M/s BHEL	Feb-14	Dec-18	Completed	100%	100%	100%
5	Cooling Towers	M/s BHEL	Feb-14	Dec-18	Completed	100%	100%	100%
6	CW Pump house	M/s BHEL	Feb-14	NA	NA	NA	NA	NA
7	WPT Plant	M/s BHEL	Feb-14	Dec-18	Completed	100 %	100 %	100 %
8	DM Plant	M/s BHEL	Feb-14	Dec-18	Completed	100%	100%	100%
9	Compressed Air System	M/s BHEL	Feb-14		Completed	100%	100%	100%
10	Fire Protection System	M/s BHEL	Feb-14		U#2-Jan'23 U#3-Jun'23	100%	50%	0%
11	Switch Yard	BHEL-TBG/Arun Construction Technico India Pvt. Ltd.	Feb-14	Dec-18	U#2-Jan'23 U#3-Jan'23	100%	70%	70%
12	Station Transformers	M/s BHEL	Feb-14	Mar-18	U#2-Feb'23 U#3-Mar'23	70%	25%	22%
13	Unit Transformers	M/s BHEL	Feb-14	Jul-18	U#2-May'23 U#3-Sep'23	100%	30%	30%
14	Railway Siding	M/s BHEL	Feb-14	NA	NA	NA	NA	NA
15	Power Evacuation Lines	M/s BHEL			Aug'22	0%	0%	0%

CRITICAL ISSUES

- ♦ Works of BoP package (BHEL) needs to be expedited.(CHP/AHP most critical)
- ♦ Forest Clearance in ATS –NK Chandwa line to be expedited. CCL Yet to Handover the Land for pipe conveyer Ext CHP.
- ♦ Support of State Govt of Jharkhand is required for following:
 1. Acquisition / transfer/ possession of balance 30 Acres land for Ash Dyke and Reservoir
 2. Providing administrative support during execution, on GM land, where claims of land encroachers has been rejected recently.
 3. Expediting Forest clearance for land under Acquisition by CCL for external CHP.

REASONS OF DELAY

- ♦ Main plant layout was changed to avoid GM land which Govt. was not in position to handover due to encroachments.
- ♦ Delay in Award of Critical Packages by BHEL. Air Cooled Condenser (ACC) Mechanical Package awarded in Mar'17 with a delay of 31months; ACC civil package was awarded in May'17 with a delay of 27 months.
- ♦ Delay due to slow work progress by EPC agency (M/s BHEL). Slow progress of Air Cooled Condenser works by M/s BHEL may affect the current commissioning target of project.
- ♦ Agitation by villagers for demand of additional compensation against already acquired land (about 2200 Acres). Project Work was completely stopped by the agitators,for about 40 days during Local Agitation again started on 23.02.2022

TELANGANA THERMAL POWER PROJECT, Unit# 1 & 2 (2X800 MW, St-I) / NTPC (CENTRAL SECTOR)

NTPC Telangana, PO Ramagundam (Sub Office), Karim Nagar, Telangana:- 505208

E-Gen Portal Registration No. (U#1 - 1200001966; U#2 - 1200001967)

Project Developer / Implementing Agency - NTPC			Main Plant Vendor - BHEL (EPC)		
Unit No.	LOA		Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Feb-2016		May-2020	Nov-2022	
Unit#2			Nov-2020	Feb-2023	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Indigenous, Non- pit head		ORIGINAL ESTIMATED COST OF THE PROJECT		10599.00
COAL COMBUSTION TECHNOLOGY	Ultra-supercritical		LATEST ESTIMATED COST		10997.70
APPROVAL DATE / NTP	Jan-2016		DATE OF FINANCIAL CLOSURE		29.01.2016
EPC/BTG/BoP Contractor Details (Package Wise)	SG Island – BHEL – 05.02.2016; TG Island – GE – 05.02.2016		YEAR WISE EXPENDITURE		
			2015-16	6.34	
PPA	1360 MW power has been allocated to Telangana. Balance 240 MW is unallocated.		2016-17	798.21	
COAL LINKAGE/FSA	Linked with Mandakini-B captive coal mine (PRC-20 MMTPA); however, NTPC has approached MoC on 26.12.2020 for surrendering the coal mine. Tapering linkage against the linked coal mine was initially allocated from WCL cost-plus. In July’2020, the linkage has been shifted to SCCL. Coal quantity quantified by the Coal Controller is 6.846 MTPA.		2017-18	1062.65	
			2018-19	2535.67	
			2019-20	2599.45	
			2020-21	1308.35	
START UP POWER AGREEMENT	Start up Power has been granted for Telangana STPP by SRLDC on 26-6-2020 through RSTPS-TeSTPP 400 KV D/C line		2021-22	828.00	
POWER EVACUATION SYSTEM	Tx Line Developer	TSTRANSCO	EXPENDITURE OF JULY’2022		96.21
	Tx Line Name Tx Voltage Level	i) TeSTPP-Narsapur, 400 KV, D/c Line. ii) TeSTPP- Ramadugu ,400 KV, D/c line.	TOTAL EXPENDITURE (upto 31.07.2022)		9489.00
	Configuration of Tx Line (S/C or D/C)	D/C			
LAND POSSESSION	Being accommodated within the land possessed with NTPC Ramagundam project. No new land acquired for the project.				
WATER ALLOCATION	60 cusecs from Yellampally Barrage on Godavari river				
MOEF CLEARANCE	20.01.2016, Valid upto 19.01.2024				
CIVIL AVIATION CLEARANCE	29.03.2011				
CPCB CLEARANCE	Not Applicable				
SPCB CLEARANCE	Extension for Stg-1 approved by TSPCB up to 19-01-2023				
FOREST CLEARANCE	Not Applicable				

TELANGANA THERMAL POWER PROJECT, Unit# 1 & 2 (2X800 MW, St-I) / NTPC (CENTRAL SECTOR)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)					
Sl.	MILESTONE	UNIT-01		UNIT-02	
		Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date
1	COMPLETION OF BOILER FOUNDATION	Complete		Complete	
2	START OF BOILER ERECTION	Mar-17	Dec-17	Sep-17	Dec-17
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	Complete		Complete	
5	CONDENSER ERECTION START	Feb-18	Jul-18	Aug-18	Feb-19
6	TG ERECTION START	May-18	Aug-18	Nov-18	Mar-19
7	HP PIPING ERECTION START				
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	Nov-18	Nov-21	May-19	Apr-22
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION		May-22		Aug-22
10	TG BOX UP	Apr-19	Sep-19	Oct-18	May-20
11	HP PIPING ERECTION COMPLETION				
12	START OF OIL FLUSHING	Complete		Complete	
13	BOILER LIGHT UP	Jun-19	Jun-22	Dec-19	Nov-22
14	CHEMICAL CLEANING COMPLETION				
15	STEAM BLOWING START		Aug-22		Dec-22
16	STEAM BLOWING COMPLETION	Sep-19	Sep-22	Mar-20	Dec-22
17	ROLLING & SYNC.	Nov-19	Sep-22	May-20	Jan-23
18	FULL LOAD	Jan-20	Oct-22	Jul-20	Jan-23
19	TRIAL RUN	May-20	Nov-22	Nov-20	Feb-23
20	COD				

STATUS OF MAIN PLANT PACKAGE (BTG) : SG - BHEL, TG - GE							
Sl.	Packages	AREA	UNIT-01	UNIT-02			
			% Completion	% Completion			
1	BOILER	CIVIL	100%	88%			
		STRUCTURE	97%	84%			
		PRESSURE PARTS	100%	90%			
2	TG	CIVIL	100%	100%			
		STRUCTURE	100%	100%			
		TG ERECTION	100%	100%			
3	ESP	UNDER PROGRESS	96%	92%			
4	FGD	CIVIL WORK	96%	93%			
		MATERIAL SUPPLY	100%	100%			
		ERECTION WORK	91%	81%			
STATUS OF BOPs							
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated /Actual Date of Completion	UNIT-01 % Completion	UNIT-02 % Completion
1	Chimney	BHEL	05.02.16	30.08.19 (U1) 28.02.20(U2)	Oct-22	100%	80%
2	Coal HandlingPlant	Conveyor Package – Tata Projects Ltd	10.01.17	10.03.20	U1-Sep22; U2-Feb23	90%	80%
		Wagon Tippler – Tata Projects Ltd	10.01.17	10.03.20	Dec22	50%	
		Stacker Reclaimer - Tata Projects Ltd	10.01.17	10.03.20	U1-Sep22; U2-Jan23	97%	75%
3	Ash Handling	BHEL	05.02.16	27.11.19	U1-Nov22; U2-Jan23	90%	75%
4	Fuel Oil System	TATA Projects	10.01.17	09.01.20	U2-Oct22	100%	95%
5	Cooling Towers	TATA Projects	10.01.17	10.01.20	U2-Jan23	100%	70%
6	CW Pump	TATA Projects	10.01.17	10.02.20	U2-Oct22	100%	90%
7	WPT Plant	TATA Projects	10.01.17	10.03.20	Completed	100%	100%
8	DM Plant	TATA Projects	10.01.17	23.09.08	Completed	100%	100%
9	Compressed Air System	TATA Projects	10.01.17	29.10.14	Completed	100%	100%
10	Fire Protection System	TATA Projects	10.01.17	10.05.20	U1-Sep22; U2-Jan23	95%	80%
11	Switch Yard	TATA Projects	10.01.17	10.12.19	Completed	100%	100 %
12	Station Txer	TATA Projects	10.01.17	10.06.20	Completed	100%	100 %
13	Unit Txer	TATA Projects	10.01.17	10.06.20	U2-Dec22	100%	95 %
14	Railway Siding	TATA Projects	10.01.17	10.03.20	Dec22	70%	
15	Power evacuation	TSTransco			Completed	100%	100%

CRITICAL ISSUES

♦ Poor site mobilization and delayed in materials supply by BHEL is hampering site work progress.

REASONS OF DELAY

- ♦ Delay in Boiler design due to new De-Nox & De-Sox norms (New Env. norms came after opening of Price Bid and were incorporated in the contract). Accordingly, there was delay in Completion of Basic Engg. and Supply of Boiler / TG structures.
- ♦ Slow progress by BHEL sub-agency M/s B&R.
- ♦ Delay in Sand supply / Procurement at site (Due to restrictions by State Government of Telangana).
- ♦ Delay due to ongoing COVID-19 pandemic since Mar'20. Non-availability of Industrial oxygen during second wave.

PATRATU TPS, Unit# 1, 2 & 3 (3X800 MW) / PVUNL (CENTRAL SECTOR)

Patratu Vidyut Utpadan Nigam Limited, Patratu, PO: PTPS, Patratu, Distt. Ramgarh, Jharkhand , PIN – 829119
E-Gen Portal Registration No. (U#1 - 1200002399; U#2 - 1200002400; U#3 - 1200002401)

Project Developer / Implementing Agency - PVUNL			Main Plant Vendor - M/S BHEL (EPC-08.03.2018)			
Unit No.	LOA		Original Trial Run Date	Anticipated / Actual	Trial Run Date	
Unit#1	Mar-2018		Jan-22	Jun-2024		
Unit#2			Jul-22	Dec-2024		
Unit#3			Jan-23	Jun-2025		
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)			
FUEL TYPE	Coal, Pithead		ORIGINAL ESTIMATED COST OF THE PROJECT		17112.00	
COAL COMBUSTION TECHNOLOGY	Ultra Supercritical		LATEST ESTIMATED COST		18668.00	
APPROVAL DATE / NTP	Nov-2017		DATE OF FINANCIAL CLOSURE			
EPC/BTG/BoP Contractor Details (Package Wise)	EPC package awarded to BHEL on 08.03.2018.		YEAR WISE EXPENDITURE			
			2015-16	-----		
PPA	85% allocated to Jharkhand, PPA signed on 30.03.2016. 15% of power will remain as unallocated quota at the disposal of GoI		2016-17	-----		
COAL LINKAGE/FSA	12 MTPA for Ph-I from Banhardih Coal Mine at a distance of about 110 km. Banhardi Coal Mine transferred to PVUNL vide deed of adherence signed on 02.06.2017.		2017-18	992.11		
	Bridge allocation granted by SLC(LT) upto 24-06-2024; Allocation from CCL; Coal quantity quantified is 9.17 MTPA.		2018-19	601.86		
START UP POWER AGREEMENT	Through 7.5 kms Transmission line : Patratu-Patratu (Main Plant to Katia Substation) D/C Line		2019-20	695.09		
POWER EVACUATION SYSTEM	Tx Line Developer	JUSNL	2020-21	1228.66		
	Tx Line Name Tx Voltage Level	i) Patratu (PVUNL) –Patratu, 400 kV D/C line (7.5 km). ii) Patratu STPP-Koderma, 400 KV D/c Line (160 Km). iii) Patratu STPP-Chandil, 400 KV D/c Line (150 Km).	2021-22	1846.48		
		Configuration of Tx Line (S/C or D/C)	D/C	EXPENDITURE OF JULY’22	202.91	
				TOTAL EXPENDITURE (upto 31.07.22)	6043.08	
LAND POSSESSION	Correction of 268.92 acres of land in the records of forest department in favour of PVUNL and also change of nature of land as non-forest					
WATER ALLOCATION	Project is envisaged with Air Cooled Condenser Technology. In principle commitment for 27 cusecs water available from Nalkari Dam Reservoir vide agreement dt 25.01.2016 with GoJ.					
MOEF CLEARANCE	EAC recommended for grant of EC for the project on EAC meeting held on 25.09.17. EC letter received on 07.11.17. Validity till 06.11.24.					
CIVIL AVIATION CLEARANCE	Received on 03.06.2016.					
CPCB CLEARANCE	Not Applicable					
SPCB CLEARANCE	SPCB Clearance: CTE received on 19.10.2018. Validity till 06.11.24.					
FOREST CLEARANCE	No forest land in the main plant area.					

STATUS AS ON 01.07.2022

PATRATU TPS, Unit# 1, 2 & 3 (3X800 MW) / PVUNL (CENTRAL SECTOR)																
UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)								STATUS OF MAIN PLANT PACKAGE (BTG) : M/S BHEL								
Sl.	MILESTONE	UNIT-01		UNIT-02		UNIT-03		Sl.	Packages	AREA	UNIT-01	UNIT-02	UNIT-03			
		Original Date of Completion	Anticipate d / Actual Date of Completion	Original Date of Completion	Anticipate d / Actual Date of Completion	Original Date of Completion	Anticipate d / Actual Date of Completion				% Completion	% Completion	% Completion			
1	COMPLETION OF BOILER FOUNDATION	May-19	Apr-19	Nov-19	Dec-19	May-20	Jan-21	1	BOILER	CIVIL	76.9%	74.4%	64.8%			
2	START OF BOILER ERECTION	May-19	Aug-19	Nov-19	Dec-19	May-20	Jan-21			STRUCTURE	65.0%	66.9%	53.5%			
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA		NA				PRESSURE PARTS	57.2%	39.5%	19.2%			
4	BOILER CEILING GIRDER LIFTING COMPLETION	Feb-20	Mar-21	Aug-20	May-21	Feb-21	Jan-22	2	TG	CIVIL	60.9%	47.6%	31.7%			
5	CONDENSER ERECTION START	Feb-20	Jan-23	Aug-20	Jul-23	Feb-21	Jan-24			STRUCTURE	80.3%	21.6%	0.0%			
6	TG ERECTION START	Jun-20	Mar-22	Dec-20	Jul-22	Jun-21	Dec-22									
7	HP PIPING ERECTION START	Jul-20	Aug-22	Jan-21	Dec-22	Jul-21	Jun-23	3	ESP	UNDER PROGRESS	57.6%	62.1%	34.9%			
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	Jan-21	Nov-22	Jul-21	Jan-23	Jan-22	Jul-23	4	FGD	CIVIL WORK	80.0%	56.0%	42.0%			
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	Jun-21	Apr-23	Dec-21	Jun-23	Jun-22	Dec-23			MATERIAL SUPPLY	0.7%	2.0%	0.0%			
10	TG BOX UP	May-21	Jun-23	Nov-21	Oct-23	May-22	Apr-24			ERECTION WORK	6.1%	0.0%	0.0%			
11	HP PIPING ERECTION COMPLETION	May-21	Jun-23	Nov-21	Oct-23	May-22	Apr-24	STATUS OF BOPs (BHEL - EPC)								
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated/ Actual Date of Completion	UNIT-01	UNIT-02	UNIT-03								
						% Completion	% Completion	% Completion								
1	Chimney	BHEL PSWR	U1-21.07.18; U2-26.07.18; U3-31.01.20	U1-48.01.21; U2-05.02.21; U3-05.03.22	Feb-25	100% RCC	84.9% RCC	54.9% RCC								
2	Coal Handling Plant	BHEL PSWR	12.01.2020	08.08.2021	Feb-25	42.0% RCC complete										
		BHEL PSWR – Wagon Tippler		27.07.2021	Feb-25											
		BHEL PSWR – Stacker Reclaimer	09.06.2021		Feb-25											
3	Ash Handling Plant	BHEL PSWR	15.10.2019	08.12.2021	Feb-25	52.7% RCC complete										
4	Fuel Oil System	BHEL PSWR	07.10.2020	08.06.2021	Feb-25	36.3% civil works										
5	Cooling Towers	NA (ACC is envisaged)	08.04.2022		Feb-25	Footing RCC works-15.1% completed										
6	CW Pump house	NA (ACC is envisaged)				NA(Air Cooled Condenser)										
7	WPT Plant	BHEL PSWR	14.01.2021	20.03.2021	Feb-25	37.5% RCC complete										
8	DM Plant	BHEL PSWR		27.03.2021	Feb-25	19.4% RCC complete										
9	Compressed Air System	BHEL PSWR	04.07.2020	03.02.2021	Feb-25	Civil Work in progress										
10	Fire Protection System	BHEL-PESD, Hyderabad	25.05.2021	18.05.2021	Feb-25	64% RCC civil works										
11	Switch Yard	BHEL-TBG	01.05.2020	08.10.2021	Feb-25	71.5% RCC complete										
12	Station Transformers	BHEL-Bhopal		18.02.2021	Feb-25	Work yet to start										
13	Unit Transformers	BHEL Jhansi		17.02.2021	Feb-25	Work yet to start										
14	Railway Siding	PMC Contractor-M/s RITES	02.12.2019		01.04.23	Award of sub pkg yet to be done										
15	Power Evacuation Lines	JUSNL			Feb-25	Work yet to start										

CRITICAL ISSUES

- CHP Package: Entire CHP supply is awarded to 4 different agencies by BHEL. Commercial issues between BHEL & sub-agencies are affecting the supplies of Stacker Re-claimer, Track Hopper, Wagon Tippler, Conveyor system.
- Award of Start-up power line and balance 02 STU lines by GoJ: Start up powerline i.e., Patratu- Patratu (Main Plant to Katia Substation) D/C Line (7.5 Kms)- Proposal Approved. NIT done on 09.04.2021 by JUSNL. Bid opened on 17.06.21. Cabinet approval for award of line work received on 10.02.2022 but agency decline to accept the offer. JUSNL has retendered the work on 05.03.2022. BOD (Tech) done on 02.05.22. BOD (Price) opened on 24.05.2022. Award and execution is critical to ensure timely availability of Startup Power for U#1 Boiler Hydro test.
- Patratu STPP- Koderma (JUSNL) 400kV D/C line (160 km): Erection of these lines is to be done by JUSNL under state funding. Investment approval received on 10.02.22. NIT done on 15.05.2022. BOD (Tech) extended to 15.07.22. Work is to be executed by JUSNL. Patratu STPP- Chandil (JUSNL) 400kV D/C line are (150 km): Erection of these lines are to be done by JUSNL under state funding. Investment approval received on 10.02.22. NIT done on 15.05.22. BOD (Tech) extended to 15.07.22. Work is to be executed by JUSNL. The above two lines are critical for evacuation of power.

REASONS OF DELAY

- Poor performance of few sub-agencies of BHEL.

GHATAMPUR THERMAL POWER PROJECT, Unit# 1, 2 & 3 (3x660 MW) / NUPPL (CENTRAL SECTOR)

Near Village Lahurimau-Kasimpur, Ghatampur Tehsil, P.O.: Samuhi-209206, Kanpur Nagar District, Uttar Pradesh
E-Gen Portal Registration No. (U#1 - 1200002439; U#2 - 1200002440; U#3 - 1200002441)

Project Developer / Implementing Agency - NUPPL			Main Plant Vendor - M/s L&T (SG) and M/s GE (TG)			
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	Trial Run Date		
Unit#1	Aug-2016	May-2020	May-2023			
Unit#2		Nov-2020	Aug-2023			
Unit#3		May-2021	Nov-2023			
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)			
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT		17237.80	
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST		Not Revised	
APPROVAL DATE / NTP	GoI Sanction - 27.07.2016		DATE OF FINANCIAL CLOSURE		22.06.2021	
EPC/BTG/BoP Contractor Details (Package Wise)	Contractor Details: 1. SG Package (GA1)- L&T-MHI Power Boilers Pvt. Ltd/ LoA Date-02-08-2016 2. TG Package (GA2)- GE Power Systems IndiaPvt. Ltd /LoA Date-02-08-2016 3. BoP Package (GA3)- BGR Energy Systems Ltd / LoA Date-21-11-2016		YEAR WISE EXPENDITURE			
PPA	75% PPA Signed with Uttar Pradesh Power Corporation Ltd.(UPPCL).Signing of balance 25% PPA is balance.		2016-17		927.76	
COAL LINKAGE/FSA	Allocation Date- 03.10.2016. Allocated Mine (Source) - Pachwara South Coal Block Grade - G10 Quantity- Net Geological Reserve 373.52 MT. Extractable reserve - 262.84MT; Pachwara South Coal Block will be fully functional by the end of Financial Year 2026-27 and will be able to meet the coal requirement of NUPPL. Hence, NUPPL is seeking coal under bridge linkage by the time Pachwara South Coal Block will be fully functional.		2017-18		1228.45	
			2018-19		3517.83	
			2019-20		3525.17	
			2020-21		2260.09	
			2021-22		1901.77	
START UP POWER AGREEMENT	There are four incoming lines for 132KV Start-up power. Four lines are from: 1. Sarh-1 to NUPPL, 2. Ghatampur to NUPPL, 3. Sarh-2 to NUPPL, 4. Hamirpur to NUPPL; Out of four two are connected and we are availing power through two lines (Ghatampur to NUPPL & Sarh-2 to NUPPL).		EXPENDITURE OF JULY'2022		107.51	
POWER EVACUATION SYSTEM	Tx Line Developer	M/S GTL				
	Tx Line Name Tx Voltage Level	i)765 KV, S/C, Ghatampur-Agra line; ii) 765 KV, S/C, Ghatampur- Hapur Line; iii) 400 KV D/C,Ghatampur-Kanpur line				
	Configuration of Tx Line (S/C or D/C)	both				
LAND POSSESSION	Total Pocket land-52.33 Ha. (As per initial approval); Total Pocket land registered/ Acquired- 47.4790 Ha. (As per current reconciliation);					
WATER ALLOCATION	80 cusec from UP Irrigation department (44.6 km from GTPP)					
MOEF CLEARANCE	Clearance obtained date from concerned authority:- 17.06.2015 validity of it (If any):- 7 Years					
CIVIL AVIATION CLEARANCE	Clearance obtained date from concerned authority:- 13.12.2013 Validity : - 5 Years, NUPPL had sent compliance to AAI regarding the					
CPCB CLEARANCE	NOT APPLICABLE					
SPCB CLEARANCE	Clearance obtained date from concerned authority:- 17.11.2017; validity of it.- 5 Years					
FOREST CLEARANCE	NOT APPLICABLE					
			TOTAL EXPENDITURE (upto 31.07.2022)			13837.87

GHATAMPUR THERMAL POWER PROJECT, Unit# 1, 2 & 3 (3x660 MW) / NUPPL (CENTRAL SECTOR)

UNIT WISE MILESTONES ANTICIPATED / ACTUAL)							
Sl.	Milestones	UNIT-01		UNIT-02		UNIT-03	
		Original Date of Completion	Anticipated / Actual Date of Completion	Original Date of Completion	Anticipated / Actual Date of Completion	Original Date of Completion	Anticipated / Actual Date of Completion
1	COMPLETION OF BOILER FOUNDATION	01.01.2017	17.03.2017	01.07.2017	21.10.2020	28.12.2017	29.01.2021
2	START OF BOILER ERECTION	01.09.2017	27.02.2018	01.03.2018	30.06.2018	28.08.2018	04.12.2018
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA		NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	01.05.2018	25.11.2018	01.11.2018	04.04.2019	01.05.2019	12.09.2019
5	CONDENSER ERECTION START	19.07.2018	09.03.2019	19.01.2019	03.01.2020	19.07.2019	02.03.2021
6	TG ERECTION START	03.07.2018	08.02.2019	03.01.2019	29.02.2020	03.07.2019	30.04.2021
7	HP PIPING ERECTION START	12.01.2019	30.10.2019	12.07.2019	21.02.2019	12.01.2019	30.06.2021
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	NA		NA		NA	
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	01.05.2019	06.01.2021	01.11.2019	24.02.2021	01.05.2020	29.08.2021
10	TG BOX UP	02.07.2019	23.10.2019	02.01.2020	15.05.2021	02.07.2020	30.09.2022
11	HP PIPING ERECTION COMPLETION	10.06.2019	31.08.2021	10.06.2020	15.11.2022	12.06.2020	31.01.2023
12	START OF OILFLUSHING	30.11.2019	27.10.2020	31.05.2020	30.10.2022	30.11.2020	31.12.2022
13	BOILER LIGHT UP	30.11.2019	28.02.2022	30.05.2020	31.01.2023	30.11.2020	31.05.2023
14	CHEMICAL CLEANING COMPLETION	30.10.2019	24.07.2021	30.04.2020	31.12.2022	30.10.2020	31.04.2023
15	STEAM BLOWING START	15.12.2020	23.06.2022	30.05.2020	15.02.2023	30.11.2020	15.06.2023
16	STEAM BLOWING COMPLETION	30.01.2020	15.08.2022	15.06.2020	15.03.2023	15.12.2020	15.07.2023
17	ROLLING & SYNC.	01.03.2020	30.09.2022	31.08.2020	30.04.2023	01.03.2021	31.08.2023
18	FULL LOAD	01.04.2020	28.02.2023	31.10.2020	30.06.2023	01.04.2021	31.10.2023
19	TRIAL RUN	29.05.20	May-23	27.11.20	Aug-23	29.05.21	Nov-23
20	COD	01.06.20	30.06.23	30.11.20	31.09.23	01.06.21	31.12.23

STATUS OF MAIN PLANT PACKAGE (BTG) : SG - L&T MHI, TG - GE								
Sl.	Packages		AREA			UNIT-01	UNIT-02	UNIT-03
						% Completion	% Completion	% Completion
1	BOILER		CIVIL			83.80%	84.62%	80.01%
			STRUCTURE			97.80%	87.49%	78.65%
			PRESSURE PARTS			100.00%	100.00%	100.00%
2	TG		CIVIL			99.66%	96.43%	93.72%
			STRUCTURE			100.00%	99.81%	95.95%
3	ESP		UNDER PROGRESS			98.74%	97.12%	60.95%
4	FGD		CIVIL WORK			The Board in its 63rd Meeting held on 25.09.2021, has decided for cancelling the present tender for FGD and to go for retender. The cost estimate of Rs. 923 Cr (base- September'21) for FGD retender has been approved in 66th Board Meeting of NUPPL. Qualification requirement and Tender specification for FGD has been approved in 27th PC committee meeting held on 22.02.2022. NIT issued on 04.03.2022. Pre-		
			MATERIAL SUPPLY					
			ERECTION WORK					
STATUS OF BOPs								
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated/ Actual Date of Completion	UNIT-01	UNIT-02	UNIT-03
						% Completion	% Completion	% Completion
1	Chimney	BGR Energy System Ltd.	21.11.2016	20.11.2019	U1-Oct22; U2-Jan23; U3-May23	99.25%	72.25%	36.36%
2	Coal Handling Plant	Conveyor Pkg – BGR Energy System Ltd.	21.11.2016	20.07.2019	Jan23, May23, Sep23	44%	18%	9%
		Wagon Tippler - BGR Energy System Ltd.	21.11.2016	U1-Jul19, U2&3-Jan20	U1-Jan23, U2&3-May23	20%	0%	
		Stacker Reclaimer - BGR Energy System Ltd.	21.11.2016	U1-Jun19, U2&3-Feb20	U1-Jan23, U2&3-May23	27%	9%	
3	Ash Handling Plant	BGR Energy System Ltd.	21.11.2016	Jul19, Mar20, Feb20	Feb23, Jun23, Oct23	61%	59%	55%
4	Fuel Oil System	L&T MHI Power Boilers Pvt Ltd.	21.11.2016	24.10.2019	26.08.2022	99.00%		
5	Cooling Towers	BGR Energy System Ltd.	21.11.2016	20.11.2020	10.02.2023	Civil:93%	Civil:57.99%	Civil:42.15%
6	CW Pump house	BGR Energy System Ltd.	21.11.2016	20.11.2020	Oct22, Nov22, May23	75%	21%	20%
7	WPT Plant	BGR Energy System Ltd.	21.11.2016	20.04.2019	10.12.2022	95%		
8	DM Plant	BGR Energy System Ltd.	21.11.2016	20.04.2019	10.2.2022	100%		
9	Compressed Air System	L&T MHI Power Boilers Pvt Ltd	02.08.2016	20.07.2019	16.12.2022	95%		
10	Fire Protection System	BGR Energy System Ltd.	21.11.2016	20.11.2020	Feb23, Jun23, Oct23	49.24%	0%	0%
11	Switch Yard	BGR Energy System Ltd.	21.11.2016	20.02.2020	31.12.2022	400kV-59%, 765kV-0%, Outdoor Switchyard-53%		
12	Station Transformers	GE-Power Systems India Pvt. Ltd.	02.08.2016	Apr19, Oct19, Apr20	Feb21, Aug22, Oct22	100.0%	96.0%	50.0%
13	Unit Transformers	GE-Power Systems India Pvt. Ltd.	02.08.2016	Apr19, Oct19, Apr20	Jul22, Nov22, Feb23	100.0%	85.0%	50.0%
14	Railway Siding	RTES	29.03.2019	28.03.2021	31.12.2022	Civil work - 88.00%		
15	Power Evacuation Lines	Ghatampur Transmission Ltd	12.06.2018	28.02.2020	10.02.2021	400kV GTPS-Kanpur -100%		
				31.11.2020	27.03.2021	765kV GTPS-Agra -100%		
				31.03.2021	25.12.2021	765kV GTPS-Hapur - 100%		

CRITICAL ISSUES

Work of all the BoP areas, put on hold, are likely to be restored by end of August 2022. Financial problems being faced by M/s BGR

REASONS OF DELAY

Work of all the BoP areas has been put on hold since August 2021 and presently, no work is going on the site due to financial issues being faced by M/s BGR. BGR is not able to pay its sub vendors.

KHURJA SUPER STPP, Unit# 1 & 2 (2x660 MW) / THDC (CENTRAL SECTOR)

Khurja Distt. Bulandshahar, Uttar Pradesh -203131

E-Gen Portal Registration No. (U#1 - 1200002023; U#2 - 1200002024)

Project Developer / Implementing Agency - THDC			Main Plant Vendor: SG Package - M/s L&TMHI and TG Pkg-BHEL		
Unit No.	LOA		Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Aug-2019		Jul-2023	Feb-2024	
Unit#2			Jan-2024	Aug-2024	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT		11089.42
COAL COMBUSTION TECHNOLOGY	Ultra Supercritical		LATEST ESTIMATED COST		Not Revised
APPROVAL DATE / NTP	07.03.2019.		DATE OF FINANCIAL CLOSURE		
EPC/BTG/BoP Contractor Details (Package Wise)	Zero Date : 29.08.2019 (with respect to Award of Main Plant Package i.e. Steam Generator & Associated Packages)		YEAR WISE EXPENDITURE		
PPA	PPAs for entire off take-off power to be generated from Khurja STPP have been signed by THCDIL prior to 05.01.2011 with Uttar Pradesh, Uttarakhand, Rajasthan, Himachal Pradesh and Delhi. Out of 1320 MW, 60% power (792 MW) is to be supplied to UP & balance 40% power (528 MW) is to be supplied to other beneficiary states as per allocation to be done by Ministry of Power.		2016-17		338.92
			2017-18		10.66
COAL LINKAGE/FSA	For Coal linkage, Ministry of Coal, GoI vide allotment order dtd.17.01.2017 has allotted Amelia Coal Mine in District Singrauli, Madhya Pradesh to THDCIL to meet out fuel requirements of the project. Grade of Coal: G9 (Avg. GCV = 4746 Kcal/Kg). Net Geological Reserve in Amelia Coal Mine is 162.05 Million Ton (OC) out of this Extractable Coal Reserve is 139.48 Million Ton.		2018-19		148.87
			2019-20		439.95
			2020-21		789.69
START UP POWER AGREEMENT	Connectivity has been granted by CTU vide its letter NoC/CTU/N/05/1200002404 dated.18.03.2020 for evacuation of 528 MW power from Khurja (2x660 MW) STPP to ISTS beneficiaries. Signing of Connectivity agreement is under process. In line with the granted connectivity, power evacuation system is under implementation through Power Grid Corporation Of India Limited and is likely to completed by June-2022.Thereafter THDCIL will request RLDC for availing start up power as per CERC Regulations.		2021-22		2158.93
			EXPENDITURE OF JULY'2022		215.92
POWER EVACUATION SYSTEM	Tx Line Developer	PGCIL and UPPTCL	TOTAL EXPENDITURE (upto 31.07.2022)		
	Tx Line Name Tx Voltage Level	i) Khurja STPP- Aligarh 400 KV, D/C line (PGCIL) ii) Aligarh-Shamli 400 KV line , D/C, LILOOing at Khurja STPP (UPPTCL).	4805.77		
	Configuration of Tx Line (S/C or D/C)	D/C			
LAND POSSESSION	Small Patches of land within the boundary of already acquired 1201 Acre land by UPSIDC and handed over to THDCIL .				
WATER ALLOCATION	Formal water commitment letter for providing 43 Cusec water for Makeup Water System from Upper Ganga Canal at just 11 Km from Project site issued by Water Resource Department, GoUP on 12.06.2014.				
MOEF CLEARANCE	Environmental Clearance has been accorded to Khurja STPP by MOEF&CC on 30.03.2017 with validity upto 29.03.2024.				
CIVIL AVIATION CLEARANCE	Clearance for construction of chimney for Khurja STPP has been obtained from Airport Authority of India (AAI) on 19.04.2018 with validity up to 17.07.2023.				
CPCB CLEARANCE	NOT APPLICABLE				
SPCB CLEARANCE	“Consent to Establish” has been granted by SPCB Uttar Pradesh on 13.06.2018 with validity upto 01.06.2023.				
FOREST CLEARANCE	NOT APPLICABLE				

KHURJA SUPER STPP, Unit# 1 & 2 (2x660 MW) / THDC (CENTRAL SECTOR)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)						STATUS OF MAIN PLANT PACKAGE (BTG) : M/s L&T MHI Power Boilers Pvt.									
Sl.	MILESTONE	UNIT-01		UNIT-02		Sl.	Packages	AREA	UNIT-01		UNIT-02				
		Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date				%	%					
1	COMPLETION OF BOILER FOUNDATION	29.09.2020	20.01.2021	29.03.2021	15.11.2021	1	BOILER	CIVIL	100.00%		100.00%				
2	START OF BOILER ERECTION	29.10.2020	20.02.2021	29.04.2021	17.08.2021			STRUCTURE	23.00%		12.00%				
								PRESSURE PARTS	24.00%		0.00%				
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA		2	TG	CIVIL	93.11%		70.08%				
4	BOILER CEILING GIRDER LIFTING COMPLETION	28.05.2021	12.02.2022	28.11.2021	31.08.2022			STRUCTURE	67.60%		15.82%				
5	CONDENSER ERECTION START	02.09.2021	25.03.2022	02.03.2022	25.09.2022			PRESSURE PARTS	0.00%		0.00%				
6	TG ERECTION START	03.09.2021	25.05.2022	03.03.2022	26.11.2022	3	ESP	UNDER PROGRESS	12.00%		0.00%				
7	HP PIPING ERECTION START	28.06.2021	30.09.2022	28.12.2021	28.01.2023	4	FGD	CIVIL WORK	100% of Piling & 27.71% RCC completed		100% of Piling & 19.78% of RCC completed				
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	29.05.2022	30.12.2022	29.11.2022	30.06.2023			MATERIAL SUPPLY	38.00%		0.00%				
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	29.08.2022	29.02.2023	29.02.2023	29.08.2023			ERECTION WORK	0.00%		0.00%				
10	TG BOX UP	04.08.2022	25.01.2023	04.02.2023	25.07.2023	STATUS OF BOPs									
11	HP PIPING ERECTION COMPLETION	26.10.2022	26.04.2023	26.04.2023	26.10.2023	Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC- BHEL)	Date of Award	Scheduled Date of Completion	Anticipated /Actual Date of Completion	UNIT-01 % Completion	UNIT-02 % Completion		
12	BOILER LIGHT UP	29.10.2022	11.05.2023	29.04.2023	11.11.2023	1	Chimney	L&T MHI Power Boilers Pvt. Ltd	27.09.2020	14.04.2023	14.10.2023	Unit-1: RCC- 60.31%; Unit-2: RCC-55.69%			
13	CHEMICAL CLEANING COMPLETION	29.10.2022	10.06.2023	29.04.2023	10.12.2023	2	Coal Handling Plant	Thyssenkrupp Industries India Pvt. Ltd.	04.08.2021	04.12.2023	04.12.2023	36.00%			
14	OIL FLUSHING COMPLETION	03.11.2022	26.03.2023	03.05.2023	26.09.2023	3	Ash Handling Plant	M/s L&T MHI Power Boilers Pvt. Ltd	11.06.2020	20.02.2023	20.08.2023	100% of Piling and 25% of RCC			
						4	Fuel Oil System	M/s L&T MHI Power Boilers Pvt. Ltd	30.09.2021	08.10.2022	08.04.2023	90% LDO tanks; 29% FOPH			
15	STEAM BLOWING START	29.11.2022	11.06.2023	29.05.2023	11.12.2023	5	Cooling Towers	M/s Paharpur Cooling Towers Ltd	16.04.2021/ 13.10.2021	14.06.2023/ 14.12.2023	14.06.2023/ 14.12.2023	U-1: 49.53% of civil work completed	U-2: 27.86% of civil work completed		
						6	CW Pump house	Flowmore Ltd.	01.10.2021	30.09.2023	30.09.2023	Drg. Approval - 96%; Equipment Supply - 20%			
16	STEAM BLOWING COMPLETION	29.12.2022	30.09.2023	29.06.2023	30.03.2024	7	WPT Plant	Gaja Engineering Pvt. Ltd.	30.11.2021	30.09.2023	30.09.2023	Civil Work: 11%			
						8	DM Plant								
						9	DM Water Transfer Pump House								
17	ROLLING & SYNC.	02.04.2023	07.11.2023	01.10.2023	07.05.2024	10	Compressed Air System					Tender in process			
						11	Fire Protection System					Tender in process			
18	FULL LOAD	02.06.2023	06.01.2024	02.12.2023	06.07.2024	12	Switch Yard	GET&D	16.09.2020	25.03.2023/ 25.09.2023	25.03.2023/ 25.09.2023	70.0%			
						13	Ash Dyke Package	M/s JPW Infratech Pvt Ltd	11.03.2022	10.09.2024	10.09.2024	9.0%			
19	TRIAL RUN	02.07.2023	20.02.2024	02.01.2024	20.08.2024	14	Station Transformers	BHEL	09.08.2020	04.02.2022/ 30.07.2022	04.08.2022/ 30.01.2023	60.0%			
						15	Unit Transformers	BHEL	08.09.2020	15.07.2022	15.01.2023	50.0%			
20	COD	02.08.2023	20.03.2024	02.02.2024	18.09.2024	20	Railway Siding	M/s Jhajhariya Nirman Ltd; M/s ISC-CMIPL (JV)	13.11.2020	13.09.2022	May,2023	47 %			
						21	Power Evacuation Lines	M/s Unitech Power Transmission M/s Hyosung India	02.03.2021	01.06.2022	31.12.2022	90% Tx line work completed			

CRITICAL ISSUES

♦ Law & Order issue in taking possession of small patches of land within the boundary of already acquired 1201 Acre land by UPSIDC and handed over to THDCIL.

REASONS OF DELAY

♦ 6 Months Post Award delay due to COVID-19 Pandemic.

BUXAR THERMAL POWER PROJECT, Unit# 1 & 2 (2x660 MW) / SJVN (CENTRAL SECTOR)

Village-Chausa, Tehsil-Chausa, Distt.-Buxar, Pin- 802114, Bihar

E-Gen Portal Registration No. (U#1 - 1200002481; U#2 - 1200002482)

Project Developer / Implementing Agency - SJVN			Main Plant Vendor - M/S L&T		
Unit No.	LOA		Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Jun-2019		May-2023	Jun-2023	
Unit#2			Sep-2023	Dec-2023	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT		10439.09
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST		Not Revised
APPROVAL DATE / NTP	Investment Approval accorded by Govt. of India vide MoP		DATE OF FINANCIAL CLOSURE		26.11.2020
EPC/BTG/BoP Contractor Details (Package Wise)	Main Plant works has been awarded in single EPC package to M/s. L&T on 22.06.2019.		YEAR WISE EXPENDITURE		
PPA	PPA signed with Govt. of Bihar on 05.01.2011 and further reconfirmed on 09.01.2018.		2013-14	46.68	
COAL LINKAGE/FSA	Allocated Mine - CCL, Magadh-Amrapali; Distance from mine - 465 km (non pithead). Letter of Assurance (LoA) for 4.976 MTPA of G9 to G14 grade coal issued by Central Coalfields Ltd. (CCL) on 10.12.2018. Coal may be supplied either from Amrapali coal block or Magadh coal block.		2014-15	15.18	
			2015-16	378.08	
			2016-17	23.96	
			2017-18	21.73	
START UP POWER AGREEMENT	Start up power will be arranged through South Bihar Power Distribution company Ltd. (SBPDCL).		2018-19	68.21	
POWER EVACUATION SYSTEM	Tx Line Developer	BSPTCL, Govt. of Bihar	2019-20	344.50	
	Tx Line Name Tx Voltage Level	i) Buxar TPS- Naubatpur 400 KV, D/C	2020-21	1100.05	
		ii) Buxar TPS- Dumraon (New) 220 KV, D/C	2021-22	2691.06	
		iii) Buxar TPS- Karmnasa (New) 220 KV, D/C	EXPENDITURE OF JULY'2022		178.00
	iv) Buxar TPS- Dehri 220 KV, D/C	TOTAL EXPENDITURE (upto 31.07.2022)		5768.32	
	Configuration of Tx Line (S/C or D/C)	D/C			
LAND POSSESSION	Total Land Required-1283 Acre;1058.335 Acre (for Main Plant), 147 acre (for Rail Corridor) and 78 acre (for Water Pipeline corridor & intake etc.) land under possession.				
WATER ALLOCATION	MoU for utilization of 55 cusec of water signed between STPL and Water Resource Deptt., Govt. of Bihar on 29.08.2016.				
MOEF CLEARANCE	Accorded by MOEF&CC on 28.02.2017.(Validity- 27.02.2024)				
CIVIL AVIATION CLEARANCE	Accorded by Airport Authority of India on 12.04.2017 (Fresh NOC issued on 18.11.2018). (Validity-17.11.2028)				
CPCB CLEARANCE	NOT APPLICABLE				
SPCB CLEARANCE	“Consent to Establish” (NOC) granted by Bihar State Pollution Control Board on 03.09.2019.				
FOREST CLEARANCE	NOT APPLICABLE				

BUXAR THERMAL POWER PROJECT, Unit# 1 & 2 (2x660 MW) / SJVN (CENTRAL SECTOR)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)					
Sl.	MILESTONE	UNIT-01		UNIT-02	
		Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date
1	COMPLETION OF BOILER FOUNDATION	21.JUL.20	01.MAY.21	19.NOV.20	28.OCT.21
2	START OF BOILER ERECTION	20.AUG.20	21.OCT.20	20.DEC.20	23.NOV.21
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	19.APR.21	31.JAN.22	20.AUG.21	31.OCT.22
5	CONDENSER ERECTION START	03.AUG.21	31.MAY.22	03.DEC.21	03.DEC.22
6	TG ERECTION START	21.SEP.21	20.AUG.22	20.JAN.22	15.DEC.22
7	HP PIPING ERECTION START	16.OCT.21	02.MAY.22	15.FEB.22	15.DEC.22
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	20.APR.22	30.NOV.22	21.AUG.22	30.SEP.23
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	NA		NA	
10	TG BOX UP	21.AUG.22	22.FEB.23	20.DEC.22	21.SEP.23
11	HP PIPING ERECTION COMPLETION	30.JUL.22	28.FEB.23	29.NOV.22	29.AUG.23
12	START OF OIL FLUSHING	28.AUG.22	23.MAR.23	27.DEC.22	22.SEP.23
13	BOILER LIGHT UP	21.OCT.22	22.JAN.23	21.FEB.23	22.OCT.23
14	CHEMICAL CLEANING COMPLETION	15.OCT.22	25.JAN.23	15.FEB.23	25.OCT.23
15	STEAM BLOWING START	01.NOV.22	12.APR.23	04.MAR.23	26.OCT.23
16	STEAM BLOWING COMPLETION	18.DEC.22	05.MAY.23	20.APR.23	10.NOV.23
17	ROLLING & SYNC.	20.FEB.23	31.MAY.23	21.JUN.23	30.NOV.23
18	FULL LOAD	21.MAR.23	25.JUN.23	21.JUL.23	25.DEC.23
19	TRIAL RUN	21.May.23	30.Jun.23	21.Sep.23	31.Dec.23
20	COD	07.JUL.23	07.JUL.23	07.JAN.24	07.JAN.24

STATUS OF MAIN PLANT PACKAGE (BTG) : M/s L&T ltd							
Sl.	Packages	AREA				UNIT-01	UNIT-02
						% Completion	% Completion
1	BOILER	CIVIL				98.1%	83.4%
		STRUCTURE				57.2%	24.7%
		PRESSURE PARTS				41.0%	-
2	TG	CIVIL				63.1%	2.4%
		STRUCTURE				72.7%	2.3%
		TG ERECTION				-	-
3	ESP	UNDER PROGRESS				25.2%	3.3%
4	FGD	CIVIL WORK				35.7%	35.7%
		MATERIAL SUPPLY				25.0 %	25.0 %
		ERECTION WORK				0 %	0 %
STATUS OF BOPs							
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC- BHEL)	Date of Award	Scheduled Date of Completion	Anticipated /Actual Date of Completion	UNIT-01	UNIT-02
						% Completion	% Completion
1	Chimney	L&T Limited (EPC)	22.JUN.19	28.JUN.23	28.JUN.23	17.40%	
2	Coal Handling Plant	L&T (Conveyor pkg)	22.JUN.19	19.NOV.22	28.JAN.23	2.22%	
		L&T (Wagon tipler)	22.JUN.19	21.NOV.22	21.DEC.22	11.20%	
		L&T/ Thyssenkrup (Stacker reclaimr)	22.JUN.19	23.OCT.22	23.DEC.22	2.4%	
3	Ash Handling Plant	L&T /Macawber Beekay Pvt ltd	22.JUN.19	19.JUL.23	19.JUL.23	8.31%	
4	Fuel Oil System	L&T/ Shalkoot Mechanique Pvt. Ltd	22.JUN.19	31.AUG.22	31.DEC.22	14.35%	
5	Cooling Towers	L&T/ Paharpur Cooling Towers Ltd	I-22.JUN.19 II-22.JUN.19	I-20.FEB.23 II-20.JUN.23	I-20.FEB.23 II-20.JUN.23	I-37.14% II-18.57%	
6	CW Pump house	L&T/ Xylem Water Solutions India Pvt Ltd	I-22.JUN.19 II-22.JUN.19	I-23.FEB.23 II-23.JUN.23	I-23.FEB.23 II-23.JUN.23	I-12.56% II-10.42%	
7	WPT Plant	L&T/ Driplex Water Engineering Pvt Ltd	I-22.JUN.19 II-22.JUN.19	I-05.APR.23 II-05.AUG.23	I-05.APR.23 II-05.AUG.23	I-13.30% II-6.30%	
8	DM Plant	L&T/ Driplex Water Engineering Pvt Ltd	22.JUN.19	21.JUN.23	21.JUN.23	40.77%	
9	Compressed Air System	L&T / L&T-MHPS Boilers Pvt. Ltd	22.JUN.19	20.OCT.22	20.DEC.22	9.20%	
10	Fire Protection System	L&T/ Flowmore Limited	22.JUN.19	10.JUL.23	10.JUL.23	6.98%	
11	Switch Yard	L&T/ ABB Power Products & Systems India Ltd	22.JUN.19	21.NOV.22	21.JAN.22	39.44%	
12	Station Transformers	L&T/ ABB Power Products & Systems India Ltd	I-22.JUN.19 II-22.JUN.19	I-22.APR.22 II-22.AUG.22	I-22.OCT.22 II-22.FEB.23	I-11.42% II-4.32%	
13	Unit Transformers	L&T/ ABB Power Products & Systems India Ltd	I-22.JUN.19 II-22.JUN.19	I-29.MAR.23 II-29.SEP.23	I-29.MAR.23 II-29.SEP.23	I-4.00% II-4.00%	
14	Railway Siding	BITES Ltd.	13.JUN.19	31.OCT.22	31.DEC.22	12.5 %	
15	Power Evacuation Lines	BSPTCL, Govt. of Bihar	23.NOV.21	31.DEC.22	31.DEC.22	33.7 %	

CRITICAL ISSUES

i) Law and Order: Construction activities of project have been commenced but construction work is being disrupted by locals frequently. Deployment of CISF is required for uninterrupted construction activities of the project.

REASONS OF DELAY

BTG :

Covid-19 Pandemic and subsequent lockdowns, Non-availability of industrial Oxygen cylinders due to Covid-19, State government restriction for transportation of aggregates, sand mining etc.

BOP:

Delayed acquisition of land for Water Corridor & Intake and Rail Corridor., Covid-19 Pandemic and subsequent lockdowns, Non-availability of industrial Oxygen cylinders due to Covid-19, State government restriction for transportation of aggregates, sand mining etc.

OBRA 'C' TPP, Unit# 1 & 2 (2x660 MW) / UPRVUNL (STATE SECTOR - NORTHERN REGION)

Village-Obra, Tehsil-Obra, District-Sonebhadra, Pin-231219 Uttar Pradesh

E-Gen Portal Registration No. (U#1 - 1200001696; U#2 - 1200001697)

Project Developer / Implementing Agency - UPRVUNL			Main Plant Vendor - (BTG) : M/s. Doosan Power Systems India Pvt. Ltd.	
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Dec-2016	Dec-2020	Jun-2023	
Unit#2		Apr-2021	Dec-2023	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)	
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT	8777.71
COAL COMBUSTION TECHNOLOGY	Ultra-Supercritical		LATEST ESTIMATED COST	10416.00
APPROVAL DATE / NTP	Date of NTP or Approval Date: 22.12.2016		DATE OF FINANCIAL CLOSURE	13.11.2013; 30.05.2019 for additional amount.
EPC/BTG/BoP Contractor Details (Package Wise)	22.12.2016. EPC contract awarded to M/s Doosan Power Systems India Pvt. Ltd., Gurugram(Haryana)		YEAR WISE EXPENDITURE	
PPA	PPA signed with UP Power Corporation Ltd for 100% share to state of UP		2015-16	7.24
COAL LINKAGE/FSA	Allocated Mine - Saharpur Jamarpani mines, Jharkhand; Distance from mine - 651 km (non pithead); Allocation Date: 13.08.2015. Grade of Coal -G10		2016-17	423.77
			2017-18	277.83
START UP POWER AGREEMENT	Start up power from UPPTCL		2018-19	855.90
POWER EVACUATION SYSTEM	Tx Line Developer	UPPTCL	2019-20	2175.96
	Tx Line Name Tx Voltage Level	i) LILO of 765 kV Anpara'D'- Unnao S/C at Obra 'C' TPS; ii) 400 kV D/C Jaunpur- Obra line (upto LILO point of Obra'B' – Obra 'C' Line).	2020-21	1220.62
	Configuration of Tx Line (S/C or D/C)		2021-22	1826.42
LAND POSSESSION	Brown Field project, therefore Land already in Possession. For ash dyke construction, land acquisition of 113.42 Ha under progress. Initially ash disposal of Obra 'C' will be made in existing obra 'B' Ash Pond and in parallel land aquisition work for Obra'C' is in progress.		EXPENDITURE OF JULY'2022	61.86
WATER ALLOCATION	Water requirement to be fulfilled from return channel of Obra-B plant. Additional requirement (if any) shall be met from the reservoir of Rihand Dam.		TOTAL EXPENDITURE (upto 31.07.2022)	7572.54
MOEF CLEARANCE	Clearance obtained date 21.06.2016			
CIVIL AVIATION CLEARANCE	Clearance obtained date : 12.07.2016 Valid upto 21.07.2021			
CPCB CLEARANCE	Not Applicable			
SPCB CLEARANCE	Not Applicable			
FOREST CLEARANCE	Wild life Clearance obtained date 07.06.2016			

OBRA 'C' TPP, Unit# 1 & 2 (2x660 MW) / UPRVUNL (STATE SECTOR - NORTHERN REGION)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)					
Sl.	MILESTONE	UNIT-01		UNIT-02	
		Original Date of Completion	Anticipated / Actual Date of Completion	Original Date of Completion	Anticipated / Actual Date of Completion
1	COMPLETION OF BOILER FOUNDATION	11-Mar-18	15-Feb-19	16-Jun-18	21-Feb-19
2	START OF BOILER ERECTION	22-Apr-18	28-May-18	22-Aug-18	21-Jan-19
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	21-Sep-18	7-Mar-19	21-Jan-19	10-Nov-19
5	CONDENSER ERECTION START	23-Nov-18	17-Aug-20	23-Mar-19	2-Apr-22
6	TG ERECTION START	22-Jan-19	2-Nov-20	23-May-19	10-Nov-22
7	HP PIPING ERECTION START	12-Jan-19	1-Mar-20	22-May-19	2-Jan-21
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	22-Sep-19	27-Sep-20	23-Jan-20	20-Apr-22
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	22-Sep-19	27-Sep-20	23-Jan-20	20-Apr-22
10	TG BOX UP	22-Feb-20	15-Dec-21	20-Jun-20	11-Jan-23
11	HP PIPING ERECTION COMPLETION	20-Mar-20	14-Mar-22	20-Jul-20	15-Oct-22
12	START OF OILFLUSHING	23-Feb-20	10-Mar-22	21-Jun-20	12-Apr-23
13	BOILER LIGHT UP	21-Apr-20	26-Apr-22	19-Aug-20	31-Mar-22
14	CHEMICAL CLEANING COMPLETION	25-Mar-20	16-Mar-22	25-Jul-20	30-Oct-22
15	STEAM BLOWING START	22-May-20	29-Aug-22	19-Sep-20	1-May-23
16	STEAM BLOWING COMPLETION	22-Jun-20	09-Oct-22	19-Oct-20	31-May-23
17	ROLLING & SYNC.	30-Jul-20	15-Mar-23	27-Nov-20	21-Sep-23
18	FULL LOAD	1-Sep-20	21-May-23	31-Dec-20	21-Nov-23
19	TRIAL RUN	21-Dec-20	Jun-23	21-Apr-21	Dec-23
20	COD	21-Dec-20	Jun-23	21-Apr-21	Dec-23

STATUS OF MAIN PLANT PACKAGE (BTG) : Doosan Power Systems India Pvt.							
Sl.	Packages	AREA				UNIT-01	UNIT-02
						% Completion	% Completion
1	BOILER	CIVIL				95.4%	67.89%
		STRUCTURE					
		PRESSURE PARTS					
2	TG	CIVIL				93.54%	37.83%
		STRUCTURE					
		PRESSURE PARTS					
3	ESP	PASS STATUS				93.95%	55.56%
4	FGD	CIVIL WORK				89.54%	61.98%
		MATERIAL SUPPLY					
		ERECTION WORK				24.47%	0.00%
STATUS OF BOPs (DPSI-EPC)							
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC- BHEL)	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01	UNIT-02
						% Completion	% Completion
1	Chimney	M/s.Simplex	27.11.2018	01.12.2019	18.08.2022	96.54%	
2	Coal Handling Plant	KCC (Conveyor package)		19.05.2020	24.10.2022	50.00%	
		Aneja (Wagon Tripler)	23.11.2018	23.02.2020	10.01.2023	59.24%	
		Aneja (Stacker Reclaimer)	02.05.2018	05.04.2020	30.08.2022	73.21%	
3	Ash Handling Plant	AKC, PNC	09.04.2018	29.06.2020	22.08.2022	48.97%	
4	Fuel Oil System	AKC, Sangha, Singrauli, Jiwala	30.11.2018	04.05.2020	13.08.2022	89.10%	
5	Cooling Towers	PCTL	01.08.2018(C T-01), 14.12.2018(C T-02)	25.11.2019(C T-01), 26.03.2020(C T-02)	02.09.2022, 03.09.2022	65.08%	60.50%
6	CW Pump house	GDCL	06.06.2018	05.07.2020	12.08.2022	89.58%	
7	WPT Plant	Rajpati Vishwakarma, Sahil Kumar, KNIL, IEIL	20.11.2018	13.09.2020	13.08.2022	93.63%	
8	DM Plant	Rajpati Vishwakarma, Sahil Kumar, KNIL,IEIL	03.10.2018	04.11.2019	12.08.2022	97.98%	
9	Compressed Air System	GDCL	23.11.2018	04.05.2020	16.08.2022	89.33%	
10	Fire Protection System	Lloyd	08.04.2019	17.10.2019	23.01.2023	24.87%	
11	Switch Yard	KNIL , GDCL, GET&D	01.08.2018	30.01.2020	12.08.2022	93.40%	
12	Station Transformers	GDCL. GET&D	10.11.2018	27.09.2019	28.06.2022	100.00%	
13	Unit Transformers	GDCL, GET&D	10.03.2019	06.02.2020	16.08.2022	94.13%	
14	Railway Siding	DPSI			Dec,2022	87 %	
15	Power Evacuation Lines	GET&D	08.11.2017	24.07.2020	27.12.2022	90 %	

CRITICAL ISSUES

- GT has failed during Factory acceptance test and short circuit test .
- Commercial issues between DPSI and their sub-vendors

REASONS OF DELAY

- Covid-19 I & II wave.
- Steel Price Hike, Dispute between DPSI and its sub-vendors,

JAWAHARPUR STPS, Unit# 1 & 2 (2X660 MW) / UPRVUNL (STATE SECTOR - NORTHERN REGION)

Jawaharpur STPS, Malawan, Etah, UP - 207001

E-Gen Portal Registration No. (U#1 - 1200002452; U#2 - 1200002496)

Project Developer / Implementing Agency - UPRVUNL			Main Plant Vendor - M/S Doosan Power Systems India	
Unit No.	LOA		Original Trial Run Date	Anticipated / Actual Trial Run Date
Unit#1	Dec-2016		Dec-2020	Jun-2023
Unit#2			Apr-2021	Dec-2023
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)	
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT	8078.56
COAL COMBUSTION TECHNOLOGY	Ultra Super Critical		LATEST ESTIMATED COST	10566.27
APPROVAL DATE / NTP	Approval of DPR and Intial project cost by U.P.Government of DPR Vide letter dated 04.09.2015		DATE OF FINANCIAL CLOSURE	
EPC/BTG/BoP Contractor Details (Package Wise)	22.12.2016- date of Award to EPC Contractor M/s Doosan Power Systems India Power Limited - scope including BTG,BOP		YEAR WISE EXPENDITURE	
PPA	Details of PPA signed or under process whichever is applicable with defining share % if any.		2016-17	445.21
COAL LINKAGE/FSA	Allocated Mine - Saharpur Jamarpani mines, Jharkhand; Distance from mine - 1190 km (non pithead)		2017-18	400.26
	Bridge Linkage from CCL/ECL for 4.461 MTPA		2018-19	844.96
START UP POWER AGREEMENT	For 220 KV signed with UPPTCL		2019-20	2295.94
POWER EVACUATION SYSTEM	Tx Line Developer	PGCIL & UPPTCL	2020-21	2034.08
	Tx Line Name Tx Voltage Level	i) LILO of 765kV Mainpuri - Gr. Noida S/C at Jawaharpur TPS; ii) Jawaharpur TPS-Firozabad 400kV D/C line.	2021-22	2224.36
	Configuration of Tx Line (S/C or D/C)		EXPENDITURE OF JULY'2022	185.15
LAND POSSESSION	765 Acre land for Power House under Possession		TOTAL EXPENDITURE (upto 31.07.2022)	8888.53
WATER ALLOCATION	Lower Ganga Canal - 38 cusec			
MOEF CLEARANCE	MOEF clearance granted in 63rd Meeting of the reconstituted EAC (Thermal Power) was held on 29th & 30th August, 2016			
CIVIL AVIATION CLEARANCE	Chimney clearance from AAI vide letter dated 12.06.2015			
CPCB CLEARANCE	NA			
SPCB CLEARANCE	Ref No- 58264/UPPCB/Aligarh(UPPCBRO)/CTE/ETAH/ 2019 dated 24.10.2019 valid up to 09.10.2024			
FOREST CLEARANCE	Clearance obtained vide letter no. 1904/14-1 dated 15.03.2016			

JAWAHARPUR STPS, Unit# 1 & 2 (2X660 MW) / UPRVUNL (STATE SECTOR - NORTHERN REGION)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)					
Sl.	MILESTONE	UNIT-01		UNIT-02	
		Original Date of Completion	Anticipated / Actual Date of Completion	Original Date of Completion	Anticipated / Actual Date of Completion
1	COMPLETION OF BOILER FOUNDATION	31.12.2017	05.03.2019	03.05.2018	29.05.2019
2	START OF BOILER ERECTION	22.04.2018	20.08.2018	22.08.2018	20.11.2018
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	06.09.2018	14.06.2019	06.01.2019	14.11.2019
5	CONDENSER ERECTION START	22.01.2019	16.09.2020	22.05.2019	12.06.2021
6	TG ERECTION START	22.01.2019	23.11.2020	22.05.2019	25.02.2022
7	HP PIPING ERECTION START	18.02.2019	01.11.2019	22.06.2019	15.02.2021
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	21.09.2019	10.11.2020	21.01.2020	30.11.2021
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION				
10	TG BOX UP	22.02.2020	25.07.2022	20.06.2020	01.02.2023
11	HP PIPING ERECTION COMPLETION	23.08.2019	10.07.2022	23.12.2019	20.08.2022
12	START OF OILFLUSHING	23.02.2020	12.02.2022	21.06.2020	13.12.2022
13	BOILER LIGHT UP	26.04.2020	27.05.2022	23.08.2020	31.12.2022
14	CHEMICAL CLEANING COMPLETION	15.03.2020	03.05.2022	13.07.2020	30.01.2022
15	STEAM BLOWING START	26.05.2020	16.09.2022	21.09.2020	12.02.2023
16	STEAM BLOWING COMPLETION	21.06.2020	12.10.2022	21.10.2020	10.03.2023
17	ROLLING & SYNC.	21.08.2020	28.02.2023	21.12.2020	30.04.2023
18	FULL LOAD	01.09.2020	09.03.2023	01.01.2021	09.05.2023
19	TRIAL RUN	20.12.2020	30.06.2023	20.04.2021	31.12.2023
20	COD	21.12.2020	30.06.2023	21.04.2021	31.12.2023

STATUS OF MAIN PLANT PACKAGE (BTG) : M/S DPSI							
Sl.	Packages	AREA				UNIT-01	UNIT-02
						% Completion	% Completion
1	BOILER	CIVIL				100 %	100%
		STRUCTURE				96.86 %	86.69%
		PRESSURE PARTS				100%	100 %
2	TG	CIVIL				100 %	98.50%
		STRUCTURE				98.4 %	95.45 %
3	ESP	STRUCTURE				82.59%	18.76 %
4	FGD	CIVIL WORK				100%	99.6 %
		MATERIAL SUPPLY				95.6%	85.10%
		ERECTION WORK				84.40%	11.10%
STATUS OF BOPs (DPSI-EPC)							
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC-BHEL)	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01 % Completion	UNIT-02 % Completion
1	Chimney	Simplex	16.03.2017	05.11.2019	09.11.2022	73.62%	
2	Coal Handling Plant	tkII/ NeoStructo(Conveyor package)	10.10.2017	23.04.2020	12.10.2022	85.24%	
		tkII/ NeoStructo (Wagon Tripler)	10.10.2017	24.12.2019	03.02.2023	86.12%	
		tkII/ NeoStructo (Stacker Reclaimer)	10.10.2017	15.09.2019	09.10.2022	97.73%	
3	Ash Handling Plant	Main vendor/subcontractor	30.12.2016	26.09.2020	25.08.2023	65.46%	
4	Fuel Oil System	Main vendor/	21.02.2017	10.04.2020	30.08.2022	99.58%	
5	Cooling Towers	Paharpur	05.03.2018, 10.09.2018	26.11.2019, 27.03.2020	25.08.2022, 12.11.2022	96.57%	83.16%
6	CW Pump house	DPSI/ Jyoti	10.01.2017	05.12.2019	30.08.2022	97.96%	
7	WPT Plant	Civil : Tecknow	14.10.2018	06.09.2019	30.08.2022	89.93%	
8	DM Plant	EPC : Ion Exchange	21.08.2019	16.11.2019	28.08.2022	98.98%	
9	Compressed Air System	Atlas / Jyoti	13.03.2017	19.05.2020	05.10.2022	71.14%	
10	Fire Protection System	Lloyd	17.02.2017	05.04.2020	29.08.2022	91.42%	
11	Switch Yard	GE T&D	17.01.2017	26.03.2020	19.01.2022	90.26%	
12	Station Transformers	Zagson	31.01.2019	03.09.2019	23.09.2022	60.78%	
13	Unit Transformers	Zagson	16.08.2019	23.09.2019	20.11.2022	34.43%	
14	Railway Siding				Feb,2023	Civil work 65%	
15	Power Evacuation Lines	DPSI		21.08.2020	28.02.2023	100 %	100 %

CRITICAL ISSUES

- GT has failed during Factory acceptance test and short circuit test .
- Commercial issues between DPSI and their sub-vendors.

REASONS OF DELAY

1st and 2nd wave of COVID-19 pandemic have caused delay in project, the project is approximately 18 Months delayed.

PANKI THERMAL POWER PROJECT, Unit# 1 (1X660MW) / UPRVUNL (STATE SECTOR - NORTHERN REGION)

Panki TPP, Distt. Kanpur UP, 208020
E-Gen Portal Registration No. (U#1 - 1200001768)

Project Developer / Implementing Agency - UPRVUNL			Main Plant Vendor - M/s BHEL		
Unit No.	LOA	Original Trial Run Date	Anticipated /	Actual	Trial Run Date
Unit#1	Mar-2018	Sep-2021	Jan-2024		
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT		5816.70
COAL COMBUSTION TECHNOLOGY	Super Critical		LATEST ESTIMATED COST		Not Revised
APPROVAL DATE / NTP	20.03.2018		DATE OF FINANCIAL CLOSURE		22.06.2018
EPC/BTG/BoP Contractor Details (Package Wise)	BHEL, LOA: 31.03.2018		YEAR WISE EXPENDITURE		
PPA	Signed on 17.01.2017		2018-19		543.29
COAL LINKAGE/FSA	Allocated Mine - Saharpur Jamarpani mines, Jharkhand; Distance from mine - 896 km (non pithead). Expected grade of coal is G-10. FSA on 30.01.2017		2019-20		837.26
START UP POWER AGREEMENT	20.10.2020		2020-21		1131.48
POWER EVACUATION SYSTEM	Tx Line Developer	UPPTCL	2021-22		951.81
	Tx Line Name Tx Voltage Level	Panki TPS - Panki , 400 KV, D/C line (UPPTCL)	EXPENDITURE OF JULY'2022		128.71
	Configuration of Tx Line (S/C or D/C)		TOTAL EXPENDITURE (upto 31.07.2022)		4039.08
LAND POSSESSION	It is extension project. Hence Land is available				
WATER ALLOCATION	Lower Ganga Canal and Tertiary Treatment Plant, Bingawan (Kanpur)				
MOEF CLEARANCE	Clearance obtained vide letter no. J-13012/35/2013-IA- I(T) dated :- 29.06.2017				
CIVIL AVIATION CLEARANCE	Clearance obtained vide letter no. AAI/NOC/2012/453/104-106 dated:- 18.01.2013				
CPCB CLEARANCE	MOEF clearance obtained on 29.06.2017				
SPCB CLEARANCE	Clearance obtained vide letter no. 24271/UPPCB/Kanpur Nagar(UPPCBRO)/CTE/Kanpur Nagar/2018 dated : 25.06.2018				
FOREST CLEARANCE	Clearance obtained vide letter no. 484/14-1 dated:- 11.08.2015				

PANKI THERMAL POWER PROJECT, Unit# 1 (1X660MW) / UPRVUNL (STATE SECTOR - NORTHERN REGION)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)			
Sl.	MILESTONE	UNIT-01	
		Original Date of Completion	Anticipated / Actual Date of Completion
1	COMPLETION OF BOILER FOUNDATION	29.04.2019	13.01.2020
2	START OF BOILER ERECTION	30.04.2019	24.04.2019
3	BOILER DRUM LIFTING (if sub-critical unit)	NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	20.11.2019	23.02.2020
5	CONDENSER ERECTION START	30.04.2020	28.08.2021
6	TG ERECTION START	30.04.2020	04.10.2021
7	HP PIPING ERECTION START	03.11.2019	30.06.2022
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	30.09.2020	17.12.2021
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	22.02.2021	27.02.2023
10	TG BOX UP	31.01.2021	28.02.2023
11	HP PIPING ERECTION COMPLETION	29.08.2020	30.09.2022
12	START OF OILFLUSHING	30.01.2021	24.11.2022
13	BOILER LIGHT UP	28.02.2021	28.02.2023
14	CHEMICAL CLEANING COMPLETION	10.03.2021	24.04.2023
15	STEAM BLOWING START	09.04.2021	24.05.2023
16	STEAM BLOWING COMPLETION	30.04.2021	14.06.2023
17	ROLLING & SYNC.	31.05.2021	31.07.2023
18	FULL LOAD	30.06.2021	15.09.2023
19	TRIAL RUN	30.09.2021	31.01.2024
20	COD	30.09.2021	31.01.2024

STATUS OF MAIN PLANT PACKAGE (BTG) : M/s BHEL						
Sl.	Packages	AREA	UNIT-01			
			% Completion			
1	BOILER	CIVIL				100.00%
		STRUCTURE WORKS				72.79%
		PRESSURE PARTS				95.92%
2	TG	CIVIL				83.52%
		STRUCTURE WORKS				91.89%
		TG AUX				25.01%
3	ESP	PASS STATUS				87.67%
4	FGD	CIVIL WORK				43.88%
		MATERIAL SUPPLY				13.00%
		ERECTION WORK				1.98%
STATUS OF BOPs						
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01 % Completion
1	Chimney	Bygging	27.11.2018	01.12.2019	10.09.2022	99.17%
2	Coal Handling Plant	Thyseen Krupp & RVPR (Conveyor Package)		19.05.2020	24.12.2022	46.00%
		Thyseen Krupp & Kanwar (Wagon Tripler)	23.11.2018	23.02.2020	10.01.2023	93.54%(RCC)
		Thyseen Krupp & Kanwar (Stacker Reclaimer)	02.05.2018	05.04.2020	29.10.2022	88.76%(Civil Works) 51.40%(Erection)
3	Ash Handling Plant	Indure/ Kanwar	09.04.2018	29.06.2020	16.11.2022	89.00%
4	Fuel Oil System	GMW/ Simplex	30.11.2018	04.05.2020	10.08.2022	93.00%
5	Cooling Towers	Paharpur	01.08.2018, 14.12.2018	25.11.2019, 26.03.2020	28.07.2022, 07.08.2022	99.80%
6	CW Pump house	MHI/ Simplex	06.06.2018	05.07.2020	10.09.2022	70.00%
7	WPT Plant	GDCL	20.11.2018	13.09.2020	18.10.2022	81.00%
8	DM Plant	BGR & Simplex	03.10.2018	04.11.2019	01.09.2022	89.00%
9	Compressed Air System	ATLAS COPCO	23.11.2018	04.05.2020	10.12.2022	100.00%
10	Fire Protection System	BHEL	08.04.2019	17.10.2019	23.01.2023	13.00%
11	Switch Yard	JSPPL	01.08.2018	30.01.2020	12.06.2022	97.00%
12	Station Transformers	BHEL	10.11.2018	27.09.2019	28.06.2023	5.00%
13	Unit Transformers	BHEL	10.03.2019	06.02.2020	28.05.2023	Nil
14	Railway Siding	RITES			March-2023	55.0%
15	Power Evacuation Lines	UPPTCL	08.11.2017	24.07.2020	27.12.2022	50 %

CRITICAL ISSUES

- BoP vendors seeking price compensation due to hike in steel price.
- Re-tendering of some BoP packages, delaying the project.
- Delay in Auxiliary boiler material supply (Trichy) and its readiness.
- Inadequate manpower at site

REASONS OF DELAY

Due to COVID 19 outbreak and its consequences.

BHUSAWAL SUPERCRITICAL TPP, Unit# 1 (1X660 MW) / MAHAGENCO (STATE SECTOR - WESTERN REGION)

Village Pimpri Sekam, Tal- Bhusawal, Distt.- Jalgaon, Maharashtra, 425307

E-Gen Portal Registration No. (U#1 - 1200002450)

Project Developer / Implementing Agency - MAHAGENCO			Main Plant Vendor - M/S BHEL (EPC Contract-17.01.2018)		
Unit No.	LoA	Original Trial Run Date	Anticipated /	Actual	Trial Run Date
Unit#1	Jan-2018	May-2022		Jun-2023	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT		4548.00
COAL COMBUSTION TECHNOLOGY	Super Critical		LATEST ESTIMATED COST		4550.97
APPROVAL DATE / NTP	25-09-2009		DATE OF FINANCIAL CLOSURE		NA
EPC/BTG/BoP Contractor Details (Package Wise)	M/s BHEL (EPC Contract, LoA:17.01.2018)		YEAR WISE EXPENDITURE		
PPA	Long Term Power Purchase Agreement dated 24.12.2010 with Maharashtra state Electricity Distribution Co. ltd for 100% of installed capacity		2018-19		59.41
COAL LINKAGE/FSA	Allocated Mine - WCL, Umred/Ghugus; Distance from mine – 403/430km; Allocation Date: 11-09-2020, Source:WCL mines ,Grade: G9/G10, Quantity : 318 million tonne.		2019-20		584.06
START UP POWER AGREEMENT	Maharashtra State Electricity Transmission Company Limited (MSETCL) vide letter no MSETCL/CO/STU/302 B/B_GC/No. 12757, dated 06/12/2018 approved Grid connectivity, which is valid till 06.06.2021. Letter regarding extension up to Dec-2022, is sent to STU, MSETCL on 07.05.2021.		2020-21		1381.85
POWER EVACUATION SYSTEM	Tx Line Developer	MSETCL	2021-22		1173.80
	Tx Line Name Tx Voltage Level	LILOing of Bhusawal-II - Aurangabad I, 400 KV, D/C line at Thaptitanda	EXPENDITURE OF JULY'2022		50.95
	Configuration of Tx Line (S/C or D/C)		TOTAL EXPENDITURE (upto 31.07.2022)		3630.14
LAND POSSESSION	Total Land Required: 120.39 Hectare Total land acquired: 118.415 Hectare Total land in use: 118.415 Hectare				
WATER ALLOCATION	Source: - Tapi River Quantity: - 18.85 MM3 Per Annum.				
MOEF CLEARANCE	Clearance obtained date from concerned authority: 27/11/2012 validity : 26/11/2022				
CIVIL AVIATION CLEARANCE	Clearance obtained date from concerned authority: 27/08/2008 validity : 23/02/2022				
CPCB CLEARANCE	Not Applicable				
SPCB CLEARANCE	Clearance obtained date from concerned authority: 10/06/2020 validity : The consent to establish is granted for period up to commissioning of the unit or up to 5 years whichever is earlier.				
FOREST CLEARANCE	Clearance obtained date from concerned authority: 14/01/2020 validity: 26/11/2022.				

BHUSAWAL SUPERCRITICAL TPP, Unit# 1 (1X660 MW) / MAHAGENCO (STATE SECTOR - WESTERN REGION)						
UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)				STATUS OF MAIN PLANT PACKAGE (BTG) : M/S BHEL		
Sl.	MILESTONE	UNIT-01		Sl.	Packages	AREA
		Original Date of Completion	Anticipated / Actual Date of Completion			UNIT-01 % Completion
1	COMPLETION OF BOILER FOUNDATION	25.11.2019	15.11.2019	1	BOILER	CIVIL
2	START OF BOILER ERECTION	30.11.2019	22.11.2019			STRUCTURE WORKS
3	BOILER DRUM LIFTING (if sub-critical unit)	NA	NA			PRESSURE PARTS
4	BOILER CEILING GIRDER LIFTING COMPLETION	30.06.2020	20.01.2021	2	TG	CIVIL
5	CONDENSER ERECTION START	31.10.2020	30.03.2022			STRUCTURE WORKS
6	TG ERECTION START	30.11.2020	03.03.2022			PRESSURE PARTS
7	HP PIPING ERECTION START	11.05.2021	22.03.2021	3	ESP	PASS STATUS
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	31.05.2021	Aug,2022	4	FGD	CIVIL WORK
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	10.11.2021	Aug,2022			MATERIAL SUPPLY
10	TG BOX UP	30.11.2021	Nov,2022			ERECTION WORK
11	HP PIPING ERECTION COMPLETION	25.04.2022	Jan, 2023	STATUS OF BOPs		
12	START OF OILFLUSHING	04.12.2021	Mar,2023	Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC- BHEL)
13	BOILER LIGHT UP	30.11.2021	Nov,2022			Date of Award
14	CHEMICAL CLEANING COMPLETION	20.12.2021	Dec,2022			Scheduled Date of Completion
15	STEAM BLOWING START	24.01.2022	Dec,2022			Anticipated/Actual Date of Completion
16	STEAM BLOWING COMPLETION	19.02.2022	Jan, 2023			UNIT-01 % Completion
17	ROLLING & SYNC.	31.03.2022	Mar,2023	1	Chimney	M/s Powermech
18	FULL LOAD	30.04.2022	May,2023	2	Coal Handling Plant	M/s BJCL & Macawber Beekay Pvt Ltd.(Conveyor package)
19	TRIAL RUN	31.05.2022	June-2023			M/s BJCL& Promac (Wagon tippler)
20	COD	31.05.2022	June,2023			M/s BJCL& Promac(Stacker Reclaimer)
				3	Ash Handling Plant	M/s BJCL & Macawber Beekay Pvt Ltd.
				4	Fuel Oil System	M/s. New Fire Engineers Pvt Ltd.
				5	Cooling Towers	M/s Hayagrev civil engineering Pvt Ltd
				6	CW Pump house	M/s Alpha power engineering services Pvt Ltd,G&J Pvt Ltd.
				7	WPT Plant	M/s Clear Water company
				8	DM Plant	M/s Wipro Enterprises Pvt Ltd
				9	Compressed Air System	M/s Elgi equipment Ltd.
				10	Fire Protection System	M/s Alpha power engineering services Pvt Ltd
				11	Switch Yard	M/s BNC Power Projects Ltd
				12	Station Transformers	M/s BHEL
				13	Unit Transformers	M/s BHEL
				14	Railway Siding	ISC Projects
				15	Power Evacuation Lines	MSETCL/BNC Power Projects

CRITICAL ISSUES

- Slow progress in BoP area - CHP, AHP, CT, WPT plant.
- Inadequate manpower mobilization at site by BHEL

REASONS OF DELAY

Due to Covid-19 pandemic.

SRI DAMODARAM SANJIVIAIAH TPS, St- II, Unit# 1 (1X800 MW) / APPDCL (STATE SECTOR - SOUTHERN REGION)

Nelatur (Village), near Krishnapatnam, Muthukuru (Mandal), SPSR Nellore (District) Andhra Pradesh – 524 347

E-Gen Portal Registration No. (U#1 -1200001078)

Project Developer / Implementing Agency -APPDCL			Main Plant Vendor - BTG order placed on BHEL on 02.11.2015	
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Nov-2015	Jun-2019		Oct.,2022
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)	
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT	4276.03
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST	7922.72
APPROVAL DATE / NTP	16 Feb, 2013		DATE OF FINANCIAL CLOSURE	17.09.2014
EPC/BTG/BoP Contractor Details (Package Wise)	BTG contractor: BHEL and BoP: TPL		YEAR WISE EXPENDITURE	
PPA	PPA entered with APDISCOMS to sell 90% of the declared capacity		2015-16	7.08
COAL LINKAGE/FSA	Allocated Mine - MCL, Talcher (Odisha); Distance from mine - 1225 km (non pithead); MCL has issued LoA to supply 3.548 MTPA vide letter dated 04-03-2018.		2016-17	568.03
START UP POWER AGREEMENT	From the existing Stage-I (2x800 MW) Units.		2017-18	1664.72
POWER EVACUATION SYSTEM	Tx Line Developer	APTRANSCO	2018-19	2886.73
	Tx Line Name Tx Voltage Level	Power evacuation system is available. Power will be evacuated through existing 400 kV lines connected to switchyard St-I.	2019-20	1062.04
	Configuration of Tx Line (S/C or D/C)		2020-21	885.36
LAND POSSESSION	51 Acres of land is used for Stage-II from the available land of 1344.80Acres which is already under possession of APPDCL. No additional land is required for Stage-II (1x800MW)		2021-22	920.53
WATER ALLOCATION	Seawater about 6,556 Cum/Hr		EXPENDITURE OF JULY 2022	64.44
MOEF CLEARANCE	MoEF clearancce obtained on 02-07-2015 for 7 Years		TOTAL EXPENDITURE (upto 31.07.2022)	8203.87
CIVIL AVIATION CLEARANCE	Case No. MM315/2011: AAI/SR/NOC/RHQ, Dt. 25.06.2012			
CPCB CLEARANCE	Same as MOEF Clearance			
SPCB CLEARANCE	APPCB/VIJ/NLR/159/CFO/2014-494 DT. 08.05.2014			
FOREST CLEARANCE	RC. No. 646/2013/WL-1, Dt. 23.02.2012			

SRI DAMODARAM SANJIVIAH TPS, St- II, Unit# 1 (1X800 MW) / APPDCL (STATE SECTOR - SOUTHERN REGION)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)			
Sl.	MILESTONE	UNIT-01	
		Original Date of Completion	Anticipated / Actual Date of Completion
1	COMPLETION OF BOILER FOUNDATION	17.04.2017	27.05.2017
2	START OF BOILER ERECTION	06.04.2017	26.06.2017
3	BOILER DRUM LIFTING (if sub-critical unit)	NA	NA
4	BOILER CEILING GIRDER LIFTING COMPLETION	06.04.2017	04.02.2018
5	CONDENSER ERECTION START	26.08.2017	24.08.2018
6	TG ERECTION START	23.11.2017	03.10.2018
7	HP PIPING ERECTION START	01.04.2018	21.11.2019
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	27.03.2018	01.07.2019
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	16.11.2018	18.12.2019
10	TG BOX UP	14.11.2018	29.02.2020
11	HP PIPING ERECTION COMPLETION	15.05.2019	In Progress
12	START OF OILFLUSHING	30.11.2018	19.03.2020
13	BOILER LIGHT UP	11.12.2018	31.12.2019
14	CHEMICAL CLEANING COMPLETION	25.12.2018	07.12.2020
15	STEAM BLOWING START	27.12.2018	20.03.2021
16	STEAM BLOWING COMPLETION	21.01.2019	08.06.2021
17	ROLLING & SYNC.	14.01.2019	10.11.2021
18	FULL LOAD	14.03.2019	31.08.2022
19	TRIAL RUN	Jun,29	Oct.,22
20	COD	Jun-19	Oct.,22

STATUS OF MAIN PLANT PACKAGE (BTG) : M/S BHEL- EQUIPMENT PKG and						
Sl.	Packages	AREA	UNIT-01			
			% Completion			
1	BOILER	CIVIL	98%			
		STRUCTURE				
		PRESSURE PARTS				
2	TG	CIVIL	97%			
		STRUCTURE				
		TG ERECTION				
3	ESP	UNDER PROGRESS	99%			
4	FGD	CIVIL WORK	Tender was cancelled as no response from bidders. Revised specification is under preparation.			
		MATERIAL SUPPLY				
		ERECTION WORK				
STATUS OF BOPs						
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01 % Completion
1	Chimney	TPL / Bygging	11.04.2017	17.04.2019	31.10.2019	100%
2	Coal Handling Plant	(Conveyor package) TPL / ISGEC	13.10.2017	31.05.2019	31.08.2022	93%
		(Wagon tippler)	-	-	-	NOT APPLICABLE
		(Stacker Reclaimer)	-	-	-	
3	Ash Handling Plant	TPL / MBPL	13.07.2018	31.05.2019	30.9.2022	93%
4	Fuel Oil System	TPL / United System	06.04.2018	01.04.2019	20.04.2021	100%
5	Cooling Towers	TPL / Hayagrev	24.07.2017	09.03.2019	18.03.2021	100%
6	CW Pump house	TPL / Xylem & DSS	21.11.2016	20.02.2019	27.05.2021	100%
7	WPT Plant	TPL / BGR	25.12.2017	04.02.2019	05.12.2019	100%
8	DM Plant	TPL / BGR		30.04.2019	22.01.2021	100%
9	Compressed Air System	TPL / ELGI	24.11.2018	25.02.2019	29.12.2019	100%
10	Fire Protection System	TPL / AGNICE	10.08.2018	27.04.2019	30.9.2022	92%
11	Switch Yard	TPL / ABB	02.02.2018	30.04.2019	11.10.2019	100%
12	Station Transformers	M/s BHEL		06.12.2018	14.10.2019	100%
13	Unit Transformers	M/s BHEL		06.12.2018	31.8.2022	90%
14	Railway Siding	Not Applicable	-	-	-	-
15	Power Evacuation Lines	Generated power will be evacuated with exiting 400kv lines connected to switch yard				Available

CRITICAL ISSUES

- TG vibration problem.
- FGD works is yet to start.

REASONS OF DELAY

- Due to Covid-19 pandemic all the works are held up at site from the third week of March 2020 due to announcement of Lockdown. 3. Due to Covid-19 pandemic 2nd wave all the works are held up at site from the third week of April 2021 due to unprecedented situations of Covid -19 2nd wave.
- Unit started for partial trial load operations on 21.03.2022 and loaded up to 270 MW. TG vibrations occurred. Shut down of unit was done on 28.3.22. After TG vibration rectification work, restart of unit will be done in August 2022 and COD to be completed by September 2022.

Dr. NARLA TATA RAO TPS, St-V, Unit# 1 (1x 800 MW) / APGENCO (STATE SECTOR - SOUTHERN REGION)

Ibrahimpatnam (Village & Mandalam), Krishna District, Andhra Pradesh. PIN: 521456

E-Gen Portal Registration No. (U#8 - 1200000271)

Project Developer / Implementing Agency - APGENCO			Main Plant Vendor - M/S BHEL (BTG)			
Unit No.		LOA	Original Trial Run Date		Anticipated / Actual Trial Run Date	
Unit#1		Dec-2015	Apr-2019		August,23	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)			
FUEL TYPE		Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT		5286.54
COAL COMBUSTION TECHNOLOGY		Supercritical		LATEST ESTIMATED COST		7586.67
APPROVAL DATE / NTP		Administrative approval accorded on 09.07.2014		DATE OF FINANCIAL CLOSURE		
EPC/BTG/BoP Contractor Details (Package Wise)		BTG/BHEL(LoA :15.12.2015) and BoP: M/s BGR (LoA: 06.07.2016)		YEAR WISE EXPENDITURE		
PPA		PPA is available with DISCOMS of erstwhile APGENCO in combined AP. The same is being revised with APDISCOMS				
COAL LINKAGE/FSA		Allocated Mine - MCL (non-pithead); Distance from mine - 930 km (non pithead); MCL issued LoI for supply of 3.548 MTPA vide letter dated 12-11-2018. Grade of coal - G13; Bridge Linkage - Not Applicable		2015-16		6.60
START UP POWER AGREEMENT		Not Applicable		2016-17		422.91
POWER EVACUATION SYSTEM		Tx Line Developer		2017-18		2099.15
		Tx Line Name Tx Voltage Level		2018-19		1495.18
		Configuration of Tx Line (S/C or D/C)		2019-20		1032.00
LAND POSSESSION		85 Acres land is available within plant boundary for Main plant & facilities and green belt. This is extension project being constructed in the available land of Dr. NTPS Project.		2020-21		585.00
WATER ALLOCATION		Irrigation department vide letter dt:05.03.2015 agreed to supply 25 Cusecs water from Krishna river upstream of Prakasam barrage, Vijayawada.		2021-22		773.50
MOEF CLEARANCE		MoEF issued clearance for imported coal vide letter dated:26.06.2015 and the same was revised vide letter dt:11.04.2019.		EXPENDITURE OF JULY '2022		52.04
CIVIL AVIATION CLEARANCE		Aviation clearance was obtained vide letter dated:15.10.2012		TOTAL EXPENDITURE (upto 31.7.2022)		6977.30
CPCB CLEARANCE		CPCB clearance is Not Applicable				
SPCB CLEARANCE		APCB issued consent for establishment vide letter dated:28.09.2015 and the same amended vide letter dt:07.03.2020				
FOREST CLEARANCE		Forest Clearance is Not applicable				

Dr. NARLA TATA RAO TPS, St-V, Unit# 1 (1x 800 MW) / APGENCO (STATE SECTOR - SOUTHERN REGION)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)			
Sl.	MILESTONE	UNIT-01	
		Original Date of Completion	Anticipated / Actual Date of Completion
1	COMPLETION OF BOILER FOUNDATION	15.11.2016	20.06.2017
2	START OF BOILER ERECTION	25.10.2016	22.05.2017
3	BOILER DRUM LIFTING (if sub-critical unit)	NA	NA
4	BOILER CEILING GIRDER LIFTING COMPLETION	06.04.2017	27.12.2017
5	CONDENSER ERECTION START	23.09.2017	22.08.2018
6	TG ERECTION START	05.12.2018	03.02.2021
7	HP PIPING ERECTION START	19.12.2018	10.01.2019
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	27.03.2018	03.03.2019
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	16.11.2018	24.10.2019
10	TG BOX UP	24.08.2019	16.06.2021
11	HP PIPING ERECTION COMPLETION	11.02.2019	15.07.2021
12	START OF OIL FLUSHING	17.06.2020	18.12.2020
13	BOILER LIGHT UP	15.05.2019	28.12.2019
14	CHEMICAL CLEANING COMPLETION	12.12.2018	12.03.2020
15	STEAM BLOWING START	27.12.2019	05.04.2021
16	STEAM BLOWING COMPLETION	09.02.2019	01.06.2021
17	ROLLING & SYNC.	22.02.2021	07.12.2021
18	FULL LOAD	30.04.2019	15.01.2023
19	TRIAL RUN	20.04.2019	Aug.,23
20	COD	14.06.2019	Aug.,23

STATUS OF MAIN PLANT PACKAGE (BTG) : M/S BHEL						
Sl.	Packages	AREA	UNIT-01			
			% Completion			
1	BOILER	CIVIL	97.30%			
		STRUCTURE	89.00%			
		PRESSURE PARTS				
2	TG	CIVIL	89.20%			
		STRUCTURE	95.23%			
		PRESSURE PARTS	97.00%			
3	ESP	PASS STATUS	98.00%			
4	FGD	CIVIL WORK	Price bid is opened, bid evaluation is under progress.			
		MATERIAL SUPPLY				
		ERECTION WORK				
STATUS OF BOPs						
Sl.	Packages/ Linked ProjectMilestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01 % Completion
1	Chimney	M/s BGRESL	16.05.2017	11.05.2019	Major works completed.	97%
2	Coal HandlingPlant	M/s BGRESL (Conveyor package)	16.09.2016	30.03.2019	31.12.2022	50%
		M/s BGRESL (Wagon Tripler)	30.05.2018	30.01.2019	31.12.2022	80%
		M/s BGRESL (Stacker Reclaimer)	01.05.2018	30.06.2018	31.12.2022	45%
3	Ash Handling Plant	M/s BGRESL	24.10.2016	01.05.2019	31.12.2022	39%
4	Fuel Oil System	M/s BGRESL	18.02.2017	08.11.2018	05.03.2021	100%
5	Cooling Towers	M/s BGRESL	17.01.2017	16.05.2019	Major works completed. Charged on 11.9.2021.	85%
6	CW Pump house	M/s BGRESL	02.03.2017	20.05.2019	30.11.2022	95%
7	WPT Plant	M/s BGRESL	02.11.2016	15.12.2018	30.11.2022	80%
8	DM Plant	M/s BGRESL	02.11.2016	15.12.2018	30.11.2022	95%
9	Compressed Air System	M/s BGRESL	21.02.2017	23.06.2018	31.12.2022	90%
10	Fire Protection System	M/s BGRESL	15.02.2017	06.04.2019	31.12.2022	70%
11	Switch Yard	M/s BGRESL / M/s Sri Sai Contractors	16.09.2017	30.03.2018	30.11.2022	95%
12	Station Transformers	M/s BHEL / M/s KSL Contractors	30.01.2019	06.01.2020	12.06.2020	100%
13	Unit Transformers	M/s BHEL / M/s KSL Contractors	05.03.2020	06.12.2020	30.11.2022	90%
14	Railway Siding	M/s BGRESL	01.06.2019	31.10.2021	31.12.2022	30%
15	Power Evacuation Lines	Unit-8 Switchyard is extended from existing switchyard of Unit-7 and Power evacuation is proposed through lines onthe existing switchyard.				

CRITICAL ISSUES

- Slow work in CHP/AHP area.
- Delay in readiness of RHS mills and bunkers

REASONS OF DELAY

- Due to change in Boiler design for implementation of revised norms regarding reduction of Nox levels initial delay was occurred.
- Due to the impact of Covid-19 and subsequent lockdowns in first & second wave has severely impacted the labour & supplies.
- All the labour stranded at site during first lockdown left the site after relaxation of lockdown and partial lockdowns imposed by various states during second wave of covid has affected the supplies. BOP supplies are severely impacted due to steep increase in raw material prices.
- BOP supplies are severely impacted due to steep increase in raw material prices

YADADRI TPS, Unit# 1, 2, 3, 4 & 5 (5x800 MW) / TSGENCO (STATE SECTOR - SOUTHERN REGION)

Veerlapalem village, Damercharla Mandal, Nalgonda, Telangana -508208

E-Gen Portal Registration No. (U#1-1200001092; U#2-1200001093; U#3-1200001094; U#4-1200001095; U#5-1200001096)

Project Developer / Implementing Agency - TSGENCO			Main Plant Vendor - BHEL (EPC)		
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	COD Date	
Unit#1	Oct-2017	Oct-2021	Jun-2023		
Unit#2		Oct-2021	Aug-2023		
Unit#3		Jun-2022	Dec-2023		
Unit#4		Jun-2022	Apr-2024		
Unit#5		Oct-2022	Aug-2024		
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT		25099.42
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST		29965.48
APPROVAL DATE / NTP	04.10.2014 (MoU entered with BHEL)		DATE OF FINANCIAL CLOSURE		*
EPC/BTG/BoP Contractor Details (Package Wise)	LOI was issued to M/s BHEL as EPC contractor (BTG & BOP) on 01.06.2015 . Revised LOI issued on Dt:17.10.2017 for considering new norms & impact of GST with zero date as 17.10.2017.		YEAR WISE EXPENDITURE		
PPA	Power purchase Agreement entered on 11.03.2020 with TSDISCOMS		2015-16		499.46
COAL LINKAGE/FSA	Allocated Mine - SCCL; Distance from mine - 270 km (non pithead); Ministry of Coal vide File No.23014/1/2018-CLD, Dt:15-02-2018 has granted coal linkage from SCCL for supply of 14 MTPA of coal (grade-G9).		2016-17		59.29
			2017-18		941.44
START UP POWER AGREEMENT	As per clause no.2.2 of PPA ,TSDISCOMS shall provide electrical energy to TSGENCO for construction, start up and maintenance, also for commissioning of the project.		2018-19		2129.24
			2019-20		2935.56
POWER EVACUATION SYSTEM	Tx Line Developer	TSTRANSCO	2020-21		4427.54
	Tx Line Name Tx Voltage Level	i) YTPS –Dindi, 400 KV, S/C line; ii) YTPS-Choutuppal,400 KV, S/C line; iii) YTPS-Damarcherla, 400 KV, S/C line;	2021-22		3582.33
	Configuration of Tx Line (S/C or D/C)	iv) YTPS-Janagaon, 400 KV, S/C line.	EXPENDITURE OF JULY'2022		492.74
LAND POSSESSION	(Details about land area still to be acquired). Ac.5459.39 Gts		TOTAL EXPENDITURE (upto 31.07.2022)		15843.61
WATER ALLOCATION	Water Source from river Krishna Qty- 208cuses(i.e.6.60 TMC per year) allotted vide G.O.Ms.No.13, Dt:30.01.2015		* M/s REC Ltd vide Lr dt 11-08-2015. M/s PFC Ltd vide Lr dt 19-07-2015		
MOEF CLEARANCE	EC obtained from MoEF&CC vide Lr.No.J-13012/18/2015-IA.I(T), Dt.29- 06-2017 with a validity of 7 years from the date of issue of MoEF clearance(i.e upto 29.06.2024)				
CIVIL AVIATION CLEARANCE	1.NOCID:NADI/SOUTH/B/071216/149982,Dt:26.07.2016. 2.NOCID:NADI/SOUTH/B/071216/149984,Dt:26.07.2016. 3.NOCID:NADI/SOUTH/B/071216/149988,Dt:26.07.2016.				
CPCB CLEARANCE	Not Applicable				
SPCB CLEARANCE	Consent for Establishment (CFE) received from TSPCB vide Order No.10/TSPCB/CFE/RO-NLG/HO/2017, Dt.25-07-2017.				
FOREST CLEARANCE	Approval was accorded by Central Govt. Ministry of Environment, Forest, Climate Change, MoEF &CC, GOI, FC Section, New Delhi for diversion of forest land to an extent of 1892.35 hectares vide lr.no.F.No.8.07/2015-FC dt.07-07-2015 Subsequent G.O. was issued by Govt. of Telangana vide G.O.Ms.No.38,dt.30-07-2015 by EFS & T (For) Department.				

YADADRI TPS, Unit# 1, 2, 3, 4 & 5 (5x800 MW) / TSGENCO (STATE SECTOR - SOUTHERN REGION)**STATUS OF BTG WORKS**

Sl.	Packages	AREA	UNIT-01	UNIT-02	UNIT-03	UNIT-04	UNIT-05
			% Completion	% Completion	% Completion	% Completion	% Completion
1	BOILER	CIVIL	100.00%	100.00%	100.00%	100.00%	100.00%
		STRUCTURE	61.82%	66.14%	50.55%	59.45%	47.74%
		PRESSURE PARTS	68.05%	71.55%	38.87%	63.39%	30.69%
2	TG	CIVIL	98.0%	98.0%	97.0%	97.0%	96.0%
		STRUCTURE	97.93%	89.53%	95.26%	69.29%	59.11%
		TG ERECTION	30.50%	31.50%	0.00%	0.00%	0.00%
3	ESP	UNDER PROGRESS	92.88%	89.00%	84.33%	83.32%	69.93%
4	FGD	CIVIL WORK	YET TO START, Engineering Under Progress				
		MATERIAL SUPPLY					
		ERECTION WORK					

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)

Sl.	MILESTONE	UNIT-01		UNIT-02		UNIT-03		UNIT-04		UNIT-05	
		Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date
1	COMPLETION OF BOILER FOUNDATION	08.01.20	08.01.20	29.12.19	29.12.19	11.02.20	11.02.20	16.02.20	16.02.20	23.03.20	23.03.20
2	START OF BOILER ERECTION	18.02.20	18.02.20	30.07.20	30.07.20	18.03.20	18.03.20	30.07.20	30.07.20	14.08.20	14.08.20
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA		NA		NA		NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	31.01.21	20.03.21	31.03.21	31.03.21	11.04.21	11.04.21	09.06.21	09.06.21	07.09.21	07.09.21
5	CONDENSER ERECTION START	31.03.21	20.10.21	31.05.21	03.01.22	30.05.21	31.08.22	31.07.21	31.08.22	15.10.21	30.08.22
6	TG ERECTION START	03.05.21	30.12.21	30.06.21	31.03.22	31.08.21	31.08.22	30.10.21	31.08.22	30.11.21	31.08.22
7	HP PIPING ERECTION START	01.04.21	15.09.21	01.05.21	01.01.22	01.06.21	15.07.22	01.07.21	31.07.22	01.08.21	31.07.22
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	31.01.22	31.07.22	31.03.22	31.06.22	31.05.22	31.08.22	31.07.22	31.08.22	30.09.22	30.09.22
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	15.07.22	15.09.22	15.09.22	15.09.22	15.11.22	15.11.22	15.01.23	15.01.23	15.03.23	15.03.23
10	TG BOX UP	31.05.22	30.12.22	31.07.22	31.11.22	31.08.22	28.02.23	30.10.22	31.03.23	30.11.22	30.03.23
11	HP PIPING ERECTION COMPLETION	13.10.22	13.10.22	13.11.22	13.11.22	13.12.22	13.12.22	13.01.23	13.01.23	13.02.23	13.02.23
12	START OF OIL FLUSHING	30.04.22	30.10.22	31.05.22	30.09.22	31.07.22	30.01.23	30.09.22	28.02.23	30.10.22	30.03.23
13	BOILER LIGHT UP	31.07.22	31.10.22	30.09.22	30.09.22	30.11.22	30.11.22	31.01.23	31.01.23	31.03.23	31.03.23
14	CHEMICAL CLEANING COMPLETION	05.09.22	05.11.22	29.09.22	05.11.22	29.10.22	05.11.23	29.11.22	28.02.23	29.12.22	15.04.23
15	STEAM BLOWING START	14.09.22	14.11.22	14.10.22	14.11.22	14.11.22	14.01.23	14.12.22	05.03.23	14.01.23	25.04.23
16	STEAM BLOWING COMPLETION	14.10.22	14.12.22	14.11.22	30.11.22	14.12.22	30.01.23	14.01.23	14.02.23	14.02.23	15.05.23
17	ROLLING & SYNC.	30.10.22	30.01.23	31.12.22	31.12.22	31.01.23	31.03.23	31.03.23	30.04.23	30.06.23	31.05.23
18	FULL LOAD	12.02.23	15.02.23	15.03.23	15.03.23	15.04.23	15.04.23	15.05.23	15.05.23	15.06.23	15.06.23
19	TRIAL RUN		Jun,23		Aug,23		Dec,23		Apr,24		Aug.,24
20	COD	28.02.23	Jun,23	31.03.23	Aug,23	30.04.23	Dec,23	31.05.23	Apr.,24	30.06.23	Aug.,24

YADADRI TPS, Unit# 1, 2, 3, 4 & 5 (5x800 MW) / TSGENCO (STATE SECTOR - SOUTHERN REGION)

STATUS OF BOPs										
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01	UNIT-02	UNIT-03	UNIT-04	UNIT-05
						% Completion	% Completion	% Completion	% Completion	% Completion
1	Chimney	Bygging India Ltd for Unit #1&2; Paharpur for Unit #3&4; Bygging India Ltdfor Unit #5	03.02.20	31.07.22	31.12.22	Shell Concreting-100%		Shell Concreting-100%		SC-100%
			24.02.20 12.02.20			Flue can fabrication 76.29%		Flue can fabrication 83.82%		FCF-56.03%
2	Coal Handling Plant (Civil)	Powermech (Conveyor package)	09.08.20	31.12.22	31.12.22	49.73%				
		Powermech (Wagon tripler)	10.12.20	30.06.23	30.06.23	77.62%				
		Powermech (Stacker Reclaimer)	08.10.20	30.06.23	30.06.23	95.45%				
3	Ash Handling Plant (Civil)	BHEL/ Powermech	08.06.21	31.12.22	31.12.22	32.31%				
4	Fuel Oil System	BHEL/Thermosystems	19.02.21	31.07.22	31.07.23	16.75%				
5	Cooling Towers	BHEL/NBCC for Unit #1 (Now M/s Paharpur) BHEL/Gammon for Unit#2 BHEL/NBCC for Unit#3 BHEL/Gammon for Unit#4 BHEL/NBCC for Unit#5	09.01.21 18.12.20 06.02.21 25.02.21 18.03.21	30.10.22 28.02.23 31.03.23 30.04.23 31.05.23	30.10.22 28.02.23 31.03.23 30.04.23 31.05.23	8.11%	10.12%	6.27%	6.80%	4.55%
6	CW Pump house	CW pump house & channel - BHEL/HES				78.68	78.68	41.18	41.18	41.18
7	WPT Plant (Civil)	BHEL/SCC	03.02.21	31.01.22	31.01.23	65.75%				
8	DM Plant (Civil)	BHEL/SCC	01.10.20	31.01.22	31.02.23	79.66%				
9	Compressed Air System (Civil)	BHEL/HES	12.02.21	31.05.22	30.03.23	99.08%				
10	Fire Protection System	BHEL	-	31.07.22	30.06.23	0.00%				
11	Switch Yard (Civil)	BHEL/Bluechip	13.02.21	31.07.22	30.12.22	58.84%				
12	Generator Transformers	BHEL/EIPL for Unit-1 BHEL/KEPL for Unit-2	14.12.19 17.10.20	30.10.22 31.12.22	30.10.22 31.12.22	98.50%	97.00%	98.50%	96.00%	89.00%
13	Station Transformers	BHEL/EIPL for Unit-3 BHEL/KEPL for Unit-4	26.10.19 22.10.19	31.01.23 31.03.23	31.01.23 31.03.23					
14	Unit Transformers	BHEL/KEPL for Unit-5	18.12.19	31.05.23	31.05.23					
15	Railway Siding	Work in progress								
16	Power Evacuation Lines	TS TRANSCO/MEIL	06.08.20	24.02.22	31.12.22	80.0%				

CRITICAL ISSUES

- Slow progress in BoP area – AHP, CT, CHP .
- Delay in EoT crane thereby hampering the other works.
- Mismanagement in material receipt at site by BHEL.
- Inadequate senior officers posting at site by BHEL, in view of single large project .
- REC/PFC has stopped disbursing the loan to this project affecting the progress of the project and causing delay in execution.

REASONS OF DELAY

- 1) Delay in agency finalization of Main plant civil works and Boiler erection works.
- 2) The works of YTPS were adversely affected due to Covid-19 (1.0) as lockdown was imposed by State Government. Further upon resumption of the site works also, the works could not progress at the required pace, due to acute shortage of man power as most of the available workers at site have left.
- 3) The impact of monsoons and unprecedented rains during other seasons resulted in frequent dewatering caused interruption to the movement of men and machinery which affected the work progress at YTPS site.
- 4) The outbreak of Covid-19 (2.0) again hit the country with higher magnitude from March 2021 onwards. Number of workers and engineers are effected with Covid-19 in the project. Erection works are hampered due to non-availability of oxygen cylinders as the oxygen is diverted to Hospitals as per the directions of State Government.

YELAHANKA COMBINED CYCLE PP (YCCPP), Unit# 1 (1x370 MW) / KPCL (STATE SECTOR - SOUTHERN REGION)

Yelahanka Combined Cycle Power Plant (YCCPP), Doddballapura Road, Bengaluru, Karnataka-560064

E-Gen Portal Registration No. (U#1 -1200002031)

Project Developer / Implementing Agency - KPCL			Main Plant Vendor - BHEL (EPC Contract-03.11.2015)		
Unit No.	LOA	Original Trial Run Date	Anticipated /	Actual	Trial Run Date
Unit#1	Nov-2015	Feb-2018	Jan.,2023		
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	RLNG (Regasified Liquefied Natural Gas)		ORIGINAL ESTIMATED COST OF THE PROJECT		1571.18
COAL COMBUSTION TECHNOLOGY	NOT APPLICABLE		LATEST ESTIMATED COST		2055.23
APPROVAL DATE / NTP	Approval Date: Government Of Karnataka Order No. EN78PPC2010 Bengaluru dated:05.07.2011		DATE OF FINANCIAL CLOSURE		31.03.2021
EPC/BTG/BoP Contractor Details (Package Wise)	EPC Contractor: M/s BHEL LOA Date:03.11.2015		YEAR WISE EXPENDITURE		
PPA	Under Process		2015-16		4.87
COAL LINKAGE/FSA	NOT APPLICABLE		2016-17		152.89
START UP POWER AGREEMENT	20 MVA on HT basis vide BESCOM Letter No. CEE/BMAZ-N/SEE(O)/AEE-2/18-19/2473-78 dated:17.11.2018		2017-18		1050.00
POWER EVACUATION SYSTEM	Tx Line Developer	KPTCL	2018-19		140.93
	Tx Line Name Tx Voltage Level	3 nos. of 220 kV lines are ready (Dec-2018) for the power evacuation	2019-20		171.41
	Configuration of Tx Line (S/C or D/C)		2020-21		219.28
LAND POSSESSION			2021-22		263.80
			EXPENDITURE OF JULY '2022		5.52
			TOTAL EXPENDITURE (upto 31.07.2022)		2283.24
WATER ALLOCATION	15 MLD Tertiary treated plant at JAKKUR is supplying water to YCCP Plant				
MOEF CLEARANCE	Approval No : State Level environment impact assessment authority(SEIAA) no SEIAA20IND 2014 DATED 1/9/2015				
CIVIL AVIATION CLEARANCE	Approval no : AAI /KIA/ATM/NOC/488-92 DATED 5/5/2015				
CPCB CLEARANCE	NOT APPLICABLE				
SPCB CLEARANCE	Approval No : KSPCB/CFE/CEO/KPCL/2015-16/H1033 DATED 02/11/2015				
FOREST CLEARANCE	Letter No: SEIAA 20 IND 2014 dtd 01.09.2015				

YELAHANKA COMBINED CYCLE PP (YCCPP), Unit# 1 (1x370 MW) / KPCL (STATE SECTOR - SOUTHERN REGION)									
UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)					STATUS OF MAIN PLANT PACKAGE (BTG) : (BHEL-BTG VENDOR)				
Sl.	MILESTONE		UNIT-01 (GT+ST)		Sl.	Packages	AREA	UNIT-01 (GT+ST)	
			Original Date of Completion	Anticipated / Actual Date of Completion				% Completion	
1	COMPLETION OF BOILER FOUNDATION		30.06.2016	14.11.2016	1	BOILER	CIVIL	100%	
2	START OF BOILER ERECTION		01.07.2016	09.11.2016			STRUCTURE	99%	
							PRESSURE PARTS	99%	
3	BOILER DRUM LIFTING (if sub-critical unit)		10.03.2017	07.04.2017	2	Gas T/ TG	CIVIL	100%	
							STRUCTURE	99%	
							TG ERECTION	99%	
4	BOILER CEILING GIRDER LIFTING COMPLETION		30.11.2016	21.12.2016	3	ESP	Not Applicable	Not Applicable	
5	CONDENSER ERECTION START		14.08.2017	Nov-17	4	FGD	CIVIL WORK	Not Applicable	
							MATERIAL SUPPLY		
6	TG ERECTION START						ERECTION WORK		
STATUS OF BOPs									
	Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC- BHEL)		Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01 % Completion	
	1	Chimney	M/s BHEL (Mech.) M/s BJCL (Civil)		Nov, 2015 18.08.2016	14.10.2017 -	06.04.2017 10.11.2016	100% 100%	
	2	Coal Handling Plant	NA		NA	NA	NA	NA	
	3	Ash Handling Plant	NA		NA	NA	NA	NA	
	4	Fuel Oil System	NA		NA	NA	NA	NA	
	5	Cooling Towers	M/s BHEL/ Paharpur (Mech.) M/s BHEL/ BJCL (Civil)		09.11.2015 05.01.2017	09.02.2018 -	31.12.2021 31.03.2021	100% 100%	
	6	CW Pump house	M/s BHEL (Mech.) M/s BHEL/BJCL (Civil)		09.11.2015 02.11.2016	09.05.2018 -	11.07.2020 30.11.2020	100% 100%	
	7	WPT Plant	NA		NA	NA	NA	NA	
	8	DM Plant	M/s BHEL/GE (Mech.) M/s BHEL/BJCL (Civil)		09.11.2015 06.02.2017	09.05.2018 -	06.02.2021 31.03.2017	100% 100%	
	9	Compressed Air System	M/s BHEL/ELGI (Mech.) M/s BHEL/BJCL (Civil)		Nov,2015 10.03.2018	17.08.2017 -	16.05.2019 31.10.2019	100% 100%	
	10	Fire Protection System	M/s BHEL (Mech.) M/s BHEL/BJCL (Civil)		09.11.2015 20.11.2020	09.05.2018 -	15.07.2021 30.04.2021	100% 100%	
	11	Switch Yard	M/s BHEL-TBG (Elect.) M/s BHEL (TBG) (Civil)		03.01.2015 17.04.2017	04.04.2018 -	19.01.2019 05.11.2018	100% 100%	
	12	Station Transformers	M/s BHEL/BJCL (Civil)		10.04.2017	-	31.03.2020	100%	
	13	Generator Transformers	M/s BHEL PSSR		03.11.2015	04.04.2018	21.01.19-GT 23.12.19-ST	100%	
	14	Unit Transformers	M/s BHEL PSSR (Elect.) M/s BHEL/BJCL (Civil)		03.01.2015 10.04.2017	04.04.2018 -	21.01.2019- ST 31.03.2020	100%	
	15	Railway Siding	NA		NA	NA	NA	NA	
	16	Power Evacuation Lines	KPTCL		21.12.2017	System ready	28.12.2018	95%	

CRITICAL ISSUES

Project is ready. Commissioning is pending due to non-availability of Gas from M/s GAIL.

REASONS OF DELAY

mainly by M/s BHEL EPC contractor due to non-mobilization of required man power & prioritization of works.

ENNORE SEZ STPP, Unit# 1 & 2 (2X660 MW) / TANGEDCO (STATE SECTOR - SOUTHERN REGION)

Voyalur Village, Minjur 601203, Thiruvallur Dist. Tamil Nadu

E-Gen Portal Registration No. (U#No - 1200001984, U#2 No - 1200001985)

Project Developer / Implementing Agency - TANGEDCO			Main Plant Vendor - M/s BHEL (EPC)	
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Sep-2014	27.01.18	Mar,2024	
Unit#2		27.03.18	May,2024	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)	
FUEL TYPE	Coal, Indigenous & Imported		ORIGINAL ESTIMATED COST OF THE PROJECT	9800.00
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST	9800.00
APPROVAL DATE / NTP	27.09.2014		DATE OF FINANCIAL CLOSURE	
EPC/BTG/BoP Contractor Details (Package Wise)	M/s BHEL (EPC), LoA: 27.09.2014		YEAR WISE EXPENDITURE	
PPA	State sector project. Hence entire 100% power from this project will be utilized by TAMILNADU		2016-17	558.04
COAL LINKAGE/FSA	Allocated Mine - Chandrabila Coal Block, Odisha; Distance from mine - 1300 km (non pithead); Total requirement is 5.95MTPA, comprising of indigenous 3.68 MTPA & imported 2.26 MTPA respectively MoU has already been signed between MMTC & TANGEDCO on 25.06.2012 for the supply of Import coal for this project. Bridge Linkage with SCCL available for indigenous coal.		2017-18	2276.51
			2018-19	4688.11
			2019-20	1550.04
			2020-21	750.13
			2021-22	260.14
			EXPENDITURE OF JULY'2022	12.63
START UP POWER AGREEMENT	By TAGEDCO		TOTAL EXPENDITURE (upto 31.07.2022)	5748.19
POWER EVACUATION SYSTEM	Tx Line Developer	TANGEDCO	(Tripartite agreement between TANGEDCO, M/s BHEL (EPC contractor), PFC (Lender) signed on 21.11.2016 and Loan agreement between PFC andTANGEDCO signed on 18.01.2017.)	
	Tx Line Name	Ennore SEZ SCTPP - North Chennai (765KV PS), 400 KV, D/C line		
	Tx Voltage Level			
Configuration of Tx. Line (S/C or D/C)				
LAND POSSESSION	Acquisition of Land does not arise since own Land of TANGEDCO (Out of 1100 acres available at Ash Dyke of NCTPS , only 500 Acres of ash dyke is utilized for the development of the subject project)			
WATER ALLOCATION	Supply of 4 MGD water from CMWSSB obtained. However desalination plant is envisaged in the project.			
MOEF CLEARANCE	MOEF Letter No. J 13012 / 36/2010-1A.II(T) dt.07.01.2014. Validity extended upto 31.12.2023 as per MoEF lr. Dt.09.04.2021			
CIVIL AVIATION CLEARANCE	Airport Authority has been addressed to issue NOC vide Letter No: Se/C/P&E/EE/EMC/AEE/C/F.ETPS-SEZTPP/D768 dt 17.4.2010. No Objection certificate issued by Airport Authority of India for the construction of chimney for the proposed Ennore SEZ TPP- 2X800 MW Project vide Lr.Ref:AAI/SR/NOC/dt 13.5.2010-validity 7years available. Validity extended upto 13.5.2022 vide their letter dt 19.5.2017.			
CPCB CLEARANCE	Not applicable			
SPCB CLEARANCE	Consent to establish under Air and water Acts issued by TNPCB vide order 2002229941522 Dt.26.11.2020 extended the validity upto 06.01.2021. Extension of validity upto 31.12.2023 is under process.			
FOREST CLEARANCE	Not applicable			

ENNORE SEZ STPP, Unit# 1 & 2 (2X660 MW) / TANGEDCO (STATE SECTOR - SOUTHERN REGION)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)					
Sl.	MILESTONE	UNIT-01		UNIT-02	
		Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date
1	COMPLETION OF BOILER FOUNDATION	13.08.15	14.09.17	13.10.15	07.06.18
2	START OF BOILER ERECTION	25.08.15	15.09.17	28.10.15	08.06.18
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA	
4	BOILER CEILING GIRDER LIFTING COMPLETION	28.01.16	30.11.18	28.03.16	16.05.19
5	CONDENSER ERECTION START	27.04.17	16.08.22	20.06.17	16.10.22
6	TG ERECTION START	10.06.17	30.08.22	10.08.17	30.10.22
7	HP PIPING ERECTION START	27.04.16	16.09.21	27.06.16	16.11.21
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	28.12.16	15.02.20	27.02.17	29.03.21
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	28.04.17	25.08.22	28.06.17	08.10.23
10	TG BOX UP	27.09.17	11.10.23	27.11.17	11.12.23
11	HP PIPING ERECTION COMPLETION	27.05.17	27.11.23	27.07.16	27.01.24
12	START OF OILFLUSHING	27.10.17	01.10.23	27.12.17	01.12.23
13	BOILER LIGHT UP	30.05.17	06.09.23	29.09.17	06.11.23
14	CHEMICAL CLEANING COMPLETION	10.06.17	02.10.23	10.08.17	02.12.23
15	STEAM BLOWING START	20.06.17	01.10.23	20.08.17	01.12.23
16	STEAM BLOWING COMPLETION	15.07.17	29.11.23	15.09.17	29.01.24
17	ROLLING & SYNC.	27.11.17	30.12.23	27.01.18	30.02.24
18	FULL LOAD	27.10.17	14.01.24	27.12.17	14.03.24
19	TRIAL RUN		Mar,2024		May,2024
20	COD (TRIAL RUN)		Mar,2024		May,2024

STATUS OF MAIN PLANT PACKAGE (BTG) : M/S BHEL							
Sl.	Packages	AREA	UNIT-01		UNIT-02		
			% Completion	% Completion			
1	BOILER	CIVIL	90.00%	90.00%			
		STRUCTURE	92.50%	83.48%			
		PRESSURE PARTS	92.50%	82.94%			
2	TG	CIVIL	39.88%	71.63%			
		STRUCTURE	39.88%	71.63%			
		TG ERECTION	Yet to start	Yet to start			
3	ESP	UNDER PROGRESS	75.52%	63.89%			
4	FGD	CIVIL WORK	Specification under finalization.				
		MATERIAL SUPPLY					
		ERECTION WORK					
		STATUS OF BOPs (BHEL-EPC)					
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC- BHEL)	Date of Award	Scheduled Date of Completion	Anticipated/ Actual Date of Completion	UNIT-01	UNIT-02
						% Completion	% Completion
1	Chimney	M/s Simplex	30.01.17	28.03.17	04/23	100 %	100 %
2	Coal Handling Plant	Contractor for erection M/s Promac	09.02.17	27.10.17	10/23	100 % (Civil)	
		M/s.Bevcon (Conveyor package supply), M/s.FLSIDITH- Pipe	18.03.17	27.10.17	10/23	40.29 %	
		M/s.Promac : Stacker Reclaimer supply, M/s.Elecon : Vibrating	09.02.17	27.10.17	10/23	40 %	
3	Ash Handling Plant	M/s.Indure (for supply and erection for mechanical packages) , M/s.Turbo Engineers for Slurry disposal pipes supply M/s.Weir for Slurry pumps supply, M/s.Atlas Copco& M/s.Ingersoll for Compressor supply M/s.Suraj	14.09.17	27.10.17	Oct,23	21.95%	
4	Fuel Oil System	M/s.New Fire Engineers Pvt Ltd.	13.06.17	30.03.17	Apr.,23	50.7 % (Civil) 35.8 % (Mech.)	
5	Cooling Towers	M/s.Simplex (Design – Paharpur)	30.01.17	29.04.17	Sep,23 (U-1) Oct,23 (U-2)	28.24%	12.26%
6	CW Pump house	CW Pump House - M/s Cornerstone (De- scoped from M/s.Simplex),CW Piping: BHEL / M/s Vijay Gowtham- (De-scoped from M/s.Simplex)	27.12.19	29.04.22	Sept,23	5.2% -Civil 8.52% - Piping	
7	WPT Plant	M/s.Otoklin Global business services for supply and erection	18.01.18	30.03.17	Sept,23	27.75%	
8	DM Plant	M/s Cornerstone (De-scoped from M/s.Simplex)	27.09.14	30.03.17	July,23	35.45%-Civil	
9	Compressed Air System	M/s.ELGI Equipments Ltd.	27.11.17	30.03.17	Mar,23	80.9% - Civil	
10	Fire Protection System	BHEL- PE&SD	July,18	30.03.17	Aug,23	5% - Civil	
11	Switch Yard	BHEL-TBG (Awarded to Sakthi Kanna Construction Ltd & M/s.Vijay Gowtham- De-scoped from M/s.Simplex)	27.09.14	30.03.17	March,23	71.84% - Civil	
12	Station Transformers	M/s Cornerstone	19.11.19	30.03.17	Apr.,23	34.67%- Civil	
13	Unit Transformers	M/s Cornerstone	19.11.19	30.08.17	May,23	29.58%- Civil	
14	Railway Siding	NA	NA	NA	NA	NA	NA
15	Power Evacuation Lines	TANGEDCO Ennore SEZ SCTPP- North Chennai(765 KV PS), 400 KV, D/C line			Mar.,2023	Power will be evacuated through DC 400 KV TL, i.e. 2 nos 400 KV lines to 765 KV pooling station and 2 nos 400 KV lines to ETPS – work under progress.	

CRITICAL ISSUES

- Slow progress in Cooling Tower, AHP, CHP and WPT plant.
- Coal linkage yet to be received.

REASONS OF DELAY

- Zero date is 27.09.2014, Works commenced at Site on 09.10.2016. Project works temporarily suspended from 07.09.2015 to 18.10. 2016 due to litigation. Original completion schedule is March 2018. Work resumed at Site from 19.10.2016. Completion schedule re-fixed to 06.05.2019 (without levy of LD & penalty) due to time loss of 407 day due to court case. Time extension granted from 06.05.2019 to upto 31.08.2020 for U#1 and 31.10.2020 for Unit 2 without prejudice to levy of LD & Penalty clauses.
- Entire project civil works were awarded to M/s. Simplex. Wherever slow progress of work noticed, BHEL has de scoped the certain works from M/s. Simplex based on TANGEDCO's request, but still the progress is very poor from M/s. Simplex.
- Project activities became slow since 24th March 2020 due to lock down enforced by GOI in view of COVID-19 outbreak. Permission accorded by Distt Collector (Thiruvallur) for resumption of work at site with only 600 manpower on 25.04.2020.Work resumed by BHEL from 18.05.2020.

UPPUR STPP, Unit# 1 & 2 (2x800 MW) / TANGEDCO (STATE SECTOR - SOUTHERN REGION)

Uppur STPP, Ramnad District - 623503, Tamil Nadu

E-Gen Portal Registration No. (U#1 - NA; U#2 - NA)

Project Developer / Implementing Agency - TANGEDCO			Main Plant Vendor - M/S BHEL		
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	Trial Run Date	
Unit#1	Feb-2016		On Hold		
Unit#2			On Hold		
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)		
FUEL TYPE	Coal, Indigenous & Imported (MMTC)		ORIGINAL ESTIMATED COST OF THE PROJECT		12778.00
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST		Not Applicable
APPROVAL DATE / NTP	BGT-SE/E/T & H(P)/OT No. 01/ 2015-16. BOP-SE/E/T&H(P)/OT.No.1/2020-21. SWIOP-SE/C/TP/OT.NO.2/2016-17.		DATE OF FINANCIAL CLOSURE		Financial tie up with M/s. PFC
EPC/BTG/BoP Contractor Details (Package Wise)	Order placed on M/s. BHEL on 27/02/2016.		YEAR WISE EXPENDITURE		
PPA	NOT APPLICABLE. State sector project.		2016-17		16.74
COAL LINKAGE/FSA	Allocated Mine - SCCL (A.P.) to provide coal 3.942 MTPA; Distance from mine - 700 km (non pithead); Also, MoU entered with M/s. MMTC for supply of imported coal of 5.02 MTPA on dated 25-05-2015.		2017-18		226.62
			2018-19		1594.15
			2019-20		924.32
START UP POWER AGREEMENT	230 KV/11 KV Karaigudi Feeder		2020-21		366.61
POWER EVACUATION SYSTEM	Tx Line Developer	TANTransco	2021-22		
	Tx Line Name Tx Voltage Level	Uppur SCTPP – Virudhunagar, 765 KV, D/C line	EXPENDITURE OF JULY 2022		0.00
	Configuration of Tx Line (S/C or D/C)		TOTAL EXPENDITURE (upto 31.7.2022)		2298.00
LAND POSSESSION	Land required for the project is under TANGEDCO Possession. EPC Contracts awarded to M/s. BHEL & M/S L&T has been suspended as per the NGT(SZ), Chennai Judgment dated 17.03.2021, delivered on Appeal No. 144 of 2016(SZ) filed in the designated court for a period of six months or until further orders.				
WATER ALLOCATION	Tamil Nadu Maritime Board has issued NOC for construction of Jetty for drawal and discharge of cooling water, vide 27.4.2015.				
MOEF CLEARANCE	Ministry of Environment and Forest has accorded clearance for the above Project on 18.05.2016.				
CIVIL AVIATION CLEARANCE	Clearance expired on 21.11.2019. Clearance further extended upto 21.11.2024.				
CPCB CLEARANCE	NOT APPLICABLE. State sector project.				
SPCB CLEARANCE	CRZ committee of MOEF recommended the Project on 28.1.16 and MOM published in web site on 8.2.16.				
FOREST CLEARANCE	NOT APPLICABLE				

* NOTE : The EPC contracts awarded to M/s. BHEL & M/S L&T have been suspended as per the NGT(SZ), Chennai Judgment dated 17.03.2021, delivered on Appeal No. 144 of 2016 (SZ) filed in the designated court for a period of six months or until further orders. Considering the issues like NGT order, land litigation, local fishermen litigation and BOP package retendering works, TANGEDCO Board vide on 29.04.2021 has accorded approval to shift the existing 2x800 MW Uppur STPP to Udangudi site as 2x800MW Udangudi Stage-III and consider Uppur as a fresh project once all the legal issues in NGT and other places are settled and to approach GOTN for administrative approval. Energy Secretary/GoTN has been addressed vide Letter dtd 10.05.2021 for approval of the above. Further, as informed by TANGEDCO, CMD has accorded approval on 27.08.2021 to form a high committee comprising of three directors and four Chief Engineers to re-study the shifting of UPPUR Project. High Level Committee have furnished report on 22.10.2021 and recommended that the 2X800 MW Uppur Project shall be executed at Uppur itself. TANGEDCO Board in its 102nd meeting held on 29.10.2021 has directed to obtain opinion from the Consultant M/s. Ernst & Young regarding the viability and feasibility of this project and the same is in progress.

UPPUR STPP, Unit# 1 & 2 (2x800 MW) / TANGEDCO (STATE SECTOR - SOUTHERN REGION)													
UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)						STATUS OF MAIN PLANT PACKAGE (BTG)							
Sl.	MILESTONE	UNIT-01		UNIT-02		Sl.	Packages	AREA	UNIT-01		UNIT-02		
		Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date				% Completion	% Completion			
1	COMPLETION OF BOILER FOUNDATION		Revised schedule of activity is not available. Project is expected to be commissioned by 2024-25.		Revised schedule of activity is not available. Project is expected to be commissioned by 2024-25.	1	BOILER	CIVIL	23%	30%			
2	START OF BOILER ERECTION	03.06.18		03.06.18		STRUCTURE		55%	31%				
3	BOILER DRUM LIFTING (if sub-critical unit)	NA		NA		PRESSURE PARTS		1%	0%				
4	BOILER CEILING GIRDER LIFTING COMPLETION					2	TG	CIVIL	Works yet to commence				
5	CONDENSER ERECTION START	23.01.20		23.01.20		STRUCTURE							
6	TG ERECTION START	19.03.20		19.03.20		TG ERECTION							
7	HP PIPING ERECTION START	19.12.19		19.12.19		3	ESP	UNDER PROGRESS	14%	6%			
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	22.07.19		22.07.19		4	FGD	CIVIL WORK	Contract is yet to be awarded				
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	20.01.20		20.01.20		MATERIAL SUPPLY							
10	TG BOX UP	13.02.20		13.02.20		ERECTION WORK							
11	HP PIPING ERECTION COMPLETION	19.12.19		19.12.19		STATUS OF BOPs							
12	START OF OILFLUSHING	19.03.20		19.03.20		Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated /Actual Date of Completion	UNIT-01 % Completion	UNIT-02 % Completion
13	BOILER LIGHT UP	12.02.20		12.02.20		1	Chimney	The contract was short closed due to huge price escalation sought by M/s RIL.				The contract was short closed due to huge price escalation sought by M/s RIL.	The contract was short closed due to huge price escalation sought by M/s RIL.
14	CHEMICAL CLEANING COMPLETION	19.03.20		19.03.20		2	Coal Handling Plant						
15	STEAM BLOWING START	16.04.20		16.04.20		3	Ash Handling Plant						
16	STEAM BLOWING COMPLETION	16.04.20		16.04.20		4	Fuel Oil System						
17	ROLLING & SYNC.	06.05.20		06.05.20		5	Cooling Towers						
18	FULL LOAD	03.06.20		03.06.20		6	CW Pump house						
19	TRIAL RUN	Nov-20		Nov-20		7	WPT Plant						
20	COD	01.02.21		01.02.21		8	DM Plant						
				9	Compressed Air System								
				10	Fire Protection System								
				11	Switch Yard								
				12	Station Transformers								
				13	Unit Transformers								
				14	Railway Siding								
				15	Power Evacuation Lines								

CRITICAL ISSUES

The EPC contracts awarded to M/s. BHEL & M/S L&T have been suspended as per the NGT(SZ), Chennai Judgment dated 17.03.2021, delivered on Appeal No. 144 of 2016(SZ) filed in the designated court for a period of six months or until further orders. Considering the issues like NGT order, land litigation, local fishermen litigation and BOP package retendering works, TANGEDCO Board on 29.04.2021 has accorded approval to shift the existing 2x800 MW Uppur STPP to Udangudi site as 2x800MW Udangudi Stage-III and consider Uppur as a fresh project once all the legal issues in NGT and other places are settled and to approach GOTT for administrative approval. Energy Secretary/GoTN has been addressed vide Letter dtd 10.05.2021 for approval of the above.

Against NGT order, SLP was filed by TANGEDCO in Supreme court on 16.04.2021. Honourable Supreme court of India granted stay on the impugned judgment passed by NGT on 01.07.2021. In the review meeting of energy department chaired by Hon'ble Chief Minister on 22.07.2021, it was requested to restudy the shifting of Uppur project considering the energy demand. CMD has accorded approval on 27.08.2021 to form a high level committee comprising of three Directors and four Chief Engineers to restudy the shifting of Uppur Project. TANGEDCO Board in its 102nd meeting held on 29.10.2021 has directed to obtain opinion from the Consultant M/s Ernst & Young regarding the viability and feasibility of this project and the same is in progress. Consultant has furnished the report on 07.01.22 and recommended "To develop the Project at Uppur site itself" and the same was placed before the TANGEDCO Board in its 105th meeting held on 19.01.2022. The Board Directed to place the subject in the next Board meeting for deliberations. In the next Board meeting held on 19.3.2022, the Board directed to restudy the viability & feasibility of consultant's report submitted.

REASONS OF DELAY

NGT Order to stop the work.

NORTH CHENNAI STPP St - III, Unit# 1 (1X800MW) / TANGEDCO (STATE SECTOR - SOUTHERN REGION)

NCTPP Stage III, Athipattu village, Ponneri Tk, Thiruvallur Dt, Chennai - 600 120.

E-Gen Portal Registration No. (U#1 - 1200002174)

Project Developer / Implementing Agency - TANGEDCO			Main Plant Vendor - M/s BHEL (BTG)			
Unit No.		LOA	Original Trial Run Date		Anticipated / Actual Trial Run Date	
Unit#1		Jan-2016	Apr-2019		Mar-2023	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)			
FUEL TYPE		Coal, Indigenous & Imported(MMTC)	ORIGINAL ESTIMATED COST OF THE PROJECT		6376.00	
COAL COMBUSTION TECHNOLOGY		Super critical	LATEST ESTIMATED COST		8722.86	
APPROVAL DATE / NTP		BTG : SE/E/T & H (P)/ OT No. 02/2015-16 ; BOP : SE/E/T & H (P) OT No.04/2015-16	DATE OF FINANCIAL CLOSURE		28.1.2017	
EPC/BTG/BoP Contractor Details (Package Wise)		BTG contractor-BHEL(LoA: 29.01.2016), BOP contractor-M/s BGR(LoA: 28.10.2016)	YEAR WISE EXPENDITURE			
PPA		NOT APPLICABLE. State sector project.				
COAL LINKAGE/FSA		Allocated Mine - SCCL; Distance from mine - 606 km (non pithead);. Ministry of Coal recommended for longterm coal linkage for 1.971 MTPA Indigenous coal to SCCL. FSA Executed between TANGEDCO and SCCL for indigenous coal. MoU has been entered with M/s. MMTC for supply of Imported coal of 1.450 MTPA on 25.05.2015.	2012-13		0.21	
START UP POWER AGREEMENT		Start up Power Arrangement is through 220 KV level by LILO of NCTPS 1 to Ennore Feeder. Station Transformer was chargedon 05.09.2020.	2013-14		0.40	
POWER EVACUATION SYSTEM		Tx Line Developer	TANTRANSCO	2014-15		0.13
		Tx Line Name Tx Voltage Level	NCTPS St-III -North Chennai (PS), 765 KV, D/C line	2015-16		0.25
		Configuration of Tx Line (S/C or D/C)		2016-17		198.08
LAND POSSESSION		The proposed site is within the existing NCTPS complex and land is already under possession of TANGEDCO.	2017-18		929.75	
WATER ALLOCATION		The raw water requirement for this project will be met from existing cooling water fore-bay of NCTPS, Stage-II. The make-up water for cooling water, boiler make up and other sweet water requirements are to be met from desalination plant under construction for this project. Construction water from M/s. CMWSSB available to the contractor from 07.01.2017.	2018-19		2243.52	
MOEF CLEARANCE		Environmental clearance issued by MoEF on 20.01.2016 valid for a period of seven years.	2019-20		2090.62	
CIVIL AVIATION CLEARANCE		Chimney constructed for full height and the same was informed to Airports Authority of India.	2020-21		928.95	
CPCB CLEARANCE		NOT APPLICABLE. State sector project.	2021-22		760.29	
SPCB CLEARANCE		Approval has been obtained on 13.04.2017.	EXPENDITURE OF JULY'2022		18.42	
FOREST CLEARANCE		Not applicable, since the site is not coming under Forest area.	TOTAL EXPENDITURE (upto 31.7.2022)		7340.03	
			(In-princippal approval for financial assistance of Rs.5006.992 crores with Debt : Equity ratio of 80 : 20 for setting up of 1 x 800 MW Supercritical Thermal Power Plant in Tiruvallur District of Tamil Nadu has been received from M/s. REC on 05.08.2016. Loan has been sanctioned on 22.11.2016. Loan Agreement was signed on 28.01.2017.)			

NORTH CHENNAI STPP St - III, Unit# 1 (1X800MW) / TANGEDCO (STATE SECTOR - SOUTHERN REGION)										
UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)				STATUS OF MAIN PLANT PACKAGE (BTG)						
Sl.	MILESTONE	UNIT-01		Sl.	Packages	AREA	UNIT-01			
		Original Date of Completion	Anticipated / Actual Date of Completion				% Completion			
1	COMPLETION OF BOILER FOUNDATION	31.10.2016	14.06.18	1	BOILER	CIVIL	95.00%			
2	START OF BOILER ERECTION	29.11.16	30.08.17			STRUCTURE	93.60%			
3	BOILER DRUM LIFTING (if sub-critical unit)	NA	NA			PRESSURE PARTS	99.70%			
4	BOILER CEILING GIRDER LIFTING COMPLETION	11.05.17	31.07.18	2	TG	CIVIL	100.00%			
5	CONDENSER ERECTION START	29.08.17	02.01.19			STRUCTURE	98.00%			
6	TG ERECTION START	28.10.17	25.02.19			TG ERECTION	97.80%			
7	HP PIPING ERECTION START	24.10.17	25.03.18	3	ESP	UNDER PROGRESS	99.00%			
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	28.02.18	31.12.19	4	FGD	CIVIL WORK	WORK AWARDED on 22.2.2021. DESIGN AND ENGINEERING WORKS UNDER PROGRESS.			
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	26.09.18	October ,22			MATERIAL SUPPLY				
10	TG BOX UP	07.11.18	12/22			ERECTION WORK				
11	HP PIPING ERECTION COMPLETION	13.04.19	10/22	STATUS OF BOPs - BGRESL/Chennai						
12	BOILER LIGHT UP	29.10.18	October,22	Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency	Date of Award	Scheduled Date of Completion	Anticipated /Actual Date of Completion	UNIT-01
13	CHEMICAL CLEANING COMPLETION	27.02.19	11/22							% Completion
14	START OF OILFLUSHING	29.11.18	03.11.20	1	Chimney	M/s. BGR ESL	10.03.17	25.06.19	30.09.22	97%
15	STEAM BLOWING START	31.12.18	12/22	2	Coal Handling Plant		21.07.17	25.07.19	31.01.23	77%
16	STEAM BLOWING COMPLETION	29.01.19	01/23	3	Ash Handling Plant		25.11.17	28.07.19	31.01.23	65%
17	ROLLING & SYNC.	28.02.19	02/23	4	Fuel Oil System		27.07.17	28.06.19	30.09.22	95.5%
18	FULL LOAD	28.03.19	02/23	5	Cooling Towers		16.05.17	21.09.19	30.9.22	85.5%
19	TRIAL RUN	28.04.19	03/23	6	CW Pump house		09.01.18	28.05.19	30.09.22	80%
20	COD	28.07.19	03/23	7	WPT Plant		16.06.17	17.05.19	30.9.22	83.5%
				8	DM Plant		06.10.17	28.05.19	30.9.22	85%
				9	Compressed Air System		10.12.17	28.08.19	31.01.22	100%
				10	Fire Protection System		01.07.17	14.05.19	31.10.22	85.25%
				11	Switch Yard		19.08.17	26.10.19	31.12.22	85%
				12	Station Transformers	BHEL	24.07.18	28.04.19	05.09.20	100%
				13	Unit Transformers	BHEL	06.03.18	27.02.19	31.08.22	91%
				14	Railway Siding	NA	NA	NA	NA	NA
				15	Power Evacuation Lines	TANTRANSCO, NCTPS St-III -North Chennai (PS), 765 KV, D/C line	12.01.18	11.11.19	October ,22	90%

CRITICAL ISSUES

- Ash Handling Plant- Under-reamed piling and ADPL erection work held up due to NGT issue.
- Piling activities inside water bodies, viz., Buckingham canal, Kosasthalaiyar river and Bridge across Boat canal are critical as monsoon rain affects the work progress.

REASONS OF DELAY

Due to COVID Lock down in 2020 & 2021 and non-availability of Industrial Oxygen in 2020 & 21, Delay in CW pipe line readiness.

UDANGUDI STPP - St-I, Unit# 1 & 2 (2x660MW) / TANGEDCO (STATE SECTOR - SOUTHERN REGION)

Distt. Thoothukudi, Tamil Nadu [TANGEDCO]

E-Gen Portal Registration No. (. Unit-1: 1200002175, Unit -2: 1200002176)

Project Developer / Implementing Agency - TANGEDCO			Main Plant Vendor - M/s BHEL (EPC)	
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Dec-2017	Jan-2021	Mar-2024	
Unit#2		Mar-2021	Jun-2024	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)	
FUEL TYPE	Coal, Indigenous & Imported (Indonesia)		ORIGINAL ESTIMATED COST OF THE PROJECT	13076.71
COAL COMBUSTION TECHNOLOGY	Supercritical		LATEST ESTIMATED COST	13076.71
APPROVAL DATE / NTP	BGT-SE/E/T & H(P)/OT No. 01/ 2015-16. BOP-SE/E/T&H(P)/OT.No.1/2020-21. SWIOP-SE/C/TP/OT.NO.2/2016-17.		DATE OF FINANCIAL CLOSURE	Financial tie up with M/s. PFC
EPC/BTG/BoP Contractor Details (Package Wise)	Awarded to BHEL as EPC contractor on 07.12.2017		YEAR WISE EXPENDITURE	
PPA	NOT APPLICABLE. State sector project.		2017-18	118.93
COAL LINKAGE/FSA	Allocated Mine - Chandrabila Coal Block for indigenous coal of G13 Grade for 3.647 MTPA and MDO selection is under process. Distance from mine (appx) : Railway distance for movement of coal through Rail-cum-Sea route via Paradip port is 200 km.(Chandrabila to Paradip port), from Paradip port to Udangudi captive Port, sea distance is 1224 Nautical Miles. Total requirement is 5.893 MTPA with Indigenous coal of 3.647 MTPA and import coal of 2.246 MTPA. Import coal (2.246 MTPA) will be procured to the requirements. Bridge Linkage with SCCL available for indigenous coal		2018-19	336.43
START UP POWER AGREEMENT	230 KV/ 11 KV Karaigudi Feeder		2019-20	654.76
POWER EVACUATION SYSTEM	Tx Line Developer	Udangudi STPP – Ottapidaram, 400 KV, D/C line (BHEL/L&T)	2020-21	1778.54
	Tx Line Name Tx Voltage Level		2021-22	1711.00
	Configuration of Tx Line (S/C or D/C)		EXPENDITURE OF JULY'2022	200.311
LAND POSSESSION	Land required for the project is under TANGEDCO Possession. EPC Contracts awarded to M/s. BHEL & M/S L&T has been suspended as per the NGT(SZ), Chennai Judgment dated 17.03.2021, delivered on Appeal No. 144 of 2016(SZ) filed in the designated court for a period of six months or until further orders.		TOTAL EXPENDITURE (upto 31.07.2022)	6132.587
WATER ALLOCATION	Tamil Nadu Maritime Board has issued NOC for construction of Jetty for drawal and discharge of cooling water, vide 27.4.2015.			
MOEF CLEARANCE	Ministry of Environment and Forest has accorded clearance for the above Project on 18.05.2016.			
CIVIL AVIATION CLEARANCE	Clearance expired on 21.11.2019. Clearance further extended up to 21.11.2024.			
CPCB CLEARANCE	NOT APPLICABLE. State sector project.			
SPCB CLEARANCE	CRZ committee of MOEF recommended the Project on 28.1.16 and MOM published in web site on 8.2.2016.			
FOREST CLEARANCE	NOT APPLICABLE			

UDANGUDI STPP - St-I, Unit# 1 & 2 (2x660MW) / TANGEDCO (STATE SECTOR - SOUTHERN REGION)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)					
Sl.	MILESTONE	UNIT-01		UNIT-02	
		Original Date	Actual / Anticipated Date	Original Date	Actual / Anticipated Date
1	COMPLETION OF BOILER FOUNDATION	12.09.18	10.04.21	12.11.18	21.04.21
2	START OF BOILER ERECTION	27.09.18	20.09.19	27.11.18	16.09.19
3	BOILER DRUM LIFTING (if sub-critical unit)	-	-	-	-
4	BOILER CEILING GIRDER LIFTING COMPLETION	09.02.19	26.06.21	09.04.19	18.06.21
5	CONDENSER ERECTION START	15.08.19	14.11.22	15.10.19	30.12.22
6	TG ERECTION START	12.09.19	30.11.22	12.11.19	15.01.23
7	HP PIPING ERECTION START	30.10.19	28.11.22	30.10.19	14.01.23
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	27.02.20	28.03.2023	02.09.2020	05.03.2023
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	02.07.20	07.03.23	02.09.20	02.04.23
10	TG BOX UP	30.07.20	10.11.23	30.09.20	25.12.23
11	HP PIPING ERECTION COMPLETION	06.08.20	27.07.23	06.10.20	11.09.23
12	START OF OILFLUSHING	30.07.20	11.10.23	30.09.20	30.11.23
13	BOILER LIGHT UP	09.07.20	27.06.2323	09.09.20	04.05.23
14	CHEMICAL CLEANING COMPLETION	30.07.20	26.07.23	30.09.20	10.09.23
15	STEAM BLOWING START	13.08.20	12.11.2023	13.11.20	30.12.2023
16	STEAM BLOWING COMPLETION	03.09.20	28.12.23	03.11.20	10.02.24
17	ROLLING & SYNC.	12.11.20	28.01.24	12.01.21	10.03.24
18	FULL LOAD	31.12.20	15.02.24	28.02.21	05.04.24
19	TRIAL RUN	07.01.21	Mar,24	07.03.21	Jun,24
20	COD	25.02.21	Mar,24	25.04.21	Jun,24

STATUS OF MAIN PLANT PACKAGE (BTG) : M/S BHEL							
Sl.	Packages	AREA	UNIT-01		UNIT-02		
			% Completion	% Completion			
1	BOILER	CIVIL	79.00%	82.13%			
		STRUCTURE	69.21%	68.06%			
		PRESSURE PARTS	88.25%	86.38%			
2	TG	CIVIL	79.76%	36.70%			
		STRUCTURE	58.97%	26.95%			
		TG ERECTION	32.63%	16.24%			
3	ESP	UNDER PROGRESS	92.63%	93.17%			
4	FGD	CIVIL WORK	Work yet to be awarded				
		MATERIAL SUPPLY					
		ERECTION WORK					
STATUS OF BOPs (BHEL-EPC)							
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC- BHEL)	Date of Award	Scheduled Date of Completion	Anticipated /Actual Date of Completion	UNIT-01 % Completion	UNIT-02 % Completion
1	Chimney	M/s.BHEL/ M/s Bygging- Civil Structural Erection	08.10.18	26.10.19 03.12.20	06.08.22 28.09.23	99.11% 40.61%	
2	Coal Handling Plant	M/s. BHEL/ M/s Kanwar/ M/s Priya- Civil	01.03.22	25.06.20	16.12.23	23.7%	
		M/s. BHEL/ M/s.RPP/URC Structural Erection	15.07.19	25.06.20	27.01.23	25.51%	
		M/s. BHEL/IGG	09.05.19	-	13.11.23	-	
3	Ash Handling Plant	M/s.BHEL/ RPP/Srinic- Civil M/s.BHEL/ M/s.RPP/URC- Structural Erection M/s. BHEL Mechanical Equipment	11.05.20 15.07.19 15.03.19	25.06.20 25.06.20 30.11.20	06.05.23 06.05.23 24.10.23	32.5% - -	
4	Fuel Oil System	M/s.BHEL/ M/s.RPP Civil	25.07.19	22.01.20	02.12.22	60.50%	
5	Cooling Towers	M/s.BHEL/ M/s.Gammon	16.12.2019	22.10.20	19.05.23	12.06%	
6	CW Pump house	M/s.BHEL/ M/s.B&B; M/s.BHEL/ M/s.Akash Techno	04.06.19	17.01.20	05.04.23	36.94%	
7	WPT Plant	M/s.BHEL/ M/s.B&B	04.06.19	07.02.20	22.11.23	38.97%	
8	DM Plant	M/s.BHEL/ M/s.RPP	25.07.19	12.10.19	23.09.23	20.64%	
9	Compressed Air System	M/s.BHEL / M/s.Power Mech	07.01.22	01.11.20	13.01.23	93.80%	
10	Fire Protection System	M/s. BHEL	-	22.10.20	18.05.23	-	
11	Switch Yard	M/s. BHEL/ M/s. RB Electrical	25.06.21	23.05.19	31.12.22	69.30%	
12	Station Transformers	M/s.BHEL / M/s.Power Mech	30.12.21	15.06.20	27.02.23	82.60%	
13	Generator Transformers						
14	Unit Transformers						
15	Railway Siding	NA	NA	NA	NA	NA	
16	Power Evacuation Lines	Udangudi STPP – Ottapidaram, 400 KV, D/C line (BHEL/L&T)	27.01.20	11.10.20	Dec,-22	85.00%	

CRITICAL ISSUES

- Persistent shortfall in manpower
- Fisherman issue at coal jetty

REASONS OF DELAY

COVID 19, Labor shortage / Vendor Mobilization delay by Contractor, Fishermen issue at Coal Jetty

SAGARDIGHI TPP, St-III, Unit# 1 (1X660 MW) / WBPDC (STATE SECTOR - EASTERN REGION)

PS-Sagardighi, PO-Manigram, Pin-742237, Block-Sagardighi, Subdivision-Jangipur, District-Murshidabad, West Bengal
E-Gen Portal Registration No. (U#1 - 1200002116)

Project Developer / Implementing Agency - WBPDC			Main Plant Vendor - M/S BHEL (EPC Contract-27.12.2018)	
Unit No.	LOA	Original Trial Run Date	Anticipated / Actual	Trial Run Date
Unit#1	Dec-2018	Jan-2024	Sep.-2024	
CLEARANCES AND STATIC DATA			FINANCIAL DATA (Fig. in Rs. Crore)	
FUEL TYPE	Coal, Indigenous		ORIGINAL ESTIMATED COST OF THE PROJECT	3862.65*
COAL COMBUSTION TECHNOLOGY	Super Critical		LATEST ESTIMATED COST	4567.32#
APPROVAL DATE / NTP	Notice to Proceed Date : 01.07.2020; The proposal was approved in the State Cabinet held on 23.03.2018.		DATE OF FINANCIAL CLOSURE	02.01.2017
EPC/BTG/BoP Contractor Details (Package Wise)	EPC contract awarded to BHEL (LOA : 27.12.2018)		YEAR WISE EXPENDITURE	
PPA	Power Purchase Agreement executed with WBSEDCL		2018-19	70.00
COAL LINKAGE/FSA	Allocated Mine - Pachhwara (North) Captive Coal Mine of WBPDC.		2019-20	56.25
	Distance from mine - 150 km (non pithead);		2020-21	362.47
	Coal will be sourced mainly from captive coal mines of WBPDC		2021-22	330.97
START UP POWER AGREEMENT	Start up power shall be obtained from the other running units of the Sagardighi Thermal Power Project.		EXPENDITURE OF JULY'2022	42.08
POWER EVACUATION SYSTEM	Tx Line Developer		TOTAL EXPENDITURE (upto 31.07.2022)	842.58
	Tx Line Name	i) STPP – New Sagardighi, 220 KV, D/C line, ii) STPP- Farakka, 400 KV D/C line, iii) STPP-Purulia 400 KV D/C line, iv) STPP- Baharampore 400 KV, D/C line, v) STPP- Gokarna 400 KV D/C line.	* Approved in the State Cabinet held on 23.03.2018 # Awaiting Approval	
	Tx Voltage Level			
	Configuration of Tx Line (S/C or D/C)			
LAND POSSESSION	Adequate land is available for the project. (WBPDC have 365 Ha of land under possession for Phases I, II & III of the plant and another 184 Ha for ash disposal.)			
WATER ALLOCATION	Source: River Bhagirathi/Hooghly Quantity:74.36 cusec of water intotal for the entire Project. Permission vide F. No. TE-15015/1/2019/NMCG, Dated: 01.07.2019 accorded by National			
MOEF CLEARANCE	Environmental clearance vide F. No. J-13012/01/2019-IA. I (T) dated 24.03.2020 accorded by MoEF & CC Govt. of India for new unit No 5			
CIVIL AVIATION CLEARANCE	NOC for height Clearance vide NOC ID: MALD/EAST/B/100316/175516, Dated: 19.10.2016 obtained from			
CPCB CLEARANCE	Not Applicable			
SPCB CLEARANCE	Online application for Grant of Consent to Establish / NoC has been be made to WBPCB on 27.03.2021			
FOREST CLEARANCE	Not Applicable			

SAGARDIGHI TPP, St-III, Unit# 1 (1X660 MW) / WBPDC (STATE SECTOR - EASTERN REGION)

UNIT WISE MILESTONES (ANTICIPATED / ACTUAL)			
Sl.	MILESTONE	UNIT-01	
		Original Date of Completion	Anticipated / Actual Date of Completion
1	COMPLETION OF BOILER FOUNDATION	19.04.2021	16.10.2021
2	START OF BOILER ERECTION	29.04.2021	27.03.2021
3	BOILER DRUM LIFTING (if sub-critical unit)	NA	NA
4	BOILER CEILING GIRDER LIFTING COMPLETION	30.12.2021	22.06.2022
5	CONDENSER ERECTION START	03.03.2022	10.08.2022
6	TG ERECTION START	02.05.2022	15.09.2022
7	HP PIPING ERECTION START	25.11.2022	
8	BOILER HYDRO TEST (DRAINABLE) COMPLETION	30.12.2022	
9	BOILER HYDRO TEST (NON-DRAINABLE) COMPLETION	29.05.2023	
10	TG BOX UP	01.06.2023	
11	HP PIPING ERECTION COMPLETION	26.08.2023	
12	START OF OILFLUSHING	28.03.2023	
13	BOILER LIGHT UP	13.06.2023	
14	CHEMICAL CLEANING COMPLETION	28.06.2023	
15	STEAM BLOWING START	13.07.2023	
16	STEAM BLOWING COMPLETION	12.08.2023	
17	ROLLING & SYNC.	01.09.2023	
18	FULL LOAD	01.11.2023	
19	TRIAL RUN	01.01.2024	Sept.,-2024
20	COD	Jan-24	Sept.,-2024

STATUS OF MAIN PLANT PACKAGE (BTG) : M/S BHEL						
Sl.	Packages	AREA	UNIT-01			
			% Completion			
1	BOILER	CIVIL				100%
		STRUCTURE				23.79%
		PRESSURE PARTS				1.80%
2	TG	CIVIL				100%
		STRUCTURE				-
3	ESP	CIVIL WORKS				100%
		STRUCTURAL WORKS				38.64%
4	FGD	NOT STARTED YET				
STATUS OF BOPs						
Sl.	Packages/ Linked Project Milestones	Vendor/Contracting Agency (EPC- BHEL)	Date of Award	Scheduled Date of Completion	Anticipated/Actual Date of Completion	UNIT-01
						% Completion
1	Chimney	M/s. BHEL	17.08.2021 (ZERO)	17.05.2023		Detail Engineering in Progress
2	Coal Handling Plant	Conveyor package: Bengal Tools Limited	27.12.2018 (ZERO)	15.12.2023		Excavation work & Sheet Piling for Twin Wagon Tippler has started.
		Twin Wagon Tippler : ThyssenKrupp	DATE AS PER	13.12.2023		
3	Ash Handling Plant	Existing Stacker Reclaimer of Stage-II will be used				Detail Engineering in Progress
4	Fuel Oil System	M/s. MacawberBeekey Pvt. Ltd.	27.12.2018 (ZERO)	28.03.2024		
5	Cooling Towers	M/s. BHEL	DATE AS PER CONTRACT	27.08.2023		
6	CW Pump house	M/s. Paharpur Cooling Towers Limited	01.07.2020)	16.06.2023		
8	WPT Plant	M/s. BHEL		09.12.2023		
9	DM Plant	Will be used from Existing				Existing from Stage – II Project will be used.
11	Compressed Air System	M/s. BHEL		25.08.2023		Detail Engineering is in Progress
12	Fire Protection System	M/s. BHEL	27.12.2018 (ZERO)	24.03.2024		
15	Switch Yard	M/s. BHEL	DATE AS PER CONTRACT	22.03.2024		Detail Engineering is in Progress
16	Station Transformers	M/s. BHEL	01.07.2020)	30.03.2023		
18	Unit Transformers	M/s. BHEL		27.08.2023		Detail Engineering is in Progress
19	Railway Siding	Railway siding exists. M/s. Rites will do the modification job for connecting Twin Wagon Tippler for Stage 3.				
20	Power Evacuation Lines	Power Evacuation from the proposed unit shall be done through the existing electrical network consisting of following feeders i) STPP – New Sagardighi, 220 KV, D/c line, ii) STPP- Farakka, 400 KV D/c line, iii) STPP-Purulia 400 KV D/c line, iv) STPP- Baharpore 400 KV, D/C line, v) STPP- Gokarna 400 KV D/C line.				

CRITICAL ISSUES

- Delay in EoT crane commissioning

REASONS OF DELAY

Effect of COVID -19 during Project Tenure:, Scarcity of Industrial Oxygen affected fabrication work. Quarantine of workers & officials.
2. Restrictions affected mobilisation. Delay in sequential supply of Critical Items, mainly Boiler Pressure Parts from BHEL-Trichy works.

ABBREVIATIONS

Sl. No.	Abbreviation	Description
1	AHP	Ash Handling Plant
2	BFP	Boiler Feed Pump
3	BLU	Boiler Light Up
4	BOP	Balance of Plant
5	BTG	Boiler Turbine Generator
6	C&I	Control & Instrumentation
7	CHP	Coal Handling Plant
8	COD	Commercial Operation Date
9	CRH	Cold Re Heat
10	CW System	Cooling Water System
11	DM Plant	De Mineralization Plant
12	EPC	Erection Procurement & Commissioning
13	ESP	Electro Static Precipitator
14	FD Fan	Forced Draft Fan
15	FGD	Flue Gas Desulfurization
16	FL	Full Load
17	FO System	Fuel Oil System
18	FSA	Fuel Supply Agreement
19	GT	Generator Transformer
20	HCSO	High Concentrated Slurry Disposal
21	HPT	High Pressure Turbine
22	HRH	Hot Re Heat
23	HT	Hydraulic Test
24	ID Fan	Induced Draft Fan
25	IDCT	Induced Draft Cooling Tower
26	LOA	Letter of Award
27	MDBFP	Motor Driven Boiler Feed Pump
28	MGR	Merry Go Round
29	MOEF&CC	Ministry of Environment, Forests & Climate Change
30	NDCT	Natural Draft Cooling Tower
31	PA Fan	Primary Air Fan
32	PPA	Power Purchase Agreement
33	ROW	Right Of Way
34	SBO	Steam Blowing Operation
35	SCR	Selective Catalytic Reduction
36	SG	Steam Generator
37	ST	Station Transformer
38	Synch.	Synchronization
39	TDBFP	Turbine Driven Boiler Feed Pump
40	TG	Turbine Generator
41	WT	Wagon Tippler
42	WTP	Water Treatment Plant
43	UT	Unit Transformer
44	GHP	Gypsum Handling Plant
45	LHP	Limestone Handling Plant
