

केंद्रीय विद्युत प्राधिकरण

(जल विद्युत स्कंध)



निर्माणाधीन जल विद्युत परियोजनाओं की प्रगति

(विद्युत अधिनियम, 2003 के तहत के.वि.प्रा. के दायित्व की पूर्ति में)

त्रैमासिक समीक्षा संख्या. 106

QUARTERLY REVIEW No. 106

जुलाई ~ सितम्बर, 2021

जल विद्युत् परियोजना प्रबोधन प्रभाग

नई दिल्ली

अक्टूबर~ 2021

I N D E X

Chapter	Contents	Page No.
	Preface	1-2
	Executive Summary	3-4
1.	Milestones achieved during the quarter July ~ September, 2021.	5
2.	Plan wise hydro capacity targets/ achievements from 4 th plan onwards.	6
2.1	Year/Plan wise hydro capacity addition in the country.	7-8
2.1(a)	Hydro Capacity addition during 2012-13	9
2.1(b)	Hydro Capacity addition during 2013-14	10
2.1(c)	Hydro Capacity addition during 2014-15	11
2.1(d)	Hydro Capacity addition during 2015-16	12
2.1(e)	Hydro Capacity addition during 2016-17	13-14
2.1(f)	Hydro Capacity addition during 2017-18	15
2.1(g)	Hydro Capacity addition during 2018 -19	16
2.1(h)	Hydro Capacity addition during 2019-20	17
2.1(I)	Hydro Capacity addition during 2020-21	18
2.1(J)	Hydro Capacity addition during 2021-22	19
2.2	Summary of Hydro Capacity Addition expected during 2021-26	20
2.2(a)	Hydro Capacity addition programmed for 2021-22	21
2.2(b)	Hydro Capacity addition programmed for 2022-23	22
2.2(c)	Hydro Capacity addition programmed for 2023-24	23
2.2(d)	Hydro Capacity addition programmed for 2024-25	24
2.2(e)	Hydro Capacity addition programmed for 2025-26	25
3.	Growth of installed capacity.	26
3.1	Growth of hydro capacity.	27
4.	Trend of hydro capacity addition. (hydro and thermal mix	28
5.	List of sanctioned, Under Execution H.E. Projects.	29
6.	Status of Sanctioned, Under Execution H.E. Projects.	30-50
7.	Financial status of Under Execution H.E. Projects	51-52
8.	Status of environment & forest clearance of sanctioned H.E.Projects.	53
9.	Status of Award of civil package for Under Execution H.E. Projects.	54
9.1	Summary of ordering status of TG sets of Under Execution H.E. Projects.	55
9.2	Status of ordering status of TG sets of Under Execution H.E. Projects.	56-57
9.3	Ordering Status of various packages of Under Execution H.E. Projects.	58-66
10.	Status of financial closure of Private Sector H.E. Projects.	67
11.	Details of Under Execution H.E. Projects having Time/Cost over-run	68-77

PREFACE

Present Review

This quarterly review which is **106th** in the series covers the period from **July ~ September, 2021**. The objective of this review is to provide up to date information in respect of Hydro Electric (HE) Projects above 25 MW, which are under construction/ implementation in the country.

This quarterly review has been brought out by CEA on the basis of data received from various project authorities, visit made to different HE projects and discussions held with the executing agencies, contractors, suppliers of equipment and other stakeholders from time to time.

Milestone Achieved during July ~ September ,2021

Details of HE Projects synchronised Rolled/Commissioned and other major milestones achieved during the Quarter is indicated in Chapter-1.

Plan / Year wise Hydro Capacity Addition / Under Execution

Hydro Capacity Addition – Financial Year Wise Lists are placed in Chapter 2.2(a) to 2.2 (l). Summary of Hydro Capacity Addition is in Ch. 2.3 (2020-26), Hydro Electric Projects Under Execution – Year wise Lists are placed in Chapter 2.3(a) to 2.3(g).

Growth of Installed Capacity, Hydro Capacity Addition

A Graphical representation of Trends & Growth of Installed Capacity, Hydro Capacity Addition of Hydro-Thermal-Nuclear HEPs during Plans/Years is placed in Chapter 3 & 4.

Sanctioned Hydro Electric Projects

A Sector wise list of Sanctioned H.E. project Under Execution is placed in Chapter 5.

Status of Sanctioned Hydro Electric Projects

Broad present status of HE projects commissioned during the financial year & Under Execution is given in Chapter 6.

Financial Status of Hydro Electric Projects

Financial status of HE projects supplied by project authorities (unaudited) is given in Chapter 7.

Status of Environment & Forest Clearances of H.E. Projects.

The status of Environmental & Forest clearance of HE projects is given in Chapters 8.

Dates of Award of First Civil Package

The date of award of First Civil Package for HE projects under execution is indicated in Chapter 9.

Ordering Status of TG set.

Details of Ordering status of TG Set for HE projects under construction is given in Chapters 9.1 and 9.2.

Status of Financial closure of Private Sector Hydro Electric Projects

Details of financial closure of Private Sector HE projects is given in Chapter-10.

Time & Cost Over-run of Ongoing Hydro Projects

The Status of Time & Cost Over-run of HE projects under execution is given in Chapter 11.

Exclusions

The review does not cover HE projects categorised as renewable, each with a total installed capacity of 25 MW and below, as these schemes come under the purview of Ministry of New & Renewable Energy (MNRE).

Any suggestions/feedback for further improvement in the quarterly review shall be appreciated.

The report is in fulfilment of CEA's obligation under Electricity Act, 2003.

Executive Summary

ALL INDIA POWER SECTOR INSTALLED CAPACITY (AS ON 30.09.2021).

Installed Capacity (IC)	MW	Percentage of total IC
Thermal:	234023.72	(60.18 %)
Renewable		
a) Large hydro (above 25MW)	46512.22	(11.96 %)
b) Other Renewables (solar, wind, biomass small hydro etc.)	101532.85	(26.11%)
Nuclear	6,780.00	(1.74 %)
TOTAL (IC)	388,848.79	

Sector wise Hydro Capacity under Execution: A hydro capacity of **12,663.50 MW** is under execution.

Sector wise summary is given as under: -

Sector	Under Active consideration		Presently stalled		Under Execution (MW)	
	Nos	MW	Nos	MW	Nos	MW
Central	13	7,464	2	1,021	15	8485
State	10	2,593.5	2	128	12	2721.50
Private	3	520	6	937	9	1457
Total:	26	10,577.50	10	2,086	36	12663.50

Sector wise program/Achievement summary for the financial year 2021-22 (till 30.09.21) is as under :

Year	Monitorable Targets (MW)	Capacity Addition Achieved (MW)	Sector					
			Central		State		Private	
			Tgt.	Act.	Tgt.	Act.	Tgt.	Act.
2021-22	493	213	-	-	100		393	213

Monitorable Targets for Hydro Capacity Addition for the year 2021-22:

Monitorable Targets for hydro capacity addition for the year 2021-22 is **493 MW** (100 MW in State Sector and 393 MW in Private Sector). Details are as under: -

Sl. No.	Particular	Unit Nos.	Cap. (MW)	Capacity Addition as Programmed	Remarks
A.	State Sector				
1	Pallivasal KSEB, Kerala 2x30=60 MW	Unit #1 Unit # 2	30 30	December'21 December'21	Likely to slip to 2022-23 Likely to slip to 2022-23
2	Thottiyar KSEB, Kerala 1x30+1x10=40MW	Unit #1 Unit # 2	10 30	December'21 December'21	Likely to slip to 2022-23 Likely to slip to 2022-23
	Sub- total (A):		100 MW		
B.	Private Sector				
3	Sorang HSPCL, H.P. 2x50=100 MW	Unit #1 Unit # 2	50 50	September'21 September '21	Commissioned (Both units each of 50 MW capacity were commissioned in September '2021)
4	Bajoli Holi GMRBHPPL, H.P. 3x60=180 MW	Unit #1 Unit # 2 Unit # 3	60 60 60	October '21 October 21 October '21	Nov'.2021(Likely) Nov'.2021(Likely) Nov'.2021(Likely)
5	Rongnichu MBPCL, Sikkim 2x56.5=113 MW	Unit #1 Unit # 2	56.5 56.5	May'21 May'21	Commissioned (Both units each of 56.5 MW capacity were commissioned in June'2021)
	Sub- total (B):		393 MW		
	Total (A+B)		493 MW		213 MW has been commissioned till 30.09.21

NOTE: The Vyasi HEP(120MW) which is scheduled for commissioning during 2022-23 may be commissioned during March 2022(2021-22) under best efforts.

CHAPTER- 1

Milestones achieved during the Quarter July ~ September, 2021

1. Capacity addition: -

Sl. No.	Particulars	Unit No.	Capacity (MW)	Remarks
1.	Sorang HSPCL, H.P.	Unit #1	50	Taken into capacity addition on 23.09.2021
		Unit #2	50	Taken into capacity addition on 21.09.2021
		Total	100 MW.	
Total during the current quarter (Private Sector) – 100 MW.				

2. Major Awards in the quarter

(a) Lower Kopili (APGCL)(2x55+2x2.5+1x5 =120 MW) : Letter of award issued for Electrical Mechanical package for Lower Kopili to M/s ANDRITZ HYDRO Private Ltd. on 9th September 2021 .

(b) Luhri HEP Stage –I (210 MW) : Letter of award issued for Electrical Mechanical package of Luhri to M/s Voith hydro on 16th July 2021 and contract signed on 12th August 2021.

(c) Rangit-IV (3x40=120MW): The Civil and EM works were awarded to M/s Ritwick and M/s ANDRITZ HYDRO Private Ltd during the quarter.

3. Restart of Works (Stalled Projects)

(a) Rangit-IV(3x40=120MW) : The project after take over by NHPC Ltd. was restarted after re awarding major civil works in August 2021 and Project works have been re-started.

CHAPTER - 2

Plan wise Hydro capacity Target Vs Achievement since 4th Plan

Plan / Year	Target (MW) (Original)	Capacity Addition (MW)	% Achieved
4th Plan (1969-74)	3518.00	1058.39	30.08
5th Plan (1974-79)	4654.00	3867.77	83.11
Annual Plan (1979-80)	548.00	550.9	100.53
6th Plan (1980-85)	4768.00	3076.05	64.51
7th Plan (1985-90)	5541.25	3828.41	69.09
Annual Plan (1990-91)	1006.50	445.5	44.26
Annual Plan (1991-92)	754.30	436	57.8
8th Plan (1992-97)	9282.15	2427.65	26.15
9th Plan (1997-02)	9817.70	4538.25	46.23
10th Plan (2002-07)	14393.20	7886	54.79
11th Plan (2007-12)	15627.00	5544	35.48
12 th Plan (2012-17)	10897.00	5479	50.28
2017-18	1305.00	795	60.92
2018-19	840.00	140	16.67
2019-20	1190.00	300	25.21
2020-21	606.00	510	84.16
2021-22	493.00	213	43.20

CHAPTER - 2.1

Year/Plan wise Hydro Capacity Addition in the Country

S.No.	Year	Target (Original)	Capacity Addition (MW)	% Achieved	Remarks
1st Five Year Plan (1.1.51 to 31.12.55)					
1	1951		15.89		
2	1952		140.00		
3	1953		16.00		
4	1954		62.17		
5	1955		<u>146.13</u>		
	Total :		<u>380.19</u>		
2nd Five Year Plan (1.1.56 to 31.03.61)					
6	1956		121.96		
7	1957-58		152.48		
8	1958-59		147.52		
9	1959-60		168.71		
10	1960-61		<u>386.51</u>		
	Total :		<u>977.18</u>		
3rd Five Year Plan (1.4.61 to 31.03.66)					
11	1961-62		502.44		
12	1962-63		517.25		
13	1963-64		230.67		
14	1964-65		221.71		
15	1965-66		<u>735.01</u>		
	Total :		<u>2207.08</u>		
Annual Plans (1966-67, 67-68, 68-69)					
16	1966-67		633.48		
17	1967-68		729.70		
18	1968-69		419.99		
4th Five Year Plan (1.4.69 to 31.03.74)					
19	1969-70		227.79		
20	1970-71		248.53		
21	1971-72		228.38		
22	1972-73		173.80		
23	1973-74		<u>179.89</u>		
	Total :	3518	<u>1058.39</u>	30.08	
5th Five Year Plan (1.4.74 to 31.03.79)					
24	1974-75		563.94		
25	1975-76		934.36		
26	1976-77		561.30		
27	1977-78		995.32		
28	1978-79		<u>812.85</u>		
	Total :	4654	<u>3867.77</u>	81.11	
Annual Plan (1979-80)					
29	1979-80	548	550.90	100.18	
6th Five Year Plan (1.4.80 to 31.03.85)					
30	1980-81		407.25		
31	1981-82		381.59		
32	1982-83		883.05		
33	1983-84		799.70		
34	1984-85		<u>604.46</u>		
	Total :	4768	<u>3076.05</u>	64.51	

S.No.	Year	Target (Original)	Capacity Addition (MW)	% Achieved	Remarks
7th Five Year Plan (1.4.85 to 31.03.90)					
35	1985-86		1012.00		
36	1986-87		704.525		
37	1987-88		1069.285		
38	1988-89		532.70		
39	1989-90		<u>509.90</u>		
	Total :	5541.25	<u>3828.41</u>	69.09	
Annual Plans (1990-91, 91-92)					
40	1990-91	1006.5	445.50	44.26	
41	1991-92	754.3	436.00	57.8	
8th Five Year Plan (1.4.92 to 31.03.97)					
42	1992-93	372.95	372.95		
43	1993-94	957.65	797.15		
44	1994-95	1192.55	450.00		
45	1995-96	1846	147.05		
46	1996-97	4913	<u>660.50</u>		
	Total :	9282.15	<u>2427.65</u>	26.15	
9th Five Year Plan (1.4.97 to 31.03.2002)					
47	1997-98	233	233.00		
48	1998-99	312	542.50		
49	1999-2000	1543	1371.50		
50	2000-01	2223	1285.00		
51	2001-02	5506.7	<u>1106.25</u>		
	Total :	9817.7	<u>4538.25</u>	46.22	
10th Five Year Plan (1.4.02 to 31.03.07)					
52	2002-03	585	635.00		
53	2003-04	3740	2590.00		Highest till date.
54	2004-05	2401	1015.00		
55	2005-06	2010	1340.00		
56	2006-07	5657	2306.00		3rd Highest
	Total :	14393	7886.00	54.79	
11th Five Year Plan (1.4.07 to 31.03.12)					
57	2007-08	2423	2423		2nd Highest.
58	2008-09	1097	969		
59	2009-10	1805	39		
60	2010-11	1741	690		
61	2011-12	8561	1423		
	Total :	15627	5544.00	35.48	
12th Five Year Plan (1.4.12 to 31.03.17)					
62	2012-13	802 ★	510		
63	2013-14	1198 ★	1058		
64	2014-15	842 ★	736		
65	2015-16	1691 ★	1516		
66	2016-17	1714 ★	1659		4th Highest
	Total :	10897	5479	50.23	
67	2017-18	1305 ★	795	60.92	
68	2018-19	840 ★	140	16.67	
69	2019-20	1190 ★	300	25.21	
70	2020-21	606 ★	510	84.16	
71	2021-22 (till Sept. 21)	493 ★	213	43.20	

★ Targets set at the beginning of the year.

Chapter- 2.1a

Hydro Capacity Addition during the Year 2012-13

Sl. No.	Particular	Unit Nos.	Target (MW)	Commissioning as programmed	Actual (MW)	Actual (A)/ Anticipated	Remarks/Critical Issue
A. Central Sector							
1.	Chamera-III NHPC, H.P. 3x77= 231 MW	1 2 3	77 77 77	Jun-12 Aug-12 Oct -12	77 77 77	28.06.2012(A) 12.06.2012(A) 07.06.2012(A)	Commissioned
2.	Uri-II NHPC, J&K 4x60= 240 MW	1 2 3 4	60 60 60 60	Aug -12 Sept -12 Nov-12 Dec-12	-	Slipped Slipped Slipped Slipped	- Local agitation from mid March, 12 to June, 12 end. - TRT was flooded on 17.09.12 due to flash flood. - Filling of U/s Water conductor system delayed due to agitation by local people demanding employment in NHPC.
3.	Chutak NHPC, J&K 4x11 =44 MW	1 2 3 4	11 11 11 11	Sept-12 Sept-12 Nov -12 Dec-12	11 11 11 11	22.11.2012(A) 08.11.2012(A) 11.11.2012(A) 28.01.2013(A)	Commissioned
4.	Parbati-III NHPC, HP 4x130= 520 MW	1	130	Mar-13	-	Slipped	- Non-availability of transmission system. - Non completion of Surge shaft gates.
Sub- total (A):			645		275		
B. State Sector							
5.	Bhawani Kattalai -II TANGEDCO, T.N Tamil Nadu, 2x15 = 30 MW	1 2	15 15	June-12 July-12	-	Slipped	- Unit #1&2 synchronised at part load in July,11 & Sept,11 - Reservoir filling delayed on account of less release from Mettur dam.
6.	Bhawani Kattalai -III TANGEDCO, T.N 2x15 = 30 MW	1	15	Oct-12	15	08.12.12(A)	Commissioned
7.	Myntdu MeECL, Meghalaya 3x42 = 126 MW	3	42	Mar-13	42	07.03.2013(A)	Commissioned
Sub- total (B):			87		57		
C. Private Sector							
8.	Budhil Lanco H P 2x35=70 MW	1 2	35 35	May-12 July-12	35 35	30.05.2012(A) 26.05.2012(A)	Commissioned
Sub- total (C):			70		70		
Total (A+B+C)			802		402		
Out side the programme of 2012-13.							
1.	Teesta Low Dam –III NHPC, WB 4x33=132 MW	1 2 3	- - -	2013-14 2013-14 2013.14	33 33 33	30.01.2013(A) 20.01.2013(A) 24.02.2013(A)	Commissioned
2.	Jaldhaka (WBSEDCL) West Bengal 4x9=36 MW	4	-	-	9	08.10.2012(A)	Commissioned
Sub- total : Outside			-		108		
Grand Total: 2012-13			802		510		

Chapter- 2.1b

Hydro Capacity Addition during the Year 2013-14

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Commissioning		Remarks/Critical Issue
			Target	Actual	As Programmed	Actual (A)/ Anticipated	
A. Central Sector							
1	Teesta Low Dam-III NHPC, WB. 4x33= 132 MW	Unit # 4	33	33	April-13	01.04.2013(A)	Commissioned
2	Uri-II NHPC, J&K 4x60= 240 MW	Unit # 1 Unit # 2 Unit # 3 Unit # 4	60 60 60 60	60 60 60 60	May-13 June- 13 July- 13 July- 13	25.09.2013 (A) 16.11.2013 (A) 27.09.2013 (A) 02.02.2014 (A)	Commissioned
3	Parbati-III NHPC, HP 4x130= 520 MW	Unit # 1 Unit # 2 Unit # 3	130 130 130	130 130 130	June-13 July -13 Feb- 14	18.02.2014 (A) 27.02.2014 (A) 15.03.2014 (A)	Commissioned
4	Nimoo Bazgo NHPC, J&K 3x15 =45 MW	Unit # 1 Unit # 2 Unit # 3	15 15 15	15 15 15	Dec- 13 Nov -13 Nov-13	02.11.2013 (A) 31.10.2013 (A) 30.10.2013 (A)	Commissioned
5	Rampur SJVN Limited, HP. 6x68.67 = 412 MW	Unit # 1 Unit # 2 Unit # 5	68.67 68.67 68.67	68.67 68.67 68.67	Jan- 14 Feb- 14 Mar- 14	23.03.2014 (A) 21.03.2014 (A) 29.03.2014 (A)	Commissioned
	Sub- total (A):		914	914			
B. State Sector							
6.	Lower Jurala APGENCO, A.P. (6x40=240 MW)	Unit # 1	40	-	Dec-13	Slipped	-Unit was synchronized at part load on 29.12.13, but full load commissioning could not be achieved due to non-availability of sufficient water.
7	Bhawani Kattalai -II TANGEDCO, T.N Tamil Nadu, 2x15 = 30 MW	Unit # 1 Unit # 2	15 15	15 15	July -13 Aug- 13	27.08.2013 (A) 06.09.2013 (A)	Commissioned
8	Bhawani Kattalai -III TANGEDCO, T.N Tamil Nadu, 2x15 = 30 MW	Unit # 2	15	15	June -13	25.09.2013 (A)	Commissioned
	Sub- total (B):		85	45			
C. Private Sector							
9	Sorang Himachal Sorang Power Pvt. Ltd, H P. 2x50=100 MW	Unit # 1 Unit # 2	50 50	- -	Nov-11 Dec-11	Slipped	- Commissioning delayed, cracks developed in penstock during filling of water conductor system in 1 st week of Nov-2013.
10	Chuzachen Gati Infra. Limited, Sikkim 2x49.5= 99 MW	Unit # 1 Unit # 2	49.5 49.5	49.5 49.5	June -13 July -13	21.04.2013(A) 20.04.2013(A)	Commissioned
	Sub- total (C):		199	99			
	Total (A+B+C)		1198	1058			

Out side RFD achievements: Unit # 2 (40 MW) of Lower Jurala HEP was synchronized at part load on 10.01.2014, but full load commissioning could not be achieved due to non-availability of sufficient water.

Chapter- 2.1c

Hydro Capacity Addition during the Year 2014-15

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Commissioning		Remarks/Critical Issue
			Target	Actual	As Programmed	Actual (A)/ Anticipated	
A. Central Sector							
1	Parbati-III NHPC, HP 4x130= 520 MW	Unit # 4	130	130	Aug- 14	22.05.2014 (A)	Commissioned
2	Rampur SJVN Limited, HP. 6x68.67 = 412 MW	Unit # 3 Unit # 4 Unit # 6	68.67 68.67 68.67	68.67 68.67 68.67	Jun 14 May 14 Apr 14	31.07.2014(A) 12.06.2014(A) 04.12.2014(A)	Commissioned
Out side the Programme							
3	Koldam NTPC, H.P. 4x200 = 800 MW	Unit # 1 Unit # 2	200 200	200 200	Mar-15 Mar-15	31.03.2015 (A) 30.03.2015 (A)	Commissioned
	Sub- total (A):		736	736			
B. State Sector							
4	Lower Jurala TSGENCO, Telangana 6x40= 240 MW	Unit # 1 Unit # 2 Unit # 3 Unit # 4	40 40 40 40	0 0 0 0	Jul.-14 Jul.-14 Oct.-14 Mar.-15	Slipped	- Slipped due to flooding of Power House on 30.07.2014 during synchronization process for Unit # 1 to Unit# 3.
5	Nagarjuna Sagar APGENCO, A.P. 2x25= 50 MW	Unit # 1 Unit # 2	25 25	0 0	Sep-14 Dec-14	Slipped	- Commissioning delayed due to non-availability of water.
	Sub- total (B):		210	0			
C. Private Sector							
6	Jorethang Loop DANS Pvt. Ltd., Sikkim 2x48= 96 MW	Unit # 1 Unit # 2	48 48	0 0	Feb-15 Mar-15	Slipped	- Slipped due to non-completion of HRT.
7	Teesta-III Teesta Urja, Sikkim 6x200= 1200 MW	Unit # 6	200	0	Mar-15	Slipped	- Slipped due to Financial crunch with the Developer.
	Sub- total (C):		296	0			
	Total (A+B+C)		842	736			

Out side RFD achievements:

Unit #1 & # 2 (400 MW) of Kol Dam HEP commissioned during March, 2015.

Chapter- 2.1d

Hydro Capacity Addition during the Year 2015-16

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Commissioning		Remarks/Critical Issue
			Target	Actual	As Programmed	Actual (A)/ Anticipated	
A.	Central Sector						
1	Koldam NTPC, HP 4x200= 800 MW	Unit # 3 Unit # 4	200 200	200 200	4/15 5/15	10.04.2015(A) 12.06.2015(A)	Commissioned
2	Teesta Low Dam-IV NHPC, W.B 4x40 = 160 MW	Unit # 1 Unit # 2	40 40	40 40	2/16 3/16	14.02.2016 16.03.2016	Commissioned
3	Pare NEEPCO, Ar. Pradesh 2x55=110 MW	Unit # 1 Unit # 2	55 55		8/12 8/12	Slipped Slipped	Slipped due to inundation of dam area with flood water after overtopping of Cofferdam in June'15 and many times thereafter. Slow progress of works in Dam concreting.
	Sub- total (A):		590	480			Achieved:-480 MW
B.	State Sector						
4	Baglihar - II JKPDC, J&K 3x150= 450 MW	Unit # 1 Unit # 2 Unit # 3	150 150 150	150 150 150	9/15 9/15 2016-17	05.09.2015(A) 29.09.2015(A) 26.10.2015(A)	Commissioned
5	Kashang - I HPPCL, H.P. 1x65=65 MW	Unit # 1	65		3/16	Slipped	Slow progress of E&M works.
6	Lower Jurala TSGENCO, Telangana 6x40= 240 MW	Unit # 1 Unit # 2 Unit # 3 Unit # 4	40 40 40 40	40 40 40 40	7/15 8/15 9/15 10/15	14.10.2015(A) 30.09.2015(A) 04.01.2016(A) 05.03.2016(A)	Commissioned
7	Nagarjuna Sagar TR APGENCO, AP 2x25=50 MW	Unit # 1 Unit # 2	25 25		7/15 7/15	Slipped Slipped	Unit 1 & 2 could not be commissioned due to non-availability of rated discharge.
	Sub- total (B):		575	610			Achieved:-610 MW
C.	Private Sector						
8	Sorang HSPCL, H.P. 2x50 = 100 MW	Unit # 1 Unit # 2	50 50		11/11 12/11	Slipped Slipped	Unit # 1 synchronized , but could not be commissioned due to non-availability of rated discharge. Penstock ruptured on 18.11.2015.
9	Srinagar AHPCL, Uttarakhand 4x82.5=330	Unit # 1 Unit # 2 Unit # 3 Unit # 4	82.5 82.5 82.5 82.5	82.5 82.5 82.5 82.5	4/15 4/15 5/15 6/15	10.04.2015(A) 08.06.2015(A) 20.04.2015(A) 03.06.2015(A)	Commissioned
10	Jorethang Loop DANS Pvt. Ltd., Sikkim 2x48= 96 MW	Unit # 1 Unit # 2	48 48	48 48	9/15 10/15	22.09.2015(A) 23.09.2015(A)	Commissioned
	Sub- total (C):		526	426			Achieved:-426 MW
	Total (A+B+C)		1691	1516			Achieved:-1516 MW
	Note: 1516 MW out of 1691 MW is Commissioned during 2015-16.						

Out side RFD achievements:

Unit #3 (150 MW) of Baglihar-II HEP commissioned ahead of Programme during Oct-2015.

Chapter- 2.1e

Hydro Capacity Addition during the Year 2016-17

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Commissioning		Remarks/ Critical Issue
			Target	Actual	As Programmed	Actual(A)/ Anticipated	
A.	Central Sector						
1	Teesta Low Dam IV NHPC, West Bengal 4x40 = 160 MW	Unit # 3 Unit # 4	40 40	40 40	Jun.16 Sep.16	03.07.2016(A) 11.08.2016(A)	Commissioned
2	Pare NEEPCO, Ar. Pradesh 2x55=110 MW	Unit # 1 Unit # 2	55 55	- -	Aug.12 Aug.12	Slipped Slipped	Slow progress in Dam concreting and erection of spillway gates.
3	Kameng NEEPCO, Ar. Pradesh 4x150= 600 MW	Unit # 1 Unit # 2	150 150	- -	Dec.'09 Dec.'09	Slipped Slipped	Slow progress in Dam & HM works.
	Sub- total (C.S.):		490	80			
B.	State Sector						
1	Sainj HPPCL, H.P 2x50= 100 MW.	Unit # 1 Unit # 2	50 50	- -	Dec.16 Jan.17	Slipped Slipped	Slow progress of concreting barrage, pressure shaft & power house.
2	Kashang – I HPPCL, H.P. 1x65=65 MW	Unit # 1	65	65	May 16	10.10.2016(A)	Commissioned
3	Lower Jurala TSGENCO, Telangana 6x40= 240 MW	Unit # 5 Unit # 6	40 40	40 40	Sept.16 Nov.16	20.08.2016(A) 29.09.2016(A)	Commissioned
4	Pulichintala TSGENCO,Telangana 4x30=120 MW	Unit # 1 Unit # 2	30 30	30 -	Aug.16 Dec16	25.09.2016(A) Slipped	Commissioned Due to non-availability of water in the Dam.
5	New Umtru MePGCL,Meghalaya 2x20=40 MW	Unit # 1 Unit # 2	20 20	- -	Nov.16 Dec.16	Slipped Slipped	Slow progress of works.
6	Teesta-III Teesta Urja Ltd. Sikkim 6x200= 1200 MW	Unit #1 Unit # 2 Unit # 3	200 200 200	200 200 200	Dec.16 Jan.17 Feb.17	15.01.2017(A) 27.01.2017(A) 14.01.2017(A)	Commissioned
7	Nagarjuna Sagar TR APGENCO, Telangana 2x25= 50 MW	Unit #1 Unit #2	25 25	25 25	Aug.16 Aug.16	05.01.2017(A) 28.01.2017(A)	Commissioned
	Sub- total (B):		995	825			
C.	Private Sector						
1	Chanju-I IA Energy ; H.P. 3x12= 36 MW	Unit # 1 Unit # 2 Unit # 3	12 12 12	12 12 -	July 16 Sept.16 Dec.16	17.02.2017(A) 01.02.2017(A) Slipped	Commissioned Commissioned Slow progress of E&M works.
2	Dikchu Sneha Kinetic Power Projects (P).Ltd., Sikkim 2x48= 96 MW	Unit # 1 Unit # 2	48 48	- -	July.16 Sept.16	Slipped Slipped	Slow progress of HM & EM works.
3	Tashiding Shiga Energy Pvt. Ltd. Sikkim 2x48.5= 97 MW	Unit # 1 Unit # 2	48.5 48.5	- -	Jan.17 Feb.17	Slipped Slipped	Non completion of power evacuation system.
	Sub- total (P.S.):		229	24			

Chapter- 2.1e

	Total C.S.+S.S.+P.S.)		1714	929			
		Out Side Programme					
1	Kashang-II & III HPPCL , HP 1x65+1x65= 130MW	Unit # 1 Unit # 2	65 65	65 65	NA NA	02.01.2017(A) 22.08.2016(A)	Commissioned
2.	Teesta-III Teesta Urja Ltd. Sikkim 6x200=1200 MW.	Unit #4 Unit # 5 Unit # 6	200 200 200	200 200 200	Outside Programme	16.02.2017(A) 24.01.2017(A) 28.01.2017(A)	Commissioned
		Total Outside Programme :		730			
		Grand Total (31.03.2017)		1659			

Chapter- 2.1f

Hydro Capacity Addition during the Year 2017-18

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Commissioning		Remarks / Critical Issues
			Actual	Target	As Programmed	Actual (A)/ Anticipated	
A.	Central Sector						
1	Tuirial NEEPCO, Mizoram 2x30 = 60 MW	Unit # 1 Unit # 2	30 30	30 30	Jun '17 Sep '17	25.08.2017(A) 28.11.2017(A)	Commissioned
2	Kishanganga NHPC, J&K 3x110 = 330 MW	Unit #1 Unit # 2 Unit # 3	110 110 110	110 110 110	Jan '18 Feb '18 Mar '18	13.03.2018(A) 21.03.2018(A) 30.03.2018(A)	Commissioned
3	Pare NEEPCO, Arunachal Pradesh 2x55=110 MW	Unit # 1 Unit # 2	55 55	55 55	May'18 May'18	Slipped Slipped	Seepage from diversion tunnel during impounding of reservoir.
4	Kameng NEEPCO, Arunachal Pradesh 4x150=600 MW	Unit # 1 Unit # 2	150 150	-	Mar. '18 Mar. '18	Slipped Slipped	Leaking observed in Penstock during water filling
	Sub- total (A):		800	390	Total Commissioned in Central Sector : 390 MW		
B.	State Sector						
1	Sainj HPPCL, H.P. 2x50= 100 MW	Unit # 1 Unit # 2	50 50	50 50	May.17 Jun.17	04.09.2017(A) 04.09.2017(A)	Commissioned
2	Uhl - III BVPCL, H.P. 3x33.33=100 MW	Unit #1 Unit # 2 Unit # 3	33.33 33.33 33.33	-	Jan.'18 Feb.'18 Mar.'18	Slipped Slipped Slipped	Delay in completion of HRT lining due to heavy ingress of water in HRT.
3	Pulichintala TSGENCO,Telangana 4x30=120 MW	Unit # 2 Unit # 3	30 30	30 30	Aug.17 Oct.17	26.10.2017(A) 01.11.2017(A)	Commissioned
4	New Umtru MePGCL, Meghalaya 2x20=40 MW	Unit # 1 Unit # 2	20 20	20 20	Apr.17 Jul.17	22.04.2017 (A) 30.06.2017 (A)	Commissioned
	Sub- total (B):		300	200	Total Commissioned in State Sector :200 MW		
C.	Private Sector						
1	Chanju-I IA Energy, H.P. 3x12 = 36 MW	Unit # 3	12	12	May.17	26.07.2017 (A)	Commissioned
2	Dikchu Sneha Kinetic Power Projects Pvt. Ltd., Sikkim, 2x48MW= 96	Unit # 1 Unit # 2	48 48	48 48	Apr.17 May.17	11.04.2017 (A) 12.04.2017 (A)	Commissioned
3	Tashiding Shiga Energy Pvt. Ltd. Sikkim 2x48.5= 97 MW	Unit # 1 Unit # 2	48.5 48.5	48.5 48.5	Jul.17 Aug.17	06.11.2017 (A) 06.11.2017(A)	Commissioned
	Sub- total (C):		205	205	Total Commissioned in Private Sector : 205 MW		
	Total (A+B+C)		1305	795	Total Commissioned during 2017-18 : 795 MW.		

Chapter- 2.1g

Hydro Capacity Addition during the Year 2018-19

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Commissioning		Remarks / Critical Issues
			Target	Actual	As Programmed	Actual (A)/ Anticipated	
A.	Central Sector						
1	Pare NEEPCO, Arunachal Pradesh 2x55=110 MW	Unit # 1 Unit # 2	55 55	55 55	May'18 May'18	28.05.2018 21.05.2018	Commissioned
2	Kameng NEEPCO, Arunachal Pradesh 4x150=600 MW	Unit # 1 Unit # 2 Unit # 3 Unit # 4	150 150 150 150		March'19 March'19 March'19 March'19	Slipped to 2019-20	Non-completion of Rectification works of leakage observed in penstock1&2 during water filling..
	Sub- total (A):		710	110	Total Commissioned in Central Sector :110 MW		
B.	State Sector						
3	Uhl - III BVPCL, H.P. 3x33.33=100 MW	Unit #1 Unit # 2 Unit # 3	33.33 33.33 33.33		Aug. 18 Aug.18 Sep.18	Slipped to 2019-20	During HST, some leakage in Penstock is observed which is being rectified.
4	Pulichintala TSGENCO, Telangana 4x30=120 MW	Unit # 4	30	30	Sep.18	08.09.2018(A)	Commissioned
	Sub- total (B):		130		30		
	Total (A+B)		840		140	Total Comm. 140 MW	

Chapter-2.1h

Hydro Capacity Addition during the Year 2019-20

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Commissioning		Remarks / Critical Issues
			Target	Actual	As Programmed	Actual (A)/ Anticipated	
A.	Central Sector						
1	Kameng NEEPCO, Arunachal Pradesh 4x150=600 MW	Unit # 1 Unit # 2 Unit # 3 Unit # 4	150 150 150 150	150 150	Aug'19 Aug'19 Aug'19 Aug'19	Feb,20 Feb,20 Slipped Slipped Slipping to (March-21)	-Seepage of water during welding affecting progress of works and causing delays. -Difficult approach and working condition. -Ventilation constrains Works effected due to heavy rains this monsoon.
	Sub- total (A):		600	300			
B.	State Sector						
2.	Uhl - III BVPCL, H.P. 3x33.33=100	Unit #1 Unit # 2 Unit # 3	33.33 33.33 33.33		Oct,19 Nov,19 Dec,19	Slipping to (Dec,22)	-Difficult approach -Delay in welding of liner in bend. - Rupture in Penstock in May,2020
3	Sawra Kuddu HPPCL, H.P. 3x37=111 MW	Unit #1 Unit # 2 Unit # 3	37 37 37		Sep,19 Oct,19 Nov,19	Slipping to (March,21)	- Delay in completion of HRT works & associated transmission line. - During filling of water conductor system in May,20, leakage is observed in adit to HRT
	Sub- total (B):		211				
C.	Private Sector						
4.	Bajoli Holi GMR,H.P. 3x60=180 MW	Unit #1 Unit # 2 Unit # 3	60 60 60		Jan.,20 Feb.,20 Mar.,20	Slipping to (Dec,21)	-Works affected due to heavy rainfall in August,19 and inclement weather from early Dec,19. to end of Jan,20 -Poor financial health of civil contractor.
5.	Singoli Bhatwari L&T, Uttarakhand 2x33=99 MW	Unit #1 Unit # 2 Unit # 3	33 33 33		Mar.,20 Mar.,20 Mar.,20	Slipping to (Dec,20)	-Commissioned
6.	Sorang HSPCL Uttarakhand 2x50=100 MW	Unit #1 Unit # 2	50 50		Nov,19 Dec.,19	Slipping to Dec,21	- Poor planning of re-erection of penstock works - Weather constraints.
	Sub- total (C):		379				
	Total (A+B+C)		1190	300			

Hydro Capacity Addition during the Year 2020-21

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Commissioning		Remarks / Critical Issues
			Target	Actual	As Programmed	Actual (A)/ Anticipated	
A.	Central Sector						
1	Kameng NEEPCO, Arunachal Pradesh 4x150=600 MW	Unit # 3 Unit # 4	150 150	300	March,21 March,21	21.01.2021 11.02.2021	Commissioned Commissioned
	Sub- total (A):		300	300			
B.	State Sector						
2	Sawra Kuddu HPPCL, H.P. 3x37=111 MW	Unit #1 Unit # 2 Unit # 3	37 37 37	111	(March,21) (March,21) (March,21)	12.11.2020 05.12.2020 16.12.2020	Commissioned Commissioned Commissioned
	Sub- total (B):		111	111			
C.	Private Sector						
3.	Singoli Bhatwari L&T, Uttarakhand 2x33=99 MW	Unit #1 Unit # 2 Unit # 3	33 33 33	99	March.,20 March.,20 March.,20	19.11.2020 18.12.2020 25.12.2020	Commissioned Commissioned Commissioned
4.	Rongnichu 2x48= 96 MW* Madhya Bharat Power Corpn., Sikkim	Unit #1 Unit # 2	48 48	--	March,21 March,21	*To be commissioned in FY 2021-22 with 17 MW enhanced capacity	
	Sub- total (C):		195				
	Total (A+B+C)		606	510			

Note: 510 MW capacity addition has been achieved in FY 2020-21 out of programmed capacity of total 606 MW

Chapter -2.1 J

Hydro Capacity addition Programme for 2021-22

Sl. No.	Particular	Unit Nos.	Capacity (MW)		Capacity Addition		Remarks/Critical Issues
			Target	Actual	As Programmed	Actual/ Anticipated	
A.	State Sector						
1	Pallivasal KSEB, Kerala 2x30=60 MW	Unit #1 Unit # 2	30 30		December'21 December'21	March '22 March '22	
2	Thottiyar KSEB, Kerala 1x30+1x10=40MW	Unit #1 Unit # 2	10 30		December'21 December'21	December'21 December'21	
	Sub- total (A):		100 MW				
B.	Private Sector						
3	Sorang HSPCL, H.P. 2x50=100 MW	Unit #1 Unit # 2	50 50	100	June'21 June'21	23.09.2021 21.09.2021	Commissioned Commissioned
4	Bajoli Holi GMRBHPPL, H.P. 3x60=180 MW	Unit #1 Unit # 2 Unit # 3	60 60 60		June'21 June'21 June'21	October '21 October '21 October '21	
5	Rongnichu MBPCL, Sikkim 2x56.5=113 MW	Unit #1 Unit # 2	56.5 56.5	113	May'21 May'21	25.06.2021 30.06.2021	Commissioned Commissioned
	Sub- total (B):		393 MW	213			
	Total (A+B)		493 MW				

Chapter 2.2

SUMMARY

Hydro Capacity Addition during the Period 2021-26

Sector	2021-22*		2022-23		2023-24		2024-25		2025-26		Total	
	MW	Nos.	MW	Nos.	MW	Nos.	MW	Nos.	MW	Nos.	MW	Nos.
Central Sector	0	0	1360	3#	3520	4#	1188	3	2417	6	8485	15
State Sector	100	2	120	1	843.5	4	1210	3#	448	3#	2721.5	12
Private Sector	180	1	100	1	400	1	237	4	540	2	1457	9
Total	280	3	1580	5	4763.5	9	2635	10	3405	11	12663.5	36

Note:

At present, there are 36 no. of Hydro Electric Projects (above 25 MW) totaling to **12663.50 MW**. Central Sector – 15 nos. (8485 MW), State Sector – 11 nos. (2721.50 MW), Private Sector – 10 nos. (1457 MW). Out of these, 26 nos. of Hydro Power Project totaling to 10577.5 MW are under active construction and on 10 nos. of Hydro Power Project totaling to 2086 MW for which construction is held-up.

* **Rongnichu and Sorang HEPs commissioned during 2021-22 (in June & Sept. 21 respectively)**

Subansiri Lower and Polavaram Hydroelectric Project are bifurcated for benefits during more than one year.

Chapter- 2.2 (a)
List of under construction Hydro projects
(above 25 MW & excluding Projects under Ministry of New & Energy)
FY: 2021-22

Sl. No.	Name of Project	Unit No.	State/ Implem. Agency	Capacity (MW)	Remarks
	State Sector				
1	Pallivasal 2x30= 60 MW	U-1 to U-2	Kerala/ KSEB Ltd.	60	Project commissioning is likely to slip to 2022-23
2	Thottiyar 1x30 + 1x10= 40 MW	U-1 to U-2	Kerala/ KSEB Ltd.	40	Project commissioning is likely to slip to 2022-23
			Sub- total (State):	100	
	Private Sector				
3	Bajoli Holi 3x60= 180 MW	U-1 to U-3	Himachal Pradesh/ GMR Bajoli Holi Hydro	180	
4	Sorang 2x50= 100 MW	U-1 to U-2	Himachal Pradesh/ Himachal Sorang Power	100	Both units have been commissioned in Sept. 2021
5	Rongnichu 2x56.5= 113 MW	U-1 to U-2	Sikkim/ Madhya Bharat Power Corporation Ltd.	113	Both units have been commissioned in June, 2021
			Sub- total (Private):	393	
Total (CS+SS+PS)				493	

Chapter- 2.2 (b)
List of under construction Hydro projects
(above 25 MW & excluding Projects under Ministry of New & Energy)
FY: 2022-23

Sl. No.	Name of Project	Unit No.	State/ Implem. Agency	Capacity (MW)	Remarks
	Central Sector				
1	Naitwar Mori 2x30=60 MW	U-1 to U-2	Uttarakhand/SJVNL	60	
2	Parbati St. II 4x200= 800 MW	U-1 to U-4	Himachal Pradesh/NHPC	800	
3	Subansiri Lower 8x250= 2000 MW	U-1 to U-2	Arunachal Pradesh/NHPC	500	
			Sub- total (Central):	1360	
	State Sector				
5	Vyasi 2x60=120 MW	U-1 to U-2	Uttarakhand/UJVNL	120	
			Sub- total (State):	120	
	Private Sector				
6	Tidong-I 2x50= 100 MW	U-1 to U-2	Himachal Pradesh/M/s Statkraft India Pvt. Ltd.	100	
			Sub- total (Private):	100	
Total (CS+SS+PS)				1580	

Chapter- 2.2 C

**List of under construction Hydro projects
(above 25 MW & excluding Projects under Ministry of New & Energy)**

FY: 2023-24

Sl. No.	Name of Project	Unit No.	State/ Implem. Agency	Capacity (MW)	Remarks
	Central Sector				
1	Tehri PSS 4x250= 1000 MW	U-1 to U-4	Uttarakhand/THDC	1000	
2	Subansiri Lower 8x250= 2000 MW	U-3 to U-8	Arunachal Pradesh/NHPC	1500	
3	Teesta- VI 4x125= 500 MW	U-1 to U-4	Sikkim/NHPC	500	
4	Tapovan Vishnugad 4x130=520 MW	U-1 to U-4	Uttarakhand /NTPC	520	
			Sub- total (Central):	3520	
	State Sector				
5	Shahpurkandi 3x33+3x33+1x8 Kundam Pumped Storage	U-1 to U-7	Punjab/Irr. Deptt. & PSPCL	206	
6	(Phase-I, Phase-II & Phase-III)	U-1 to U-4	Tamil Nadu/TANGEDCO	500	
7	Uhl III 3x33.33= 100 MW	U-1 to U-3	Himachal Pradesh/BVPCL	100	
8	Parnai 3x12.5= 37.5 MW	U-1 to U-3	Jammu & Kashmir/JKSPDC	37.5	
			Sub- total (State):	843.5	
	Private Sector				
9	Maheshwar # 10x40= 400 MW	U-1 to U-10	Madhya Pradesh/SMHPCL	400	Subject to re-start of works
			Sub- total (Private):	400	
Total (CS+SS+PS)				4763.5	
# PFC as lead lender have acquired majority equity i.e. 51% in the SMHPCL w.e.f. 1 st June, 2016. Matter Sub-judice.					

Chapter- 2.2 (d)

**List of under construction Hydro projects
(above 25 MW & excluding Projects under Ministry of New & Energy)**

FY: 2024-25

Sl. No.	Name of Project	Unit No.	State/ Implem. Agency	Capacity (MW)	Remarks
	Central Sector				
1	Kiru 4x156=624 MW	U-1 to U-4	Jammu & Kashmir/CVPPL	624	
2	Rammam - III 3x40=120 MW	U-1 to U-3	West Bengal/ NTPC Ltd.	120	
3	Vishnugad Pipalkoti 4x111= 444 MW	U-1 to U-4	Uttarakhand/THDC	444	
			Sub- total (Central):	1188	
	State Sector				
3	Polavaram 12x80= 960 MW	U-1 to U-8	Andhra Pradesh/ Polavaram Project Authority	640	
4	Shongtong Karcham 3x150= 450 MW	U-1 to U-3	Himachal Pradesh/HPPCL	450	
5	Lower Kopili 2x55+2x2.5+1x5	U-1 to U-5	Assam/APGCL	120	
			Sub- total (State):	1210	
	Private Sector				
6	Phata Byung 2x38= 76 MW	U-1 to U-2	Uttarakhand/ M/s Lanco	76	Subject to re-start of works
7	Rangit-II 2x33= 66 MW	U-1 to U-2	Sikkim/ Sikkim Hydro Power Ltd.	66	Subject to re-start of works
8	Bhasmey 2x25.5= 51 MW	U-1 to U-2	Sikkim/Gati Infrastructure	51	Subject to re-start of works
9	Tangu Romai- I 2x22= 44 MW	U-1 to U-2	Himachal Pradesh/Tangu Romai Power Generation	44	Subject to re-start of works
			Sub- total (Private):	237	
Total (CS+SS+PS)				2635	


Chapter- 2.2 (e)

**List of under construction Hydro projects
(above 25 MW & excluding Projects under Ministry of New & Energy)**


FY: 2025-26

Sl. No.	Name of Project	Unit No.	State/ Implem. Agency	Capacity (MW)	Remarks
	Central Sector				
1	Ratle 4x205+1x30= 850 MW	U-1 to U-5	Jammu & Kashmir/ NHPC	850	Subject to re-start of works
2	Rangit-IV 3x40= 120 MW	U-1 to U-3	Sikkim/Jal Power corp. Ltd.	120	Subject to re-start of works
3	Lata Tapovan 3x57= 171 MW	U-1 to U-3	Uttarakhand/NTPC	171	Subject to re-start of works
4	Pakal Dul 4x250= 1000 MW	U-1 to U-4	Jammu & Kashmir/CVPPL	1000	
5	Luhri-I 2x80+2x25= 210MW	U-1 to U-4	Himachal Pradesh/SJVN	210	
6	Dhaulasidh 2x33=66 MW	U-1 to U-2	Himachal Pradesh/SJVN	66	
			Sub- total (Central):	2417	
	State Sector				
7	Lower Kalnai 2x24= 48 MW	U-1 to U-2	Jammu & Kashmir/JKSPDC	48	Subject to re-start of works
8	Koyna Left Bank PSS 2x40= 80 MW	U-1 to U-2	Maharashtra/WRD, GO Mah.	80	Subject to re-start of works
9	Polavaram 12x80= 960 MW	U-9 to U-12	Andhra Pradesh/Polavaram Project Authority	320	
			Sub- total (State):	448	
	Private Sector				
10	Kutehr 3x80=240 MW	U-1 to U-3	Himachal Pradesh/JSW Energy	240	
11	Panan 4x75= 300 MW	U-1 to U-4	Sikkim/Himgiri Hydro Energy Pvt. Ltd.	300	Subject to re-start of works
			Sub- total (Private):	540	
			Total (CS+SS+PS)	3405	


12876.5

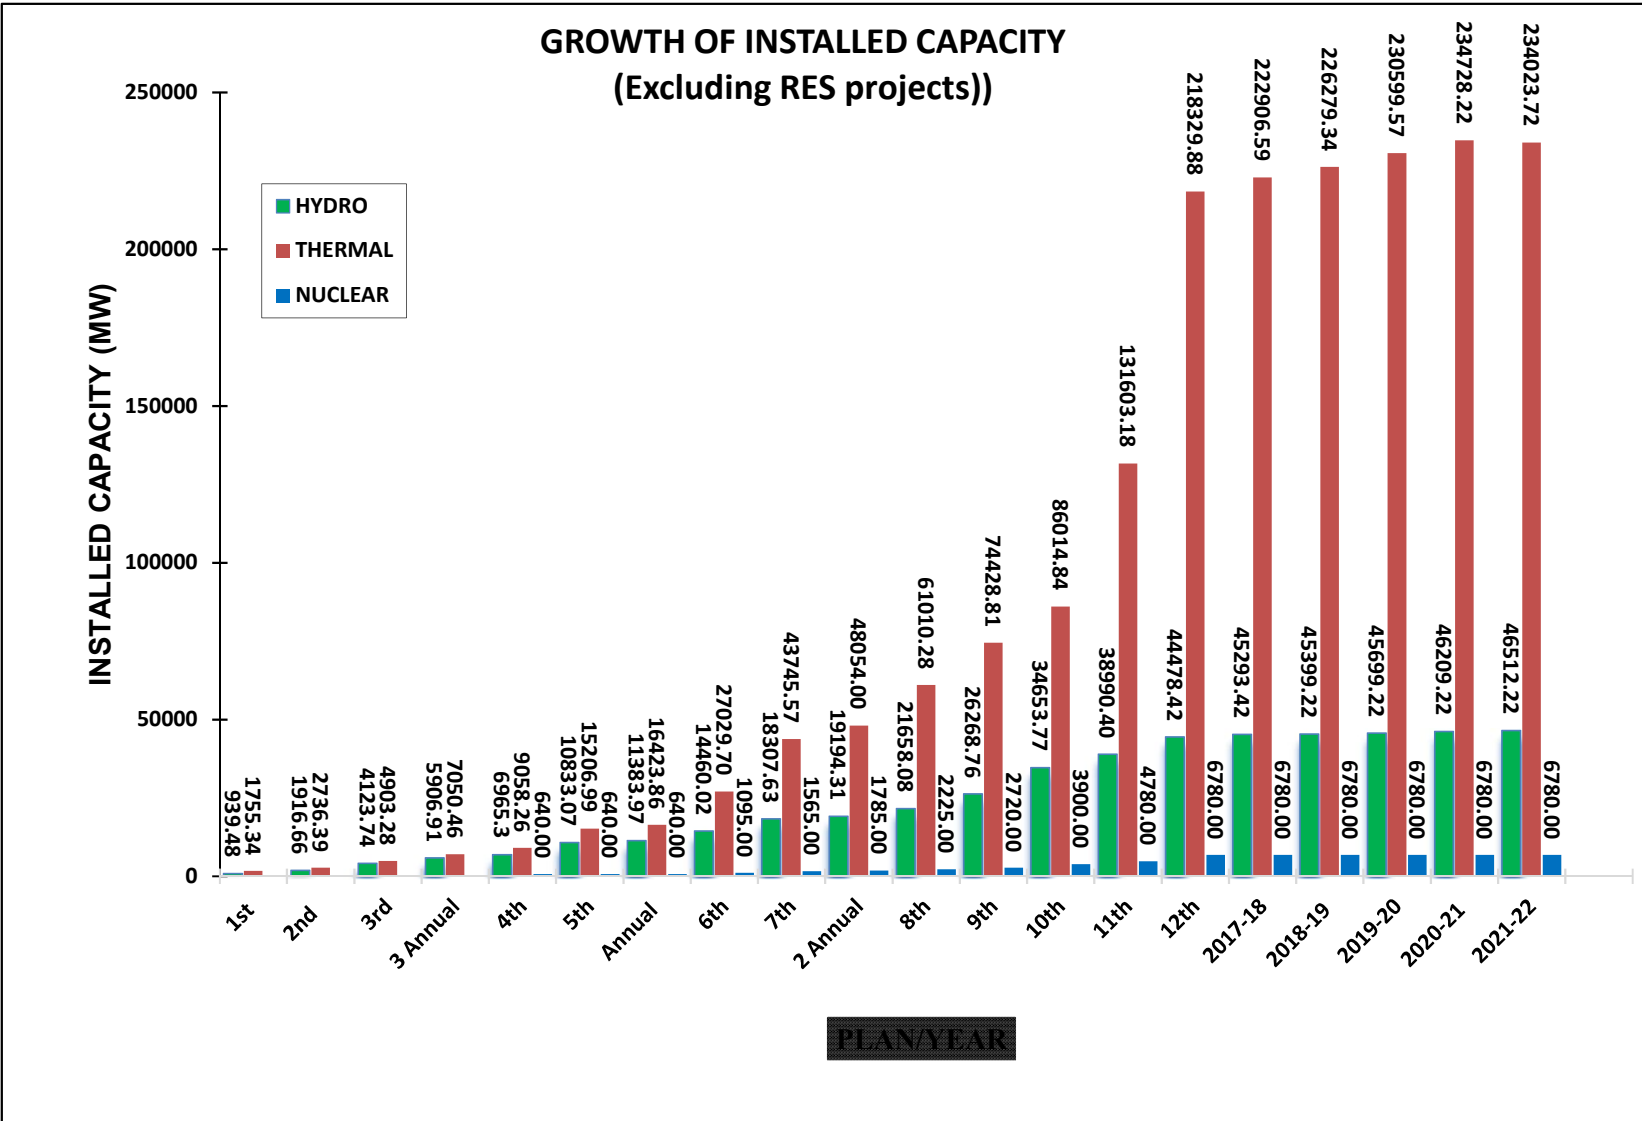

Growth of Hydro capacity in MW

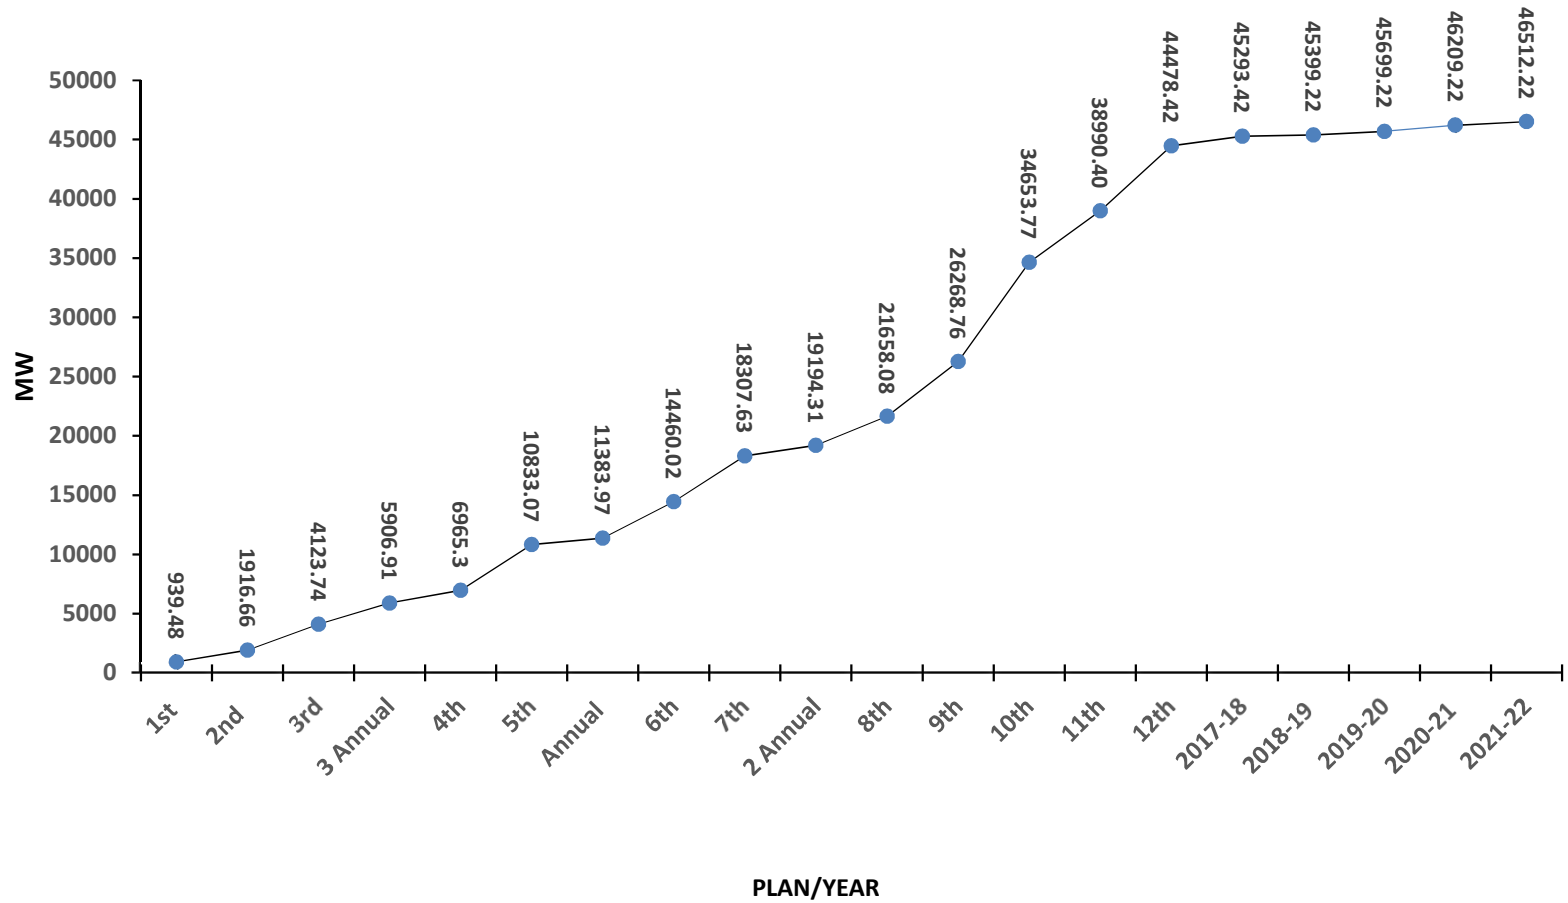

TREND OF CAPACITY ADDITION AS % OF TOTAL (Hydro Thermal Mix)

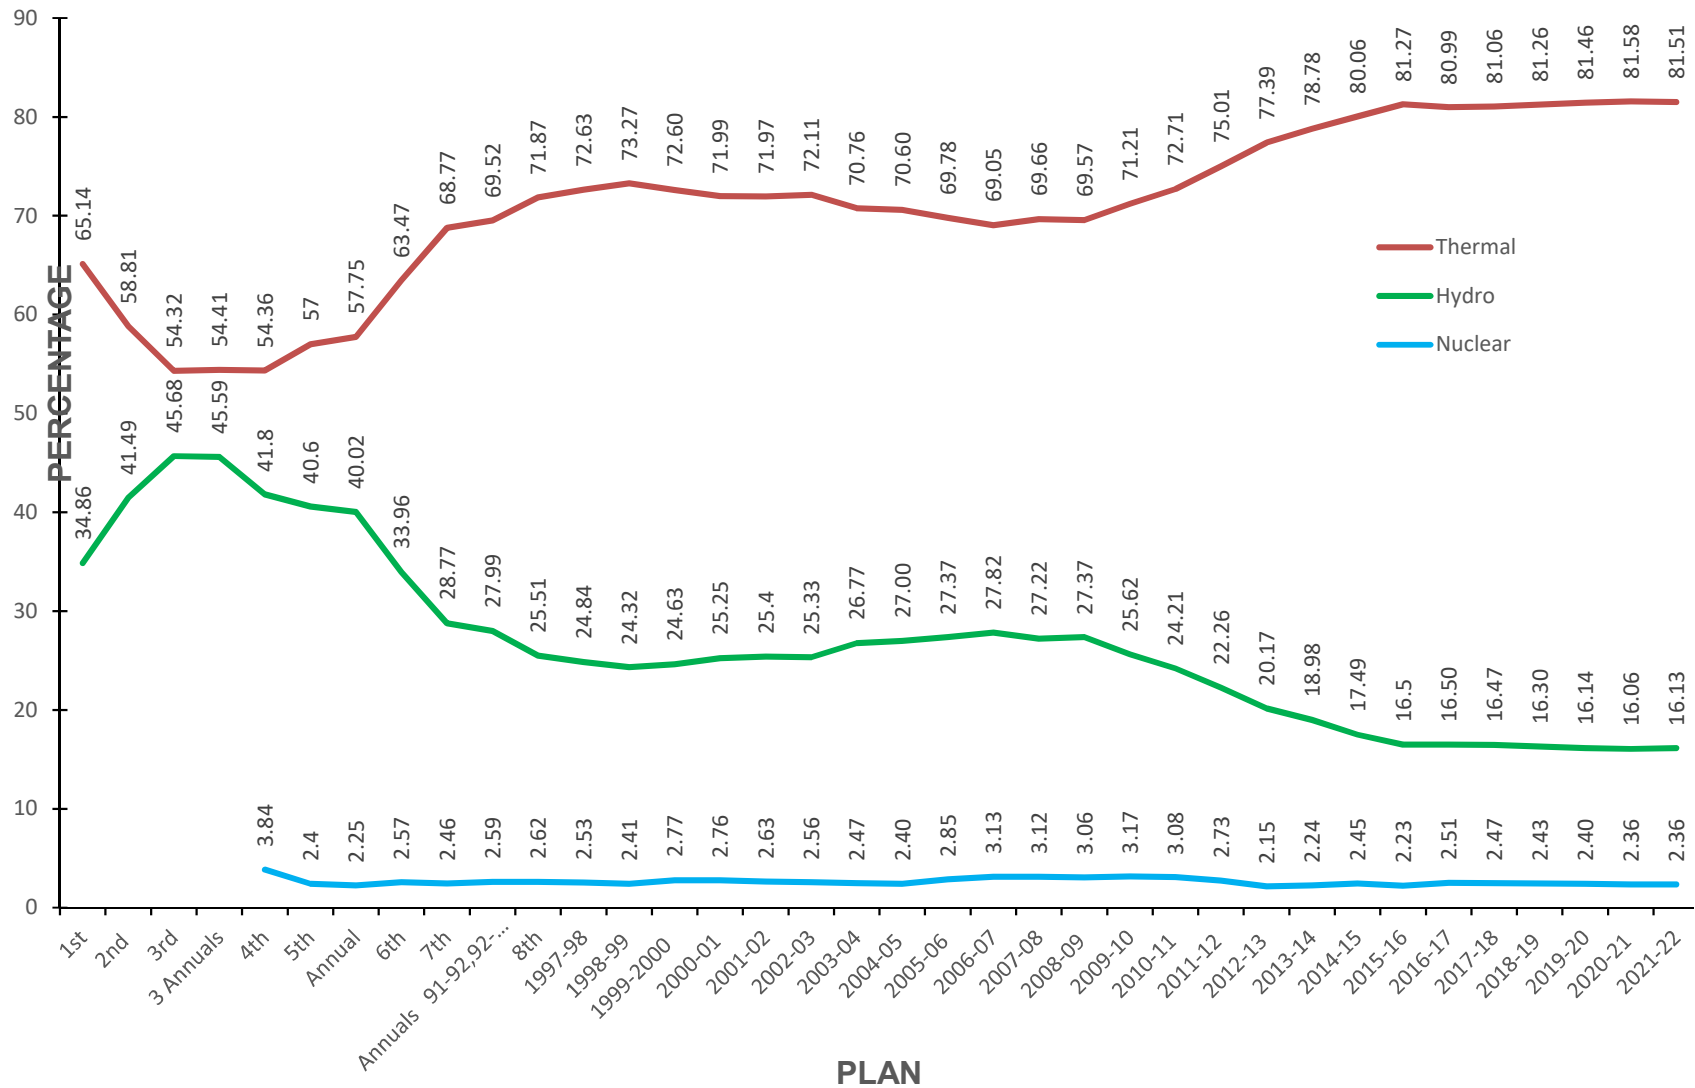

Chapter 5
Sanctioned Hydro Electric Projects for Construction
(Excluding projects under Ministry of New & Renewable Energy)

Sl. No.	Name of Scheme	State	I.C. (No. x MW)	Benefits (MW)	Date of Approval	Commissioned d/
Central Sector						
1	Pakal Dul (CVPPL)	J&K	4x250	1000.00	28.10.14	2025-26
2	Parbati St. II (NHPC)	H.P.	4x200	800.00	11.09.02	2022-23
3	Tapovan Vishnugad (NTPC)	Uttarakhand	4x130	520.00	11/2006	2023-24
4	Subansiri Lower (NHPC)	Ar. Pr./Assam	8x250	2000.00	09.09.03	2023-24
5	Tehri PSS (THDC)	Uttarakhand	4x250	1000.00	18.07.06	2022-23
6	Lata Tapovan (NTPC)	Uttarakhand	3x57	171.00	17.07.12	2025-26*
7	Vishnugad Pipalkoti (THDC)	Uttarakhand	4x111	444.00	21.08.08	2023-24
8	Naitwar Mori (SJVN)	Uttarakhand	2x30	60.00	16.10.17	2022-23
9	Ramam-III (NTPC)	West Bengal	3x40	120.00	10.09.14	2022-23
10	Teesta St. VI (NHPC)	Sikkim	4x125	500.00	08.03.19	2023-24
11	Ratle (Ratle Hydro) #	J&K	4x205+1x30	850.00	11.02.21	2025-26*
12	Kiru (CVPPL)	J&K	4x156	624.00	08.03.19	2024-25
13	Rangit-IV (NHPC)	Sikkim	3x40	120.00	06.07.07	2025-26
14	Luhri -I (SJVN)	H.P.	2x80+2x25	210.00	20:11:20	2025-26
15	Dhaulasidh (SJVN)	H.P.	2x33	66.00	01:10:20	2025-26
Sub- total (Central Sector) :				8485.00		
State Sector						
16	Parnai (JKSPDC)	J&K	3x12.5	37.50	21.10.13	2022-23
17	Lower Kalnai (JKSPDC)	J&K	2x24	48.00	16.08.13	2025-26*
18	Uhl-III (BVPCL)	H.P.	3x33.33	100.00	19.09.02	2022-23
19	Shongtom Karcham (HPPCL)	H.P.	3x150	450.00	16.08.12	2024-25
20	Vyasi (UJVNL)	Uttarakhand	2x60	120.00	25.10.11	2022-23
21	Shahpurkandi (PSPCL)	Punjab	3x33+3x33+1x8	206.00	04.05.11	2023-24
22	Koyna Left Bank (WRDMah)	Maharashtra	2x40	80.00	20.02.04	2025-26*
23	Indrasagar Polavaram (PPA)	Andhra Pradesh	12x80	960.00	25.02.09	2024-26
24	Pallivasal (KSEB)	Kerala	2x30	60.00	31.01.07	2021-22
25	Thottiyar (KSEB)	Kerala	1x30+1x10	40.00	05.06.08	2021-22
26	Kundah Pumped Storage-I (TANGENDCO)	Tamil Nadu	4x125	500.00	15.02.18	2023-24
27	Lower Kopli (APGCL)	Assam	2x55+2x2.5+1x5	120.00	Nov.2020	2024-25
Sub- total (State Sector) :				2721.50		
Private Sector						
28	Tidong-I (Statkraft India Pvt. Ltd.)	H.P.	2x50	100.00	28.07.06	2022-23
29	Tangnu Romai- I (Tangu Romai Power Genreation.	H.P.	2x22	44.00	30.11.07	2024-25*
30	Bajoli Holi (GMR)	H.P.	3x60	180.00	30.12.11	2021-22
31	Phata Byung (LANCO)	Uttarakhand	2x38	76.00	06.10.08	2024-25*
32	Maheshwar (SMHPCL) ##	M.P.	10x40	400.00	30.12.96	2023-24*
33	Bhasmey (GATI Infrstructure)	Sikkim	2x25.5	51.00	Dec-08	2024-25*
34	Rangit-II (Sikkim Hydro Power)	Sikkim	2x33	66.00	10.02.10	2024-25*
35	Panan (Himagiri Hydro Energy)	Sikkim	4x75	300.00	07.03.11	2025-26*
36	Kutehr (JSW Energy (Kutehr)Ltd.	H.P.	3x80	240.00	31.08.10	2025-26
Sub- total (Private Sector) :				1457.00		
Total - Under execution (as on 30.09.2021)				12663.50		
# Govt. of J&K, PDD have terminated PPA on 09.02.2017 and directed JKSPDC to take over the project. MoU between NHPC (51% share) & JKSPDC (49% share) signed for implementation of project in JV mode on 03.02.2019.						
## PFC as lead lender have acquired majority equity i.e. 51% in the SMHPCL w.e.f. 1st June, 2016. Matter Sub-judice.						
*Stalled Projects Commissioning subject to Re-Start of works.						

Chapter 6

Status of Under Execution Hydro Electric Projects (above 25 MW) in the Country

Sl. No.	Name of Project Executing Agency Date of CEA clearance / Approval Capacity (MW) Broad Features Cost (original/latest) In Rs. Crores.	State Comm. Sch. (original/ Now Ant.	Broad Present Status / Critical Area	Remarks/ Critical issues
A	Central Sector			
1	Parbati-II NHPC 11.09.2002 4x200 = 800 MW Broad Features : Dam – 85m High, 109. m long at top, concrete gravity type HRT- 6m x 31.23km P.House- Surface 23.5mx 39.7mx 123m. Turbine- Pelton Swyd.- 13.8/400 kV Cost: <u>Original:3919.59</u> Latest: 9897.59 (04/20 PL) Contractors Civil : Gammon / Valecha HM : Om Metals E&M : BHEL	<u>H.P.</u> <u>2009-10</u> 2022-23 (March'23)	Dam & Intake Structure (91m high and 3.7m D-shaped intake structure) - Completed. Head Race Tunnel (6m diameter, 31.526Km long) – 30.17 km (95.71%) excavation out of 31.526 km completed. TBM excavation resumed since 16.10.2015 and 2669.82 m advancement has been made till 31.08.2021. Excavation of HRT at face-3 by DBM commenced after mobilization with first blast on 3rd Jan'2021 and 646.85 m excavation has been done till 31.08.2021.. Works at Face-3 has got hampered due to heavy ingress of water at the Facesince 12.07.2021. Efforts are being made for speedy dewatering of tunnel and early resumption of excavation works. Total Overt lining: 27.67 km (88%) lining out of 31.526 km completed. Power House (23.5m x 39.7m x 123m size): Completed. Nallah Works I. Jiwa Nallah Feeder Tunnel: Completed. II. Hurla Nallah Works: Water of Hurla Nallah has been successfully diverted into HRT on 30.09.2020. III. Manihar Nallah Works: Water of Manihar Nallah diverted into Pancha Nallah on 18.08.2021. Pancha Feeder Tunnel: 740.2m out of 770m excavated. Civil works for Pancha Nallah Diversion works are in progress. E&M Works: All the Units were Synchronized with grid at part load using water from Jiwa Nallah. After fire incident on 29.07.2020, generation got suspended. After restoration works, Unit#1 &2 synchronized with grid on 17.08.20 & 29.08.20 respectively and generation restored. Restoration works of remaining 02 units are in progress. HM Works: All the major HM works completed.	• Completion of 1.35 km balance HRT • Works at HRT Face-3 hampered due to heavy ingress of water at Face since 12.07.2021. Efforts are being made for speedy dewatering of tunnel and early resumption of excavation works.
2	TapovanVishnugad NTPC 11.08.2004/Nov, 2006 4x130 = 520 MW Broad Features : Barrage–5 bays of 12m HRT- 5.4m x 11.97km P.House- underground Turbine- V.Pelton Cost: <u>Original: 2978.48</u> Latest:5867.38 Contractors Civil : Rithwik Projects Pvt. Ltd. (RPPL)/HCC / Patel engineering ltd HM : Om Metals E&M : BHEL	<u>Uttara khand</u> <u>2012-13</u> 2024-25	Barrage: Excavation Completed and Concreting 127628 cum out of 129358 cum completed. HRT: Excavation of 2.79 km out of 3.81 km by DBM & 5.50km out of 8.27km by TBM completed. 6.61 km concrete lining out of 12.09km completed PH Cavern: Excavation and concreting completed. Desilting Chamber & Intake: Excavation and concreting completed. TRT: Excavation and lining completed. Surge shaft: Excavation & Lining completed. Penstock: Excavation and Lining completed. E&M works: Pit liner erection on all 4 units completed. Turbine housing erection of all 4 units completed. Unit #1: Boxed up. Unit #2: Boxed up. Unit #3: Turbine erection completed. Unit #4: Turbine erection in progress. Bus Duct: Erection of all units completed	-Completion of HRT./ Barrage Restoration Works -Associated Transmission system -Due to flash flood in Dhauri Ganga River on 07 Feb 2021, construction work is held up.

			Critical : HRT On 07.02.2021, there was a sudden flash flood in Dhauli Ganga river due to an avalanche resulting in part damage to NTPC hydro power plant. A detailed analysis is to be done to assess the extent of physical and financial damage to the project. A team of Expert(ToE) from CWC, CEA, GSI, CSMRS and NTPC have been constituted for preparing action plan for restoration of project. Panel of Experts (PoE) comprising members from CWC, NHPC, NTPC and THDC visited sites on 21-22nd Feb 2021. Further, A Team of Experts (ToE) headed by CWC and members from CEA, CSMRS, GSI and NTPC also visited Site during 16 to 18th March 2021. The rescue cum restoration works have been taken up in line with their recommendations. A warning system is operational at the project site and further the process of design and installation of a comprehensive Early warning system in process.	
3	Tehri PSS, THDC, 18.7.06 Nov-11 (Revised CCEA) 4x250=1000 MW Broad Features : Surge Shaft: U/s – 2 nos. D/s – 2 nos Power House: U/G TRT: 2, Dia 9m and Length 1070m & 1160m Turbine: VF reversible pump turbine Cost: Original: 1657.60 Latest: 4835.60 (02/2019 PL) Contractors Turnkey : Alstom, France/ HCC	<u>Uttara</u> <u>khand</u> <u>2010-11</u> <u>2023-24</u> (Dec'23)	Upstream (Tehri Dam) and Downstream (Koteshwar Dam), intake and Head Race Tunnels (2 Nos.) already completed along with Tehri Stage-I works. Widening of Upstream Surge Shaft-3&4 (Depth 140m each): Cumulative widening completed in a depth of 104.0 m and 112.0 m respectively. Downstream Surge Shaft-3&4 (Depth 80.9 m each): Widening of DSSS-3 & 4 has been completed. Butterfly Valve Chamber (BVC 78X10X26m): Excavation completed. Penstock Assembly Chamber (PAC 95X12X19.30 m): Excavation completed. Upper Horizontal Penstocks (UHP): Excavation of UHP-5 & 7 (Scope: 35 m each) has been completed and in UHP-6 & 8 (Scope: 45 m each), UHP-6 completed and UHP-8 completed upto 34.0 m. Vertical Penstocks (4 Nos. each of Dia 6.1 m and 135 m depth): Widening of vertical penstock 5, 6, 7 & 8 is in progress in PAC and completed in a depth of 72.8 m, 27.8m, 102.8 m & 56.8m respectively. Power House (203m x 28.20m x 56m size): Excavation completed and erection of EM equipment is in progress in all 4 units. Control Room: All 9 slabs have been casted. Further, cleaning work is in progress and architectural works are being taken up. Tail Race Tunnels- 3 & 4 (2406 m): Excavation: -Heading & Benching: Completed 2123 m & 1680 m respectively. Lining - Invert & Overt: Completed 1427.9 m & 626.6 m respectively. E&M Works: Both EOT cranes have been commissioned in service bay .	- Poor Geology in under ground works of BVC, PAC, TRT, PH Cavern etc. - Slow progress of works - Cash flow crisis with M/s. HCC.
4	Lata Tapovan, NTPC Aug-2012 3x57= 171 MW Broad Features :	<u>Uttara</u> <u>khand</u> <u>2017-18</u> <u>2025-26</u> (Subject to re-start of	Infrastructure works are almost completed. Main works to re-start after clearances from Hon'ble Supreme Court. EPC contract for Civil & HM works awarded to M/s L&T on 17-08-2012. E&M package awarded to M/s BHEL on 07.12.12.	Construction work stopped vide Hon'ble Supreme Court order dated 7.5.14. Clearance from Hon'ble Supreme Court for resumption of works.

	Barrage–14 bays of 11m each HRT- 7.51 Km, 4.7m dia P.House- underground Turbine- V.Francis Cost: <u>Original: 1527.00</u> Latest: 1801.07 Contractors Civil & HM : L&T E&M : BHEL	works)	MoWR vide letter dated 24.01.2019 to MoEF has communicated that only 7 out of 51 Hydro Projects which are under various stages of construction in Uttarakhand has been recommended for implementation. LataTapovan project is not included in the 7 recommended projects. ➤ Barrage (29 m high)-Not started yet. ➤ Desilting chamber (135 m L x 33m W x 17.5 m H)--Not started yet. ➤ HRT (4.7 m diameter, 7.51 km long)-Not started yet. ➤ Surge Shaft (7 m diameter 144.8 m height)-Not started yet. ➤ Pressure Shaft (3no. 2.0 m diameter 297 m long)-Not started yet. ➤ Power House (85mx 17mx 40.5m)-Not started yet. On 08.07.2020, Director /Conservator forest NDNP, submitted report to Chief Conservator forest Dehradun for LTHEPP mentioning that as per revised notification, project is out of ESZ boundaries.	
5	Vishnugad Pipakoti THDC 21.08. 2008 4x111= 444 MW Broad Features : Dam – 65m High, 89.3m long, concrete gravity HRT- 13.4 Km, 8.8m dia Horse shoe shape P. House-Underground 127mx 20.3mx 50m Turbine- Francis SWYD- 13.8/420 kV Cost:<u>Original: 2491.58</u> Latest:3860.35 (02/2019 PL) Contractors Civil &HM : HCC E&M : BHEL	<u>Uttara</u> <u>khand</u> <u>2013-14</u> <u>2024-25</u> (Jun.'24)	River diverted on 02.04.2018. Concreting of U/S coffer dam has been completed. TBM has been commissioned on 24.11.19. Desilting Chambers:-Heading of all 3 De-silting Chambers has been completed and benching 45.49% completed. HRT :Heading excavation of 810m out of 960m by DBM has been completed. TBM has been commissioned. During operation of TBM in the RBM zone, big boulders have been encountered, which has hampered TBM operation. To overcome this problem two Approach Adits are being constructed to reach the cutter head. Bypass Adit has been completed 20.5 m (Rib support 20m) out of 67m and work is in progress. Additional Bypass Adit has been completed in full length and Rib support completed for 32.6m out of 34.5m. Power House: In Machine Hall, crown excavation has been completed and strengthening of geologically weak section with steel rib supports is in progress. Transformer Hall, 124.5m crown excavation completed (out of 140m). Balance work in progress. TRT :- Heading excavation 508m out of 3070m completed. At TRT outlet area, 80% slope stabilization work has been completed	-Frequent disruption of works by local people. - Cash flow crisis with M/s. HCC.
6	Subansiri Lower NHPC 09.09.2003 8x250= 2000 MW (1000 MW in 12th Plan) Broad Features : Dam –116m High, concrete gravity HRT- 8 x 9.5m x 1145m Power House- Surface Turbine- Francis SWYD- 16/400 kV Cost: <u>Original: 6285.33</u> Latest:19992.43 (04/17 PL) Contractors Civil : BGS-SGS-Soma JV HM : Texmaco E&M : Alstom	Arunachal <u>Pradesh</u> Assam <u>2009-11</u> <u>2022-24</u> (Unit#1&2 in 2022-23 and Unit#3-8 in 2023-24)	➤ Dam (116m high and 284m long):- Dam concreting 14.68 lac Cum (70.9%) out of 20.70 lac Cum & Intake concreting 270272 cum (97%) out of 279454 cum completed. ➤ HRT (9.5m diameter):-98.5% heading excavation, 85.8% benching excavation, 65.8 % concrete overt lining and 39.7 % Invert lining completed. ➤ Surge Tunnel (8 nos., 9.5 M dia, Horse Shoe):-Heading excavation 87.4% & benching excavation 31.4% completed. ➤ Pressure Shaft (8 nos. 9.5/8/7 dia):- PS liner 313m (19.6%) out of 1594m completed. ➤ Power House (285m x 61m x 64m size):- Cumulative concrete qty achieved 173794 cum out of 512000 cum (33.9% achieved so far). ➤ E&M Works: - Concreting of Generator Barrel of Unit#1 and 2 already completed. Unit-1: Turbine Stay Ring and Spiral Case erection completed.	Project progress hampered during FY 2021-22 due to the following: •Due to fear psychosis of Covid situation and District movement restrictions affected the availability of manpower at site. •Water overtopping from Dam during Aug'21 and heavy rainfall during Aug'21 Issue: Signing of PPA is pending with Govt. of Delhi.

			Unit-2: Turbine Stay Ring and Spiral Case erection completed. Unit-3: Erection of Draft Tube (part 2 to 6) of Unit#3 already completed. All 28 nos. transformers have reached at site. 8 no. GSU transformers have been shifted to Powerhouse. Erection of EOT crane rail in Power House (for Unit - 1&2) completed. Erection work of Unit-1 is in progress (Stator and Rotor assembly is in progress). Other works like Cable tray installation at Turbine & Generator floor, cooling water pipeline work etc in progress. ➤ HM Works: Erection of Diversion Tunnel Gates: 96.66 % completed. Erection of Intake Gates: 76.48% completed. Out of total 1594m, 313 m pressure shaft steel liner erected. Fabrication and erection work of Pressure shaft liner is in progress.	
7	Teesta-VI NHPC 08.3.2019 4x125= 500 MW Broad Features: Barrage: 26.5m high HRT- 2nos, 27.52km long Pressure shaft: 4nos. 5.4m dia. 151m to 198m length, TRT: 4nos 247m each length, 7.5x7.0m D-shaped. PH- Under ground Turbine- Francis Cost: Original: 3283.08 Latest : 5748.04 (07/2018 PL) Contractors Civil : JAL & Gammon E&M : Alstom	<u>Sikkim</u> <u>2012-13</u> 2023-24 (Mar'24)	(A) Civil Works (a) Barrage: The concreting of Barrage Bay No 1 & 2 has been completed along with bridge at barrage top i.e. EL369.0m. The concreting of the Barrage bays 3 & 4 has been completed upto the radial gate. (b) De-silting Arrangement: Underground silt flushing tunnel of size 4.0 x 4.4 m D shape of approximately 3.3 km has to be constructed. Only outlet portal and 55m tunnel has been excavated, remaining is yet to be taken up. (c) Head Race Tunnel: Heading excavation of approx.11.04 km executed out of total 27.52 km, benching excavation of approx.4.27km and Overt Lining of approx.1.55 km has been completed. (d) Surge Shaft: Surface excavation in the surge shaft area including excavation in slope and benches along with its protection work has been completed. Excavation for both the surge shafts has been completed and concreting of orifice slab for Surge Shaft SS-1 has been completed. Lining work for Surge Shaft 1 & 2 is partially completed. (e) MIV Cavern: Excavation of MIV cavern is completed. (f) Power House: Excavation is completed for powerhouse cavern, transformer cavern, MIV chamber, main access tunnel, ventilation tunnel, cable tunnel and gate shaft. Columns and beams for EOT crane in Service bay, Unit-I & II completed. Columns in the balance portion of the power house cavern partly completed. Concreting works up to pedestal of spiral casing of Unit I is completed. (g) Transformer cum GIS cavern: Excavation is almost completed for Transformer cum GIS cavern and adit to the cavern. Partial excavation of cable tunnel has been excavated. (h) Downstream Surge Chamber: Excavation of Adit has been completed; however concrete lining is still to be taken up. (i) Tail Race Tunnel: Excavation of all four tail race tunnel (TRT-I, TRT-II, TRT-III & TRT-IV) have been completed leaving the required plugs of 20m length at the river end. The concrete lining of all four TRT's are completed leaving a small patch near the junction as per the excavation plan. (B) HM works: (a) Barrage Radial Gates:	The Project was earlier allotted by Govt. of Sikkim to M/s Lanco Teesta Hydro Power Ltd (LTHPL) promoted by the Lanco Group but the ongoing project works got stalled due to financial crunch faced by M/s LTHPL. Accordingly, the Corporate Insolvency Resolution Process (CIRP) was initiated vide order dated 16.03.2018 of Hon'ble NCLT, Hyderabad Bench. In the Bidding process, NHPC emerged as successful bidder for acquisition of LTHPL. Subsequently, the investment proposal for an estimated cost of Rs 5748.04 crore (Jul'18 PL), which includes Bid amount of Rs 907 crore for acquisition of LTHPL; estimated cost of balance work of Rs. 3863.95 crore and IDC & FC of Rs. 977.09 crore with completion period of 60 months was approved by the CCEA on 08.03.2019 for investment, acquisition of M/s LTHPL and execution of balance works of Teesta-VI HE Project by NHPC. The consideration amount of Rs. 897.50 Crore was released by NHPC on 09.10.2019 and the Company was taken over along with all assets and documents as a 'Going concern' completed w.e.f. 09.10.2019. Lot-I Civil works of Barrage, Desilting Basins, SFT, Intake, Part HRT-I & HRT-II and other associated structures was awarded to M/s. Jaiprakash Associates Ltd (JAL) on 31.03.2020; LOT-II Civil works of Part HRT-I & HRT-II, Surge shaft, Pressure shaft, Powerhouse, TRT & other associated structures is under re-tendering and technical evaluation is under process and price bids will be opened after security clearance from MHA. Lot-III- HM works was awarded to M/s PES Engineers Pvt. Ltd on 27.10.2020. E&M works (08 packages) have been tendered and till date 07 No. packages have been awarded to M/s GE Power (EM-I:

			i. Erection of Barrage Radial Gate No. 1 and 2 without flap has been completed and gate is in dogged position without rubber Seals. ii. All major component of Radial gate No. 3 & 4 with flap has been supplied at site. (b) Barrage Stoplogs: i. Upstream stoplogs: 4 sets of upstream stop logs fabricated. ii. Downstream Stoplogs: 3 sets of Downstream stoplogs out of 4 found fabricated. (c) Gantry Crane & Lifting Beam for Barrage Stoplog: Upstream stop logs: One stoplog gantry crane for upstream stoplogs is installed with lifting beam which require repairs to be made operational. (d) Installation of ferrules in vertical section of 1 no. Pressure shaft has been completed. (e) Supply of four Radial gates and Stoplogs (First Stage & Second Stage Embedded Parts, Gate Parts and Hoists) for the Barrage received at Site. Most of the materials for Pressure Shaft Liners received at Site from which fabrication of ferrules have been completed. (C) E & M works: Erection of Spiral Casing-Unit 1 is completed; 2 no. 200 MT. EOT cranes have been installed and refurbishment for the same is under progress; Earth Mat laying work has been completed; Cooling Water System embedded piping is completed; Most of the materials of Major T-G Package-EM-I (Turbine, Generator, MIV, Governing System, Excitation System, Control & Monitoring System and Protection System has already been supplied by M/s GE Power.	Turbine & Generator)), M/s BHEL (EM-II: Transformer & GIS), M/s Technico (EM-III: Fire Fighting), M/s SHES Air & Automation (EM-V: HVAC), M/s Aviads (EM-VI: Illumination), M/s PGCIL (EM-VII: Associated Transmission System), & M/s BC Technomation (EM-VIII: Drainage & Dewatering system). Balance E&M package EM-IV for DG Sets is under technical/commercial evaluation stage. Civil contractor (M/s JAL) for the Lot-I works, E&M-I contractor (M/s GE Power), HM contractor (M/s PES Engineers) & contractor for refurbishment of 02 No. EOT Crane (M/s Cranex) have already mobilized at Site. The works of other E&M contractors viz. M/s Technico, M/s Aviads, & M/s BC Technomation are under design approval stage. Further specialized agencies i.e. M/s Bauer for Jet Grouting & slope stabilization works and M/s Divya Construction for concrete cutting with diamond wire saw technology under Lot-I Civil works have also mobilized at Site. The progress of works have been hampered on account of 1st & 2nd wave of Covid-19 and have been subjected to series of lockdowns and restrictions imposed by Central/ State Govt. However LTHPL is making efforts to expedite the balance works to the extent possible.
8	Rammam-III NTPC Hydro Ltd. 10.09.14 3x40 = 120 MW Broad Features : Run of the River Scheme Cost : Original: 1381.84 Latest : 1592.34 Contractors Civil & HM : Simplex-Apex JV / SEW E&M : BHEL	<u>West Bengal</u> <u>2019-20</u> <u>2024-25</u> (Dec,24)	First stage river diversion done on 23.03.2016. First phase Barrage excavation completed and Raft concreting in progress. Intake structure 1 & 2: Excavation completed, SFT excavation 20% completed. HRT: Till date 1606 m HRT have been excavated (588 m from Adit-1 and 1018 m from Adit-3). Adit-2 excavations of 319 m has been done and work in progress. Excavation of Desilting chamber completed. Surge Shaft: Excavation completed. Pressure Shaft: Excavation 50% completed Power House: Excavation 94% completed. TRC: Excavation and concreting completed Switchyard : Excavation and filling completed E&M Works: 37 out of 41 Tower Erection completed. Laying of 40% earthing mat is completed. Equipment erection started.	Signing of PPA/ATS: - Clearance for signing of PPA by West Bengal Govt. awaited. Power Evacuation line/ ATS also not getting finalized due to pending decision for PPA. Acquisition of supplementary Land: - NTPC Board approved direct purchase of additionally required 14.75 acre of private land on 22.03.2017. Received NOC from Ministry of Power, GoI on 23.04.2019. For 1st & 2nd Phase land acquisition (7.864 acre+ 1.87 acre), cabinet approval & GTA purchase committee gazette notification has been done in Jan'2021. District land purchase committee meeting held on 20.07.2021. Demand note for land purchase and associated cost to be placed after the valuation of house and trees.
9	Naitwar Mori SJVN Limited 16.10.2017	<u>Uttarakhand</u> <u>2021-22</u>	➤ Barrage (30.5m high above deepest foundation, Length at top 48.9m):- Barrage excavation 1,37,875 cum (98%) out of 1,40,000 cum	➤ Completion of Powerhouse/ Barrage ➤ Power Evacuation system

	2x30=60 MW Broad Features : Barrage: 30.5m height HRT: 5.6m horse shoe, 4330m long Pressure shaft: 4m dia, 109m long Surge shaft: 18m dia, 51.65m height Cost : Original: 648.33 (10/2016 PL) Latest : 947.89 (12/2020 PL) Contractors Civil : JP Associates HM : GMW E&M : Voith	2022-23 (Jun,22)	completed. Concreting:33378 cum (77.51%) out of 43065 cum completed. Desilting tank excavation completed. Concreting: 31824 cum (54%) out of 59000 cum completed. ➤ Diversion channel completed. ➤ HRT- (5.6m modified Horse Shoe Shape, 4329 m long):- Excavation of HRT completed, Lining:1685 m (38.92%) completed. ➤ Surge Shaft (18m dia, 50.28m height):- Excavation: 38 m (75.58%) out of 50.28 m completed. ➤ Pressure shaft (4.0m dia, 97.50 m long):-83 m (85.13%) excavation completed. ➤ Power House (Underground 57.70m x 18.60m x 33.07m size):-Excavation of Power House cavern: 53185 cum (98.04%) out of 54250 cum completed. ➤ Tail Race Tunnel (D-shaped, 8.0m (W) x 8m(H), 235.62m long, TRC-6.0m(W)x5.75m(H), 60.39m long):-Excavation of TRT completed. Outfall structure completed. Tail race channel work is in progress.	
10	Pakal Dul CVPPL 03.10.2006 4x250 = 1000 MW Broad Features : Dam – 167m High, Width-305m), CFRD, HRT- 2 nos. 7.2m dia 1000m long S.Shaft-16m dia 200m Height P.House- Underground (157mx20.20mx49m) TRT- 5.5m dia, 125m long. Cost: Original:8112.12 Latest: 8112.12 Contractors Civil : Afcons – JAL – JV L&T,JAL HM: PES E&M : Voith Hydro Ltd	<u>J&K</u> <u>2020-21</u> 2025-26 (July.'25)	Gross physical achievement is 21.59%. The details are as under: ➤ Dam Package (CFRD 167m high and 305m width).- LoA issued to M/s Jaiprakash Associates on 21.6.2018 at a cost of Rs.2853 crores. Access adit to HRT-1 and HRT-2 have been completed of a total of 698.2 m. 1368.50m excavation of HRT- 1 & 2 have been completed out of a total of 4117m Diversion Tunnel (1 no, diameter 11 m, length 851 m):-Works started on 31.12.2018..Excavation in Heading and benching completed. Concrete lining(invert) of 827m have been completed out of a total of 851m. Concrete lining (overt) of 827m have been completed out of a total of 851m. Further, inlet structure works as well as other works for Diversion of river are in progress. ➤ HRT-TBM Package (HRT 2Nos., 7.2m dia, 9.6 km long each (7.3 Km through TBM))- LoA issued to M/s L&T Ltd on 3.7.2020 at a cost of Rs.2575.63 crores. Contract agreement signed on 14.08.2020. Construction of TBM Adit Portal, development of platform and associated infrastructure works are in progress Detail Engineering of TBM and Segment design are in progress. Two nos. of TBM have also been ordered by the contractor. ➤ Hydro Mechanical Package- LoA issued to M/s PES Engineers Pvt. Limited on 26.08.2019 at a cost of Rs 286.58 Crs.Detailed Engineering/manufacturing as well as supply of HM components are in progress. ➤ Electro Mechanical Package-Letter of Award issued to M/s Voith Hydro Limited on 2.1.2019 at a cost of Rs.689.76crores. Detailed Engineering of E&M equipment's including submission/checking of drawings, layout plan etc and equipment manufacturing/inspection/supply at site are in progress. ➤ Power House Package (PH Cavern 166m (L) x 20.2 m(W) x 50.5 m(H))- LoA issued to M/s Afcon –JP Associates JV on 21.2.2018 at a cost of Rs. 1051 crores. Construction work at the site is in progress. UG Excavation of Power House Cavern is in progress - 98% work completed Surge Shaft (16m diameter 200m height)	HRT & Dam works are critical.

			Construction of access road to SS top from TBM platform completed. Adit to surge shaft bottom 1 completed and excavation of Adit to SS Bottom-2 is in progress. Raise Borer for boring of Pilot Hole of Surge Shaft has been placed successfully on 10.08.2021 ➤ Pressure Shaft (Pressure Shaft-6.0 m dia-423.45m (Horizontal); 3.9 m dia- 1528.7m (Horizontal & Vertical): Excavation of adit to Pressure Shaft bottom & top has been completed. Excavation of Penstock Bottom Horizontal Portion (From MIV to PH side) is completed. Raise Borer for boring pf pilot hole of vertical PS of 291m (PS-4) has been placed successfully on 10.07.2021 and boring commenced on 16.07.2021. 113m progress achieved till date. Transformer Hall: UG Excavation Transformer Cavern – 97% work completed MIV - UG Excavation MIV Cavern - 95% work completed. Concreting of MIV cavern started	
11	Kiru CVPPL 13.06.2016 4x156=624 MW Broad Features : Dam – 135m High, Width-193m), Concrete gravity, Penstock 4nos., 5.5m dia. P.House- Underground (182mx23.6mx51.2m) TRT- 4 nos., 7.0m dia, 165 to 190m long. Cost: <u>Original:</u>4287.59 Latest: 4287.59 Contractors Civil : Patel Engg. HM: PES Engineers E&M : Andritz Hydro	<u>J&K</u> <u>2023-24</u> 2024-25 (Aug.'24)	Gross physical achievement is 10.02%. The details are as under: ➤ Construction of approach roads for Dam top (215m), DT inlet (1.6Km) & outlet (1.2Km) completed. ➤ Dam (135mhigh and 193m width): ➤ Civil works Package-Letter of Award issued to M/s Patel Engg. Limited on 24.02.2020 at a cost of Rs.2240.27 crores.Contract agreement signed on 15.6.2020. Diversion Tunnel works, Excavation of Main Access Tunnel and Adit to Pressure Shaft top & Bottom is in progress.. Dam abutment stripping is in progress. • Diversion Tunnel (1 no, diameter 9 m, length 666 m): Diversion tunnel day lighted on 01.03.2021. DT benching - 610m progress achieved against 666m total length. Overt concreting of DT is also in progress and 156m progress achieved ➤ Hydro Mechanical Package-Letter of Award issued to M/s PES Engineers Pvt. Limited on 24.02.2020 at a cost of Rs.202.10 crores. Contract agreement signed on 11.06.2020. Detailed Design Engineering/manufacturing of HM components is in progress. ➤ Electro Mechanical Package-Letter of Award issued to M/s Andritz HydroPvt. Limited on 24.02.2020 at a cost of Rs.552.52 crores. Contract agreement signed on 22.06.2020. Detailed Design Engineering/manufacturing of E&M equipment is in progress. ➤ Pressure Shaft (4 Nos., Internal Diameter : 5.5m , 316.0m to 322.0m Length) Excavation of Adit to Pressure Shaft top& Bottom is in progress and progress of 197m and 168.4m against total length of 370m and 336m achieved respectively. • Power House (182m (L)x 23.6m(W) x 51.2m(H))– Power House Pilot Excavation (182m) is completed. • Transformer Hall Cavern – TC pilot excavation (137 m) is completed ➤ TRT (4 nos., 7m diameter, varies from 165.0m to 190.0m)	The project is in initial stage of construction.

12	Ratle Ratle Hydro Electric Project Pvt. Ltd. / NHPC 19.12.2012 4x205+1x30= 850 MW Broad Features : Dam Height-133m Length-194.8m Spillway-Radia Gate-(5) Size-10.75x1420 m Diversion Tunnel:2 Nos., Circular (Right back) Pressure Tunnel:11m dia each. Pressure Shaft : 6.6 m each steel lined. P.House-Underground Turbine- Francis Average Gross Head-100.39m Addl. Unit(30MW) Housed in Main P.H. Cavity) Rated Head-98.9m Cost : <u>Original: Rs 5281.94 Crore</u> <u>Latest Rs. 5281.94 Crore</u> Contractors Civil & HM : GVK E&M : Alstom	<u>J&K</u> <u>2017-18</u> <u>2025-26</u> (Subject to re-start of works)	- Govt of India and Govt of UT of J&K decided to execute the Ratle HE Project through a Joint Venture between NHPC & JKSPDC. A Tripartite Memorandum of Understanding (MoU) was signed on 03.02.2019 and further a supplementary MoU was signed on 03.01.2021 for formation and incorporation of a Joint Venture Company (JVC) between NHPC and JKSPDC with equity contribution of 51% & 49%, respectively. - The Promoters agreement between NHPC & JKSPDC was signed on 13.04.2021 for the formation of JV. - The JV has been incorporated as Ratle Hydroelectric Power Corporation Limited on 01.06.2021. - JV Board approved the proposal for entrusting NHPC to undertake EPC (Single Package Turnkey mode) Tendering for execution of Ratle HEP in its meeting held on 05.07.2021. - EPC Single Package (Turnkey) tender for execution of 850 MW Ratle HE Project has been uploaded on cppp portal by NHPC on behalf of RHPCL on 22.07.2021. <u>Project Background- Works done by Previous Developer:</u> - The Project was previously allotted by Government of Jammu & Kashmir (GoJK) to M/s GVK Ratle Hydroelectric Project Pvt. Ltd. in May 2010. The Detailed Project Report (DPR) prepared by M/s GVK Ratle Hydroelectric Project Pvt. Ltd. was appraised by Central Electricity Authority (CEA) vide O.M dated 19.12.2012. - The preliminary works, such as, construction of access roads, bridges and diversion tunnel were started in 2013. But work was stopped in July 2014 due to various issues between M/s GVK & GoJK. - GoJK terminated award of the project/PPA with M/s GVK Ratle Hydroelectric Project Pvt. Ltd vide its Letter dt. 09.02.2017. Further, state Govt. decided to develop the project through JKSPDC. <u>Civil works (executed earlier by GVK):</u> ➤ Upstream bridge completed. ➤ Upstream roads, Downstream access roads and road from upstream to downstream have been completed. ➤ Diversion Tunnel (2 nos. Each of 11m dia, 472m & 552m long):- Excavation of DT1 298m (63%) out of 472m and DT2 192m (35%) out of 552m completed. ➤ Dam (133m high):- Not started ➤ Pressure Shaft (4nos. 6.6m diameter 211m, 197m, 184m, 172m long for main units, 1 no., 3m dia, 162m long for aux. unit):- Not started ➤ Power House (168m x 24.5m x 49m size):- Not started	Project presently stalled. JV company to start construction after award of works.
----	--	--	--	--

13	Rangit-IV Jal Power corp. Ltd. 06.07.2007 3x40= 120 MW Broad Features: Dam: Concrte 44m high .HRT : D- 6.4m L- 6.5km Power House : Surface Turbine: Francis Cost: Original:726.17 Latest : 938.29 (10/19 PL) Contractors Civil : Ritwik (27.08.2021) HM : PES (28.06.2021) E&M : Andritz (08.07.2021)	<u>Sikkim</u> <u>2011-12</u> 2025-26	➤ Dam (44m high and 135.3 m long): 4.09 lac Cum (83%) excavation out of 4.927 Lac Cum is completed. Concreting of 61045 Cum (35.22 %) out of 1.732 Lac cum is completed. Approximately 2.0 Lac Cum of material deposited due to flooding, to be removed/cleared from the working area. ➤ Desilting chamber (3 nos. each of 120 m length x 13m width x 15 m depth):-2143m (64%) excavation out of 3360 m is completed. ➤ HRT (6.40m diameter, 6.488 km long): 58.48 % Excavation is completed. ➤ Surge Shaft (18m diameter 59m height): Excavation of Surge Shaft is completed ➤ Pressure Shaft (1 No. 5.5 m diameter 236.55 m long): 212.34 m (90%) excavation completed. ➤ Penstocks (3 No. of 3.2m diameter, 232.49 m long): 205.29 m (88%) excavation is completed ➤ Power House (82.30m x 20m x 41.38m size): Out of total 1.18 Lac Cum of Excavation, 1.15 Lac Cum of excavation completed and out of total 19900 Cum of concreting, 8565 cum (43.04%) of concreting completed. ➤ E&M Works: 76% Supplies of E&M Package-I and 17% supplies of Package-II have been received at site	Works recently awarded.
14	Luhri Stage-1 SJVN Ltd. 01.05.2018 2x80+2x25=210 MW Broad Features: Dam: 86 m high HRT: 9m dia 38 km length Power House:Underground Turbine: Francis Cost: Original - 1810.56(05/2020) Contractor : Civil: Luhri Hydro Power Consortium	<u>Himachal Pradesh</u> <u>2025-26</u> <u>2025-26</u> <u>(Jan'26)</u>	CCEA approval accorded on 4.11.2020. Civil & Hydro-mechanical Works awarded on 24.11.2020 and Contract Agreement signed on 22.12.2020. Electro-mechanical package awarded on 16.07.2021. ➤ Diversion Tunnel (598 m): DT Intel portal development completed on 25.05.21. 37529 cum (56%) of total 66458 cum outlet portal development completed. ➤ Dam: Stripping of Dam-abutments (right bank) is in progress. ➤ Power House: 28850 cum (14.66%) out of total 196829 cum stripping of power house (right bank) completed. ➤ Tail race channel: 48350 cum (15.15%) out of total 318969 cum stripping (right bank) completed ➤ Construction of Bailey bridge completed on 06.05.2021. ➤ Construction of approach roads: Approach road from Bailey bridge to Batching plant completed. Realignment of NH is under progress.	Acquisition of part Private land.
15	Dhulasidh Hydro Electric Project SJVN Ltd (2x33 MW = 66 MW) Cost: Original: Rs. 687.97 Cr	<u>Himachal Pradesh</u> <u>2025-26</u> <u>2025-26</u> (May '25)	Investment approval accorded on 1.10.2020. ➤ Main Civil works awarded on 06.05.2021. Mobilization by the contractor is in process. ➤ Diversion tunnel: 125 m out of 253 m heading excavation completed. ➤ Dam: Over-burden removal including site clearance started. ➤ Project access roads are under construction.	Approval of Cabinet, GoHP regarding purchase of Private land/Govt. land awaited.

B	State Sector			
16	Parnai JKSPDC 21.10.2013 3x12.5= 37.5 MW Broad Features: Barrage: 107m Long, 11.7m High HRT: D Shape, 9236m long, 3.2m dia Surge Shaft: 3.2m Dia Power House- Surface- 60x12x28 Cost: <u>Original:</u> 640.86 Latest 640.86 Contractors Civil : Patel & Alstom E&M : Andritz	<u>J&K</u> <u>2017-18</u> <u>2023-24</u> (Dec,23)	The implementation of the project has been undertaken by awarding the EPC contract in favour of M/s. Patel Engg. Ltd. in 2013. Barrage:- Excavation 37181cum out of total 46364 cum completed. Concreting 23604 cum out of 34589 cum completed. HRT (D-shaped, 3.2m diameter, 9.236km long):- 5002m out of 9236m excavation completed. Pressure shaft (1no. 2mdia, 1733mlong): Excavation 14823 cum out of total 34560 cum completed. 536 cum out of 7212 cum concreting has been completed. Surge shaft (3.2m dia.) : Excavation:704cum out of 14000cum completed. Power house: excavation 23550 Cum excavation out of 60000 Cum has been completed.	- Slow progress of works - Contractual Issues.
17	Lower Kalnai JKSPDC 16.08.2013 2x24= 48 MW Broad Features: Dam: 110m Span, 49m High HRT: D Shape, 3960m long, 4m dia Surge Shaft: 14m Dia Power House- 55x23.45x32.4 Cost: <u>Original:</u> 576.87 Latest 576.87 Contractors Civil : Coastal E&M : GE	<u>J&K</u> <u>2017-18</u> <u>2025-26</u> (Subject to re-start of works)	EPC contract awarded to M/s. CPL in Sept., 2013. Diversion tunnel has been completed and river diversion made on 30.11.2016. Work on coffer dams has been started Dam:- Excavation work completed for right abutment of the dam bridge. Excavation of left abutment completed upto 50%. HRT:- Adit excavation is in progress. . 'Works on all fronts at Dam and Power House site are stalled since 24.01.2018 due to payment dispute with subcontractors and due to non-settlement of extension of time of the contract by the JKSPDC .The contract with M/s. Coastal Projects Ltd. has been terminated and re-tendering for selection of EPC contractor is under process.	- Project stalled - Re-award of works
18	Shahpurkandi Irrigation Deptt. &PSPCL 04.05.2011 3x33+3x33+1x8=206 MW Cost: <u>Original:</u> 1835.50 Latest 1938.74 (Power Component) Contractors Civil & HM for Main Dam with two Head Regulators : Soma – BUREYA JV Power Houses : M/s OMIL JV E&M : BHEL	<u>Punjab</u> <u>2015-16</u> <u>2024-25</u> (Dec.23)	Main Dam: Overall 67% work of Main Dam portion has been completed. Hydro Mechanical work for dam, fabrication work is completed by 94.41 % and 27.62 % of erection work. Hydel Channel: Excavation / concreting is in advance stage of completion at Shahpurkandi Channel and on Ravi Canal Hydel Channel work is yet to be started. Works of Dam stopped since 29.08.2014 due to inter-state dispute between states of J&K & Punjab on sharing of waters of river Ravi & tariff. An agreement was signed on 8.9.2018 between Chief Secretary, Govt. of Jammu & Kashmir and Chief Secretary, Govt. of Punjab. The Punjab Cabinet ratified the above agreement. Zero date of the project is 1st November, 2018. NIT for Civil works of Power House was floated and work is awarded to M/s OMIL JV on 24.02.2021 for both power houses. The civil work for both power houses has been started. E&M contract work earlier accorded to BHEL has been revived, Project is programmed for Commission by August,2024.	
19	Uhl-III Beas Valley Power Corporation Ltd. (HPSEB) 19.09.02 / (TEC -2x50 MW) 3x33.3 =100 MW	<u>H.P.</u> <u>2006-07</u> <u>2023-24</u> (Dec'23)	All works completed in July, 2018. During Hydro Static pressure Test (HST) of Penstock, some leakage was observed. Repair of penstock & HST completed by March, 2020. On 17.05.2020 after Trial run of Unit-1, during synchronisation to grid transmission load	

	(Revised vide HPSEB letter dt. 19.01.07. Broad Features: HRT-4.15m x 8.47 km S.Shaft- 13m x 68.8m Penstock- 3.4m x 1851.946 m (main) P.House- Surface Turbine- V. Francis Cost: <u>Original: 431.56</u> Latest:1281.52 Contractors Civil : Continental / Abir HM : PES E&M : BHEL		rejection was done but the penstock ruptured along penstock ferrule # 345 which is about 110m upstream of surface power house. The restoration of the Penstock by replacing/recladding the SAILMA 550HI steel and that of power House is under progress . Tender for restoration of Penstock was floated and four bidders have been participated. The Techno Commercial evaluation is under process.	
20	Shongtong Karcham H.P. Power Corpn. Ltd. Clearance: 16.08.2012 3x150= 450 MW Broad Features: Intake Tunnel: 4 Nos. Horse shoe 6.4m dia 192 to 280m length HRT- Circular, 10.5m dia, 8096m long. Power House- Under ground Turbine- VF. Switchyard: 400 Kv. Cost: <u>Original: 2807.83</u> Latest:2807.83 Contractors Civil & HM : Patel E&M : Andritz	H.P. <u>2016-17</u> 2024-25 (Mar'25)	River Diversion achieved on 10.02.2017. Barrage: Downstream Coffor Dam completed. Upstream Coffor Dam 84% completed. HRT:Heading excavation 7121.27 m out of 7712.7m completed. Benching excavation 2721.93 m completed Surge shaft: Pilot hole excavation completed. Power House:- 100% excavation of Powerhouse Cavern, 100% excavation of Transformer hall completed. Concreting of EOT crane beam completed.	
21	Vyasi UJVNL 25.10.2011 (TEC) 2x60= 120 MW Broad Features: Dam: Conc. Gravity H- 86m L-207.2m HRT- Circular, 7m dia, 2.7Km long. Power House- Surface Turbine- VF. Switchyard: 220 Kv. Cost: <u>Original: 936.23</u> Latest:1581.01 Contractors Civil : Gammon / MPCC E&M : BHEL	<u>Uttarakhand</u> <u>2014-15</u> 2022-23 (Apr,22)	Civil Works: Dam :Excavation completed. Total 360402 cum concreting has been done in dam blocks out of 3.63 lakhs cum. Diversion Channel : Completed. Head Race Tunnel (2.7 Km): Excavation works completed. Both overt and invert lining has been completed. Pressure Shaft: Excavation works completed of pressure shafts completed. Concreting completed. Grout hole plugging is under progress. Surge Shaft :Excavation has been completed (100% done). 7600 cum out of 7600 cum concreting has been completed. Power House: Excavation works and concreting of substructure completed. Concreting of super structure is 94% completed.	-Dam and E&M works are Critical. -Local issues regarding compensation under R&R package.
22	Koyna Left Bank PSS WRD, Mah. 20.02.2004 2x40 = 80 MW Broad Features: Water from the existing ShivajiSagar Lake (Koyna reservoir) is to be utilized for generation. Intake Tunnel: Dia – 7.20 M Length – 235.5 M (including Lake tap) HRT: Dia – 7.20 M Length – 80 M	<u>Maharashtra</u> <u>2014-15</u> 2025-26 (Subject to re-start of works)	Civil Works: Excavation of intake structure 4781 cum out of 14105 cum and lining 2485 cum out of 3381 cum completed. Excavation of Switchyard completed. Excavation of Approach tunnel & Ventilation tunnel is in progress. Tail surge shaft :Excavation in soft strata completed. Excavation for inclined / vertical / lateral shafts in hard rock 6448 / 9223 cum completed. TRT : 364 / 24003 cum excavation completed. Machine Hall : Underground Excavation is under progress. 22600 cum excavation out of 55050 cum completed. E&M works:	-Slow progress of works. -Funds constraints due to increase in Project cost. RCE under approval. - Contractual Issues - The proposal to construct the project on BOT basis had been sent to State Govt., as no response has been received from State Govt., WRD is planning to take up the project after availability of funds. The project works are stalled since March, 2015.

	Penstock – 2 nos ,Dia – 2.9M Length – 10 M each P.House – Underground Turbine – Reversible Cost: <u>Original: 245.02</u> Latest:1403.77 Contractors Civil &HM : BT Patil – Malaxmi JV / Patel E&M : LitostrojSlovenia&Koncar, Croatia		The contract for details engineering manufacturing supply, supervision erection, testing commissioning and putting into commercial use of pump turbine, generator motor and associated equipments is signed with M/s IVRCL Ltd., Pune on 16.12.2010. Further TG set has been ordered as under: Turbine/Pump: M/s Litosroj Power, Slovenia (European Union) Generator/Motor: M/s Koncar Power, Plant & Electric Traction Engineering, Croatia (European Union). EOT Crane :- Works awarded to M/s Pedvak Cranes Private Limited Hyderabad on 12.04.2013.	
23	Polavaram APGENCO / Irrigation Deptt., A.P. 21.07.2010/ 25.02.2009 12x80= 960 MW Broad Features: ECRF Dam- L-2454 m, H-57.9m, Spillway- L-1128m, Spill gate -48 Nos. Approach channel-175m. Intake tunnel: Ø 9m, L-130m (12 Nos) Power House- Surface type, Turbine- Vertical Kaplan Tail Race Channel- 1130m. Cost: <u>Original: 4956.39</u> Latest:5338.95 (Power Component) Contractors Civil :Navyug contract terminated and awarded to M/s Megha Engineering and Infrastructure Ltd. (MEIL) (EPC contractor) E&M : BHEL	Andhra Pradesh <u>2017-18</u> 2024-26	A) Spillway, Earth cum Rockfill Dam, Power House Foundations Works awarded in March, 2013 to M/s. Transtroy- JSC EC UES JV. ECRF DAM:Earth work of 508.06 L.Cum /833.169L.Cum is completed. Diaphragm Wall concreting – completed. SPILLWAY: Excavation-838.80 L Cum out of 1115.59 L Cum completed. Concreting 9.60 L Cum out of 36.79 L cum completed. Gates: RadialGate fabrication – 11010 MT completed out of 18000 MT (61.17%). Power House: Earth work of 112.20 L Cum / 114 L.Cum is completed & embankment of 9.79 L.Cum / 10 L.Cum is completed. 'Works stalled since 19.07.2019 as APGENCO asked contractor M/s Navayuga Engineering Company Ltd. (NECL) to stop all works and termination of contract issued on 14.08.2019. The writ petition filed by NECL was disposed by Hon'ble High Court on 14.12.2020. Final Contract concluded with new contractor M/s MEIL for execution of PHEP works on 30.03.2021..Effective zero date of project is 30.03.2021. The Engineering Designs & Drawings for various components of Project are under progress and the witnessing of the Turbine Model Test was 14.07.2021. Power House excavation work is under progress and 71% excavation progress achieved.	
24	Pallivasal KSEB 2x30= 60 MW 31.01.2007 Broad Features: HRT: 3.50m X 3396m Surge Shaft: 7.0m X 49m Pressure Shaft: 2.50m X 1019.20m Penstock: 2.nos., 1161.20m each. Power House: Surface Turbine: Pelton S. Yard: 220kV – Single bus Cost: <u>Original: 222.00</u> Latest: 550.00 Contractors Single Package (Except Intake & balance Tunneling works) ESSAR – DEC – CPPL JV -M/s Bumi-Zillion JV (for Intake works & balance Tunneling works) -M/s Anchor structure-PSE-SSIPCJV, M/s. Shri	Kerala <u>2010-11</u> 2021-22 (Likely to slip to 2022-23)	Contract for Civil &HM works has been terminated w.e.f. 13.09.18. Balance work has been re-tendered on the risk & cost of Contract, Subsequently balance works have been awarded to M/s. Sri Sarvasna Industries Pvt. Ltd. and M/s. DSE Anchor Structure. Intake structure: Excavation completed. Leading channel of Water conductor system replaced by cut & cover/soil tunnel and accordingly intake is shifted. HRT: Excavation –3347/3347 m completed. Overt conc. 1808/3347 m completed. Invert Conc.. – 1675/3347 m completed. SurgeTank / Forebay: Excavation completed. Concreting.423/843 m³ completed. Pressure Shaft: Excavation completed. Fabrication of steel liner completed and erection of 906/1096 m completed. Surface penstock: Excavation –112800/122600 m³. Concreting- 123800/12850 m³ and 1923m out of 2036m erection completed. Power House: Excavation & Concreting completed. Tail race Channel (2 Nos.): Excavation & lining completed.	-Re-award of works for E&M works.

	Sarvasana Industries Pvt. Ltd.		E&M Works: 67% supply completed, balance of E&M works –Tendering finalized. The overall progress achieved :- 88.49%.	
25	Thottiyar KSEB 1x30 + 1x10= 40 MW 05.06.2008 Broad Features: Weir: 222m Long 11 blocks 7.5m height Tunnel: Circular 2.6m dia 199m long. Power House: Surface Turbine : Vertical Pelton Cost: <u>Original: 136.79</u> Latest: 280 Contractors Civil & HM : PRIL- Sri Sarvana Industries	<u>Kerala</u> <u>2012-13</u> 2021-22 (Likely to slip to 2022-23)	Original contract for Civil & HM works foreclosed without risk & cost of Contractor M/s. Coastal Project Ltd. -Civil & HM works re-awarded to M/s PRIL-Sri Sarvana Industries Pvt. Ltd. on 05.01.2018. KSEB decided to execute E&M works departmentally & tendering was awarded to M/s Fitwell. Civil Works: Weir: 70% completed 9 out of 11 block completed. Approach Channel & Intake: 3909.00 m3 excavation out of 9584 m3. done. Power Tunnel: Excavation completed & Concreting 272.00 m3 Out of 615 m3 completed. Steel line fabrication 22.5 MT and erection 3 MT out of 27 MT completed. Penstock, Anchor, Rocker support: - Excavation 32391 m3 out of 37839.37 m3. concreting 4398 m3 out of 12082 m3 completed, Fabrication of penstock 1804 MT out of 2286.32MT completed and erection 401 out of 2341 MT completed. Power House, switchyard & allied works: 39258/43690 m3 excavation and 7845 /16209 m3 concreting completed. E&M Works: Tender for erection of supplied Electro/ Hydro Mechanical equipment for power house was awarded to M/s Fitwell. Work commenced on 10.07.2020 and at present 28% work have been completed. Over all Progress of the project is around 66% and it is expected that the project can be commissioned by Mar,21.	
26	Kundah Pumped storage (Phase-I, Phase-II & Phase-III) TANGEDCO 4x125= 500 MW Broad Features: HRT: Ø 8.5mX1247.33m. Surge Shaft: Ø (28m/16m/10m) x68m depth. Pressure Shaft: 2 Nos. Ø 5.50m X 463.38 m (each) Penstock: 4.nos. Ø 3.9m x45.4m each. Power House: Under Ground. Tail race surge chamber: 10m(W);52m(L);48m(H) Tail Race Tunnel: Ø 8.5mx895m Turbine: Francis reversible turbine. Cost: <u>Original: 1216.59</u> Latest: 1831.29 Contractors Civil &HM : Patel / Kundah PSP E&M: MEIL	<u>Tamil Nadu</u> <u>2022-23</u> 2023-24 (Apr'23)	Civil & H&M Works: - Phase-I, Package I & II (Civil and HM works), LOI issued for package - I to M/s Patel engineering, and for package - II M/s Kundah PSP Consortium on 15.02.2018. The site was handed over on 05.03.2018. HRT: Excavation 1153 m.out of a total 1247 m. have been completed. Pressure Shaft: :excavation of Lower Horizontal Portion of Pressure Shafts PS1 & PS2 Completed. Pilot tunnel excavation in Inclined portion of PS1 completed and in PS2 is under progress. Head race Surge Shaft: excavation completed. Tail Race Surge Chamber: - Benching 90% completed and further benching under progress Power House: Excavation up to 1931 m completed and further excavation in bus ducts are under progress. TRT: Excavation 869m out of 895 completed. E&M Works: - Phase-I, Package –III, 1st unit of 125 MW and Phase-II (2x125MW) & Phase –III (1x125 MW) Supply, erection, testing & commissioning works awarded to M/s Megha Engineering & Infrastructure Ltd. on 28.11.2019. Virtual Model Test Completed , Design and Engineering works are under progress.	Environmental clearance validity expired on 07.05.2020. MoEF&CC issued TOR for Project works at site for a period of 6 Months from date of issue of TOR or grant of new E.C. Action is being taken to obtained fresh E.C

27	Lower Kopli APGCL 2x55+2x2.5+1x5= 120 MW Broad Features: Dam: Conc. Gravity HRT- Circular, 7m dia, 3.64Km long. Power House- Surface Turbine- VF. Switchyard: 220 Kv. Cost: <u>Original:1115.91</u> Latest:1847.07 Contractors Civil : L&T	<u>Assam</u> <u>2023-24</u> <u>2024-25</u> (Jun,24)	At present detailed survey work, geotechnical investigation work etc. are being carried out by M/s L&T. Civil work preliminary survey and geotechnical investigations going on at site . Overall Physical progress - 20% Overall financial progress - 12% HM work – not yet started E&M works – in tendering stage.	
C	Private Sector			
28	Tangnu Romai-I M/s Tangnu Romai Power generation 2x22= 44 MW 30.11.2007 (TEC by HPSEB) Broad Features: Barrage at EL ± 2555 m HRT-3.1m dia & 7.220 km length Surge Shaft- 5m dia, Top Level 2570 m & Bottom Level 2520 m Penstock- 2 m dia & 609.3 m length P.House- Surface Turbine – Vertical Francis Cost: <u>Original:255.00</u> Latest:641.89 Contractors Civil & HM : Sai Urja E&M : Andritz	<u>H.P.</u> <u>2014-15</u> <u>2024-25</u> (Subject to re-start of works)	Civil works awarded on 14.06.2010 to M/s Sai Urja Hydel Project (P) Ltd. Barrage and Diversion Cannel: 26211 cum out of 93800 cum excavation completed. Desilting Chambers & SFTPC: Excavation completed. SFT excavation 420 / 450.66 m completed. HRT: 2826m out of 6300m excavation completed. Power House, Switchyard & Misc.: 60275 m ³ out of 72000 m ³ excavation completed. In February-2015, due to land slide the steel bridge on Pabbar River, connecting Project components has been completely damaged. The restoration works are completed.	- Works are stalled due to finance issues since Jan, 2015.
29	Bajoli Holi M/s GMR Bajoli Holi Hydro Power Pvt. Limited 31.12.2011 3x60= 180 MW Broad Features Dam Height-66 M Dam Length-178 M Desilting Chamber- 2 Nos. 240 Mx14.5 MX 10.8 M HRT- Length-15.538 Km., 5.6 M dia P.H. –Surface Cost: <u>Original 1696.93</u> Latest 2689.00 Contractors Civil &HM : Gammon E&M : Alstom/ GE	<u>H.P.</u> <u>2018-19</u> <u>2021-22</u> (Nov,21)	The project is in advance stage of completion & Scheduled for commissioning during Nov, 21.	
30	Tidong-I M/s Statkraft India Pvt. Ltd. 2x50 = 100 MW 28.07.2006 Broad Features: HRT–D-3.5m L- 8461 m P.H. Surface Turbine –Vertical Pelton Cost: <u>Original543.15</u> Latest 1472 Contractors Civil &HM : SCL Infratech / Himalaya	<u>H.P.</u> <u>2013-14</u> <u>2022-23</u> (October 22)	Barrage& River Diversion Works: Common Excavation completed and 71700.84/73409.00 open cut rock excavation completed. 32144 cum out of 37159 cum concreting done. Head Regulator & Desilting arrangement: Common excavation completed. 9763 cum open cut rock excavation out of 10,000 cum completed. HRT (8409m): Excavation completed and 7353/8409 m lining concreting has been completed. Surge Shaft: Excavation 79m/89m completed. Pressure Shaft: Excavation completed. 1165m / 1388.8m lining completed.	- Transmission Line critical.

	E&M : Alstom		Power house and Tail race channel- 87709 cum out of 92500 cum excavation completed. 11237 cum out of 16156 cum concreting completed. Overall 76 % of Powerhouse civil works completed. E&M works Supply 97% completed and erection 54% M/s Statkraft India Pvt Ltd has acquired the 100% equity of the project on 04.09.2018.	
31	Kutehr M/s JSW Energy (Kutehr) Ltd. 3x80 = 240 MW 31.08.2010 Broad Features: Cost: Original: 1798.13 Latest : 1798.13 Contractors Civil & HM : M/s Angelique – PCC consortium, M/s MF Bumi Geotech Pvt. Ltd. & M/s. PES Engineers Pvt. Ltd. E&M : M/s Andritz Hydro Pvt Ltd.	<u>H.P.</u> 2024-25 2025-26 (Nov'25)	Civil works, HM works and E&M works awarded on 20.10.2019, 19.09.2019 and 13.02.2020 respectively. River diversion achieved on 25.01.2020. Barrage (27m high): Barrage excavation (left bank) completed to the tune of 125696 Cum out of 129400 Cum. Concreting of upstream keys completed. Apron concreting to the tune of 3189 cum out of 9137 cum completed. Left training wall concreting to the tune of 669 cum out of 11065 cum completed. HRT : Five out of Six Construction Adits to HRT completed (i.e. 1431 m out of 1612 m completed). 1922m out of 14538 m of Head Race Tunnel excavation completed.	-
32	Phata Byung M/s Lanco 06.10.2008 2x38 MW = 76 MW Broad Features: Dam – 26m high HRT- 3.2 m dia & 9.38 km length Turbine – Frances Cost: Original: 520.00 Latest : 1133 Contractors Civil : Lanco HM : Cimmco E&M : Alstom	<u>Uttara khand</u> 2012-13 2024-25 (Subjct to re-start of works)	Dam concreting: 17800/18000 cum concreting completed. P.H.: Excavation completed & Concreting in progress. HRT: Excavation almost completed. 1400 m Lining has been completed. Excavation and lining of Intake-I & Intake-II completed. Pressure shaft: Excavation completed & lining is under progress. TRT: Excavation 178/235m completed. E&M Works: Pit liner erection of units completed. EOT Crane installed and Commissioned. Ferrule Fabrication work is in progress. Work progress is stalled since July'17 on account of main EPC contractor and holding Company M/s Lanco Infratech Limited (LITL) being referred to NCLT under the Corporate Insolvency Resolution Process (CIRP) and subsequently, the initiation of liquidation proceeding as per NCLT Liquidation order in August 2018. However, the preservation works of Project are being carried out regularly at site by the Company, Lanco Mandakini Hydro Energy Private Limited (LMHEPL). Presently, the company is undergoing a corporate insolvency resolution process initiated under IBC for resolution and revival of the project since June 2020. Under this process, the resolution professional appointed by the NCLT has initiated the process for inviting prospective investors for the project.	- Works severely affected due to flash floods in June, 2013. - Works are stalled since July, 2017 due to Funds constraints with the developer. - Presently, the company is undergoing corporate insolvency resolution process initiated under IBC for resolution and revival of the project.
33	Maheshwar, SMHPCL 30 12 96/ 29.9.2006 (FC) 10x40= 400 MW Broad Features: Dam-35m High, concrete gravity	<u>M. P.</u> 2001-02 2023-24 (Subjct to re-start of	Civil & HM Works: All major civil works completed. All 27 nos radial gates commissioned. Unit Erection: Unit-10: Initial spinning achieved on 14.10.2011. Unit-9 & 8: Ready for spinning.	- Completion of R&R works and E&M works. - Works held up due to Fund constraints with developer. - Sub - Judice in NCLT.

	P.Shaft-10x7.82m x 52m P.House - Surface Turbine- Kaplan Cost: <u>Original:</u> 1569.27 Latest: 8121.00 Contractors Civil & HM : Sew E&M : BHEL	works)	Unit-7: Guide apparatus trial assembly in progress. Unit-6: Erection of turbine embedded parts & foundation parts completed. Unit-5 to 1: Erection of units is in initial stages. Works suspended since Nov-11 due to cash flow problem with developer. M.P. Power Management Company Ltd. has terminated the Power Purchase Agreement, R&R Agreement & Escrow Agreement with SMHPCL on 18.04.2020 & 20.04.2020 respectively .	
34	Bhasmey Gati Infrastructure 2x25.5= 51 MW Broad Features : Dam-33.2m High, Symmetrical gravity HRT-5.3m dia&5.132 km length , Circular. Surge Shaft- 89.8m Hight& 14m dia. P.House-Outdoor Turbine-VF TRT-2 Nos, L- 50m Swityard-132/11 KV Cost :Original : 408.50 Latest : 746.01 Contractors Civil : Simplex E&M : Voith	<u>Sikkim</u> <u>2012-13</u> <u>2024-25</u> (Subject to re-start of works)	Project is in initial stage of construction. River diversion achieved. Barrage: 61555cum/194600cum excavation completed. HRT: 1670m/4460m excavation completed. PH: 136105 cum/185937cum excavation completed. Surge Shaft : 8567cum / 22000cum Surface excavation completed. Overall Physical progress: 38% .	- Slow progress of works - Works stalled since Sept., 2016 due to paucity of funds. -No investor showing interest for executing the project.
35	Rangit-II Sikkim Hydro Power Limited 10.02.2010 2x33= 66 MW Broad Features : Dam-47m High, Concrete Gravity HRT-3.9m dia&4.745 km length , Surge Shaft- 65.5m High & 10m dia. Underground Pressure Shaft : 1.7 m dia& 2.5 km length. P.House-Outdoor Turbine- Pelton Vertical Swityard- GIS, 132/11KV Cost :Original : 496.44 Latest : 496.44 Contractors Civil & HM : Coastal E&M : Gammon	<u>Sikkim</u> <u>2015-16</u> <u>2024-25</u> (Subject to re-start of works)	EPC contract awarded to M/s Coastal in February, 2012. Diversion Tunnel: River diversion through diversion tunnel has been achieved. Dam :Excavation 53100cum out of 85000cum completed. HRT: Excavation 623m out of 4745m completed. Surge Shaft: Excavation completed. Concreting 37/1667 cum done. Pressure shaft: Excavation of pressure shaft I - 25m out of 128m and pressure shaft II - 154m out of 377m completed Power House: Excavation of surface power house is being taken up. Overall Physical progress: 40% .	Works are stalled due to non releasing of funds by lenders because of Power evacuation and land acquisition issues. Works restarted. A meeting with financiers were held on 23.09.2016 for release of funds. The developer was asked to submit certain document for release of funds. Works are stalled since December, 2017 due to funds constraints with developer. Project is in NCLT since 30.07.2020.
36	Panan Himagiri Hydro Energy Pvt. Ltd. 07.03.2011 4x75= 300 MW Broad Features : Dam-115m from deepest foundation level Desilting Chambers : Underground, 2 Size (14Lx22Wx2.5H)	<u>Sikkim</u> <u>2018-19</u> <u>2025-26</u> (Subject to re-start of works)	Civil works awarded on 22.02.2014. Infrastructural works and geological investigations are in progress. Starting of civil construction works is held up for want of the National Board of Wild Life (NBWL) clearance. There was a case challenging the Eco-Sensitive zone notification of MoEF& Climate Change in NGT. The case is disposed on 21.8.2017. The developer applied for issuance of clearance from Forest, Environment & Wild Life	-Works stalled for want of NoC from State Govt. from NBWL angle. - Issue of Mantham Lake.

	HRT- modified horse shoe, 6 m dia& 9549m length , Surge Shaft- 102 m High & 15m dia. Pressure Shaft : 2/4, 3.4/2.4m dia, 707.4 m- Long P.House-Surface Turbine-Vertical Francis Cost :Original: 1833.05 Latest :2671.00 <u>Contractors</u> Civil : Essar		Management Dept., Govt. of Sikkim from NBWL angle. In August, 2016, there was a huge land slide thereby creating a lake which obstruct the approach to project components. Developer are pursuing with concerned department of GoS for early decision on dismantling of Mantham Lake or developing an alternative road to reach the dam site to start main project civil works in full swing at the earliest. Overall Physical progress: NIL	
--	---	--	---	--

Grand Total : 36 nos. – 12,663.5 MW

Status of Under Execution Hydro Electric Projects in Bhutan

Sl. No.	Name of Project / Capacity (MW)/Executing Agency/Date of CEA clearance / Approval / Broad Features/Commissioning Schedule	Award of works	Present Status/ Issue																		
1.	Punatsangchhu-I 6x200=1200 MW PHPA, Bhutan Date of TEA: 27.07.2007 Broad Features : Dam – 136m High, 279.2m long, Concrete gravity (RCC) HRT- 10m x 8.948 km Pressure Shaft: Two nos. 6.0mx482.20m each Surge Shaft: 24.5mx128.5m TRT: 10.0m x1182.20m P.House-Underground Turbine- Vertical Francis SWYD- 400 kV Original Commissioning Schedule: Nov’ 2016 Anticipated commissioning schedule : 2024-25 (As presented in the 22 nd PHPA-I meeting held on 25.09.2019 which will be revised after decision on Dam Vs Barrage) Original Cost: Rs.3514.80 Crores Latest revised Cost: Rs9375.60Cr.(Dec 2013 PL) Expenditure: Rs. 8093.98 Crores(Sept. 2021)	Civil Works: Package-I: L&T Ltd. on 27.03.2009 Package-II: Gammon India Ltd on 27.03.2009 Package-III:HCC ltd. 27.03.09 E&M Main Works: Package-I : BHEL Ltd. on 04.02.2010 Package-II: BHEL Ltd. on 27.02.2012 Package-III: Hyosung Corporation on 28.02.2012 Package-IV: SudkabelGmbh on 27.05.2011 Package-V: Schneida Electric Ltd. on 21.11.2013. Transmission Works: Joyti Structures & Gammon (India) JV on 12.08.2010 (Amended on 10.6.2013)	- Overall physical progress achieved is 87.30% as on 30.09.3021 - Package wise progress of major components is as follows:<table><tr><th>Package</th><th>Component</th><th>Physical Progress (%)</th></tr><tr><td>MC-1</td><td>Dam and associated components HRT</td><td>69.87</td></tr><tr><td>MC-2</td><td>HRT</td><td>100</td></tr><tr><td>MC-3</td><td>Power House and associated component</td><td>98.81</td></tr><tr><td>EM</td><td>Electromechanical Works</td><td>96.91</td></tr><tr><td>Transmis sion</td><td>Associated Transmission Lines</td><td>99.94</td></tr></table> - Cumulative Physical Progress is 87.30%. Critical/ Major issue: Movement & subsidence at right bank hill. Completion of dam works. ➤ Final decision regarding construction of Barrage vs Dam. ➤ Shortage of manpower in MC#3 and EM contract Package to complete the balance work due to limited quarantine facilities inside Bhutan.	Package	Component	Physical Progress (%)	MC-1	Dam and associated components HRT	69.87	MC-2	HRT	100	MC-3	Power House and associated component	98.81	EM	Electromechanical Works	96.91	Transmis sion	Associated Transmission Lines	99.94
Package	Component	Physical Progress (%)																			
MC-1	Dam and associated components HRT	69.87																			
MC-2	HRT	100																			
MC-3	Power House and associated component	98.81																			
EM	Electromechanical Works	96.91																			
Transmis sion	Associated Transmission Lines	99.94																			
2.	Punatsangchhu-II 6x170=1020 MW PHPA, Bhutan Date of TEA: 30.04.2010 Broad Features : Dam – 86m High, 213.5m long, concrete gravity HRT- 11m x 8.58 km	Civil Works: Package- CI : JP Associate Ltd. on 25.07.2011 Package-CII: Gammon India Ltd on 25.07.2011 Package-CIII: JP Associate Ltd. on 25.07.2011	Dam (86 m high and 213.5 m wide) Excavation completed. Adverse geological situation faced at the left bank of the dam stands resolved. Conc.8.765 lakh cum completed out of 9.08 lakh cum. Desilting Chamber and Silt Flushing Tunnel All works of Desilting Chamber and Silt Flushing Tunnel stand completed except Concreting of 2063 cum and silt flushing gate and miscellaneous work																		

Sl. No.	Name of Project / Capacity (MW)/Executing Agency/Date of CEA clearance / Approval / Broad Features/Commissioning Schedule	Award of works	Present Status/ Issue
	Pressure Shaft: 3 nos. 5.5mx997m each Surge Shaft:31 m x137m TRT: 11.0m x3163m P.House-Underground Turbine- Vertical Francis SWYD- 400 kV Original Commissioning Schedule: June' 2017 Anticipated commissioning schedule: 2022-23 Original Cost: Rs.3777.80 Crores (03/2009PL) Latest1st revised Cost: Rs7290.62Cr.(03/ 2015 PL) Latest 2nd revised Cost:8977.045 Crore Expenditure: Rs. 7245.318 Crores(31 July. 2021)	E&M Main Works: Package-I: BHEL Ltd. on 18.07.2012 Package-II: BHEL Ltd. on 7.05.2013 Package-III: Hyosung Corporation on 7.05.2013 Package-IV:LS Cables & System Ltd. on 7.05.2013 Package V : M/s ABB Ltd. on 18.11.2014 Package VI : M/s BAEL, Bhutan on 31.12.2018 Package VII (A) : M/s S.K. Systems on 13.02.2017 Package VII (B) : M/s Technico (India) on 21.03.2017 Package VIII (A) : M/s Avids Technovators Pvt Ltd. on 18.11.2019 Transmission Works: Bhutan Power Corp.Ltd on 16.01.2014 (on deposit work basis)	which are pending due to unavailability of manpower. Total Progress for C-I Package – 92.83% HRT (11m diameter, 8.58 km long) HRT in C-2 package is completed in all respect and extensive grouting has also been carried out. It is ready to be taken over. Only invert lining of 439 m in C-3 package is remaining. Total Progress for C-II Package – 99.08% Surge Shaft (31m diameter 137 m height) Excavation and lining completed and HM works of Gate is yet to be taken up. Pressure Shaft Erection & backfill concrete of Steel Liner 1236 M completed out of 1454 M. (95.50%). The balance work lies in bottom Adit of pressure shaft which is at present used as access road to North Surge Tunnel and can be taken up only after the North Surge Tunnel is completed in all respect. Power House (236 m x 23m x 51m size) Machine Hall Excavation is completed. Unit-I & II have reached to Spiral case level and Electro Mechanical works of Erection of Spiral case is in progress. Civil work in Unit-III upto MIV level is completed and from MIV floor level to Spiral case level is in progress. Planned 30m Excavation of draft tube tunnel VI from Machine hall side is completed and Preparation for raft concrete for erection of Draft tubes VI will be taken up soon. Similarly for draft tube V initial 30m excavation from Machine Hall is in progress. The balance length of tunnel in both Draft tube V& VI will be done from DSSG side. Transformer hall (216.1 X 14.7 X 26.5) Excavation is completed and 30m of GIS slab is also completed. Firewall and raft foundation for accommodating 3 transformers is also completed and lying of floor is in progress and rail line for shifting Transformer will be laid soon. Down Stream Surge Gallery About 47% excavation had been completed before the collapse of the DSSG. Now the DSSG is divided into two caverns of North and South with abandoned portion in-between. Balance excavation in South and North has to be taken up once strengthening and restoration works of DSSG is completed. As of now grouting of the loose muck in abandoned portion is

Sl. No.	Name of Project / Capacity (MW)/Executing Agency/Date of CEA clearance / Approval / Broad Features/Commissioning Schedule	Award of works	Present Status/ Issue
	3. Kholongchhu HEP (4x150 MW = 600 MW)	Civil works:-	completed. Construction of RCC wall at both North and South to hold the loosed grouted muck is also completed. Installation of Passive Cable Anchor is in progress. 4 rows both in North and south out of 10 and 12 rows respectively stand completed. Installation of FMI is in also in progress. Total Progress for C-III Package – 80.95% E&M Works: Erection and Commissioning of EOT crane has been completed upto Unit-II. Erection works of Spiral case for Unit-I is substantially completed and for unit-II stay ring welding is in progress. Stator for Unit-I and Unit-II are at 99 and 79% progress. Similarly Rotor for Unit-I and Unit-II is at 71% and 34% progress. Regarding the supply part more than 80% of the supply EM supply stands completed. Total Progress for E&M Package – 80.09% Total Progress for Transmission work – 100% Overall Cumulative Physical Progress of the Project is 90.83%. Critical: - Restoration & completion of downstream Surge gallery works. - E&M works. Package 2A : Construction of portals of Adit -4 & 5 and construction of site camps are in progress. Package 2B : Construction of approach roads & portal of Adit-2 in progress. Access roads (31.97 km) and road to desilting chamber (848 m) completed.

Sl. No.	Name of Project / Capacity (MW)/Executing Agency/Date of CEA clearance / Approval / Broad Features/Commissioning Schedule	Award of works	Present Status/ Issue
	A joint venture company between SJVN Ltd and DGPC Bhutan (50:50) created on 12.06.2015 as “Kholongchuu Hydro Energy Ltd.” DPR approved by CEA on 5.11.2012 and RGoB on 23.05.2013 EC obtained on 21.07.2014 FC obtained on 13.11.2012 Construction license obtained on 16.7.2015 Dam – 94.35 m (above foundation) high concrete gravity dam, 372 m long HRT- 5.7 m dia, 15.77 km long, Horse shoe shap. Pressure shafts – 2nos. Of 3.3.m dia and 1300 and 1286 m long Turbine – 4 no. Pelton type.	All three main civil works packages awarded on 04.03.2021 Package-I Work awarded to M/s Jaipraksh Associates. Contract Agreement yet to be signed. Package-II Work awarded to Ms Valecha – Rigsar JV. Contract Agreement signed on 26.05.2021 and 10.06.2021 for 2A & 2B. Package – III Work awarded to M/s Jaipraksh Associates. Contract Agreement yet to be signed.	Bridge –I & II completed on 08.01.2018 & 24.01.2018. Widening of Doksum-Buyang Highway in progress. Work is being executed through Department of Roads, RGoB and 15.18 km out of 16.503 km completed. Widening of balance road is inprogress. Work for temporary site office at Power House, Adits, Surge Shaft and Pressure Shaft completed. Electrical work in progress. Integrated township at Duksam (KHEL Colony) work is in progress. Work for providing construction power completed.

Chapter-7

Financial Status of Under Construction H.E.P.

Figures in Crores

Sl. No.	Name of project/ State	Capacity (MW)	Benefits (MW)	Cost	Ant .Cost.	Total Expend. Upto Mar'18	Total Expend. Upto Mar'19	Total Expend. Upto (Mar' 20)	Expend. inFY 2020-21	Total Expend. Upto Mar'21	Actual Expend.till Sept. 21(FY2021-22)
	(State)			(PL)	(PL)						
	Under Execution										
	Central Sector										
1	Pakal Dul (CVPPL)	4x250	1000	8112.12	8112.12	993.93	1086.32	1465.44	429.55	1894.99	2047.41
	J&K			(03/2013)	(03/2013)						
2	Parbati -II(NHPC)	4x200	800	3919.59	9897.59	6670.12	7277.60	7858.50	989.94	8848.44	9260.94
	H.P.			(12/2001)	(04/2018)						
3	Tehri PSP (THDC),	4x250	1000	1657.60	5024.35	2540.27	2792.49	3374.95	565.59	3940.54	4225.82
	Uttarakhand			(12/2005)	(02/2019)						
4	Tapovan Vishnugad (NTPC)	4x130	520	2978.48	5867.38	3521.00	3938.20	4467.43	425.99	4893.42	5122.69
	Uttarakhand			(03/2004)	(04/2019)						
5	Lata Tapovan(NTPC)	3x57	171	1527.00	1527.00	148.00	149.16	149.21	*	149.21	149.93
	Uttarakhand			(07/2012)	(07/2012)						
6	Vishnugad Pipalkoti (THDC)	4x111	444	2491.58	4397.80	1393.66	1604.36	1936.99	270.96	2207.95	2297.07
	Uttarakhand			(03/2008)	(02/2019)						
7	Ramam-III (NTPC)	3x40	120	1381.84	1381.84	322.00	447.75	517.86	142.20	660.06	715.32
	West Bengal			09/2014	09/2014						
8	Subansiri Lower (NHPC)	8x250	2000	6285.33	19992.43	9966.92	10749.37	12225.96	1380.72	13606.68	14209.80
	Ar. Pradesh/Assam			(12/2002)	(04/2017)						
9	Naitwar Mori (SJVN)	2x30	60	648.33	648.33	100.37	198.68	355.65	214.15	569.80	679.95
	Uttarakhand			(10/2016)	(10/2016)						
10	Teesta St. VI (NHPC)	4x125	500	5748.04	5748.04		897.50		*		1138.44
	Sikkim			(07/2018)	(07/2018)						
11	Rattle	4x205 + 1x30	850	5281.94	5281.94	1451.00			*		3.60
	J&K			(NA)	(NA)	(Mar-16)					
12	Kiru (CVPPL)	4x156	624	4287.59	4287.59		128.10	305.35	185.68	491.03	588.47
	J&K			(9/2014)	(9/2014)						
13	Luhri-I	2x80+2x25	210	1912.59				178.18	239.77	417.95	515.52
	H.P.			(2017)							
14	Rangit-IV	3x40	120	726.16	1692.60	818.44			*		166.38
	Sikkim			(2011-12)	(06/2016)	(Jun-17)					
15	Dhaulasidh (SJVN)	2x33	66						#		168.72
	Himachal Pradesh										
	Sub Total: Central Sector		8485.00	46958.19	73859.01	27925.71	29269.53	32835.52	4844.55	37530.86	41140.13
	State Sector										
16	Parnai	3x12.5	37.50	640.86	640.86	136.50	189.62	221.69	19.48	241.17	279.00
	J&K			(NA)	(NA)						
17	Lower Kalnai	2x24	48	576.87	576.87	87.94			*		*
	J&K			(NA)	(NA)	(Dec-17)					
18	Uhl-III	3x33.33	100	431.56	1281.52	1459.21	1602.78	1927.49	157.38	2084.87	2115.96
	H.P.			(09/2002)	(12/2012)	(Feb-18)	(Feb-19)	(Mar,20)			
19	Shontong Karcham	3x150	450	2807.83	2807.83	657.56	918.05	1130.90	189.42	1320.32	1445.53
	H.P.			(07/2011)	(07/2011)						
20	Vyasi	2x60	120	936.23	1581.01	430.67	825.73	1213.14	355.61	1568.75	1693.54
	Uttarakhand			(02/2010)	2019						
21	Shahpurkandi #	3x33+3x33 +1x8	206	1835.50	1938.74	650.00	729.96	1241.58	241.84	1483.42	1600.69

Sl. No.	Name of project/ State	Capacity (MW)	Benefits (MW)	Cost	Ant .Cost.	Total Expend. Upto Mar'18	Total Expend. Upto Mar'19	Total Expend. Upto (Mar' 20)	Expend. inFY 2020-21	Total Expend. Upto Mar'21	Actual Expend.till Sept. 21(FY2021-22)
	(State)			(PL)	(PL)						
	Punjab			(4/2008)	(2/2018)	(Mar-18)					
22	Koyna Left bank PSS	2x40	80	245.02	1403.77	165.39	165.39	165.39	*	165.39	*
	Maharashtra			(1999)	(2014)						
23	Polavaram HEP (PPA)	12x80	960	3013.68	5338.95	608.74	758.708	802.18	0.00	802.18	802.24
	Andhra Pradesh			(2010-11)	(2016-17)						
24	Pallivasal (KSEB)	2x30	60	222	550	259.35	302.36	356.18	39.25	395.43	416.98
	Kerala			(1999)	(2018)						
25	Thottiyar (KSEB)	1x30 +	40	136.79	280	61.08	63.61	100.79	23.45	124.24	102.95
	Kerala	1x10		(2007)	(2018)						
26	Kundah Pumped Storage-I	4x125	500.00	1216.59	1831.29	136.74	221.52	270.09	72.95	343.04	390.54
	Tamil Nadu / (TANGENDCO)			(2007-08)	(2014)						
27	Lower Kopili	55+2x2.5+1x	120						#		446.41
	Assam										
	Sub-total: State Sector		2721.50	12062.93	18230.84	4653.18	5777.73	7429.43	1099.38	8528.81	9293.84
	Private Sector										
28	Sorang #	2x50	100	586.00	586.00	1380			117.83	117.83	NA
	H.P.			(4/2005)	(4/2005)	(Jun-17)					
29	Tidong-I	2x50	100	543.15	1472.00		163.74	780	78.00	858.00	1088.10
	H.P.			(06/2018)							
30	Tangnu Romai- I	2x22	44	255.00	641.89	329.36			*		*
	H.P.			(1/2007)	(2018)	(Mar-18)					
31	Bajoli Holi	3x60	180	1696.93	2689	1740.00	2188.00	2481	588.00	3069.00	3365.00
	H.P.			(12/2011)	(05/2020)	(Mar-18)					
32	Phata Byung	2x38	76	520.00	1132.00	1135.00	1263.00		*		*
	Uttarakhand			(2013-14)	(9/2016)	(Dec-17)	(Dec-18)				
33	Maheshwar	10x40	400	1569.27	6793.00				*		Nil
	M.P.			(1996-97)	(2016-17)						
34	Bhasmey	2x25.5	51	408.50	746.01	353.00			*		Nil
	Sikkim			(2012-13)	(03/2018)	(Jun-17)					
35	Rangit- II	2x33	66	496.44	496.44	125.76	126.83		*		*
	Sikkim			(2011-12)	(2011-12)	(Feb-18)	(June-18)				
36	Panan	4x75	300	1833.05	2671.00	165.00	170.00	155.10	*	155.10	0.05
	Sikkim			(2009)	(2018)		(Nov.18)				
37	Kutehr (JSW Energy (Kutehr))	3x80	240.00	1798.13	1798.13			279.97	133.00	412.97	571.59
	H.P.			(09/2011)	(09/2011)						
38	Rongnichu #	2x56.5	113	491.32	1453.34	126.53	1085.00	1376.24	198.42	1574.66	
	Sikkim			(NA)	(2018)	(Mar-18)	(Mar.19)		(Mar,21)		
	Sub-total: Private Sector		1557.00	9706.47	19025.47	5228.12	3911.57	3696.07	916.83	4612.90	5024.74
	Total : (Under Execution):		12,763.50	68,727.59	111,115.32	37,807.01	38,958.83	43,961.02	6,860.76	50,672.57	55,458.71
<i>Note:-It is to mention that investment data is tentative (un-audited) as furnished by the developers in the monthly progress reports</i>											

Rongnichu Project (113 MW) already been commissioned in June 2021(FY 2021-22)and Sorang Project (100 MW) already been commissioned in September 2021(FY2021-22)

Chapter 8

Status of Environmental and Forest Clearance of Under Construction Hydro Electric Projects

Status of Environmental and Forest Clearance of Under Construction Hydro Electric Projects								
Sl. No.	Name of Project	State	I.C. (No.xMW)	Benefits (MW)	Date of TEC Clearance	Date of Env. Clearance	Date of Forest Clearance	Date of I. Approval
A Commissioned during 2020-21								
1	Kameng (NEEPCO). Two(2) unit commissioned.	Ar.Pr.	4x150	300.00	30.04.91	29.03.01	03.08.2000	02.12.04
2	Sawra Kuddu HPPCL, commissioned.	H.P.	3x 37	111.00	01.06.07	01.05.07	01.06.06	01.06.07
3	Singoli Bhatwari L&T, commissioned.	Uttarakhand	3x 33	99.00		24.08.07	16.01.09	11.07.08
B Commissioned during 2021-22								
1	Rongnichu #	Sikkim	2x56.5	113.00	-	04.04.07	18.05.09	01.10.08
2	Sorang	H.P.	2x50	100.00	-	07.09.06	Nov, 06	June, 06
C Under Execution								
I	Central Sector							
1	Pakal Dul (CVPPL)	J&K	4x250	1000	03.10.06	12.07.12	15.12.15	28.10.14
2	Parbati-II (NHPC)	H.P.	2x400	800.00	03.01.01	04.06.01	04.09.2001	11.09.02
3	Tehri PSS (THDC)	Utt.	4x250	1000.00	10.10.88	19.07.90	04.06.87	18.07.06
4	Tapovan Vishnugad (NTPC)	Utt.	4x130	520.00	11.08.04	08.02.05	22.04.06	11/2006
5	Lata Tapovan (NTPC)	Utt.	3x57	171.00	08.02.06	21.02.07	30.04.07	01.08.12
6	Vishnugad Pipalkoti (THDC)	Utt.	4x111	444.00	09/2006	22.08.07	28.05.13	21.08.08
7	Ramam-III (NTPC)	W.B.	3x40	120.00	12.09.06	17.08.07	18.10.08	10.09.14
	Subansiri Lower (NHPC)	Ar.	8x250	2000.00	13.01.03	16.07.03	24.06.2004	09.09.03
8		Pr./Asm.						
9	Naitwar Mori (SJVN)	Uttarakhand	2x30	60.00	02.03.10	16.06.2016	05.08.2016	16.10.17
10	Teesta St. VI	Sikkim	4x125	500.00	27.12.2006	21.09.06	23.05.2008	08.03.2019
11	Ratle (NHPC)	J&K	4x205+1x30	850.00	19.12.2012	12.12.12	27.04.12	11.02.2021
12	Kiru (CVPPL)	J&K	4x156	624.00	13.06.2016	24.06.16	19.05.16	08.03.19
13	Rangit-IV	Sikkim	3x40	120.00	06.07.2007	16.05.07	26.12.07	06.07.07
14	Luhri -I (SJVN)	H.P.	2x80+2x25	210.00	01.05.2018	17.03.2020	28.03.2019	20.11.2020
15	Dhaulasidh (SJVN)	H.P.	2x33	66.00	25.06.2011	21.02.2013	11.08.2020	01.10.2020
Sub-total (Central Sector):				8485.00				
II	State Sector							
16	Parnai (JKSPDC)	J&K	3x12.5	37.50	11.12.1992	24.12.2010	17.05.2013	25.10.2013
17	Lower Kalnai (JKSPDC)	J&K	2x24	48.00	16.08.2013	22.08.2014		16.08.2013
18	Uhl-III	H.P.	3x33.33	100.00	19.09.02	15.11.02	20.12.02	26.09.03
19	Shongtong Karcham	H.P.	3x150	450.00	16.8.12	19.05.11	22.03.11	-
20	Vyasi	Uttarakhand	2x60	120.00	25.10.2011	22.04.10	14.10.13	25.10.2011
21	Shahpurkandi	Punjab	x33+3x33+1x	206.00	08/2009	18.11.81	Not Reqd.	04.05.11
22	Koyna Left Bank PSS	Mah.	2x40	80.00	-	16.05.07	Not Reqd.	20.02.04
23	Indrasagar Polavaram (PPA)	Andhra Pr.	12x80	960.00	21.07.2010	28.07.10	21.07.10	25.02.09
24	Pallivasal Extn.	Kerala	2x30	60.00	31.01.07	Not Reqd.	11.07.07	31.01.07
25	Thottiyar	Kerala	1x30 + 1x10	40.00	05.06.08	Not Reqd.	11.07.07	05.06.08
26	Kundah Pumped Storage-I (T.Tamil Nadu)		4x125	500.00	15.02.18	08.05.07	27.11.08	03.12.08
	Lower Kopli (APGCL)	Assam	2x55+2x2.5	120.00	24.05.16			
27			+1x5			04.09.2019	04.12.2020	Nov,2020
Sub-total (State Sector):				2721.50				
III	Private Sector							
28	Tidong-I	H.P.	100.00	100.00	-	18.06.08	18.06.08	23.07.07
29	Tangnu Romai- I	H.P.	2x22	44.00	-	01.05.09	19.01.10	30.11.07
30	Bajoli Holi	H.P.	3x60	180.00	-	24.01.11	08.07.11	30.12.11
31	Phata Byung	Uttarakhand	2x38	76.00	-	01.05.09	-	30.11.07
32	Maheshwar	M.P.	10x40	400.00	-	07.01.94	Not Reqd.	29.09.06
33	Bhasmey	Sikkim	2x25.5	51.00	-	15.05.07	13.09.10	-
34	Rangit- II	Sikkim	2x33	66.00	-	16.04.10	22.10.10	10.2.10
35	Panan	Sikkim	4x75	300.00	-	02.01.07	21.09.10	07.03.11
36	Kutehr	H.P.	3x80	240.00		05.07.11	19.02.13	31.03.10
Sub-total (Private Sector):				1457.00				
Total : Under Execution				12663.50				

Chapter 9

Status of Civil Package Award (First Package) of Under Construction Hydro Electric Projects

Sl. No.	Name of Project	State	Capacity (MW)	Benefits	Date of CCEA/ Investment	Date of letter of award
Central Sector						
1	Pakal Dul(CVPPL)	J&K	4x250	1000.00	28.10.14	21.02.2018
2	Parbati-II (NHPC)	H.P.	4x200	800.00	11.09.02	09/2002
3	Tehri PSP	Uttarakhand	4x250	1000.00	18.07.06	23.06.2011
4	Tapovan Vishnugad (NTPC)	Uttarakhand	4x130	520.00	11/06	11/2006
5	Lata Tapovan (NTPC)	Uttarakhand	3x57	171.00	08/2012	17.08.2012
6	Vishnugad Pipalkoti (THDC)	Uttarakhand	4x111	444.00	21.08.08	17.01.2014
7	Ramam-III	W.B.	3x40	120.00	10.9.14	10.09.2014
8	Subansiri Lower (NHPC)	Ar.Pr./ Assam	8x250	2000.00	09.09.03	19.12.2003
9	Naitwar Mori (SJVN)	Uttarakhand	2x30	60.00	16.10.2017	05.12.2017
10	Teesta St. VI	Sikkim	4x125	500.00	08.03.19	03/2007
11	Ratle (NHPC)	J&K	4x205+1x30	850.00	19.12.12	04.07.2013
12	Kiru (CVPPL)	J&K	4x156	624.00	08.03.2019	24.02.2020
13	Rangit-IV	Sikkim	3x40	120.00	06.07.07	22.11.2007
14	Luhri -I (SJVN)	H.P.	2x80+2x2	210.00	20.11.20	24.11.2020
15	Dhaulasidh (SJVN)	H.P.	2x33	66.00	01.10.2020	06.05.2021
Sub-total (Central Sector):				8485.00		
State Sector						
16	Parnai (JKSPDC)	J&K	3x12.5	37.50	21.10.2013	25.10.2013
17	Lower Kalnai (JKSPDC)	J&K	2x24	48.00	16.08.2013	12.09.2013
18	Uhl-III	H.P.	3x33.33	100.00	19.09.02	02.04.2003
19	Shongton Karcham	H.P.	3x150	450.00	16.08.12	04.08.2012
20	Vyasi	Uttarakhand	2x60	120.00	25.10.11	10.12.2013
21	Shahpurkandi	Punjab	3x33+3x33+1x8	206.00	04.05.11	11.02.2013
22	Koyna Left Bank PSS	Mah.	2x40	80.00	20.02.04	20.06.2007
23	Indrasagar Polavaram (PPA)	Andhra Pr.	12x80	960.00	21.02.2012	20.12.2017
24	Pallivasal	Kerala	2x30	60.00	31.01.07	31.01.2007
25	Thottiyar	Kerala	1x30 + 1x10	40.00	05.06.08	22.12.2008
26	Kundah Pumped Storage-I (TAN)	Tamil Nadu	4x125	500.00	03.12.08	15.02.2018
27	Lower Kopli (APGCL)	Assam	2x55+2x2.5+1x5	120.00	Nov,2020	21.08.2020
Sub-total (State Sector):				2721.50		
Private Sector						
28	Tidong-I	H.P.	100.00	100.00	23.07.07	07.11.2008
29	Tangnu Romai- I	H.P.	2x22	44.00	2014-15	14.06.2010
30	Bajoli Holu	H.P.	3x60	180.00	30.12.11	29.05.2013
31	Phata Byung	Uttarakhand	2x38	76.00	06.10.08	12.04.2008
32	Maheshwar	M.P.	10x40	400.00	30.12.96	20.02.1997
33	Bhasmey	Sikkim	2x25.5	51.00	Dec-08	12.04.2010
34	Rangit-II	Sikkim	2x33	66.00	10.02.10	24.10.2011
35	Panan	Sikkim	4x75	300.00	07.03.11	22.02.2014
36	Kutehr (JSW Energy (Kutehr)Ltc	H.P.	3x80	240.00	31.03.10	20.10.2019
Sub-total (Private Sector):				1457.00		
Total - Under Execution:				12663.50		

Chapter 9.1

Ordering Status of TG sets for Under Construction Hydro Electric Projects					
Summary- Units Ordered					
Sector	Benefits	Capacity Ordered			Not yet ordered
	(MW)	BHEL	Others	Total Ordered	
Central Sector	8485.00	2055.00	5514.00	7569.00	916.00
State Sector	2721.50	1386.00	1335.50	2721.50	0.00
Private Sector	1457.00	400.00	757.00	1157.00	300.00
Total: Under Execution	12663.50	3841.00	7606.50	11447.50	1216.00

Chapter 9.2

Ordering Status of TG sets of Under Construction Hydro Electric Projects

Sl. No.	Name of the Project/State	Capacity (No.x MW)	Benefits (MW)	Make/Supplier of TG set	Date of Order
A. Central Sector					
BHEL Units					
1	Parbati-II (NHPC),(H.P.	4x200	800.00	BHEL	24.12.02
2	Tapovan Vishnugad (NTPC), Utt.	4x130	520.00	BHEL	01/2008
3	Lata Tapovan, Uttarakhand	3x57	171.00	BHEL	12/2012
4	Vishnugad Pipalkoti (THDC)	4x111	444.00	BHEL	18.11.14
5	Ramam-III (NTPC)	3x40	120.00	BHEL	19.02.15
Sub-total- BHEL			2055.00		
Other Units					
6	Tehri PSP (THDC)	4x250	1000.00	Alstom, France	27.07.11
7	Subansiri Lower (NHPC), Ar. Pr.	8x250	2000.00	Alstom, France & India	11.02.05
8	Naitwar Mori (Uttarakhand)	2x30	60.00	Voith Hydro Pvt. Ltd.	11.06.18
9	Teesta St. VI, (Sikkim)	4x125	500.00	Alstom, India	04/2009
10	Pakal Dul(J&K)	4x250	1000.00	Voith Hydro Pvt. Ltd.	01/2019
11	Rangit-IV, (Sikkim)	3x40	120.00	Andritz Hydro, India	28.08.09
12	Kiru (CVPPL)	4x156	624.00	M/s Andritz Hydro Pvt. Ltd.	24.02.20
13	Luhri -I (SJVN)	2x80+2x25	210.00	Voith Hydro Pvt. Ltd.	16.07.21
Sub-total- Others			5514.00		
Sub-total (Central Sector):			7569.00		
B State Sector					
BHEL Units					
14	Uhl-III (H.P.) BVPCL	3x33.33	100.00	BHEL	15.02.07
15	Shahpurkandi, Punjab ; PSPCL	3x33+3x33+1x8	206.00	BHEL	28.02.14
16	Vyasi , Uttarakhand UJVNL	2x60	120.00	BHEL	31.07.14
17	Polavaram (PPA) Andhra Pr.	12x80	960.00	BHEL	30.03.21
Sub-total- BHEL			1386.00		
Chinese					
18	Pallivasal, Kerala ;KSEB	2x30	60.00	Dongfang Elec.Corp., China	31.01.07
19	Thottiyar, Kerala KSEB	1x30 + 1x10	40.00	Chongqing, China	22.12.08
Sub-total- Chinese			100.00		
OTHER UNITS					
20	Koyna Left Bank PSS, Maharashtra	2x40	80.00	IVRCL Ltd	16.12.10
21	Shontong Karcham, H.P.	3x150	450.00	Andritz Hydro, India	04.03.15
22	Parnai (JKSPDC) J&K	3x12.5	37.50	Andritz Hydro, India	-
23	Lower Kalnai (JKSPDC) J&K	2x24	48.00	GE Power India Pvt. Ltd.	-
24	Kundah Pumped Storage-I (Tamil Nac	4x125	500.00	Megha Engineering & Infrastructure Ltd.	28.11.2019
25	Lower Kopli (APGCL)	2x55+2x2.5+1x5	120.00	M/s ANDRITZ HYDRO Private Ltd	09.09.2021
Sub-total- Others			1235.50		
Sub-total (State Sector):			2721.50		

Sl. No.	Name of the Project/State	Capacity (No.x MW)	Benefits (MW)	Make/Supplier of TG set	Date of Order
C	Private Sector				
	BHEL Units				
26	Maheshwar (M.P.)	4x100	400.00	BHEL	25.06.07
	Sub-total- BHEL		400.00		
	OTHER UNITS				
27	Tidong-I, (H.P.)	100.00	100.00	Alstom, India	28.02.11
28	Tangnu Romai- I, (H.P.)	2x22	44.00	Andritz Hydro, India	17.04.13
29	Phata Byung, (Uttarakhand)	76.00	76.00	Alstom, India	12.04.08
30	Bhasmey, (Sikkim)	2x25.5	51.00	Voith Hydro, India	14.04.10
31	Rangit-II, (Sikkim)	2x33	66.00	Gammon India Ltd.	24.03.12
32	Bajoli Holi, (H.P.)	3x60	180.00	Alstom, India	20.02.15
33	Kutehr(HP)	3x80	240.00	Andritz Hydro Pvt. Ltd., India	13.02.20
	Sub-total- Others		757.00		
	Sub-total (Private Sector):		1157.00		
	Under Execution Total (Units Ordered):		11447.50		
<u>Units not yet ordered</u>					
<u>A</u>	Central Sector				
34	Ratle (J&K)	4x205+1x30	850.00		
35	Dhualasidh (SJVN)	2x33	66.00		
	Sub-total (Central Sector):		916.00		
<u>B</u>	State sector		0.00		
<u>C</u>	Private Sector				
36	Panan, Sikkim	4x75	300.00		
	Sub-total (Private Sector):		300.00		
Total: (Units not yet ordered)			1216.00		
Total: Under execution			12663.50		

Chapter 9.3

Status of ordering of various packages for Under Construction Hydro Electric Projects

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State <u>Region</u>	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencem ent)/ Completion
Under Execution							
A Central Sector							
1	Pakal Dul CVPPL 03.10.2006/ 28.10.2014 4x250 = 1000MW	UT of J&K North Region	Civil works	Power House Package- Power House, Transformer Cavern, MIV cavern, Valve House, TRT , Pressure shaft , Surge Shaft and associated works.	M/s. Afcons- Jaiprakash Associates JV	1051.00	<u>21.02.2018</u> 20.12.2022
				Dam Pkg. - Diversion Tunnel works, Dam works, Spillways, and Part of HRT by DBM and associated works.	M/s Jaiprakash Associates	2853.00	<u>21.06.2018</u> 20.03.2023
			E&M Works	Letter of Award Issued: Supply, Erection & commissioning of E&M components.	M/s. Voith Hydro Limited	703.63	<u>02.01.2019</u> 01.11.2023
			H&M Works	Letter of Award Issued: Supply, Erection & commissioning of HM components.	M/s PES Engineers Pvt. Ltd	286.58	<u>26.08.2019</u> 25.06.2023
			HRT- TBM	Letter of Award Issued- HRT by TBM	M/s L&T Ltd.	2575.63	<u>03.07.2020</u> 02-01-2025
2	Parbati-II NHPC 12.10.1999/ 11.09.2002 4x200 = 800 MW	Himachal Pradesh, North Region	Civil works	Lot-1: Civil & HM works for Dam and Part HRT (0-3500m)	M/s Patel-SEW JV,	322.9	<u>11.09.2002</u> <u>13.08.2011</u> (revised)
				Lot-2: Civil & HM works of HRT (3500-24733m)	M/s Himachal JV	419.89	11.09.2002 10.09.2007
				Contract terminated in March-12 and Fresh awarded as under.			
				Lot-2A: Balance civil works of HRT by TBM	M/s Gammon-CMC JV, Mumbai	455.63	<u>13.08.2013</u> 27.01.2020 (revised)
				Lot-2B: Balance civil works of HRT by DBM and associated HM works *contract has been terminated on 22.12.2018	M/s Valecha Engg. Ltd, Mumbai	176.30	<u>21.11.2013</u> 24.01.2018 (revised)
				Lot 2C : Execution of 1500 m Head Race Tunnel by DBM	M/s Gammon Engineers Contractors Pvt Limited	211.64	<u>02.06.2020</u> <u>01.03.2023</u>
				Lot-3: Civil & HM works of Power House, Pressure Shaft, Surge Shaft & Part HRT (24733-31525)	M/s Gammon India Ltd.	603.69	<u>13.09.2002</u> 24.05.2016 (revised)
				Lot-4: Jiwa Nallah Works	M/s BJ_Techno-HAS (JV)	56.47	<u>11.09.2002</u> 10.09.2007
				Contract terminated and Fresh awarded as under:			
				Lot-4A: Balance Civil & HM works of Jiwa Nallah and associated works *contract has been terminated on 25.05.2019	M/s Coastal Projects, Noida	78.34	<u>22.06.2011</u> 24.03.2015 (revised)

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State <u>Region</u>	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencem ent)/ Completion
			E&M works	Generating Units, EOT Crane Main step up Transformers, Switch Yard and	M/s BHEL	354.44	<u>24.12.2002</u> 23.04.2007
				Electrical & Mechanical Auxiliaries	M/s BHEL	34.2	<u>24.12.2002</u> 23.04.2007
				Design, Manufacture, Supply, Erection , Testing & commg.	M/s BHEL	391.11	<u>29.12.2006</u> 02/2011
			H&M Works	Hydro-Mechanical Packages	M/s Patel-Sew JV	23.61	<u>11.09.2002</u> 13.08.2011 (revised)
3	Tehri PSS, THDC, 18.7.06 Nov-11 (Revised CCEA) 4x250=1000 MW	<u>Uttara khand NR</u>	EPC/ Turnkey Contract	i. Planning, Design and Engg. ii. Civil works iii. Supply of EM & HM (off shore) iv. Supply of E&M and HM (on shore) E&M and HM services	Consortium of M/S Alstom Hydro France and Hindustan Construction Company with M/s Alstom Hydro, France as lead partner	Total in 1843.49 E&M equip:- Euro 62.92 million + 474.43 Cr.	<u>23.06.2011</u> 27.07.11 26.01.2016 (Commencem ent <u>Date</u>)
							U-1: 48 Mth. U-2: 50 Mth. U-3: 52 Mth. U-4: 54 mth. (from commenc.)
4	Tapovan Vishnugad NTPC 11.08.2004/Nov, 2006 4x130 = 520 MW	<u>Uttara khand NR</u>	Civil works	Construction of Barrage and De- silting chambers	M/s SSJV Projects Pvt. Ltd. and M/s ZVS, Russia	276..91	01/2007 07/2012 Contract terminated in Nov-10.
				Contract terminated in November-10 and fresh award made in July-12			
				Construction of Barrage and De- silting chambers (Balance Works)	M/s Rithwik Projects Pvt. Ltd., Hyderabad.	457.57	07/2012 03/2015
				Works have been re-awarded. Details to be provided.	M/s L&T Ltd. and M/s Alpine Mayreder Bau GmbH	455.921	11/2006 08/2012
				Power House & Penstock package	M/s Patel Engg. Pvt. Ltd.	221.28 Cr. + Euro 37.58m	05/2007 08/2012
			E&M works	Turbine generating units and associated auxiliaries	M/s BHEL	328.28 crs.	1./2008 12/12
			H&M works	Manufacturing, erection & Commissioning of various gates.	M/s Om Metal Infra project Ltd.	64.19 Cr. + €1.26m	10./07 09/12
5	Lata Tapovan, NTPC Aug-2012 3x57= 171 MW	<u>Uttara khand NR</u>	Civil & HM works	EPC Contract	M/s L&T	780.54	17.08.2012 16.08.2017
			E&M Package		BHEL	2611.04	Dec, 12 June, 17
6	Vishnugad Pipalkoti, THDC 21.08.2008 4x111= 444 MW	<u>Uttara khand NR</u>	Civil & HM works	EPC Contract	M/s HCC Ltd	1597.30	17.01.2014 16.07.2018
			E&M Package	EPC Contract	BHEL	360.36	18.11.2014 17.11.2018
7	Teesta-VI NHPC 08.03.2019/ 07./2007(FC) 4x125= 500MW	<u>Sikkim NER</u>	Civil works	Barrage, Desilting Basin, SFT, Intake part of HRT-I &HRT-II & other associated structure	M/s Jaiprakash Associate Limited	1710	31.03.2020
				Part of HRT-I &HRT-II , Surge Shaft, Power House ,TRT & other associated structure	M/s Patel Engineering Limited	1251	22.09.2021

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State <u>Region</u>	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencem ent)/ Completion
			H&M works		M/s PES Engineers Private Limited	INR 100.76 & EURO 17.5 lakhs	27.10.2021
			E&M works	E&M Package, EM-I	M/s GE Power India Ltd.	107.49	14.12.2020
				E&M Package, EM-II	M/s BHEL	150.10	04.09.2020
				E&M Package, EM-III	M/s Technico India Pvt Ltd	3.98	22.09.2020
				E&M Package, EM-IV	M/s Jakson Ltd	3.07	1.10.2021
				E&M Package, EM-V	M/s SHES Air and Automation	5.63	06.08.2021
				E&M Package, EM-VI	M/s Avidas Technovators Pvt. Ltd.,	3.89	16.04.21
				E&M Package, EM-VII	M/s PGCIL	55.57	21.12.2021
				E&M Package, EM-VIII	M/s B. C. Technomation	6.23	28.08.2021
8	Subansiri Lower NHPC 07.06.2001/09.0 9.03 8x250= 2000 MW	<u>Ar.Pr/ Assam NER</u>	Civil works	Dam/Barrage	M/s BGS – SGS - Soma JV, Hyderabad	1098.32	19.12.2003 12/2009
				Power House & Tail Race civil works	M/s L & T LTD, Chennai	921.59	19.12.2003 12/2009 (Contract Foreclosed on 28.04.2015)
				Surge Tunnel Works	M/s L & T LTD, Chennai	422.50	14.05.2009 11/2012 (Contract Foreclosed on 28.04.2015)
				Balance civil work of Powerhouse complex from HRT to Tail Race Channel	M/s Patel Engineering Ltd, Mumbai	1564.41	01.09.2021 12/2023
			E&M works	Supply of CIF/CIP: Supply of all off shore equipments and material including general and specified spares.	Consortium of M/s Alstom Power Hydraulique, France And M/s Alstom Project India Ltd.	Euro 76.80 million + US\$ 6,779,760.	11.02.2005 08/2010
				Ex-works supply of all equipment and material including general and specified spares of Indian origin.	Consortium of M/s Alstom Power Hydraulique, France and M/s Alstom Project India Ltd.	€ 23.21 million + US\$ 14,56 million + 727.97 crs	11.02.2005 08/2010
				Local transportation including port clearance and port charges and inland insurance and installation services.	M/s Alstom Project India Ltd.	1,23,74,37,486. 00	11.02.2005 08/2010
			H&M works	Supply, erection & commng. of gates	M/s Texmaco Ltd.	283.48 Cr. + Euro 2.22 M	19.06.2006 04/2010

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State <u>Region</u>	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencement)/ Completion
9	Ramam-III NTPC Ltd. 3x40= 120 MW	<u>W.B.</u> <u>E.R.</u>	Civil works & HM works	Approach road to right bank of barrage to access various project component, Barrage construction, Under ground de- silting chamber with SFT and 5.1 km HRT	M/s. Simplex-Apex-JV	360.83	<u>10.09.14</u> <u>09/2019</u>
				Access from bridge on Rammam river to various proj. components, 3.1 km HRT , Surface Power House, 740 m TRC and 132 KV Switchyard.	M/s. SEW Infrastructure Ltd.	265.39	<u>12.12.14</u> <u>12/2019</u>
			E&M works	Design, Engineering, Manufacturing, Supply, Insurance, Erection, Testing & Commissioning works for EM works EPC contract package.	M/s. BHEL	224.67	<u>19.02.2015</u> <u>11/2018</u>
10	Naitwar Mori (SJVN Ltd.) 02.03.2010 (2x30=60 MW)	Uttarakha nd	Civil Works	C/o all civil works of barrage, intake, desilting tank, HRT, Power house, surge shaft, TRT, Adits & infra works etc.	M/s. Jaiprakash Associates Ltd.	370.87	05.12.2017/ 04.09.2021
			E&M works	Design, engineering, manufacture, transportation, erection and commissioning of all EM components of project.	M/s. Voith Hydro Pvt. Ltd.	113.49	11.06.2018/ 10.10.2021
			H&M works	Design, engineering, procurement, fabrication, transportation, erection and commissioning of all HM components incl. Pressure shaft liner of project.	M/s GHW Pvt. Ltd.	34.44	18.04.2018/ 17.06.2022
11	Ratle GVK Ratle HEP Pvt. Ltd. (GRHEPPL) 19-12-2012 <u>4x205+1x30=</u> <u>850 MW</u>	<u>J&K</u> <u>NR</u>	NIT for the work "Turnkey execution of 850 MW Ratle Hydro Electric Project located at Kishtwar district in the Union Territory of Jammu & Kashmir, India" has been issued on 22.07.2021. Award of work is scheduled to be done within 11 months from zero date i.e. 11.02.2021.				
12.	Kiru CVPPL 13.06.2016 4x156=624 MW	<u>J&K</u> <u>NR</u>	Civil Works	Civil and HM works of DT, concrete gravity Dam, Intake, Pressure shaft, TRT and underground Power House.	M/s. Patel Engineering Ltd.	2240.27	<u>24.02.2020</u> <u>23.04.2024</u>
			HM Works	Providing all service, Model testing, transportation, testing, Commissioning of Radial Gates, Vertical Gate, Gantry Cranes, Stoplogs, Steel liner for Pressure Shaft and Trash racks.	M/s PES Engineers Pvt. Ltd.	202.10	<u>24.02.2020</u> <u>23.01.2024</u>
			E & M works	Design, Manufacture, Supply Erection, Testing & commissioning of TG, 400 KV GIS, 400 KV outdoor pothead yard equipment, Associated Accessories and Auxiliaries,	M/s Andritz Hydro Pvt. Ltd.	552.52	<u>24.02.2020</u> <u>23.07.2024</u>

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State Region	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencem ent)/ Completion
13.	Rangit-IV Jal Power Corp. Ltd. 06.07.2007/23. 10.2007(FC) 3x40 MW= 120	Sikkim NER	Civil works	Construction of Balance Civil works package: Diversion Channel, Coffe Dams, Dam, Spillway & Stilling Basin, Intake structure, Desilting Chambers, SFT, HRT, Surge Shaft, Pressure Shaft, Surface power house, TRC & other associated structures etc.	M/s Rithwik-HIPL Joint Venture	452.11	27.08.2021
			H&M works	Hydro-mechanical Works package of Rangit Stage-IV HE Project,	M/s PES Engineers Private Limited	100.40	28.06.2021
			E&M works	Electromechanical Works Package EM-2 for Design, Supply, Erection, Testing 7 Commissioning of Balance of Plant (BOP) items	M/s Andritz HydroPrivate Limited	80.12	08.07.2021
14.	Luhri Stage-1 SJVN Ltd. 01.05.2018 2x80+2x25=21 0 MW	Himacha l Pradesh	Civil and HM works	Design & engineering services, Civil and HM works of project.	M/s Luhri Hydro Power Consortium (A consortium of Patel Engineering and HES Infra Pvt. Ltd.)	976.50	24.11.2020/ 23.11.2025
			E&M works	Design, engineering, manufacture, transportation, erection and commissioning of all EM components of project.	M/s. Voith Hydro Pvt. Ltd.	420.28	16.07.2021/ 15.05.2025
15	Dhulasidh Hydro Electric Project SJVN Ltd (2x33 MW = 66MW)	Himacha l Pradesh NR	Civil and HM works	Design & engineering services, Civil and HM works of project.	M/s Rithwik Projects Pvt Ltd	526.92	06.05.2021/ 05.05.2025
			E&M works	Design, engineering, manufacture, transportation, erection and commissioning of all EM components of project.	Under Tendering	-	-
B	State Sector						
16	Parnai JKSPDC 21.10.2013 3x12.5= 37.5 MW	NR J&K	Civil works	EPC contract	M/s. Patel Engineering Ltd. & M/s. Alstom India.		25.10.2013
			E&M works	T.G. Set	M/S.Andritz Hydro, India		
17	Lower Kalnai JKSPDC 16.08.2013 2x24= 48 MW	NR J&K	Civil works	EPC contract	M/s Coastal Projects Ltd.		12.09.2013
			E&M works	T.G. Set	M/s. GE Power India Pvt. Ltd.		
18	Uhl-III, BVPC Ltd. 19.09.02 / ----- - (TEC -2x50 MW) 3x33.3 =100	H.P. NR	Civil works & HM Works	Neri Intake works & power channel	M/s SSJVPP Ltd. 12 th floor S.N.Tower 25/2 M.G.Road, Bangalore Fresh Package awarded on 25.10.08 to: Continental Corp Project Ltd.	8.68	18.04.05 15.8.07 Re-awarded on 25.10.08

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State <u>Region</u>	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencem ent)/ Completion
				Head Race Tunnel (HRT)	M/s SSJVPP Ltd. 12 th floor S.N.Tower 25/2 M.G.Road, Bangalore 560001 Package re-awarded to: Continental Corp Project Ltd., Re-awarded to M/s Abir Infrastructure Pvt. Ltd., Gurgaon.	69.58	<u>02.04.03</u> 30.04.07 15.10.2010
				Rana Intake Works & Power channel	M/s TRG Industries Pvt Ltd E- 461 Greater Kailash –II New Delhi	17.53	<u>26.07.05</u> 26.10.07
				Penstock fabrication, erection	M/s PES.Engineers Pvt. Ltd. Hyderabad-500016	57.26	<u>27.05.05</u> 27.11.07
				Power House	M/s Pilot Engg., Ludhiana	9.87	<u>19.6.2007</u> 12/2009
			E&M works	Generating Equipment & Associated Aux, Transformers	M/s BHEL	117.36	<u>15.02.07</u> 15.04.10
19	Shongtong Karcham H.P. Power Corpn. Ltd. Clearance: 16.08.2012/ 3x150= 450 MW	H.P. 2017-18 2017-18	Civil And H&M works	EPC Contract Package for Civil & HM works	M/s Patel Engineering Ltd.	103.24	<u>04.08.2012</u> 03.08.2017
20	Shahpurkandi, Irrigation Deptt/PSPCL 04.05.2011 3x33+3x33+1x8 = 206 MW	<u>Punjab NR</u>	Civil works & HM works	Main Dam alongwith Two head regulators	SOMA-BUREYA Joint Venture	687.51	<u>11.02.2013</u> Oct- 2016
				Hydel Channel	M/s Gurinder Singh Contractor	90.11	<u>26.02.2013</u> Oct- 2015
			E&M works	EPC Contract	BHEL		<u>28.02.14</u>
21	Koyna Left Bank PSS WRD, Govt. of Mah. 20.02.2004 2x40 = 80 MW	<u>Maha. WR</u>	Civil and H&M works	Barrage, Intake tunnel, Twin lake tap, Ventilation tunnel, Power house, Intake structure ,HRT, Pressure shaft, tail surge shaft, pen stoke, TRT, Bus duct tunnel, Lower intake structure	M/s B.T. Patil-Malaxmi (JV), Pune M/s Patel Engg. Ltd. Mumbai	131.91 Crs. 118.86 Crs.	<u>20.06.2007</u> 30.06.2013 <u>03.10.2007</u> 30.06.2016
			E&M works	Design, manufacture, testing & commissioning of TG unit and auxiliaries	M/s IVRCL Ltd. Pune Turbine- Litostroj Slovenia Generator- Koncar, Croatia	Euro 4.03 Crs + 177.99 Crs	<u>16.12.2010</u> 15.12.2014
22	Polavaram (PPA) 21.07.10/ 25.02.09 12x80 = 960MW	<u>Andhra Pradesh</u> <u>S.R.</u>	Civil works & HM works & E&M works	Investigation and L.P schedules etc., (Balance) &	M/s. Trans stroy-JSCECUES (JV), Hyderabad	4054.00	<u>02.03.2013</u> <u>01.03.2018</u>
				EPC contract on TURNKEY basis.	M/s. Navayuga Engineering Company Contract terminated on 14.08.2019 & re-awarded to M/s Megha Engineering and Infrastructure Limited on 01.11.2019	3220.28 Crs 2810.88 Cr.	<u>20.12.2017</u> <u>01.11.2019</u>
23	Pallivasal KSEB/ Not Req./31.1.2007 2x30=60	<u>Kerala SR</u>	Civil, H&M works and E&M works	The work was awarded to M/s ESSAR – DEC – CPPL consortium as a single package and an agreement in this regard was executed on 31.01.2007. The contractual date of completion is 48 months i.e. 01.3.2011. E&M: Dongfang Electric Corporation, China (DEC)		242.96 Crs + US\$57 million	<u>31.01.2007</u> 01.03.2011
22	Thottiyar KSEB	<u>Kerala SR</u>	Civil works	Dam, Water Conductor System, power House	M/s Coastal Projects Private Ltd-	44.23	<u>22.12.2008</u> 19.05.2012

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State Region	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencem ent)/ Completion
	1x30 + 1x10= 40 MW		H&M works	Gates, erection, commissioning	Chongqing Joint Venture, Hyderabad E&M: Chongqing, China	24.09	<u>22.12.2008</u> 19.05.2012
			E&M works	Planning, Engineering, Manufacture, Supply, Erection, testing & commissioning		75.68	<u>22.12.2008</u> 19.05.2012
25	Vyasi UJVNL 2x60=120 MW	Uttra khand	Civil works	Intake, Dam half portion of HRT 1.35 km.	M/s. Gammon India Ltd.	317 Crs.	
				Half posrtion of HRT 1.35 km, Surge Shaft, Penstock, Powerhouse, TRC	M/s. NPCC Contract value	114.59 Crs.	
			E&M works	EPC contract for E&M Works	M/s. BHEL	125 Crs.	<u>26.03.2014</u>
26	Kundah Pumped Storage Phase -4 x125=125 MW <						

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State <u>Region</u>	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencem ent)/ Completion
			E&M works	Supply, Installation, testing & commissioning of TG sets	M/s Alstom Projects, India	84	<u>28.02.2011</u> 27.05.2013
29	Tangnu Romai-I M/s Tangu Romai Power generation 2x22= 44 MW 30.11.2007 HPSEB	<u>HP</u> <u>NR</u>	Civil works	Construction of Diversion Barrage, Intake, desilting, HRT, Surge Shaft, Penstock, Power House & Tail Race Channel	M/s Sai Urja Hydel Projects (P) Ltd., Shimla	164.7	<u>14.06.2010</u> 06/2014
			E&M works	Supply, installation, T&C of TG set, Switchyard equipment & associated auxiliaries	M/s Andritz Hydro, India	56	<u>17.04.2013</u> 16.07.2015
30	Bajoli Holi M/s GMR Bajoli Holi Hydro Power Pvt. Limited 31.12.2011	<u>HP</u> <u>NR</u>	Civil works	Lot-I & Lot-II All Major Civil Works	M/s Gammon India Ltd.	369 +400	<u>29.05.2013</u> 30.11.2017
			E&M works	E&M works	M/s. Alstom, India		
31	Phata Byung M/s Lanco 06.10.2008 2x38 MW = 76 MW	<u>Uttarakha</u> <u>nd</u> <u>NR</u>	Civil works	Dam, water conductor System, power House	Lanco Infratech Ltd.	206	<u>12.04.2008</u> 07/2012
			H&M works	Design, Engineering, Manufacture, Farication & Erectio,n of all hydro- mechanical equipment	M/s CIMMCO	34	<u>12.04.2008</u> 08/2012
			E&M works	Manufacturing., Supply, erection & commng. of TG units	M/s Alstom Project, India	84	<u>12.04.2008</u> 08.2012
32	<u>Maheshwar</u> , SMHPCL 12 96/ 29.9.2006 (FC) 10x40= 400MW	<u>M. P.</u> <u>WR</u>	Civil and HM works	All civil works like dam, Power Dam, HRC, Penstock PH etc.	M/s SEW Construction –Prasad and Company Ltd.	275.0 Crs. 22.02.97	<u>22.02.1997</u> 03/2005
			E&M works	Manuf., Supply, erection & commng. of TG units	M/s BHEL	470.5 Crs. + USD \$ 11.74 M 18.05.2001	<u>25.06.2007</u> 10/ 2009
33	Bhasmey Gati Infrastructure 2x25.5 = 51 MW	<u>Sikkim</u> <u>NER</u>	Civil works	Dam, Tunnels , Power House, Surge Shaft, Pressure Shaft, Intake	M/s Simplex Infrastructure Ltd.	160	<u>12.04.2010</u> 11/2012
			H&M works	N.A.			
			E&M works	Manufacturing., Supply, erection & commng. of TG units	M/s Voith Hydro, India	93	<u>14.04.2010</u> 10/2012
34	Rangit-II Sikkim Hydro Power Limited 2x33= 66 MW	<u>Sikkim</u> <u>NER</u>	Civil &HM works	EPC Contract	M/s Coastal Project Limited	220.35	<u>13.12.2011</u> 23.10.2013
			E&M works		M/s. Gammon India Ltd.		<u>24.03.2012</u>
35	Panan Himagiri Hydro Energy Pvt. Ltd. 07.03.2011 4x75= 300 MW	<u>Sikkim</u> <u>NER</u>	Civil works	Coffer Dam, Diversion Tunnel, Dam, Desilting Basin, Power House, Surge Shaft, Pressure Shaft, Intake etc.	M/s Essar Projects (India) Ltd..	392.40 (Excl. cost of cement, Steel, explosives)	<u>22.02.2014</u> 21.02.2018 (48 months)
			E&M works	Manufacturing., Supply, erection & commng. of TG units	Under Award		
36	Kutehr M/s JSW Energy (Kutehr) Ltd. 3x80 = 240 MW 31.08.2010	<u>HP</u> <u>NR</u>	Civil works	Lot-1 Civil works for River diversion, Barrage,Power intake & Part of HRT.	-M/s Angelique-PCC Constorium.	567.00	<u>20.10.2019</u> 19.06.2023
				Lot-2 Civil works for balance HRT, Surge Shaft, Pr. Shaft, Steel liner, under ground power house, TRT, and Pothead yard.	-M/s MF Bumi Geotech private ltd.	507.40	<u>25.11.2019</u> <u>19.05.2023</u>
				Lot-3 Complete HM works	-M/s P.E.S. Engineers Pvt Ltd.	60.00	19.09.2019 (LOI date)
				Lot-1D Design, fabrication ,supply and erection of steel liner and pen stock.	-M/s Greyhound Engineers India Private Ltd.	18.00	19.09.2019 (LOI date)

Sl. No.	Project name/ Exec. Agency CEA clearance/ Approval Capacity (MW)	State <u>Region</u>	Contract	Scope of works & brief details	Contracting Agency (Name & Location)	Contract value (Rs. Crs.)	Date of Contract (commencem ent)/ Completion
			E&M works	Electro Mechanical works.	M/s Andritz Hydro Pvt. Ltd.	270.74	13.02.2020 (LOI date)

CHAPTER – 10

Status of financial closure of Under Execution Private Sector H. E. Projects

I. No.	Name of Project, State, Capacity, Date of TEC	Implementing Agency	Financial Closure Status	Remarks/ Constraints
	Under Execution			
1	Maheshwar, M.P., 10x40 MW, 30.12.96	Shree Maheshwar Hydel Power Corporation Ltd.	Financial closure achieved on 29.9.2006.	
2.*	Teesta-VI, Sikkim 4x125 MW 27.12.2006	M/s Lanco Energy Pvt. Ltd.	Financial closure achieved in July, 07.	
3.	Rangit-IV, Sikkim 3x40 MW 06.07.2007	M/s Jal Power corporation Ltd.	Financial closure achieved on 25.01.2010.	
4.	Tidong-I, H.P. 100 MW 23.07.2007	M/s Nuziveedu Seeds	Financial closure achieved on 25.03.2010.	
5.	Tangu Romai, H.P. 2x22 MW 30.11.2007	Tangu Romai Power Gen. Pvt. Ltd.	Financial closure achieved on 22.01.2010.	
6.	Phata Byung Uttarakhand 2x38 MW 06.10.2008	M/s Lanco	Financial closure achieved on 25.07.2009.	
7.	Bhasmey, Sikkim 2x25.5= 51 MW Dec, 2008	M/s Gati Infrastructure	Financial closure achieved on 25.03.2010	
8.	Rangit Stage- II Sikkim 2x33= 66 MW 10.02.2010	M/s Sikkim Hydro Power Ventures Limited	Financial closure achieved on 15 th Jan, 2014, 31 st March 2015 (Revised).	
9.	Bajoli Holi, H.P. 3x60= 180 MW 30.12.2011	M/s GMR Bajoli Holi Hydro Power Pvt. Ltd.	Financial closure achieved. Loan agreement signed with IDBI Bank.	
10.*	Ratle, J&K 4x205+1x30= 850 MW	M/s GVK Ratle HEP Pvt. Ltd. (GRHEPPL)	Financial closure achieved.	
11.	Panan, Sikkim 4x75= 300 MW 07.03.2011	Himagiri Hydro Energy Pvt. Ltd.	Financial closure with total debt of Rs. 1516.42 is tied up with PFC ((808.76 Crores), PTC (Rs. 120 Crores) & REC (Rs 587.67 Crores).	
12.	Kutehr, H.P. 3x80=240 MW	M/s JSW Energy (Kutehr) Ltd	Financial closure achieved on 14.01.2021	

*Now these are CPUS's Projects

CHAPTER-11

DETAILS OF UNDER DEVELOPMENT HYDRO ELECTRIC PROJECTS (ABOVE 25 MW) HAVING TIME/COST OVERRUN-State Wise

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
	Andhra Pradesh									
1	Polavaram (12x80 = 960 MW) APGENCO / Irr. Deptt., A.P.	1 2 3 4 5 6 7 8 9 10 11 12	80 80 80 80 80 80 80 80 80 80 80 80	2016-17 2016-17 2016-17 2016-17 2016-17 2016-17 2017-18 2017-18 2017-18 2017-18 2017-18 2017-18 (Mar'18)	2024-25 2024-25 2024-25 2024-25 2024-25 2024-25 2025-26 2025-26 2025-26 2025-26 2025-26 2025-26 (Mar,26)	96 96	3013.68 (2010-11 PL) (Power Component)	5338.95 (2016-17 PL) (Power Component)	2325.27 (77.15)	Works stalled since 19.07.2019 as APGENCO asked contractor Navayuga Engineering Company Ltd. (NECL) to stop all works and termination of contract issued on 14.08.2019. The writ petition filed by MECL was disposed by Hon'ble High Court against NECL on 14.12.2020. Final Contract concluded with new contractor M/s MEIL for execution of PHEP works on 30.03.2021
	Arunachal Pradesh									
2	Subansiri Lower (8x250 = 2000 MW) NHPC	1 2 3 4 5 6 7 8	250 250 250 250 250 250 250 250	2009-11 2009-11 2009-11 2009-11 2009-11 2009-11 2009-11 2009-11 (Sep'10)	2022-23 2022-23 2023-24 2023-24 2023-24 2023-24 2023-24 2023-24	155	6285.33 (12/02)	19992.43 (04/17)	13707.10 (218.08)	➤ Delay in transfer of forest land. ➤ Disruption of works by locals in Ar. Pradesh side. ➤ Slope failure in Power House in Jan, 2008. ➤ All works except safety works were stalled from December, 2011 to October, 2019 due to agitation launched by activists in Assam against construction of Project. Work restarted w.e.f. 15.10.2019.

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
	Assam									
3	Lower Kopili (2x55+2x2.5+1x5 =120MW)	1 2 3 4 5	55 55 5 2.5 2.5	2024-25 2024-25 2024-25 2024-25 2024-25 (Jun'24)	2024-25 2024-25 2024-25 2024-25 2024-25 (Jun'24)	NIL	1115.91 (01/15)	1847.07 (2020)	731.16 (65.52)	
	Himachal Pradesh									
4	Parbati - II (4x200 = 800 MW) NHPC	1 2 3 4	200 200 200 200	2009-10 2009-10 2009-10 2009-10 (Sept'09)	2022-23 2022-23 2022-23 2022-23 (Mar,23)	162	3919.59 (12/01)	9897.59 (04/18)	5978 (152.51)	➤ Delay in revised forest clearance. ➤ TBM suffered extensive damage due to heavy ingress of water and slush in TBM face in Nov, 2006. Due to poor geology. ➤ Flash flood in 2004,2005,2010 and 2011. ➤ Contractual issues. ➤ Cash flow issues with civil contractors.
5	Uhl-III (3x33.33 = 100 MW) BVPCL	1 2 3	33.33 33.33 33.33	2006-07 2006-07 2006-07 (Mar'07)	2022-23 2022-23 2022-23 (Dec,22)	189 189 189	431.56 (09/02)	1281.52 (12/12)	849.96 (196.95)	➤ Delay in transfer of forest land. ➤ Delay in acquisition of private land ➤ Delay in transfer of quarry sites. ➤ Contract for construction of HRT rescinded twice i.e. during April, 2008 & July, 2010 due to slow progress and non-performance by the contractor. ➤ Poor geology in HRT. ➤ Leakage in Penstock in July,2018 and Rupture in May,2020

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
6	ShongtomKarcham (3x150 = 450 MW) HPPCL	1 2 3	150 150 150	2016-17 2016-17 2016-17 (Mar'17)	2024-25 2024-25 2024-25 (Mar,25)	92 94 96	2807.83 (07/11)	2807.83 (07/11)	Nil	➤ Shifting of Army Ammunition Depot. ➤ Disruption of works by local people.
7	Bajoli Holi 3x60= 180 MW M/s GMR BajoliHoli	1 2 3	60 60 60	2018-19 2018-19 2018-19 (May'18)	2021-22 2021-22 2021-22 (Sept,21)	40	1696.93 (12/11)	3094.00 (6/20)	1397.07 (82.32)	➤ Slow progress due to poor approach to project components.
8*	Tangnu Romai-I (2x22 = 44 MW) TRPGPL	1 2	22 22	2014-15 2014-15 (Jun'14)	2024-25 2024-25 (subject to re- start of works(4 years))	129	255.00 (01/07)	641.89 (2018)	386.89 (151.72)	➤ Works are stalled since January, 2015 due to fund constraints with developer.
9	Tidong-I 2x50 =100 MW NSL Tidong (w.e.f. 04.09.2018 Statkraft India Pvt. Ltd. Has acquired the 100% equity in the project)	1 2	50 50	2013-14 2013-14 (Dec'13)	2022-23 2022-23 (Oct 22)	106	543.15 (06/18)	1472.00	928.85 (171.01)	➤ Delay in NOC by Projects affected Panchayats. ➤ Suspension of works by Govt. for one year. ➤ Funds constraints with the developer
10	Kutehr 3x80=240 MW JSW Energy (Kutehr) Ltd	1 2 3	80 80 80	2024-25 2024-25 2024-25 (Nov'24)	2025-26 2025-26 2025-26 (Nov'25)	12	1798.13 (09/2011)	2750Crs (03/2019)	951.87 (52.93)	➤ Slow mobilization due to Covid-19 Lockdown.

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
11	Luhri Hydro Electric Project Stage-I (2X 80+2X25 MW = 210 MW)	1 2 3 4	80 80 25 25	2025-26 2025-26 2025-26 (Feb'26)	2025-26 2025-26 2025-26 (Jan'26)	NIL	1810.56 (05/2020)			➤ Work started recently ➤ Rs. 1810.56 Crore which includes project cost of Rs. 1744.37 Crores (05/2020 PL) and Rs. 66.19 Crore for enabling infrastructure (to be availed as budgetary support from GoI)
12	Dhaulasidh (SJVN) 2x 33+66MW Hamirpur/ Kangra	1 2	33 33	2025-26 2025-26 (May'25)	2025-26 2025-26 (May'25)	NIL	687.97 (05/2020)			• Work started recently • (Rs. 687.97 Crores which includes project cost of Rs. 666.32 Crores (05/2020 PL) and Rs. 21.65 Crores for enabling infrastructure (to be availed as budgetary support from GoI)
	Govt. of UT of J&K									
13	PakalDul (4x250= 1000 MW) CVPPL	1 2 3 4	250 250 250 250	2020-21 2020-21 2020-21 2020-21 (Apr'20)	2025-26 2025-26 2025-26 2025-26 (July'25)	} 63	8112.12 (03/13)	8112.12 (03/13)	Nil	➤ Delay in award of works due to higher bids.
14	Parnai 3x12.5= 37.5 MW JKSPDC	1 2 3	12.5 12.5 12.5	2017-18 2017-18 2017-18 (Jan'18)	2022-23 2022-23 2022-23 (Mar,23)	} 62	640.86 (Completion cost)	640.86 (Completion cost)	Nil	➤ Delay in Land acquisition.
15*	Lower Kalnai 2x24= 48 MW JKSPDC	1 2	24 24	2017-18 2017-18 (Sep'17)	2025-26 2025-26 (subject to re- start of works (4 years))	} 102	576.87 (12/12) (Completion cost)	576.87 (12/12) (Completion cost)	Nil	➤ Works on all fronts at Dam and Power House site are stalled since 24.01.2018 due to payment dispute with subcontractors and due to non-settlement of extension of time of the contract by the JKSPDC. The contract with M/s. Coastal Projects Ltd. has been

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
										terminated and re-tendering for selection of EPC contractor is under process.
16	Kiru (4x156=624 MW) CVPPL	1 2 3 4	156 156 156 156	2023-24 2023-24 2023-24 2023-24 (Aug,23)	2024-25 2024-25 2024-25 2024-25 (Aug,24)	12	4287.59 (09/14)	4287.59 (09/14)	Nil	➤ Slow mobilization due to Covid-19 lockdown
17*	Ratle (4x205+1x30) = 850 MW RHPPL / NHPC	1 2 3 4 5	205 205 205 205 30	2017-18 2017-18 2017-18 2017-18 2017-18 (Jan,18)	2025-26 2025-26 2025-26 2025-26 2025-26 (subject to re-start of works(5 years))	98	5281.94 (11/18)	6275.00 (09/2013)	993.06 (18.80)	➤ Project was stalled since 11.07.2014 due to various issues viz. R&R issues, Local issues, Law & order problem etc. Earlier, it was under execution by private sector developer and some works already have been done. There is no progress since 11th July, 2014. JV of Govt. of UT of J&K and NHPC has been formed. CCEA clearance received. Award of works is to be done.
	Kerala									
18	Pallivasal 2x30 = 60 MW KSEB	1 2	30 30	2010-11 2010-11 (Mar'11)	2021-22 2021-22 (March,22)	132	298.018 (2004)	550.00 (2018)	251.98 (84.55)	➤ Delay in land acquisition. ➤ Poor geology strata in HRT. ➤ Works stopped by contractor since 28.1.15 to 11.04.2017 due to contractual issues. Contract terminated on 13.09.2018 and re-awarded in August, 2019.
19	Thottiyar (1x30+1x10)= 40MW KSEB	1 2	30 10	2012-13 2012-13 (Apr'12)	2021-22 2021-22 (Dec,21)	116	136.79 (2007)	280 (2018)	143.21 (104.69)	➤ Land acquisition issue. ➤ The works of weir and approach channel stopped from 2010 to 2012 by local people. ➤ The work stopped by Court from 12.12.2012 to April-2013. ➤ Financial crunch with contractor leading to foreclosure of contract in April,2017

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
										and balance works re-awarded in January, 2018.
	Madhya Pradesh									
20*	Maheshwar (10x40 = 400 MW) SMHPCL	1 2 3 4 5 6 7 8 9 10	40 40 40 40 40 40 40 40 40 40	2001-02 2001-02 2001-02 2001-02 2001-02 2001-02 2001-02 2001-02 2001-02 2001-02 (Mar'02)	2023-24 (subject to re- start of works(Two years)	264	1569.27 (96-97)	6793 (2016-17)	5223.73 (332.87)	➤ Works suspended since Nov-11 due to cash flow problem with developer. M.P. Power Management Company Ltd. has terminated the Power Purchase Agreement with SMHPCL on 18.04.2020.
	Maharashtra									
21*	Koyna Left Bank PSS 2x40 = 80 MW WRD, Maha	1 2	40 40	2014-15 2014-15 (Oct'14)	2025-26 (subject to re- start of works (4 years)	137	245.02 (1999)	379.78 (2014)	134.76 (54.99)	➤ Project stalled since July, 2015. The current expenditure on the project has already reached to almost original administrative approved cost level. Proposal for revival of the project is submitted to the Govt. of Maharashtra.
	Punjab									
22	Shahpurkandi 3x33+3x33+1x8 =206 MW, Irrigation Deptt. &PSPCL	1 2 3 4 5 6 7	33 33 33 33 33 33 8	2015-16 2015-16 2015-16 2015-16 2015-16 2015-16 2015-16	2024-25 2024-25 2024-25 2024-25 2024-25 2024-25 2024-25 (Aug, 24)	101 101	1835.50 (04/08) (Power Component)	1938.74 (02/18) (Power Component)	103.24 (5.62)	➤ Works of Dam stopped since 29.08.2014 due to inter-state dispute between states of J&K & Punjab on sharing of waters of river Ravi and Tariff.
	Sikkim									
23	Teesta Stage VI	1	125	2012-13	2023-24		5748.04	5748.04	NIL	➤ Poor geology.

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
	(4x125 = 500 MW) LancoTeesta Hydro Power Ltd. (LTHPL) (Project taken over by NHPC w.e.f. 08.03.2019)	2 3 4	125 125 125	2012-13 2012-13 2012-13 (Jul'12)	2023-24 2023-24 2023-24 (Mar,24)	140	(07/2018)	(07/2018)		➤ Land acquisition. ➤ Contractual issues ➤ Funds constraints with developer (Private) and stalled from April, 2014 to October, 2019 ➤ M/s. LTHPL came under Corporate Insolvency Resolution Process. NHPC Ltd. emerged as H1 bidder. CCEA approval was accorded to NHPC on 08.03.2019. NCLT on 26.07.2019 approved resolution plan of NHPC for acquisition of LTHPL. ➤ Taking over along with all assets and documents as 'Going concern' completed on 09.10.2019.
24*	Bhasmey (2x25.5 =51 MW) Gati Infrastructure	1 2	25.5 25.5	2012-13 2012-13 (Jun'12)	2024-25 2024-25 (subject to re- start of works(3 years))	153	408.50 (2012-13)	746.01 (03/18)	337.51 (82.62)	➤ Works are stalled since Sept., 2016 due to funds constraints with developer ➤ .
25*	Rangit-IV HE Project (3X40 = 120 MW) JPCL	1 2 3	40 40 40	2011-12 2011-12 2011- 12 (Jan'12)	2025-26 2025-26 2025-26 (subject to re- start of works(3-½ year)	170	726.17 (2011-12)	938.29 (10/19)	212.12 (29.21)	Project was stalled since October, 2013 due to funds constraints with the developer. The project was under NCLT process since 9th April, 2019. NHPC submitted EOI on 08.07.2019 and was shortlisted under final list of Prospective Resolution Applicants on dated 23.08.2019. The Resolution Plan submitted by NHPC on 04.12.2019. The Resolution Plan Approval Application was listed for hearing on 17.02.2020 before NCLT, Hyderabad ("Tribunal"). Final hearing was held on 31.07.2020. The project has been awarded to NHPC. PIB /CCEA is under process.

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
26*	Rangit-II 2x33= 66 MW Sikkim Hydro Power Ltd.	1 2	33 33	2015-16 2015-16 (Apr'15)	2024-25 2024-25 (subject to re- start of works(2- ½ years))	119	496.44 (2011-12)	496.44 (2011-12)	Nil	➤ Works are stalled since December, 2017 due to funds constraints with developer. Project is in NCLT since 30.07.2020.
27*	Panan 4x75= 300 MW Himagiri Hydro Energy Pvt. Ltd.	1 2 3 4	75 75 75 75	2018-19 2018-19 2018-19 2018-19	2025-26 2025-26 2025-26 2025-26 (subject to re- start of works(4- ½ years))	84	1833.05 (2009)	2675.00 (2020)	841.95 (45.93)	➤ Project was under construction in the private sector but stalled due to non-receipt of NOC from NBWL angle from Forest, Environment & wild life Management dept. of Sikkim Govt. Issue of construction of bridge on Mantham Lake for accessibility of site is also pending with the State Govt...
	Tamil Nadu									
28	Kundah PSP (Phase-I, Phase-II & Phase-III) (4x125=500 MW) TANGEDCO	1 2 3 4	125 125 125 125	2021-22 2021-22 2021-22 2021-22 (Aug,21)	2023-24 2023-24 2023-24 2023-24 (April,23)	20	1216.59 (2007-08)	1831.29 (2014)	614..7 (50.52)	➤ Civil & HM works have been taken up from 05/2018 only
	Uttarakhand									
29*	LataTapovan (3x57 = 171 MW) NTPC	1 2 3	57 57 57	2017-18 2017-18 2017-18 (Aug'17)	2025-26 2025-26 2025-26 (subject to re- start of works(4 years))	103	1527.00 (07/12)	1527.00 (07/12)	NIL	Subsequent to the Uttarakhand disaster in June, 2013, Hon'ble Supreme Court gave the judgment on 13.08.2013 that "MoEF as well as State of Uttarakhand not to grant any further environmental clearance or forest clearance for any hydroelectric power project in the State of Uttarakhand, until further orders". Therefore, the construction work stopped .The matter is sub-judice.
30	TapovanVishnughad (4x130 = 520 MW) NTPC	1 2 3 4	130 130 130 130	2012-13 2012-13 2012-13 2012-13 (Mar'13)	2023-24 2023-24 2023-24 2023-24	132	2978.48 (03/04)	5867.38 (04/19)	2888.90 (96.99)	➤ Heavy water ingress due to bad geology in HRT and rock fall on TBM. TBM stuck up thrice. ➤ Flash flood in Aug'12 & June, 2013 damaging coffer dam.

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
										➤ Termination of civil contracts for Barrage and HRT. ➤ Cash flow issues with civil contractors..
31	TehriPSS (4x250 = 1000 MW) THDC	1 2 3 4	250 250 250 250	2010-11 2010-11 2010-11 2010-11 (July'10)	2022-23 2022-23 2022-23 2022-23 (Dec'22)	149	1657.60 (12/05)	4825.60 (02/19)	3168 (191.12)	➤ Poor geology. ➤ Local agitation at Asena Quarry / muck disposal area. ➤ Revision of Lay out of machine hall due to poor geology. ➤ Funds constraints with contractor. ➤ Due to flash flood in Dhauliganga River on 07 Feb 2021, construction work is held up
32	Naitwar Mori (2x30 = 60 MW) SJVNL	1 2	30 30	2021-22 2021-22 (Dec'21)	2022-23 2022-23 (Jun'22)	6	648.33 (10/2016)	947.89 (12/2020)	299.56 (46.20)	➤ COVID-19 related restrictions.
33	VishnugadPipalkoti (4x111 = 444 MW) THDC	1 2 3 4	111 111 111 111	2013-14 2013-14 2013-14 2013-14 (Jun'13)	2023-24 2023-24 2023-24 2023-24 (Dec'23)	126	2491.58 (03/08)	3860.35 (02/19)	1368.77 (54.93)	➤ CCEA approval in Aug-2008 but works could not be awarded due to Forest clearance/diversion of forest land. Forest land was acquired in January-14 and subsequently works awarded in January-2014. ➤ Disruption of works by local people. ➤ Cash flow problem with contractor.
34	Vyasi 2x60=120 MW, UJVNL	1 2	60 60	2014-15 2014-15 (Dec'14)	2022-23 2022-23 (Apr,22)	88	936.23 (02/10)	1581.01 (2019)	644.78 (68.86)	➤ Delay in award of works. ➤ Agitation by Local people.
35*	PhataByung (2x38 = 76 MW), LANCO	1 2	38 38	2012-13 2012-13 (Jun'12)	2024-25 2024-25 (subject to re-start of works(3 years))	153	520.00 (2013-14)	1132 (09/16)	612 (117.69)	➤ Works stalled since July, 2017 due to Financial crunch with the contractor / developer. The company is undergoing a corporate insolvency resolution process initiated under IBC for resolution and revival of the project since June 2020. Under this process, the resolution professional appointed by the NCLT has

Sl. No	Project Name/(I.C.)/ Executing Agency	Unit No.	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Time over run (month s)	Org. Cost (Rs. in Crores) (Price Level)	Latest/Ant. Cost (Rs. in Crores) (Price Level)	Cost over run (Rs. in Crores) (%)	Reasons for time over run
1	2	4	5	6	7	8	9	10	11	12
										initiated the process for inviting prospective investors for the project.
	West Bengal									
36	Rammam-III (3x40= 120 MW)	1 2 3	40 40 40	2019-20 2019-20 2019-20 (Sep'19)	2022-23 2022-23 2022-23 (Nov,22)	} 38	1381.84 (09/14)	1381.84 (09/14)	Nil	➤ Delay in getting permission for tree felling from Govt. of West Bengal for Access road from Adit-1 to Adit-2. ➤ Cash flow issues with civil contractors. ➤ Strike / bandh during Gorkhaland agitation in 2017.

Note:- It is to mention that cost overrun has been calculated as the difference between the Latest Cost (provided by the developer to CEA alongwith the Price Level) and the Original Cost approved by the Central Government / State Government. In most of the cases the Latest cost at the current Price Level has not been provided by the developers.

* Construction is held-up.
