



देश में कार्यान्वित ताप विद्युत परियोजनाओं
की प्रगति का पुनर्वलोकन



REVIEW OF PROGRESS OF THERMAL POWER PROJECTS
UNDER EXECUTION IN THE COUNTRY

158 वाँ त्रैमासिक पुनर्वलोकन
(जनवरी-मार्च, 2017)

158th QUARTERLY REVIEW
(January to March, 2017)

केन्द्रीय विद्युत प्राधिकरण
विद्युत मंत्रालय
भारत सरकार
नई दिल्ली

**CENTRAL ELECTRICITY AUTHORITY
MINISTRY OF POWER
GOVERNMENT OF INDIA
NEW DELHI**

अप्रैल, 2017

April, 2017

(विद्युत अधिनियम, 2003 की धारा ७३ (एफ) के तहत के.वि.प्रा. के दायित्व की पूर्णता के लिये संकलित)

(In fulfillment of CEA's obligation under section 73(f) of Electricity


FOREWORD

Central Electricity Authority (CEA) has been bringing out Quarterly Review of the progress of works on various sanctioned thermal power projects under implementation in the country. The present quarterly review, 158th in the series (for the period January – March, 2017) gives the details of thermal power projects commissioned during 11th plan and Quarterwise of the First, Second, Third, Fourth & Fifth Year of 12th Plan in the country. This review also provides information in respect of thermal power projects under construction for commissioning during 12th plan and beyond.

CEA has been rendering assistance to various stake holders in timely commissioning of the project and even in pre-ponement of the project commissioning. We would like to welcome you for sharing your experiences, high standards of achievements and the constraints in project implementation. We shall endeavour to resolve the issues to the benefit of the project and therefore, request you to feel free in reporting the same for initiating the suitable remedial measures.

The quarterly review has been brought out by CEA on the basis of data received from various project authorities, visits made by the CEA engineers to different power projects and discussions held with the executing agencies and suppliers of equipments from time to time. Project authorities are requested to intimate the latest status of their projects in case the status indicated in this review has changed in any manner so that the same could be incorporated in the subsequent issues.

We whole-heartedly welcome suggestions/feed back for further improvement in the quarterly review.


Chief Engineer (TPM-II)

Index

SI.NO	CONTENTS	PAGE NO
1.0	Executive Summary	1
1.2.	11 th Plan Capacity Addition Target	1
1.2.1	Sector-wise / Fuel-wise thermal capacity addition target during 11 th Plan	1
1.2.2	Details of Capacity Addition (MW) during 11 th Plan (As per Mid-term target)	
1.2.3	Year-wise total capacity commissioned during 11 th Plan	1-2
1.3.1	Total capacity addition (MW) Programme during 12 th Plan	2
1.3.2-8	Details of capacity commissioned during 12 th Plan	2-3
2	Plan wise Thermal Capacity Targets / Achievements	3-4
2.1	Year/Plan wise Thermal Capacity Addition in the Country	4-6
3	Thermal Projects commissioned during the year 2012-13	6-8
3a	Thermal Projects commissioned during the year 2013-14	8-9
3b	Thermal Projects commissioned during the year 2014-15	9-11
3c	Thermal Projects commissioned during the year 2015-16	11-13
3d	Thermal Projects commissioned during the year 2016-17	13
4	Thermal Capacity Addition Target/Achievement for the year 2012-13	14-15
4a.	Thermal Capacity Addition Target (RFD)/Achievement for the Year 2013-14	15-16
4 b.	Thermal Capacity Addition Target (RFD)/Achievement for the Year 2014-15	17-18
4c	Thermal Capacity Addition Target (RFD)/Achievement for the Year 2015-16	19-20
4d	Thermal Capacity Addition Target (RFD)/Achievement for the Year 2016-17	21-22
5.	Thermal Power Projects Commissioned during 11 th Plan	22-25
6	Thermal Power Projects which are under construction and likely to be commissioned during 12 th Plan and beyond - Make- BHEL/ Non-BHEL (Indian)/ Chinese/Others (Expt. Chinese)	26-28
7.	Thermal Power Projects visited during the quarter (October – December, 14)	29
8.	Trend of Capacity addition as % of Total (Thermal, Hydro and Nuclear mix)	29
9.	(a) Growth of Thermal Capacity in MW	30
	(b) Bar Chart representing Plan wise Growth of Thermal Installed Capacity in MW	31
10.	Supercritical Units commissioned during 11 th Plans and beyond	32-34
11.	Details of Expenditure of Thermal Power Projects under construction	35-37

1. Executive Summary

1.2 TOTAL CAPACITY ADDITION (MW) PROGRAMME DURING 11TH PLAN (AS PER ORIGINAL TARGET) (MW)

Thermal	Hydro	Nuclear	Total
59693	15627	3380	78700

1.2.1 TOTAL CAPACITY ADDITION (MW) PROGRAMME DURING 11TH PLAN (AS PER MID TERM TARGET) (MW)

SECTOR	THERMAL		HYDRO		NUCLEAR		TOTAL	
	Target	Achieved	Target	Achieved	Target	Achieved	Target	Achieved
CENTRAL	14920.0	12790.0	2922	1550	3380	880	21222.0	15220.0
STATE	18501.4	14030.4	2854	2702	0	0	21355.4	16732.4
PRIVATE	17335.5	21719.5	2461	1292	0	0	19796.5	23011.5
TOTAL	50756.9	48539.9	8237	5544	3380	880	62373.9	54963.9

1.2.2 DETAILS OF CAPACITY ADDITION (MW) DURING 11TH PLAN (MW) (AS PER MID TERM TARGET)

Mode-wise	Mid-Term Target	Slipped	CAPACITY ADDITION		
			From Target	Additional	Total
THERMAL	50756.9	9142	41614.9	6925	48539.9
HYDRO	8237	2693	5544	0	5544
NUCLEAR	3380	2500	880	0	880
TOTAL	62373.9	14335	48038.9	6925	54963.9

1.2.3 YEAR-WISE TOTAL CAPACITY COMMISSIONED DURING 11TH PLAN

1.2.3a TOTAL CAPACITY COMMISSIONED DURING 2007-08 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	1990	1030	220	3240
STATE	3880	1393	-	5273
PRIVATE	750	-	-	750
TOTAL	6620	2423	220	9263

1.2.3b TOTAL CAPACITY COMMISSIONED DURING 2008-09 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	750	-	-	750
STATE	852.2	969	-	1821.2
PRIVATE	882.5	-	-	882.5
TOTAL	2484.7	969	-	3453.7

1.2.3c TOTAL CAPACITY COMMISSIONED DURING 2009-10 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	1740		440	2180
STATE	3079	39		3118
PRIVATE	4287	-	-	4287
TOTAL	9106	39	440	9585

1.2.3d TOTAL CAPACITY COMMISSIONED DURING 2010-11 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	3740.0	320	220	4280.0
STATE	2581.0	178		2759.0
PRIVATE	4929.5	192	-	5121.5
TOTAL	11250.5	690	220	12160.5

1.2.3 e TOTAL CAPACITY COMMISSIONED DURING 2011-12 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	4570.0	200	-	4770.0
STATE	3638.2	123	-	3761.2
PRIVATE	10870.5	1100	-	11970.5
TOTAL	19078.7	1423	-	20501.7

1.3.1 CAPACITY ADDITION (MW) PROGRAMME DURING 12TH PLAN

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	14877.6	6004	5300	26181.6
STATE	13920.4	1608		15528.4
PRIVATE	43530	3285		46815
TOTAL	72339.6	10897	5300	88525

1.3.2 DETAILS OF CAPACITY ADDITION (MW) DURING 12TH PLAN (up to 31.03.17)

Mode-wise	Target	CAPACITY ADDITION		
		From Target	Additional	Total
THERMAL	72340	56466.9	35263.6	91730.45
HYDRO	10897	5446.01	33	5479.01
NUCLEAR	5300	2000	0	2000
TOTAL	88537	63206.91	35993.6	99209.46

1.3.3 TOTAL CAPACITY (MW) COMMISSIONED DURING 2012-13

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	5023.3	374	-	5397.3
STATE	3911.0	57	-	3968.0
PRIVATE	11187.5	70	-	11257.5
TOTAL	20121.8	501	-	20622.8

1.3.4 TOTAL CAPACITY (MW) COMMISSIONED DURING 2013-14 (QUARTERWISE)

SECTOR	THERMAL					HYDRO	NUCLEAR	Total
	Q-1	Q- 2	Q-3	Q-4	Total			
CENTRAL	0	0	1160	500	1660	914	0	2574
STATE	250	871	850	1351	3322	45	0	3367
PRIVATE	2130	1250	1815	6590	11785	99	0	11884
TOTAL	2380	2121	3825	8441	16767	1058	0	17825

1.3.5 TOTAL CAPACITY (MW) COMMISSIONED DURING 2014-15 (QUARTER-WISE)

SECTOR	THERMAL					HYDRO	NUCLEAR	Total
	Q-1	Q- 2	Q-3	Q-4	Total			
CENTRAL	0	600	363.3	1695.9	2659.2	736.01	1000	4395.21
STATE	1276.1	800	600	2210.0	4886.1	0	0	4886.10
PRIVATE	2755.0	3280	600	6650.0	13285.0	0	0	13285.00
TOTAL	4031.1	4680	1563.3	10559.9	20830.3	736.01	1000	22566.31

1.3.6 TOTAL CAPACITY (MW) COMMISSIONED DURING 2015-16 (QUARTER-WISE)

SECTOR	THERMAL					HYDRO	NUCLEAR	Total
	Q-1	Q- 2	Q-3	Q-4	Total			
CENTRAL	250	1000	0	2045.6	3295.6	480	0	3775.6
STATE	1100	250	1100	4010.0	6460.0	610	0	7070
PRIVATE	1200	2386	2584	6535.0	12705.0	426	0	13131
TOTAL	2550	3636	3684	12590.6	22460.6	1516	0	23976.6

1.3.7 TOTAL CAPACITY (MW) COMMISSIONED DURING 2016-17 (QUARTER-WISE)(up to 31.03.2017)

SECTOR	THERMAL					HYDRO	NUCLEAR	Total
	Q-1	Q- 2	Q-3	Q-4	Total			
CENTRAL	0	25.5	800	2405	3230.5	80	1000	4310.5
STATE	250	500	1760	1112.25	3622.25	1555	0	5177.25
PRIVATE	1873	960	935	930	4698	24	0	4722
TOTAL	2123	1485.5	3495	4447.25	11550.75	1659	1000	14209.75

1.3.8 THERMAL / HYDRO/NUCLEAR CAPACITY ADDITIONS DURING 12TH PLAN (MW)

YEAR	THERMAL	HYDRO	NUCLEAR	Total
2012-13	20121.8	501		20622.8
2013-14	16767	1067		17834
2014-15	20830.3	736.01	1000	22566.31
2015-16	22460.6	1516	0	23976.6
2016-17 (Upto 31.03.17)	11550.75	1659	1000	14209.75
Total	91730.45	5479.01	3000	99209.46

2. Plan wise Thermal Capacity Targets / Achievements (from 4th Plan onwards)

Plan	Target (MW) (Original)	Capacity (MW) Addition	% Achieved
4th Plan (1969-74)	5746.00	2007.90	34.94
5th Plan (1974-79)	7845.00	6148.73	78.38
Annual Plan (1979-80)	2265.00	1216.87	53.72
6th Plan (1980-85)	14898.00	10605.84	71.19
7th Plan (1985-90)	15999.00	17093.40	106.84
Annual Plan (1990-91)	3962.00	2364.00	64.03
Annual Plan (1991-92)	4512.00	2370.50	52.54

8th Plan (1992-97)	20156.00	13554.90	67.20
9th Plan (1997-02)	29550.70	13800.90	46.71
10th Plan (2002-07)	25416.20	12114.24	47.66
11th Plan (2007-12)	59693.00	48539.90	81.32
12th Plan (2012-13)	15154.3	20121.80	132.77
12th Plan (2013-14)	15234.3	16767.00	110.10
12th Plan (2014-15)	14988.3	20830.30	138.97
12th Plan (2015-16)	17346.1	22460.60	129.48
12th Plan (2016-17)*	13440.5	11550.75	85.94

*Capacity addition achieved up to 31/03/2017

2.1 Year/Plan wise Thermal Capacity Addition in the Country

Sl. No.	Year	Capacity Addition (MW)	Remarks
1st Five Year Plan (1.1.51 to 31.12.55)			
1	1951	107.02	
2	1952	86.33	
3	1953	227.43	
4	1954	126.64	
5	1955	54.69	
	Total :	<u>602.11</u>	
2nd Five Year Plan (1.1.56 to 31.03.61)			
6	1956-57	69.36	
7	1957-58	184.49	
8	1958-59	140.65	
9	1959-60	193.18	
10	1960-61	<u>393.37</u>	
	Total :	<u>981.05</u>	
3rd Five Year Plan (1.4.61 to 31.03.66)			
11	1961-62	63.33	
12	1962-63	65.12	
13	1963-64	544.08	
14	1964-65	599.02	
15	1965-66	<u>895.34</u>	
	Total :	<u>2166.89</u>	
Annual Plans (1966-67, 67-68, 68-69)			
16	1966-67	431.67	
17	1967-68	1061.29	
18	1968-69	654.12	
	Total :	<u>2147.08</u>	
4th Five Year Plan (1.4.69 to 31.03.74)			
19	1969-70	497.32	
20	1970-71	358.04	
SL	Year	Capacity Addition(MW)	Remarks

No.		
21	1971-72	317.04
22	1972-73	653.54
23	1973-74	<u>181.96</u>
	Total :	<u>2007.9</u>
	5th Five Year Plan (1.4.74 to 31.03.79)	
24	1974-75	1089.18
25	1975-76	866.02
26	1976-77	790.23
27	1977-78	1204.8
28	1978-79	<u>2198.5</u>
	Total :	<u>6148.73</u>
29	1979-80	1216.87
	6th Five Year Plan (1.4.80 to 31.03.85)	
30	1980-81	1138.6
31	1981-82	1749.82
32	1982-83	2135.13
33	1983-84	2940.89
34	1984-85	<u>2641.4</u>
	Total :	<u>10605.84</u>
	7th Five Year Plan (1.4.85 to 31.03.90)	
35	1985-86	2977.00
36	1986-87	1920.00
37	1987-88	3912.00
38	1988-89	4117.30
39	1989-90	<u>4167.00</u>
	Total :	<u>17093.30</u>
	Annual Plans (1990-91, 91-92)	
40	1990-91	2364.00
41	1991-92	2370.50
	8th Five Year Plan (1.4.92 to 31.03.97)	
42	1992-93	2944.32
43	1993-94	3741.6
44	1994-95	3928.5
45	1995-96	1976.5
46	1996-97	<u>963.00</u>
	Total :	<u>13553.92</u>
	9th Five Year Plan (1.4.97 to 31.03.2002)	
47	1997-98	2993.50
48	1998-99	3724.50
49	1999-2000	2696.00
50	2000-01	2277.90
51	2001-02	<u>2009.00</u>
	Total :	<u>13700.9</u>
	10th Five Year Plan (1.4.02 to 31.03.07)	
52	2002-03	2223.10
53	2003-04	1361.60
54	2004-05	2933.92

SL No.	Year	Capacity Addition(MW)	Remarks
55	2005-06	1588.80	
56	2006-07	<u>4006.80</u>	
Total :		<u>12114.22</u>	
11th Five Year Plan (1.4.07 to 31.03.12)			
57	2007-08	6620.00	
58	2008-09	2484.70	
59	2009-10	9106.00	
60	2010-11	11250.5	
61	2011-12	<u>19078.7</u>	
Total		<u>48539.90</u>	
12th Five Year Plan (1.4.12 to 31.03.17)			
62	2012-13	20121.80	
63	2013-14	16767.00	
64	2014-15	20830.30	2nd Highest
65	2015-16	22460.60	Highest till date
65	2016-17	<u>11550.75</u>	
Total		<u>91730.45</u>	

Note: Figures from 1951 to 1984-85 indicate uprated/derated capacities

3. Thermal Projects Commissioned During the year 2012-13

S.No	Project Name & Unit No./ Implementing Agency	Capacity (MW)	Date of Commissioning
Central Sector			
1	Mouda TPP, U-1, NTPC	500	19.04.12(A)
2	Rihand STPS-III, U-5, NTPC	500	25.05.12(A)
3	Sipat TPP, U-3, NTPC	660	02.06.12(A)
4	Vindhyachal U – 11, NTPC	500	14.06.12(A)
5	Indira Gandhi TPP, U-3, NTPC	500	07.11.12(A)
6	Koderma U-2, DVC	500	15.02.13(A)
7	Tripura Gas Model-1, ONGC	363.3	03.01.13(A)
8	Vallur TPP Ph-I, U-2, NTECL	500	28.02.13(A)
9	Vindhyachal U – 12, NTPC	500	22.03.13(A)
10	Mouda TPP, U-2, NTPC	500	29.03.13(A)
11	Total Central Sector	5023.3	
State Sector			
12	Parichha Extn., U-5, UPRVUNL	250	24.05.12(A)

13	Harduaganj, U-9, UPRVUNL	250	25.05.12(A)
14	Pragati CCGT - III , GT-3, PPCL	250	27.06.12(A)
15	Mettur TPP Extn. U-1	600	11.10.12(A)
16	Ukai TPP, U-6, GSECL	500	05.03.13(A)
17	North Chennai Extn., U-2, TNEB	600	09.03.13(A)
18	Parichha Extn., U-6, UPRVUNL	250	11.03.13(A)
19	Ramgarh GT, RRVUNL	110	20.03.13(A)
20	Korba West Extn., St.III TPP, CSEB	500	22.03.13(A)
21	Satpura TPS Extn., U-10, MPPGCL	250	22.03.13(A)
22	Pipavav CCPP, Block-2, GSECL	351	27.03.13(A)
	Total of State Sector	3911	
Private Sector			
23	Jhajjar TPS(Mahatma Gandhi TPP), U-2, CLP Power	660	11.04.12(A)
24	Sterlite TPP, U-4, Sterlite Energy	600	25.04.12(A)
25	GEPL TPP, U-2, GEPL	60	28.04.12(A)
26	Salaya TPP, U-2, Essar Power	600	13.06.12(A)
27	Kasaipalli TPS, U-2, ACB India	135	21.06.12(A)
28	Simhadri TPP Ph-I, U-2 Madhucon	150	02.07.12(A)
29	Mundra UMPP, U-2, Tata Power Co.	800	25.07.12(A)
30	Bina TPP, U-1, Bina Power Ltd,	250	12.08.12(A)
31	Butibori TPP, U-1, Vidharba Ind. Ltd	300	17.08.12(A)
32	Thamminapatnam TPP, U-1, MEPL	150	09.09.12(A)
33	Tirora TPP, U-1, Adani Power Ltd.	660	11.09.11(A)
34	GEPL TPP, U-1, GEPL	60	08.09.12(A)
35	Mundra UMTTP, U-3, Tata Power Co.	800	16.10.12(A)
36	Mahadev Pd. TPP U-1, Adhunik Power Co. Ltd.	270	19.11.12(A)
37	Mundra UMTTP, U-4, Tata Power Co.	800	16.01.13(A)
38	Uno Sugan CCPP, Mod-1,Torrent Power Ltd	382.5	20.01.13(A)
39	Ratija TPP, U-1, SCPL	50	04.02.13(A)
40	Jallip-Kapurdi TPP, U-5, Raj West Power Ltd.	135	05.02.13(A)
41	EMCO Warora TPP, U-1, EMCO Energy Ltd, (GMR)	300	07.02.13(A)
42	Mahan TPP, U-1, Essar Power Ltd.	600	24.02.13(A)
43	Jallip-Kapurdi TPP, U-8, Raj West Power Ltd.	135	28.02.13(A)
44	Jallip-Kapurdi TPP, U-6, Raj West Power Ltd.	135	03.03.13(A)
45	Tuticorin TPP, U-1. Ind Barath	150	10.03.13(A)
46	Jallip-Kapurdi TPP, U-7, Raj West Power Ltd.	135	16.03.13(A)

47	Mundra UMTTP, U-5, Tata Power Co.	800	18.03.13(A)
48	Bela TPP-I, U-1, IEPL	270	20.03.13(A)
49	Tirora TPP, U-2, Adani Power Ltd.	660	25.03.13(A)
50	Amravathi TPP, U-1, Indiabulls	270	25.03.13(A)
51	Kamalanga TPP, U-1, GMR	350	28.03.13(A)
52	Mahadev Pd. TPP U-2, Adhunik Power Co. Ltd.	270	29.03.13(A)
53	Bina TPP, U-2, Bina Power Ltd,	250	31.03.13(A)
	Total of Private Sector	11187.5	
	Total in 2012-13	20121.8	

3 (a) . Thermal Projects Commissioned During the year 2013-14

S.No	Project Name & Unit No./ Implementing Agency	Capacity (MW)	Date of Commissioning	Remarks
Central Sector				
1	Rihand STPP St-III, U-6, NTPC	500	07.10.13(A)	RFD
2	Barh STPP St-II, U-4, NTPC	660	30.11.13(A)	RFD
3	Vallur TPP Ph-I, NTPC	500	28.02.14(A)	RFD
	Total Central Sector	1660		
State Sector				
4	Pragati CCGT - III , GT-4, PPCL	250	07.05.13(A)	RFD
5	Rokhia CCPP, GT-9, Govt. Of Tripura	21	13.08.13(A)	Additional
6	North Chennai TPP Extn U-1, TNEB	600	13.09.13(A)	RFD
7	Chhabra TPP Ext U-3, RRVUNL	250	14.09.13(A)	RFD
8	Shree Singhaji (Malwa) TPP, U-1, MPPGCL	600	18.11.13(A)	RFD
9	Satpura TPS Ext, U-11, MPPGCL	250	25.12.13(A)	RFD
10	Pipavav JV CCGT, Block-I, GSECL	351	05.02.14(A)	RFD
11	Pragati CCGT-III, ST-2, PPCL	250	26.02.14(A)	RFD
12	Marwa TPP, Unit-1, CSEB	500	30.03.14(A)	RFD
13	Durgapur TPS Extn., U – 8, DPL	250	31.03.14(A)	Additional
	Total of State Sector	3322		

Private Sector				
14	Thaminapatnam TPP Phase-I, U-2, Meenakshi Energy Pvt. Ltd	150	17.04.13(A)	RFD
15	Kawai TPP, U-1, Adani Power	660	30.05.13(A)	Additional
16	Sasan UMPP, U-3, Reliance Power	660	25.05.13(A)	RFD
17	Tirora TPP, Phase-II, U-1, Adani Power	660	10.06.13(A)	RFD
18	Akaltara TPP, U-1, Wardha PCL(KSK)	600	13.08.13(A)	RFD
19	EMCO Warora TPP U-2, GMR EMCO Energy Ltd	300	27.08.13(A)	RFD
20	Kamalanga TPP, U-2, GMR	350	28.09.13(A)	RFD
21	Dhariwal Infrastructure TPP, U-1, Dhariwal Infrastructure (P), Ltd.	300	03.11.13(A)	RFD
22	Niwati TPP, U-1, BLA Power LTD	45	01.12.13(A)	Additional
23	Sasan UMPP, U-2, Reliance Power	660	20.12.13(A)	RFD
24	Kawai TPP, U-2, Adani Power Rajasthan Ltd	660	24.12.13(A)	Additional
25	Tuticorin TPP, U-2. Ind Barath	150	30.12.13(A)	Additional
26	Degen CCPP, Block-I, Torrent Power	400	12.01.14(A)	Additional
27	Rajpura TPP, U-1, Nabha Power	700	24.01.13(A)	Additional
28	Amravati TPP Ph-I, U-2, India Bulls Power Ltd	270	17.02.14(A)	Additional
29	Simhapuri TPS Ph-II, U-3, Simhapuri Energy Pvt Ltd	150	21.02.14(A)	Additional
30	DB Power TPP, Unit-1, DB Power Ltd	600	23.02.14(A)	RFD
31	Nasik TPP Ph-I, U-1, India Bulls Power Ltd	270	25.02.14(A)	RFD
32	Degan CCPP, Block-3, Torrent Power	400	09.03.14(A)	Additional
33	Tamnar TPP, U-1, Jindal Power	600	10.03.14(A)	RFD
34	Kamalang TPP, U-3, GMR Energy	350	21.03.14(A)	Additional
35	Tirora TPP Ph-II, U-2, Adani Power	660	23.03.14(A)	Additional
36	Sasn UMPP, U-4, reliance Power	660	25.03.14(A)	Additional
37	Chakabura TPP, U-1, ACBIL	30	28.03.14(A)	Additional
38	Tamnar TPP, U-2, Jindal Power	600	30.03.14(A)	Additional
39	Avantha Bhandar TPP, U-1, KWPCCL	600	31.03.14(A)	Additional
40	Butibori TPP Ph-I, U-2, Vidarbha Industries Power Ltd.	300	31.03.14(A)	Additional
	Total Private Sector	11785		
	Total Thermal Capacity Addition in 2013-14	16767		

3 (b). Thermal Projects Commissioned During the year 2014-15

S.No	Project Name & Unit No./ Implementing Agency	Capacity (MW)	Date of Commissioning	Remarks
Central Sector				
1	Raghunathpur TPP Phase-I, Unit-1, DVC	600	24.08.14(A)	RFD
2	Palatana CCPP, Block-2, OTPC (JV of ILFS, ONGC & Tripura Govt.)	363.3	16.11.14(A)	RFD

3	Neyveli TPS-II Exp. , U-2, NLC	250	24.01.15(A)	Additional
4	Barh STPP-II, Unit-5, NTPC	660	04.03.15(A)	RFD
5	Tuticorin JV, U-1, NTPL (JV- NLC & TANGEDCO)	500	10.03.15(A)	RFD
6	Agartala CCPP, ST-1, NEEPCO	25,5	22.03.15(A)	Additional
7	Monarchak CCPP, GT, NEEPCO	65,4	30.03.15(A)	Additional
8	Muzaffarpur TPP Exp ,U-3, JV - NTPC & BSEB	195	31.03.15(A)	RFD
	Total Central Sector	2659.2		
State Sector				
9	Ramgarh CCPP, ST, RRVUNL	50	01.05.14(A)	RFD
10	Kalisindh TPP, Unit-1, RRVUNL	600	02.05.14(A)	RFD
11	Dhuvraan CCPP, Unit – 1, GSECL	376.1	21.05.14(A)	Additional
12	Chhabra TPP, U-4, RRVUNL	250	30.06.14(A)	RFD
13	Damodaran Sanjeevaiah TPP, U-1, APPDCL	800	28.08.14(A)	RFD
14	Malwa (Shree Singaji) TPP, Unit-2, MPPGCL	600	15.10.14(A)	RFD
15	Damodaran Sanjeevaiah TPP, U-2, APPDCL	800	17.03.15(A)	RFD
16	Sikka TPP Extn. (SS), U-3, GSECL	250	29.03.15(A)	Additional
17	Chandrapur TPS , U-8, MSPGCL	500	29.03.15(A)	RFD
18	Koradi TPP Expn., U-8, MSPGCL	660	30.03.15(A)	RFD
	Total of State Sector	4886.1		
Private Sector				
19	SaloraTPP, U-1, Vandana Vidyut Ltd	135	10.04.14 (A)	RFD
20	D gen CCPP, Block - 2, Torrent Power	400	23.04.14 (A)	Additional
21	Derang TPP, U- 1, JPL	600	10.05.14 (A)	RFD
22	Sasan UMPP, U-1, SPL	660	21.05.14 (A)	Additional
23	Dhariwal TPP, U-2, Dhariwal Industries Ltd	300	28.05.14 (A)	RFD
24	Talwandi Sabo TPP U - 1, Sterlite	660	17.06.14 (A)	RFD
25	Rajpura TPP, U-2, Nabha Power Ltd.	700	06.07.14 (A)	RFD
26	Akaltara TPP, U-2, ASK	600	22.08.14 (A)	Additional
27	Sasan UMPP, U-5, SPL	660	24.08.14 (A)	Additional
28	Nigrie TPP, U-1, JPVL	660	29.08.14 (A)	Additional
29	Tirora TPP Phase-II, APMPL	660	25.09.14 (A)	Additional

30	Mutiara TPP, U-1, Coastal Energen	600	02.12.14 (A)	Additional
31	Tamnar (TPP) Raigarh, U-3, Jindal Power	600	07.01.15 (A)	Additional
32	Haldia TPP-I, Unit-1, M/s Haldia Energy Ltd.	300	14.01.15 (A)	RFD
33	Derang TPP, U- 2, JPL	600	24.01.15(A)	Additional
34	Amravati TPP Ph-I, Unit-3, India Bulls	270	29.01.15 (A)	RFD
35	Painampuram TPP, U-1, Thermal Power Tech Corp.Ltd	660	07.02.15 (A)	RFD
36	Haldia TPP-I, Unit-2, M/s Haldia Energy Ltd.	300	16.02.15(A)	Additional
37	Nigrie TPP, U-2, JPVL	660	17.02.15 (A)	Additional
38	Raikheda TPP, U-1, GMR Chhattisgarh	685	27.02.15(A)	Additional
39	Amravati TPP Ph-I, Unit-4, India Bulls	270	04.03.15(A)	Additional
40	Simhapuri Ph-II,U-4, Simhapuri Energy Power Ltd	150	06.03.15 (A)	Additional
41	Amravati TPP Ph-I, Unit-5, India Bulls	270	12.03.15(A)	Additional
42	Sasan UMPP, U-6, SPL	660	19.03.15 (A)	Additional
43	Badadarha TPP, U-2, D.B.Power Ltd.	600	24.03.15(A)	Additional
44	Tamnar (TPP) Raigarh, U-4, Jindal Power	600	26.03.15(A)	Additional
45	Swastic Korba, Unit-1, ACB India Ltd.	25	31.03.15 (A)	RFD
	Total Private Sector	13285		
	Total Thermal Capacity Addition in 2014-15	20830.3		

3 (c). Thermal Projects Commissioned During the year 2015-16

S.No	Project Name & Unit No./ Implementing Agency	Capacity (MW)	Date of Commissioning	Remarks
Central Sector				
1	Bongaigaon TPP, Unit-1, NTPC	250	22.06.15 (A)	RFD
2.	Tuticorin TPP, Unit-2, NLC	500	09.07.15 (A)	RFD
3.	Vindhyachal TPP-V, Unit-13, NTPC	500	06.08.15 (A)	RFD
	Monarchak CCPP, ST, NEEPCO	35.6	14.01.16 (A)	RFD
	Raghunathpur TPP-I, Unit-2, DVC	600	18.01.16 (A)	RFD
	Nabi Nagar TPP, Unit-1, NTPC	250	20.03.16 (A)	Additional
	Bokaro TPS 'A' Extn., Unit-1, DVC	500	22.03.16 (A)	Additional
	Mouda STPP-II, Unit-3, NTPC	660	28.03.16 (A)	Additional
	Total Central Sector	3295.6		
State Sector				
4.	Kalisindh TPP, Unit-1, RRVUNL	600	06.06.15 (A)	RFD

5.	Anpara-D TPS, Unit- 6, UPRVUNL	500	06.06.15 (A)	RFD
6.	Sikka TPS, Unit-4, GSECL	250	25.09.15(A)	RFD
7.	Sagardighi TPS Ext., Unit-3, WBPDC	500	14.12.15(A)	RFD
8	Kakatia TPS Extn., Unit-1, TGENCO	600	31.12.15(A)	RFD
9.	Bellary TPS St-III,Unit-1, KPCL	700	01.03.16 (A)	RFD
10.	Anpara-D TPS, Unit- 7, UPRVUNL	500	06.03.16 (A)	RFD
11.	Singareni TPP, Unit-1, Singareni Collieries	600	13.03.16 (A)	RFD
12.	Koradi TPS Extn, Unit-9, MSPGL	660	15.03.16 (A)	RFD
13.	Chandrapur TPS, Unit-9, MSPGL	500	21.03.16 (A)	RFD
14.	Yermarus TPP, Unit-1, KPCL	800	29.03.16 (A)	RFD
15.	Parli TPS, Unit-8, MSPGL	250	30.03.16 (A)	RFD
16.	Total of State Sector	6460		
Private Sector				
17.	Anuppur TPP Ph-I, Unit-1, MB Power(MP)	600	20.04.15 (A)	RFD
18.	BALCO TPP, Unit-1, BALCO Pvt Ltd	300	05.06.15 (A)	RFD
19.	Bandakhar TPP, Unit-1, M/s Maruti Clean (Chhattisgarh) Ltd.	300	19.06.15 (A)	RFD
20.	Lanco Kondapalli Extn., Ph-III(PS), Block-I, Lanco Kondapalli Power Co. Ltd. (LKPC).	371	07.08.15 (A)	Additional
21.	Painampuram TPP, Unit-2, M/s. Thermal Power Tech Corporation Ltd.	660	03.09.15 (A)	RFD
22.	Lanco Kondapalli Extn., Ph-III(PS), Block-II, LKPC	371	05.09.15 (A)	Additional
23.	Vemagiri CCPP-II (PS), Block-I, GMR Rajamundry Energy Ltd.	384	12.09.15 (A)	Additional
24	ITPCL TPP, Unit-1, IL&FS TNPC Ltd.	600	19.09.15(A)	Additional
25	Vemagiri CCPP-II (PS), Block-I, GMR Rajamundry Energy Ltd.	384	05.10.15 (A)	Additional
26	Uchpinda TPP, Unit-1, RKM Powergen Co	360	28.10.15(A)	RFD
27	Talwandi Sabo TPP, Unit-2, Tal. Sabo Power	660	30.10.15(A)	RFD
28	Prayagraj(Bara) TPP, Unit – 1, Prayagraj PGCL	660	25.12.15(A)	RFD
29	Vizag TPP, Unit-1, Hinduja National Power Co Ltd	520	27.12.15(A)	RFD
30	Melamaruthur(Mutiara) TPP, Unit-2, Coastal Energen	600	02.01.16(A)	Additional
31	Lalitpur TPP, Unit-2, Lalitpur Power Gen. Co. Ltd	660	08.01.16(A)	RFD
32	Uchpinda TPP, Unit-2, RKM Powergen Co	360	28.01.16(A)	Additional
33	Goindwal Sahib TPP, Unit-1, GVK Power	270	14.02.16(A)	Additional
34	Ind Bharat TPP(Odisha), Unit-1, Ind Barat	350	25.02.16(A)	RFD

35	Goindwal Sahib TPP, Unit-2, GVK Power	270	15.03.16(A)	Additional
36	Seioni TPP Ph-I, Unit-1, Jhabua Power Ltd.	600	22.03.16(A)	Additional
37	BALCO TPP, Unit-2, BALCO Pvt Ltd	300	24.03.16(A)	RFD
38	Lalitpur TPP, Unit-1, Lalitpur Power Gen. Co. Ltd	660	26.03.16(A)	Additional
39	Raikheda TPP, Unit-2, GMR Chhattisgarh	685	28.03.16(A)	RFD
40	Talwandi Sabo TPP, Unit-3, Tal. Sabo Power	660	29.03.16(A)	RFD
41	Vizag TPP, Unit-2, Hinduja National Power Co Ltd	520	30.03.16(A)	Additional
42	Anuppur TPP Ph-I, Unit-2, MB Power(MP)	600	30.03.16(A)	Additional
	Total Private Sector	12705		
	Total Thermal Capacity Addition in 2015-16	22460.6		

3 (d). Thermal Projects Commissioned during the year 2016-17

S.No	Project Name	Implementing Agency	Unit No.	Capacity (MW)	Date of Commissioning	Remarks
Central Sector						
1	Agartalla Gas Based Power Project	NEEPCO	ST-1	25.5	23.08.2016(A)	RFD
2	Kudgi STPP Ph-I	NTPC	Unit-1	800	25-12-2016(A)	RFD
3	Bongaigaon TPP	NTPC	Unit-2	250	22.03.2017(A)	
4	Kanti TPS St-II (Muzzafarpur)	NTPC	Unit-4	195	24.03.2017(A)	
5	Mauda STPP-II	NTPC	Unit-4	660	18.03.2017(A)	RFD
6	Kudgi TPP	NTPC	Unit-2	800	23.03.2017(A)	
7	Unchahar TPS St-IV	NTPC	Unit-6	500	31.03.2017(A)	
	Total Central Sector			3230.5		
State Sector						
1	BhavnagarTPP	BECL	Unit-1	250	16.05.16 (A)	RFD
2	Marwa TPS	CSPGCL	Unit-2	500	15.07.16(A)	RFD
3	Singareni TPP	SECL	Unit-2	600	25.11.16(A)	RFD
4	Koradi TPS Expn	MAHAGENCO	Unit-10	660	28.12.16(A)	RFD
5	Sagardighi TPS-II	WPDCL	Unit-4	500	15.12.16(A)	RFD
	Namrup CCGT	APGCL	CCGT	62.25	11.01.17(A)	RFD
	Bhavnagar TPP	BECL	Unit-2	250	27.03.17(A)	RFD
	Yermarus TPP	KPCL	Unit-2	800	29.03.17(A)	RFD
.	Total of State Sector			3622.25		
Private Sector						
1	Lalitpur TPP	Lalitpur Power Gen. Co. Ltd	Unit-3	660	01.04.16(A)	RFD
2	GAMA CAPP Module-1	M/s. GAMA Infraprop Ltd	GT 1&2+ST	225	25.04.16(A)	Addl
3	ITPCL TPP	ILFS	Unit-2	600	18.04.16(A)	RFD
4	Mangaon CAPP	PGPL	Block-1	388	14.07.16(A)	Addl

5	Nawpara TPP	TRN	Unit-1	300	14.08.16(A)	RFD
6	Bara TPP	J.P.Power Ventures	Unit-2	660	06.09.16(A)	RFD
7	Sembcorp Gayatri Pvt. Ltd	SGPL	Unit-1	660	12.11.2016(A)	RFD
8	Ratiza TPS-II Ltd	Spectrum Coal & Power Ltd	Unit-2	50	10.11.16(A)	RFD
9	Kashipur CCPP	Pravara Energy Pvt	Block-1	225	20.11.16(A)	RFD
	NCC TPP(Sembcorp)	Sembcorp Gayatri Pvt. Ltd	Unit-2	660	15.02.17(A)	RFD
	Nashik TPP, Ph-I	Rattan Power	Unit-2	270	15.02.17(A)	RFD
	Total Private Sector			4698		
	Total Thermal Capacity Addition in 2016-17			11550.75		

4. Thermal Capacity Addition Target/Achievement for the year 2012-13

S.No	Project Name	Impl Agency	Targeted Cap. (MW)	Q1	Q2	Q3	Q4	Cap. (MW) Achieved
CENTRAL SECTOR								
1	Vindhyachal STPS-IV, U-11	NTPC	500		500			500
2	Rihand STPS- III, U-5	NTPC	500	500				500
3	Sipat-I, U-3	NTPC	660	660				660
4	Mouda TPP, U-1	NTPC	500		500			500
5	Indira Gandhi TPP, U-3	APCPL	500			500		500
6	Vallur TPP Ph I U-2	NTECL	500				500	500
7	Koderma TPP U-2	DVC	500			500		500
8	Tripura Gas, Module-1	ONGC	363.3			363.3		363.3
Total -Central sector			4023.3	1160	1000	1363.3	500	4023.3
STATE SECTOR								
9	Marwa TPP, U-1	CSEB	500				500	
10	Pragati CCGT - III , GT-3	PPCL	250		250			250
11	Pipavav CCPP, Block-2	GSECL	351				351	351
12	Ukai TPP Extn. U-6	GSECL	490			490		500
13	Ramgarh GT,	RRVUNL	110				110	110
14	Ramgarh ST	RRVUNL	50				50	
15	Satpura TPS Extn , U-10	MPPGCL	250				250	250
16	North Chennai Extn, U-2	TNEB	600				600	600
17	Mettur TPS Ext, U-1	TNEB	600	600				600
18	Parichha Extn, U-5	UPRVUNL	250	250				250
19	Parichha Extn, U-6	UPRVUNL	250		250			250
20	Harduaganj Ext, U-9	UPRVUNL	250	250				250
Total -State sector			3951	1100	500	490	1861	3411
PRIVATE SECTOR								
21	Simhapuri Ph-I, U-2	Madhucon	150		150			150
22	Thamminapatnam TPP-I	Meenakshi	150		150			150
23	Thamminapatnam TPP-I, U-2	Meenakshi	150			150		
24	Vandana Vidyut TPP, U-1	Vandana	135			135		
25	Kasaipalli TPP , U-2	ACB	135	135				135
26	Swastik Korba , U-1	ACB	25	25				
27	Mundra UMTTP, U-2	Tata Power	800			800		800
28	Salaya TPP, U-2	Essar Power	600		600			600
29	Jajjar TPS (Mahatma Gandhi TPP) , U-2	CLP Power	660	660				660
30	Mahadev Pd, TPP, U-1	Adhunik Power	270		270			270
31	Corporate Power Ltd -Ph-I (Maitrishi Usha), U-1	Corporate	270			270		
32	Butibori TPP Ph-II, U-1	RPL	300		300			300
33	Bela TPP-I, U-1	IEPL	270		270			270
34	EMCO Warora TPP, U-1	EMCO GMR)	300			300		300
35	Tirora TPP Ph-I, U-1	Adani Power	660		660			660
36	Tirora TPP Ph-I, U-2	Adani Power	660			660		660
37	Tirora TPP Ph-II, U-1	Adani Power	660				660	
38	Bina TPP, U-1	Bina Power	250		250			250
39	Jallipa-Kapardi TPP, U-5	Raj West	135				135	135
40	Sterlite TPP, U-4	Sterlite	600	600				600
Total -Private sector			7180	1420	2650	2315	795	5940
Total			15154.3	3680	4150	4168.3	3156	13374.3

	Thermal	15154.3						
	Overall Central Sector	4023.3	1160	1000	1363.3	500	4023.3	
	Overall State Sector	3951	1100	500	490	1861	3411	
	Overall Private Sector	7180	1420	2650	2315	795	5940	
	Total Thermal	15154.3	3680	4150	4168.3	3156	13374.3	
	Total Hydro	802	127	269	234	172	501	
	Grand Total of 2012-13	15956.3	3807	4419	4402.3	3328	13875.3	
	Additional Capacity							
	Vindhyachal STPS-IV, U-12, NTPC						500	
	Mouda TPP, U-2, NTPC						500	
	Korba West Extn., St. III TPP, CSEB						500	
	GEPL TPP, U-1, GEPL						60	
	GEPL TPP, U-2, GEPL						60	
	Mundra UMTTP, U-3, Tata Power						800	
	Mundra UMTTP, U-4, Tata Power						800	
	Mundra UMTTP, U-5, Tata Power						800	
	Uno Sugan CCGP, Module-1, Torrent Power Ltd						382.5	
	Ratija TPP, U-1, SCPL						50	
	Mahan TPP, -1, Essar Power Ltd						600	
	Jallipa-Kapurdi TPP, U-6, Raj West						135	
	Jallipa-Kapurdi TPP, U-7, Raj West						135	
	Jallipa-Kapurdi TPP, U-8, Raj West						135	
	Tuticorin TPP, U-1, Ind Barath						150	
	Amravati TPP, U-1, Indiabulls						270	
	Kamalanga TPP, U-1, GMR						350	
	Mahadev Pd, TPP, U-2, Adhunik Power Ltd						270	
	Bina TPP, U-2, Bina Power Ltd						250	
	Additional Total						6747.5	
	Thermal Total						20121.8	

4a. Thermal Capacity Addition Target (RFD)/Achievement during the Year 13-14

Sl. No.	Project Name	Developer	Capacity (MW)	Q1	Q2	Q3	Q4	Cap. (MW) Achieved
			2013-14					
	Central Sector							
1	Barh II U-4	NTPC	660			660		660
2	Vallur (Ennore) TPP U-3	NTPC/TNEB JV	500				500	500
3	Tuticorin TPPU-1	NLC/TNEB JV	500				500	
4	Tripura CCGT, Block-2	ONGC JV	363.3		363.3			
5	Rihand STPS-III U-6	NTPC	500			500		500
6	Raghuathpur TPP U-1	DVC	600				600	
	Sub-total		3123.3	0	363.3	1160	1600	1660
	State Sector							
7	Marwa TPP U- 1	CSEB	500		500			500
8	Pragati -III CCGT (Bawana) GT-4	PPCL	250	250				250
9	Pragati -III CCGT (Bawana) ST-2	PPCL	250		250			250
10	Pipavav JV CCGT Block-1	GSECL	351		351			351
11	Shree Singaji TPP U-1	MPPGCL	600	600				600
12	Satpura TPS U-11	MPPGCL	250			250		250
13	Chandrapur TPP Ext. U 8	MAHGENCO	500			500		
14	Kalisindh TPP U1	RRVUNL	600			600		
15	Chhabra TPP Ext U-3	RRVUNL	250	250				250
16	Chhabra TPP Ext U-4	RRVUNL	250				250	
17	Ramgarh ST	RRVUNL	50			50		
18	North Chennai TPP Ext U-1	TNEB	600		600			600
	Sub-total		4451	1100	1701	1400	250	3051
	Private Sector							
19	Vizag TPP,U-1	Hinduja	520				520	

20	Thamminapatnam TPP U-2	Meenakshi Energy	150		150			150
21	Tamnar TPP U-1	Jindal Power	600				600	600
22	Vandana Vidyut TPP U-1	Vandana Vidyut	135	135				
23	D B Power TPP U-1	DB Power Ltd	600			600		600
24	Swastik Korba TPP U-1	ACB	25			25		
25	Akaltara TPP U-1	KSK Mahanadi	600		600			600
26	Sasan UMPP U-3	Reliance Power	660	660				660
27	Sasan UMPP U-2	Reliance Power	660		660			660
28	Nasik TPP Ph-I, U-1	India Bulls	270		270			270
29	Dhariwal Infrastructure (P) Ltd TPP U-1	Dhariwal Infrastructure	300	300				300
30	Dhariwal Infrastructure (P) Ltd TPP U-2	Dhariwal Infrastructure	300			300		
31	EMCO Warora TPP U-2	GMR EMCO Energy Ltd	300	300				300
32	Tiroda TPP Ph-II, U-1	Adani Power	660	660				660
33	Derang TPP U1	Jindal India Thermal Power	600			600		
34	Kamalanga TPP U-2	GMR Energy	350		350			350
35	Goindwal Sahib TPP U-1	GVK Industries	270	270				
36	Talwandi Sabo TPP U-1	Sterlite	660				660	
	Sub-total		7660	2325	2030	1525	1780	5150
	Total		15234.3	3425	4094.3	4085	3630	9861
		Capacity (MW)		Q1	Q2	Q3	Q4	
	Overall Central Sector	3123.3		0	363.3	1160	1600	1660
	Overall State Sector	4451		1100	1701	1400	250	3051
	Overall Private Sector	7660		2325	2030	1525	1780	5150
	Total Thermal	15234,3		3425	4094.3	4085	3630	9861
	Total Hydro	1198		347.5	329.5	185	336	1058
	Grand Total of 2013-14	16432,3		3772.5	4423.8	4270	3966	10919
	Additional Capacity							
	DPL TPS Extn, U-8, DPL							250
	Rokhia CCPP, U-9, Govt of Tripura							21
	Kawai TPP, U-1, Adani Power							660
	Kawai TPP, U-2, Adani Power							660
	Niwati TPP, U-1, BLA Power Ltd							45
	Tuticorin TPP, U-2, Ind Barath							150
	Rajpura TPP, U-1, Nabha Power							700
	Degen CCPP, Block-1, Torrent Power							400
	Amaravati TPP Ph-I, U-2, India bulls Power Ltd							270
	Simhapuri TPS Ph-II, U-3, Simhapuri Energy Pvt. Ltd.							150
	Degen CCPP, Block-2, Torrent Power							400
	Kamalanga TPP, U-3, GMR Energy							350
	Tirora TPP Ph-II, U-2, Adani Power							660
	Sasn UMPP, U-4, Reliance Power							660
	Tamnar TPP, U-2, Jindal Poer							600
	Chakabura tPP, U-1, ACBIL							30
	Avantha Bhandar TPP, U-1, KWPCl							600
	Butibori TPP, Ph-II, U-2, Vidarbha Ind. Power Ltd.							300
	Additional Total Thermal							6906
	Total Thermal							16767
	Total Capacity (2013-14)							17825

4b. Thermal Capacity Addition Target (RFD)/Achievement for the year 2014-15

State	Project Name	Impl Agency	Unit No	Cap. (MW)	Q-1	Q-2	Q-3	Q-4	Cap. (MW) Achieved
CENTRAL SECTOR									
Bihar	Barh STPP-II	NTPC	U-5	660				660	660
	Muzaffarpur TPS Exp	KBUNL (JV of NTPC & BSEB)	U-3	195				195	195
TN	Tuticorin TPP	NTPL(JV of NLC & TANGEDCO)	U-1	500			500		500
			U-2	500				500	
Tripura	Palatana CCPP	OTPC (JV of ILFS, ONGC & Tripura Govt)	BLK-2	363.3		363.3			363.3
WB	Raghunathpur TPP, Ph-I	DVC	U-1	600		600			600
Sub Total Central Sector				2818.3	0	963.3	500	1355	2318.3
STATE SECTOR									
AP	Damodaram Sanjeevaiah TPP	APPDCL	U-1	800	800				800
			U-2	800				800	800
Chhattisgarh	Marwa TPP	CSPGCL	U-2	500			500		
Maharashtra	Chandrapur TPS	MSPGCL	U-8	500			500		500
	Koradi TPS Expn.	MSPGCL	U-8	660			660		660
	Koradi TPS Expn.	MSPGCL	U-9	660				660	
	Parli TPS Expn.	MSPGCL	U-8	250			250		
MP	Malwa TPP (Shree Singaji)	MPPGCL	U-2	600		600			600
Rajasthan	Kalisindh TPP	RRVUNL	U-1	600	600				600
	Kalisindh TPP		U-2	600				600	
	Ramgarh CCPP		ST	50		50			50
	Chhabra TPP		U-4	250	250				250
UP	Anpara-D TPS	UPRVUNL	U- 6	500				500	
Sub Total State Sector				6770	1650	650	1910	2560	4260
PRIVATE SECTOR									
AP	Painampuram TPP	Thermal Power Tech Corp.Ltd	U-1	660			660		660
	Vizag TPP	Hinduja National Power Corp.Ltd	U-1	520			520		
Chhattisgarh	Swastic Korba TPP	ACB India Ltd.	U-1	25			25		25
	Salora TPP	Vandana Vidyut Ltd	U-1	135		135			135
	Bandakhar TPP	Maruti Clean Coal	U-1	300				300	
Maharashtra	Amravati TPP Ph-I	India Bulls Power Ltd	U-3	270			270		270
	Nasik TPP Ph-I	India Bulls Realtech	U-2	270		270			
	Dhariwal TPP	Dhariwal Infrastructure Ltd	U-2	300	300				300
Orissa	Derang TPP	JIPL	U-1	600	600				600
Punjab	Rajpura TPP (Nabha)	Nabha Power Ltd	U-2	700		700			700
	Talwandi Sabo TPP	M/s Sterlite	U-1	660	660				660
		M/s Sterlite	U-2	660		660			

WB	Haldia TPP	M/s Haldia Energy Ltd.	U-1	300			300		300
	Sub Total Private Sector			5400	1560	1765	1775	300	3650
	Total Thermal			14988.3	3210	3378.3	4185	4215	10228.3
					Q-1	Q-2	Q-3	Q-4	
	Overall Central Sector			2818.3	0	963.3	500	1355	2318.3
	Overall State Sector			6770	1650	650	1910	2560	4260.0
	Overall Private Sector			5370	1560	2035	1775	0	3650.0
	Total Thermal			14958.3	3210	3648.3	4185	3915	10228.3
	Total Hydro			842	206	235.0	65	336	336.01
	Grand Total of 2014-15			15800.3	3416	3883.3	4250	4251	10564.31
	Additional Capacity								
	D gen CCPP, Block-1, Torrent Power(P)								400
	Dhuvran CCPP, Unit-1, GSECL(S)								376.1
	Sasan UMPP, Unit-1, SPL								660
	Akaltara TPP, Unit-2, KSK								600
	Sasan UMPP, Unit - 5, SPL								660
	Nigrie TPP, Unit – 1,JPVL,								660
	Tirora TPP Phase-II, Adani Power Maharashtra Pvt. Ltd.								660
	Mutlari TPP Unit-1, Coastal Energen								600
	Tamnar TPP, Unit-3, Jindal Power								600
	Neyveli TPS-II Exp. , U-2, NLC								250
	Derang TPP, U- 2, JPL								600
	Haldia TPP-I, Unit-2, M/s Haldia Energy Ltd.								300
	Nigrie TPP, U-2, JPVL								660
	Raikheda TPP, U-1, GMR Chhattisgarh								685
	Amravati TPP Ph-I, Unit-4, India Bulls								270
	Simhapuri Ph-II,U-4, Simhapuri Energy Power Ltd								150
	Amravati TPP Ph-I, Unit-5, India Bulls								270
	Sasan UMPP, U-6, SPL								660
	Agartala CCPP, ST-1, NEEPCO								25.5
	Badadarha TPP, U-2, D.B.Power Ltd.								600
	Tamnar (TPP) Raigarh, U-4, Jindal Power								600
	Sikka TPP Extn. (SS), U-3, GSECL								250
	Monarchak CCPP, GT, NEEPCO								65.4
	Additional Total Thermal								10602.0
	Total Thermal Capacity Addition								10228.3
	Total Capacity Addition								20830.3

4c. THERMAL CAPACITY ADDITION PROGRAMME (RFD) FOR THE YEAR 2015-16									
State	Project Name	Impl Agency	Unit No	Cap. (MW)	Q1	Q2	Q3	Q4	Capacity (MW) Achieved
<u>CENTRAL SECTOR</u>									
Assam	Bongaigaon TPP	NTPC	U-1	250	250				250
Bihar	Muzafferpur	NTPC	U-4	195				195	
MP	Vindhyachal TPP-V	NTPC	U-13	500			500		500
Tripura	Agratala CCPP	NEEPCO	ST-1	25.5	25.5				
Tripura	Monarchak CCPP	NEEPCO	ST	35.6		35.6			35.6
TN	Tuticorin TPP	NLC	U-2	500		500			500
WB	Raghunathpur TPP, Ph-I	DVC	U-2	600				600	600
		Total Central Sector		2106.1	275.5	535.6	500	795	1885.6
<u>STATE SECTOR</u>									
Chhattisgarh	Marwa TPP	CSPGCL		U-4	500	500			
Gujarat	Sikka TPS	GSECL	U-4	250			250		250
Karnataka	Bellary TPS St-III	KPCL	U-3	700			700		700
Karnataka	Yermarus TPP	KPCL	U-1	800				800	800
Maharashtra	Chandrapur TPS	MSPGCL	U-9	500			500		500
Maharashtra	Koradi TPS Expn.	MSPGCL	U-9	660		660			660
Maharashtra	Koradi TPS Expn.	MSPGCL	U-10	660				660	
Maharashtra	Parli TPS	MSPGCL	U-8	250				250	250
Rajasthan	Kalisindh TPP	RVUNL	U-2	600	600				600
Telangana	Singareni TPP	Singareni Collieries Co Ltd	U-1	600				600	600
Telangana	Kakatiya TPS Extn.	T GENCO	U-1	600			600		600
UP	Anpara-D TPS	UPRVUNL	U- 6	500	500				500
UP	Anpara-D TPS	UPRVUNL	U- 7	500			500		500
WB	Sagardighi TPS-Extn	West Bengal	U-3	500		500			500
WB	Sagardighi TPS-Extn	West Bengal	U-4	500				500	
		Total State Sector		8120	1100	1660	2550	2810	6460
<u>PRIVATE SECTOR</u>									
AP	Painampuram TPP	Thermal Power Tech Corporation Ltd	U-2	660		660			660
AP	Vizag TPP	Hinduja National Power Corp. Ltd	U-1	520			520		520
Chhattisgarh	Bandakhar TPP	M/s Maruti Clean (Chhattisgarh) Ltd.	U-1	300	300				300
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	U-1	360	360				360
Chhattisgarh	BALCO TPP	BALCO Pvt Ltd	U-1	300	300				300
Chhattisgarh	BALCO TPP	BALCO Pvt Ltd	U-2	300		300			300
Chhattisgarh	Raikheda TPP	GMR	U-2	685			685		685
Chhattisgarh	Salora	Vandana Vidyut	U-2	135		135			

Maharashtra	Nasik	Ratan India (Nasik) Power Ltd	U-2	270				270	
MP	Anuppur TPP Ph-I	MB Power(MP)	U-1	600	600				600
Orissa	Ind Bharat TPP (Orissa)	Ind Barath	U-1	350			350		350
Punjab	Talwandi Sabo TPP	Talwandi Sabo Power Ltd	U-2	660	660				660
Punjab	Talwandi Sabo TPP	Talwandi Sabo Power Ltd	U-3	660			660		660
UP	Lalitpur TPP	Lalitpur Power Generation Co. Ltd (LPGCL)	U-1	660		660			660
UP	Prayagraj (Bara) TPP	Prayagraj power Gen. Co. Ltd(J.P.Power Ventures)	U-1	660			660		660
		Total Private Sector		7120	2220	1755	2875	270	6715
	Grand Total 2015-16			17346.1	3595.5	3950.6	5925	3875	15060.6
					Q-1	Q-2	Q-3	Q-4	
	Overall Central Sector			2106.1	275.5	535.6	500	795	1885.6
	Overall State Sector			8120	1100	1660	2550	2810	6460.0
	Overall Private Sector			7120	2220	1755	2875	270	6715.0
	Total Thermal			17346.1	3595.5	3950.6	5925	3875	15060.6
	Total Hydro			1691	830	518	88	255	1516
	Grand Total of 2015-16			19037.1	4425.5	4468.6	6013	4130	16576.6
	Additional Capacity								
	Central Sector								
	Nabi Nagar TPP, NTPC			Unit-1					250
	Bokaro TPS 'A' Extn., DVC			Unit-1					500
	Mouda STPP-II			Unit-3					660
	Total Central Sector								1410
	Private Sector								
	Lanco Kondapalli Extn., Ph-III (PS), Lanco Kondapalli Power Co. Ltd. (LKPCL).			Block-I					371
				Block-II					371
	Vemagiri CCPP-II (PS), GMR Rajamundry Energy Ltd.			Block-I					384
				Block-II					384
	Vizag TPP, Hinduja National Power Corp. Ltd			Unit-2					520
	Uchpinda TPP, RKM Powergen (P) Ltd			Unit-2					360
	Anuppur TPP Ph-I, MB Power(MP)			Unit-2					600
	Seioni TPP, Jhabua Power Ltd.			Unit-1					600
	Goindwal Sahib TPP, GVK Power			Unit-1					270
	Goindwal Sahib TPP, GVK Power			Unit-2					270
	ITPCL TPP, IL&FS TNPC Ltd.			Unit-1					600
	Melamaruthur(Mutiara) TPP, Coastal Energen			Unit-2					600
	Lalitpur TPP, LPGCL			Unit-2					660
	Total Private Sector								5990
	Additional Total Thermal								7400
	Total Thermal Capacity Addition								22460.6
	Total Capacity Addition								23976.6

4d. THERMAL CAPACITY ADDITION TARGET (RFD) FOR THE YEAR 2016-17									
State	Project Name	Imp Agency	Unit	Capacity (MW)	Quarter wise Phasing				Capacity (MW) Achieved
					Q1	Q2	Q3	Q4	
<u>CENTRAL SECTOR</u>									
Bihar	Nabinagar TPP	NTPC	2	250				250	
Mahararashtra	Mauda STPP-II	NTPC	4	660				660	660
Chhastisgarh	Lara STPP	NTPC	1	800				800	
Bihar	Kanti TPS St-II	NTPC	4	195		195			195
Karnataka	Kudgi TPP	NTPC	1	800		800			800
Tripura	Agartala Gas Based Power Project	NEEPCO	ST-1	25.5	25.5				25.5
	Total Central			2730.5	25.5	995	0	1710	1680.5
<u>STATE SECTOR</u>									
Assam	Namrup CCGT	APGCL	GT+ST	100		67	33		62.25
Bihar	Barauni TPP	BSEB	8	250			250		
Chhastisgarh	Marwa TPS	CSPGCL	2	500	500				500
Gujrat	Bhavnagar TPP	BECL	1	250	250				250
Gujrat	Bhavnagar TPP	BECL	2	250			250		250
Karnataka	Yermarus TPP	KPCL	2	800		800			800
Mahararashtra	Koradi TPP	MSPGCL	10	660			660		660
Telangana	Singreni TPP	SCCL	2	600	600				600
West Bengal	Sagardighi TPS-II	WBPDCL	4	500			500		500
	Total State Sector			3910	1350	867	1693	0	3622.25
<u>PRIVATE SECTOR</u>									
Chhastisgarh	Nawapara TPP	TRN	1	300	300				300
Chhastisgarh	Nawapara TPP	TRN	2	300			300		
Uttarpradesh	Bara TPP	Jaypee	2	660		660			660
Tamilnadu	Utkal TPP	Ind Barath	2	350			350		
Chhastisgarh	Ucchpinda TPP	RKM	3	360		360			
Tamilnadu	ITPCL TPP	ILFS	2	600	600				600
Orissa	Lanco Babandh TPP	Lanco Babandh	1	660				660	
Uttar pradesh	Lalitpur TPP	LPGCL	3	660	660				660
Mahararashtra	Nashik TPP, Ph-I	Rattan Power	2	270	270				270
Mahararashtra	Nashik TPP, Ph-I	Rattan Power	3	270			270		
Andhra pradesh	NCC TPP (Sembcorp Gayatri Pvt. Ltd)	NCC	1	660		660			660
Andhra pradesh	NCC TPP	NCC	2	660			660		
Chhastisgarh	Binjkote TPP	SKS	1	300			300		
Chhastisgarh	Athena Singhitari TPP	Athena Chhattisgarh	1	600			600		
West Bengal	Haldia TPP	India Power	1	150		150			
	Total Private Sector			6800	1830	1830	2480	660	3150
	Grand Total 2016-17			13440.5	3205.5	3692	4173	2370	8452.75

Overall Central Sector		2730.5	25.5	995	0	1710	1680.5
Overall State Sector		3910	1350	867	1693	0	36622.25
Overall Private Sector		6800	1830	1830	2480	660	3150
Total Thermal		13440.5	3205.5	3692	4173	2370	8452.75
Additional Capacity							
Central Sector							1550
Bongaigaon TPP							250
Kudgi TPP (U-2)							800
Unchahar TPS St-IV U-6							500
State Sector							
							0
Private Sector							1548
GAMA CCPP Module, M/s. GAMA Infraprop Ltd. Uttrakhand							225
Mangaon CCPP, PGPL, Maharastra							388
Kashipur CCPP Block-1							225
Ratiza TPS_II							50
NCC TPP (Sembcorp)							660
Additional Total Thermal							
Total Thermal Capacity Addition							11550.75

5 THERMAL POWER PROJECTS COMMISSIONED DURING 11TH PLAN

Sector State	Project Name	Impl. Agency	Unit No.	Cap. (MW)	Actual. Comm. Date
2007-08					
<u>CENTRAL SECTOR</u>					
Bihar	Kahalgao St-2, Ph-1	NTPC	U-6	500	16-03-08
Chhattisgarh	Sipat-II	NTPC	U-4	500	27-05-07
Maharashtra	Ratnagiri(Dhabol) Ph-II	RGPL	Block-3	740	28-10-07
WB	Mejia TPS	DVC	U-6	250	01-10-07
Sub Total :				1990	
<u>STATE SECTOR</u>					
AP	Rayalseema TPP St-II	APGENCO	U-4	210	20-11-07
Chhattisgarh	Korba East TPP St-V	CSEB	U-2	250	11-12-07
Gujarat	Dhuvaran CCPP Extn.	GSECL	ST	40	13-08-07
Haryana	Yamuna Nagar TPP	HPGCL	U-1	300	13-11-07
			U-2	300	29-03-08
Karnataka	Bellary TPP	KPCL	U-1	500	03-12-07
Maharashtra	Paras TPS Expn,U-1	MSPGCL	U-1	250	31-05-07
MP	Sanjay Gandhi TPP Extn.-III	MPPGCL	U-5	500	18-06-07
Punjab	Guru Har Govind TPS-II	PSEB	U-3	250	03-01-08
Rajasthan	Dholpur CCGT	RRVUNL	GT-2	110	16-06-07
			ST	110	27-12-07
WB	Bakreshwar TPS	WBPDC	U-4	210	23-12-07
WB	Durgapur TPS Extn	DPL	U-7	300	24-11-07
WB	Sagardighi TPP	WBPDC	U-1	300	21-12-07
WB	Santalidih TPP Extn Ph-I	WBPDC	U-5	250	07-11-07
Sub Total :				3880	
<u>PRIVATE SECTOR</u>					
Chhattisgarh	O.P.Jindal STPP	Jindal Power Ltd.	U-1	250	02-09-07
			U-2	250	06-03-08
			U-3	250	10-02-08
Sub Total :				750	
Total :				6620	
2008-09					

CENTRAL SECTOR

Chhattisgarh	Bhilai TPP Expn	NSPCL	U-1	250	20-04-08
Chhattisgarh	Sipat-II	NTPC	U-5	500	27-12-08
Sub Total :				750	

STATE SECTOR

MP	Amarkantak TPP	MPPGCL	U-5	210	15-06-08
Punjab	Guru Har Govind TPS-II	PSEB	U-4	250	31-07-08
TN	Valuthur CCPP Extn.	TNEB	GT	59.8	06-05-08
			ST	32.4	16-02-09
WB	Sagardighi TPP	WBPDCCL	U-2	300	20-07-08
Sub Total :				852.2	

PRIVATE SECTOR

Chhattisgarh	O.P.Jindal STPP	Jindal Power Ltd.	U-4	250	17-06-08
Gujarat	Sugen CCPP(Akhakhhol)	Torrent Power Gen. Ltd.	Blk-I	382.5	04-02-09
Maharashtra	Trombay TPS Extn	Tata Power Company	U-8	250	26-03-09
Sub Total :				882.5	
Total :				2484.7	

2009-10**CENTRAL SECTOR**

Bihar	Kahalgao St-2,Ph-2	NTPC	U-7	500	31-07-09
Chhattisgarh	Bhilai TPP Expn	NSPCL	U-2	250	12-07-09
Jharkhand	Chandrapura TPS Extn.	DVC	U-7	250	04-11-09
			U-8	250	31-03-10
UP	NCP Project St-II, U-5	NTPC	U-5	490	29-01-10
Sub Total :				1740	

STATE SECTOR

AP	Vijayawada TPP -IV	APGENCO	U-1	500	08-10-09
Gujarat	Kutch Lignite TPS Extn	GSECL	U-4	75	01-10-09
Gujarat	Utran CCPP Extn	GSECL	GT	240	08-08-09
			ST	134	10-10-09
Haryana	Rajiv Gandhi TPS,Hissar	HPGCL	U-1	600	31-03-10
Maharashtra	New Parli TPP	MSPGCL	U-2	250	10-02-10
Maharashtra	Paras TPS Expn,U-2	MSPGCL	U-2	250	27-03-10
Rajasthan	Chhabra TPS	RRVUNL	U-1	250	30-10-09
Rajasthan	Giral Lignite-II	RRVUNL	U-2	125	06-11-09
Rajasthan	Kota TPP	RRVUNL	U-7	195	31-08-09
Rajasthan	Suratgarh TPP	RRVUNL	U-6	250	29-08-09
WB	Bakreshwar TPS	WBPDCCL	U-5	210	07-06-09
Sub Total :				3079	

PRIVATE SECTOR

AP	Gautami CCPP	Gautami Power Ltd	GT-1	145	03-05-09
			GT-2	145	03-05-09
			ST	174	03-05-09
AP	Konaseema CCPP	Konaseema gas Power Ltd.	GT-1	140	01-05-09
			GT-2	140	01-05-09
AP	Lanco Kondapalli Ph-II (GT)	Lanco Kondapalli	GT	233	05-12-09
Chhattisgarh	Lanco AmarkantakTPS Ph-1,U-1	Lanco Amarkantak Power Pvt. Ltd.	U-1	300	04-06-09
Chhattisgarh	Lanco AmarkantakTPS Ph-1,U-2	Lanco Amarkantak Power Pvt. Ltd	U-2	300	26-03-10
Gujarat	Mundra TPP Ph-1(U-1&2)	Adani Power Ltd	U-1	330	04-08-09
			U-2	330	17-03-10
Gujarat	Sugen CCPP(Akhakhhol)	Torrent Power Gen. Ltd.	Blk-II	382.5	07-05-09
			Blk-III	382.5	08-06-09
Karnataka	Toranagallu TPP	JSW Energy(Vijayanagar)	U-1	300	27-04-09
			U-2	300	24-08-09
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	U-1	135	16-10-09
UP	Rosa TPP Ph-I	Rosa Power Supply Co.Ltd.-Reliance Energy	U-1	300	10-02-10
WB	Budge-Budge- III	CESC	U-3	250	29-09-09
Sub Total :				4287	
Total :				9106	

2010-11

CENTRAL SECTOR

AP	Simhadri STPP Extn.	NTPC	U-3	500	31-03-11
Chhattisgarh	Korba STPP	NTPC	U-7	500	26-12-10
Haryana	Indira Gandhi TPP	APCPL	U-1	500	31-10-10
Rajasthan	Barsingsar Lignite	NLC	U-1	125	28-06-10
			U-2	125	25-01-11
UP	NCP Project St-II	NTPC	U-6	490	30-07-10
WB	Farakka STPS- III	NTPC	U-6	500	23-03-11
WB	Mejia TPS Extn	DVC	U-1	500	30-09-10
			U-2	500	26-03-11
			Sub Total	3740	

STATE SECTOR

AP	Kakatiya TPP	APGENCO	U-1	500	27-05-10
AP	Rayalseema TPP St-III	APGENCO	U-5	210	31-12-10
Delhi	Pragati CCGT - III	PPCL	GT-1	250	24-10-10
			GT2	250	16-02-11
Gujarat	Surat Lignite TPP Extn.	GIPCL	U-3	125	12-04-10
			U-4	125	23-04-10
Haryana	Rajiv Gandhi TPS,Hissar	HPGCL	U-2	600	01-10-10
Karnataka	Raichur U-8	KPCL	U-8	250	26-06-10
Rajasthan	Chhabra TPS	RRVUNL	U-2	250	04-05-10
Tripura	Baramura GT Extn.	TSECL	U-5	21	03-08-10
			Sub Total :	2581	

PRIVATE SECTOR

AP	Konaseema CCPP	Konaseema gas Power Ltd.	ST	165	30-06-10
AP	Lanco Kondapalli Ph-II (ST)	Lanco Kondapalli	ST	133	19-07-10
Delhi	Rithala CCPP	NDPL	GT-1	35.75	09-12-10
			GT-2	35.75	04-10-10
Gujarat	Mundra TPP Ph-I(U-3&4)	Adani Power Ltd	U-3	330	02-08-10
			U-4	330	20-12-10
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-1	660	26-12-10
Karnataka	Udupi TPP	UPCL	U-1	600	23-07-10
Maharashtra	JSW Ratnagiri TPP	JSW Energy(Ratnagiri) Ltd	U-1	300	24-08-10
			U-2	300	09-12-10
Maharashtra	Wardha Warora TPP	WPCL	U-1	135	05-06-10
			U-2	135	10-10-10
			U-3	135	13-01-11
Orissa	Sterlite TPP	Sterlite Energy Ltd.	U-1	600	14-10-10
			U-2	600	29-12-10
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	U-2	135	08-07-10
UP	Rosa TPP Ph-I	Rosa Power Supply Co.Ltd.- Reliance Energy	U-2	300	28-06-10
			Sub Total :	4929.5	
			Total :	11250.5	

2011-12

CENTRAL SECTOR

AP	Simhadri STPP Extn.	NTPC	U-4	500	30-03-12
Chhattisgarh	Sipat-I	NTPC	U-1	660	28-06-11
			U-2	660	24-12-11
Haryana	Indira Gandhi TPP	APCPL	U-2	500	05-11-11
Jharkhand	Kodarma TPP	DVC	U-1	500	20-07-11
TN	Neyveli TPS-II Exp.	NLC	U-1	250	04-01-12
TN	Vallur TPP Ph I	NTECL	U-1	500	28-03-12
WB	Durgapur Steel TPS	DVC	U-1	500	29-07-11
			U-2	500	23-03-12
			Sub Total :	4570	

STATE SECTOR

AP	Kothagudem TPP -VI	APGENCO	U-1	500	26-06-11
Assam	Lakwa Waste Heat Unit	APGCL	ST	37.2	24-12-11
Delhi	Pragati CCGT - III	PPCL	ST-1	250	29-02-12

Gujarat	Hazira CCPP Extn.	GSECL	GT+ST	351	18-02-12
Karnataka	Bellary TPP St-II	KPCL	U-2	500	23-03-12
Maharashtra	Bhusawal TPS Expn.	MSPGCL	U-4	500	07-03-12
			U-5	500	30-03-12
Maharashtra	Khaperkheda TPS Expn.	MSPGCL	U-5	500	05-08-11
UP	Harduaganj Ext	UPRVUNL	U-8	250	27-09-11
WB	Santalidih TPP Extn Ph-II	WBPCL	U-6	250	29-06-11
Sub Total :				3638.2	

PRIVATE SECTOR

AP	Simhapuri Energy Pvt.Ltd	Madhucon Projects Ltd	U-1	150	24-03-12
Chhattisgarh	Kasaipalli TPP	ACB India Ltd.	U-1	135	13-12-11
Chhattisgarh	Katghora TPP	Vandana Energy & Steel Ltd	U-1	35	14-02-12
Chhattisgarh	SV Power TPP	SV Power Pvt Ltd	U-1	63	07-12-11
Delhi	Rithala CCPP	NDPL	ST	36.5	04-09-11
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-2	660	20-07-11
Gujarat	Mundra TPP Ph-III	Adani Power Ltd	U-1	660	07-11-11
			U-2	660	03-03-12
			U-3	660	09-03-12
Gujarat	Mundra UMTTP	Tata Power Co.	U-1	800	25-02-12
Gujarat	Salaya TPP	Essar Power Gujarat Ltd.	U-1	600	22-02-12
Haryana	Jajjar TPP (Mahatama Gandhi TPP)	CLP Power India Pvt. Ltd	U-1	660	12-01-12
Jharkhand	Maithon RB TPP	DVC	U-1	525	30-06-11
			U-2	525	23-03-12
Karnataka	Udupi TPP	UPCL	U-2	600	17-04-11
Maharashtra	JSW Ratnagiri TPP	JSW Energy(Ratnagiri) Ltd	U-3	300	06-05-11
			U-4	300	08-10-11
Maharashtra	Mihan TPS	Abhijeet MADC Nagpur Energy Pvt Ptd	U-1	61.5	09-02-12
			U-2	61.5	09-02-12
			U-3	61.5	09-02-12
			U-4	61.5	09-02-12
Maharashtra	Wardha Warora TPP	WPCL	U-4	135	30-04-11
Orissa	Sterlite TPP	Sterlite Energy Ltd.	U-3	600	16-08-11
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	U-3	135	02-11-11
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	U-4	135	23-11-11
UP	Anpara-C	Lanco Anpara Power Pvt. Ltd.	U-1	600	15-11-11
			U-2	600	12-11-11
UP	Barkhera TPP	Bajaj Energy Pvt. Ltd	U-1	45	06-11-11
			U-2	45	28-01-12
UP	Khambarkhera TPP	Bajajb Energy Pvt. Ltd	U-1	45	17-10-11
			U-2	45	28-11-11
UP	Kundarki TPP	Bajaj Energy Pvt. Ltd	U-1	45	10-01-12
			U-2	45	29-02-12
UP	Maqsoodpur TPP	Bajaj Energy Pvt Ltd	U-1	45	03-11-11
			U-2	45	21-01-12
UP	Rosa TPP Ph-II	Reliance Power Ltd.	U-3	300	27-12-11
			U-4	300	28-03-12
UP	Utrala TPP	Bajaj Energy Pvt. Ltd	U-1	45	21-02-12
			U-2	45	19-03-12

Sub Total : 10870.5

Total : 19078.7

Total (11thPlan): 48539.9

6. Thermal Projects under construction and likely to be Commissioned during 12th Plan and beyond

State	Project Name	Impl Agency	Unit No	Cap. (MW)	BHEL (MW)	Non-BHEL (MW)	Chinese (MW)	Others (MW)	
	CENTRAL SECTOR								
Assam	Bongaigaon TPP	NTPC	U-2	250	250	---	---	---	
Assam	Bongaigaon TPP	NTPC	U-3	250	250	---	---	---	
Bihar	Barh STPP- I	NTPC	U-1	660	---	---	---	660	
Bihar	Barh STPP- I	NTPC	U-2	660	---	---	---	660	
Bihar	Barh STPP- I	NTPC	U-3	660	---	---	---	660	
Bihar	Muzaffarpur TPS Exp	JV of NTPC&BSEB	U-4	195	195	---	---	---	
Bihar	Nabi Nagar TPP	JV of NTPC & Railways	U-2	250	250	---	---	---	
Bihar	Nabi Nagar TPP	NTPC	U-3	250	250	---	---	---	
Bihar	Nabi Nagar TPP	NTPC	U-4	250	250	---	---	---	
Bihar	New Nabi Nagar STPP	JV of NTPC & BSEB	U-1	660	660	---	---	---	
Bihar	New Nabi Nagar STPP	JV of NTPC & BSEB	U-2	660	660	---	---	---	
Bihar	New Nabi Nagar STPP	NTPC	U-3	660	660	---	---	---	
Chhattisgarh	Lara TPP	NTPC	U-1	800	---	800	TG- BGR/Hitachi		
Chhattisgarh	Lara TPP	NTPC	U-2	800	---	800	Boiler- Doosan		
Jharkhand	North Karnpura TPP	NTPC	U-1	660	660				
			U-2	660	660				
			U-3	660	660				
Karnataka	Kudgi STPP Ph-I	NTPC	U-2	800	---	TG- Toshiba Boiler- Doosan		800	
Karnataka	Kudgi STPP Ph-I	NTPC	U-3	800	---			800	
Maharashtra	Mouda STPS-II	NTPC	U-4	660	660	---	---	---	
Maharashtra	SolapurSTPP	NTPC	U-1	660	---	660	TG-Alstom, Boiler- BGR		
Maharashtra	SolapurSTPP	NTPC	U-2	660	---	660	TG-Alstom, Boiler- BGR		
MP	Gadarwara STPP	NTPC	U-1	800	800	----	---	---	
			U-2	800	800				
			U-1	660	660				
MP	Khargon TPP	NTPC	U-2	660	660	----	---	---	
Odisha	Dashipalli STPP	NTPC	U-1	800	---	800	SG-BHEL, SGT- Toshiba		
			U-2	800	---	800			
Telangana	Telangana TPP Ph-I	NTPC	U-1	800	---	800			
			U-2	800		800			
TN	Neyveli New TPP	NLC	U-1	500	500				
			U-2	500	500				
UP	Ghatampur TPP	JV of NLC&UPSEB	U-1	660		660			
			U-2	660		660			
			U-3	660		660			
UP	Meja STPP	NTPC	U-1	660	---	660	TG – JSW -Toshiba Boiler- BGR Hitachi		
UP	Meja STPP	NTPC	U-2	660	---	660			
UP	Tanda TPS II	NTPC	U-1	660	660				
			U-2	660	660				
UP	Unchahar St-V	NTPC	U-6	500	500				
	Total Central Sector			24805	11805.0	9420.0	0	3580.0	
	STATE SECTOR								

AP	Dr. NT Rao TPS St-V	APGENCO	U-1	800		800		
AP	Rayalseema St-III U-6	APGENCO	U-6	600	600	---	---	---
AP	Sri Damodaran Sanjeevaiah TPS St-II	APGENCO	U-1	800		800		
Assam	Namrup CCGT	APGCL	GT	69.2	69.2	---	---	---
Assam	Namrup CCGT	APGCL	ST	29.2	29.2	---	---	---
Bihar	Barauni TPS Extn	BSPGCL	U-1	250	250			
			U-2	250	250			
Gujarat	Bhavnagar Lignite TPP	Bhavnagar Energy	U-2	250	250	---	---	---
Gujarat	Wankbori TPS Exten	GSECL	U-8	800	800	---	---	---
Karnataka	Yelahanka CCPP	KPCL	GT+ST	370	---	370		
Karnataka	Yemarus TPP	KPCL	U-2	800	---	800		
MP	Shri Singhaji TPP	MPPGCL	U-3	660	---	660	L&T	
			U-4	660	---	660	L&T	
Odisha	Ib valley TPP	OPGC	U-1	660	660			
			U-2	660	660			
Rajasthan	Chhabra Super Critical TPP	RRVUNL	U-5	660		660		
			U-6	660		660		
Rajasthan	Suratgarh TPS	RRVUNL	U-7	660	660	---		
			U-8	660	660	---	---	---
Telangana	Bhadradri TPP(Manuguru)	TSGENCO	U-1	270	270			
			U-2	270	270			
			U-3	270	270			
			U-4	270	270			
Telangana	Kothagudam TPS St-VII	TSGENCO	U-1	800	800	---	---	---
TN	Ennore SCTPP	TANGEDCO	U-1	660	660	---	---	---
			U-2	660	660	---	---	---
TN	Ennore TPP Expansion	TANGEDCO/Lanco	U-1	660	---	---	660	---
TN	North Chennai St-III	TANGEDCO	U-1	800	---	800	---	---
TN	Upper Super Critical TPP	TANGEDCO	U-1	800		800		
			U-2	800	---	800	---	---
UP	Harduaganj Exp.-II TPP	UPRVUNL	U-1	660	---	660	---	---
	Total State Sector			17218.4	7428.4	9130	660	0
	PRIVATE SECTOR							
AP	Bhavanpadu TPP	M/s East Coast Energy Ltd.	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
AP	NCC TPP	NCC Power Projects Ltd	U-2	660	---	---	660	---
AP	Thamminapatnam TPP-II	Meenakshi Energy Ltd.	U-3	350	---	---	350	---
			U-4	350	---	---	350	---
Bihar	Siriya TPP	Jas Infrastructure	U-1	660			660	
			U-2	660			660	
			U-3	660			660	
			U-4	660	---	---	660	---
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	U-3	600			600	
			U-4	600			600	
			U-5	600			600	
			U-6	600	---	---	600	---
Chhattisgarh	Binjkote TPP	M/s SKS Power Generation (Chhattisgarh) Ltd.	U-1	300	---	---	300	---
			U-2	300	---	---	300	---
			U-3	300	---	---	300	---
			U-4	300	---	---	300	---
Chhattisgarh	Deveri TPP	Visa Power Ltd	U-1	600	600	---	---	---
Chhattisgarh	Lanco Amarkantak TPS-II	LAP Pvt. Ltd.	U-3	660	---	---	660	---
			U-4	660	---	---	660	---
Chhattisgarh	Nawapura TPP	M/s TRN Energy Pvt.	U-2	300	---	---	300	---

		Ltd.						
Chhattisgarh	Salora TPPh	M/s Vandana Vidyut	U-2	135	---	---	135	---
Chhattisgarh	Singhitarai TPP	Athena Chhattisgarh Power Ltd.	U-1	600	---	---	600	---
			U-2	600	---	---	600	---
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	U-3	360	---	---	360	---
			U-4	360			360	
Jharkhand	Matrishi Usha TPP-Ph-I	M/s Corporate Power Ltd	U-1	270	270	---	---	---
			U-2	270	270	---	---	---
Jharkhand	Matrishi Usha TPP-Ph-II	Corporate Power Ltd	U-3	270	270	---	---	---
			U-4	270	270			
Jharkhand	Tori TPP Ph-I	Essar Power	U-1	600	---	---	600	---
			U-2	600			600	
Jharkhand	Tori TPP Ph-II	Essar Power	U-3	600			600	
		Rattan India Power Ltd.	U-1	270	270			
			U-2	270	270			
			U-3	270	270			
			U-4	270	270			
			U-5	270	270			
Maharashtra	Amravati TPP Ph-II							
Maharashtra	Bijora Ghanmukh TPP	Jinbhuvish Power Generation Pvt. Ltd	U-1	300	---	---	300	---
			U-2	300			300	
Maharashtra	Lanco Vidarbha TPP	Lanco Vidarbha	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
		Rattan India Power Ltd.	U-2	270	270	---	---	---
			U-3	270	270	---	---	---
			U-4	270	270	---	---	---
			U-5	270	270	---	---	---
Maharashtra		Rattan India Power Ltd.	U-1	270	270	---	---	---
			U-2	270	270	---	---	---
			U-3	270	270	---	---	---
			U-4	270	270	---	---	---
Maharashtra	Nasik TPP Ph-II		U-5	270	270	---	---	---
			U-1	150	---	---	---	150
Maharashtra	Shripur TPP	Shirpur Power	U-2	150	---	----	----	150
MP	Gorgi TPP (DB Power)	DB Power	U-1	660	660	---	---	---
MP	Mahan TPP	Essar Power MP Ltd	U-2	600	---	---	600	---
MP	Niwari TPP	BLA Power	U-2	45		45		
Orissa	Ind Barat TPP (Orissa)	Ind. Bharath	U-2	350	---	---	350	---
Orissa	KVK Nilanchal TPP	KVK Nilanchal	U-1	350	---	---	350	---
			U-2	350			350	
			U-3	350			350	
Orissa	Lanco Babandh TPP	Lanco Babandh Power Ltd	U-1	660	---	---	660	---
			U-2	660			660	
Orissa	Malibrahmani TPP (Monnet Ispat)	MPCL	U-1	525	525	---	---	---
			U-2	525	525			
TN	Tuticorin (Ind-Barath) TPP	IBPIL	U-1	660	---	---	660	---
TN	Tuticorin TPP St-IV	SEPC	U-1	525	525			
UP	Prayagraj (Bara) TPP	J.P.Power Ventures	U-3	660	660	---	---	---
WB	India Power TPP	Haldia Energy Ltd.	U-1	150	150	---	---	---
			U-2	150	150			
			U-3	150	150			
	Total Private Sector			29445.0	8805.0	45.0	20295.0	300
	Grand Total			71468.4	28038.4	18595.0	20955.0	3880.0

7. Thermal Power Projects visited during Third Quarter (January, December&January) of 2016-17


The following under construction thermal power projects in country were visited by the officers of TPM-I and TPM-II Divisions to review the progress of ongoing construction activities at project sites during the Fourth quarter of the year 2016-17:

Sl. No.	Name of Project with capacity	State
1.	Mahan TPP (2x600 MW)	MP
2.	Akaltara TPP (4x600 MW)	Chhattisgarh
3.	Lanco Amarkantak TPS II (2x660 MW)	Chhattisgarh
4.	Lara TPS (2x800 MW)	Chhattisgarh
5.	Unchahar TPP (1x500 MW)	UP
6.	Harduaganj TPP(1x660 MW)	UP
7.	Rayalaseema TPP (1x600 MW)	AP
8.	Wanakbori TPS Exp (1x800 MW)	Gujarat
9.	Ennore TPP Expansion (1x660MW)	Tamilnadu

8. Trend of Thermal & Hydro Mix as on 31.03.2017

Mode-wise	As on 31.03.2016 (In MW)	Capacity Addition during 2016-17 (In MW)					As on 31.03.2017 (In MW)
		Q1	Q2	Q3	Q4	Total	
Thermal	217239	2123	1485.5	3495	4447.25	11550.75	228790
Hydro	42783	65	255	0	1339	1659	44442
Nuclear	5780	0			1000	0	6780
Total	265802	2188	1740.5	3495	6786.25	13209.75	280012

8. TREND OF CAPACITY ADDITION AS % OF TOTAL(Thermal, Hydro & Nuclear Mix)

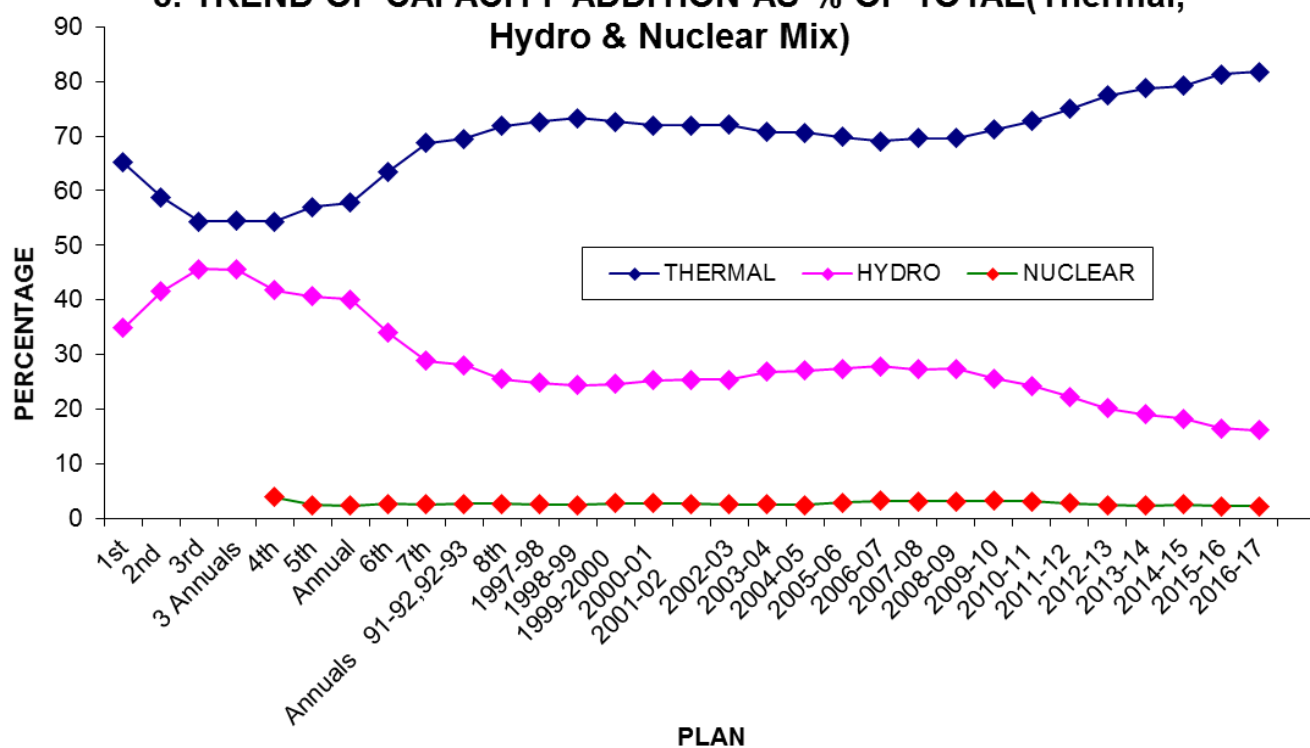


9(a) Power Generating Capacity of Thermal Units in the country since inception of 1st five year plan

Plan/ Duration	Capacity Addition (MW)	Cumulative (MW)
1st Plan (1.1.51 to 31.3.56)	602.11	1755.34
2nd Plan (1956-61)	981.05	2736.39
3rd Plan (1961-66)	2166.89	4903.28
Annual Plan (1966-67)	431.67	5334.95
Annual Plan (1967-68)	1061.29	6396.24
Annual Plan (1968-69)	654.12	7050.36
4th Plan (1969-74)	2007.9	9058.26
5th Plan (1974-79)	6148.73	15206.99
Annual Plan (1979-80)	1216.87	16423.86
6th Plan (1980-85)	10898.00	27321.86
7th Plan (1985-90)	17093.3	44415.16
Annual Plan (1990-91)	2364.00	46779.16
Annual Plan (1991-92)	2370.50	49149.66

8th Plan (1992-97)	13554.82	62704.48
9th Plan (1997-2002)	13700.90	76405.38
10th Plan (2002-07)	12114.24	88519.62
11th Plan (2007-12)	48539.90	137059.52
12th Plan (2012-17)	91730.45	228789.97

9(b) Bar Chart representing Plan-Wise Growth of Thermal Installed Capacity

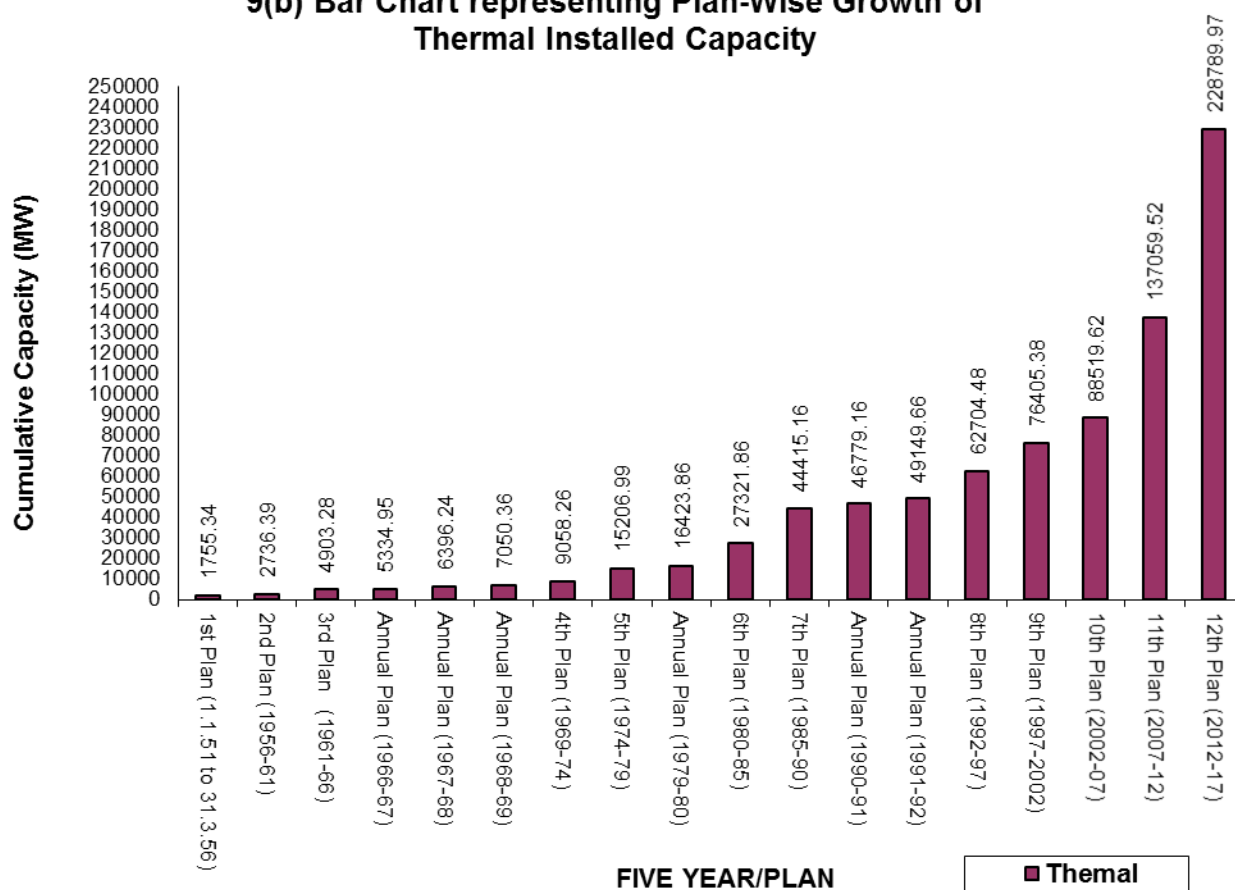

10. SUPER CRITICAL THERMAL POWER UNITS COMMISSIONED DURING 11TH PLAN AND BEYOND

<i>Sector/State</i>	<i>Project Name</i>	<i>Implimenting Agency</i>	<i>Unit No.</i>	<i>Capacity (MW)</i>	<i>Date of Actual Commissioning</i>
2010-11					
<u>PRIVATE SECTOR</u>					
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-1	660	26.12.2010
		Total (in 10-11):		660	
2011-12					
<u>CENTRAL SECTOR</u>					
Chhattisgarh	Sipat-I	NTPC	U-1	660	28.06.2011
			U-2	660	24.12.2011
	Sub Total :			1320	
<u>PRIVATE SECTOR</u>					
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-2	660	20.07.2011
	Mundra TPP Ph-III	Adani Power Ltd	U-1	660	07.11.2011
	Mundra TPP Ph-III		U-2	660	03.03.2012
	Mundra TPP Ph-III		U-3	660	09.03.2012
Gujarat	Mundra UMTTP	Tata Power Co.	U-1	800	25.02.2012
Haryana	Jajjar (Mahatama Gandhi) TPP	CLP Power India Pvt. Ltd	U-1	660	12.01.2012
	Sub Total :			4100	
	Total (in 11-12):			5420	
	Total (11th Plan):			6080	
2012-13					
<u>CENTRAL SECTOR</u>					
Chhattisgarh	Sipat-I	NTPC	U-3	660	02.06.2012
	Sub Total :			660	
<u>PRIVATE SECTOR</u>					
Gujarat	Mundra UMTTP	Tata Power Co.	U-2	800	25.07.2012
Gujarat	Mundra UMTTP	Tata Power Co.	U-3	800	16.10.2012
Gujarat	Mundra UMTTP	Tata Power Co.	U-4	800	16.01.2013
Gujarat	Mundra UMTTP	Tata Power Co.	U-5	800	18.03.2013
Haryana	Jajjar (Mahatama Gandhi) TPP	CLP Power India Pvt. Ltd	U-2	660	11.04.2012
Maharastra	Tirora TPP Phase-I	Adani Power	U-1	660	11.09.2012
Maharastra	Tirora TPP Phase-I	Adani Power	U-2	660	25.03.2013
	Sub Total :			5180	
	Total (12-13)			5840	

2013-14					
CENTRAL SECTOR					
Bihar	Barh-II	NTPC	U-4	660	30.11.2013
	Sub Total :			660	
PRIVATE SECTOR					
MP	Sasan UMTTP	Reliance Power	U-3	660	30.05.2013
MP	Sasan UMTTP	Reliance Power	U-2	660	20.12.2013
MP	Sasan UMTTP	Reliance Power	U-4	660	25.03.2014
Maharastra	Tirora TPP Ph-II	Adani Power	U-1	660	10.06.2013
Maharastra	Tirora TPP Ph-II	Adani Power	U-2	660	23.03.2014
Punjab	Rajpura TPP	Nabha Power	U-1	700	24.01.2014
Rajasthan	Kawai TPP	Adani Power	U-1	660	25.05.2013
Rajasthan	Kawai TPP	Adani Power	U-1	660	24.12.2013
	Sub Total :			5320	
	Total (13-14)			5980	
2014-15					
CENTRAL SECTOR					
Bihar	Barh-II	NTPC	U-5	660	04.03.2015
	Sub Total :			660	
State Sector					
AP	Damodaran Sanjeevaiah TPP	APPDCL	U-1	800	28.08.2014
AP	Damodaran Sanjeevaiah TPP	APPDCL	U-2	800	17.03.2015
Maharastra	Koradi TPP Expn.I	MSPGCL	U-8	660	30.03.2015
	Sub Total :			2260	
PRIVATE SECTOR					
MP	Sasan UMTTP	Reliance Power	U-1	660	21.05.2014
Punjab	Talwandi Saboo TPP	M/s Sterlite	U-1	660	17.06.2014
Punjab	Rajpura TPP	Nabha Power Ltd	U-2	700	06.07.2014
MP	Sasan UMPP	SPL	U-5	660	24.08.2014
MP	Nigrie	JPVL	U-1	660	29.08.2014
Maharastra	Tirora TPP Phase-II	Adani Power Maharashtra P Ltd	U-3	660	25.09.2014
AP	Painampuram TPP	Thermal Power Tech Corp.Ltd	U-1	660	07.02.2015
MP	Nigrie	JPVL	U-2	660	17.02.2015
Chhattisgarh	Raikheda TPP	GMR Chhattisgarh	U-1	685	27.02.2015
MP	Sasan UMPP	SPL	U-6	660	19.03.2015
	Sub Total :			6665	
	Total (14-15)			9585	

2015-16					
CENTRAL SECTOR					
Maharastra	Mouda STPP-II	NTPC	U-3	660	28.03.2016
	Sub Total :			660	
State Sector					
Karnataka	Bellary TPS St-III	KPCL	U-1	700	01.03.2016
Karnataka	Yermarus TPP	KPCL	U-1	800	29.03.2016
Maharastra	Koradi TPP Expn.I	MSPGCL	U-9	660	15.03.2016
	Sub Total :			2160	
PRIVATE SECTOR					
AP	Painampuram TPP	Thermal Power Tech Corp.Ltd	U-2	660	03.09.2015
Chhattisgarh	Raikheda TPP	GMR Chhattisgarh	U-2	685	28.03.2016
Punjab	Talwandi Saboo TPP	M/s Sterlite	U-2	660	30.10.2015
Punjab	Talwandi Saboo TPP	M/s Sterlite	U-3	660	29.03.2016
UP	Lalitpur TPP	Lalitpur Pwer Gen Co Ltd	U-1	660	26.03.2016
UP	Lalitpur TPP	Lalitpur Pwer Gen Co Ltd	U-2	660	08.01.2016
UP	Prayagraj (Bara) TPP	Prayagraj Power Gen Co Ltd	U-1	660	25.12.2015
	Sub Total :			4645	
	Total (15-16)			7465	
2016-17					
CENTRAL SECTOR					
KARNATAKA	Kudgi STPP Ph-I	NTPC	U-1	800	25.12.2016
KARNATAKA	Kudgi STPP Ph-I	NTPC	U-2	800	23.03.2017
MAHARASHTRA	Mouda STTP II	NTPC	U-2	660	18-03-2017
				2260	
STATE SECTOR					
MAHARASHTRA	Koradi TPS Expn	MAHAGENCO	U-10	660	28.12.2016
KARNATAKA	Yermarus TPP	KPCL	U-2	800	29.03.2017
				1460	
PRIVATE SECTOR					
UP	Lalitpur TPP	Lalitpur Pwer Gen Co Ltd	U-3	660	01.04.2016
UP	Prayagraj (Bara) TPP	Prayagraj Power Gen Co Ltd	U-2	660	06.09.2016
AP	Sembcorp Gayatri Pvt. Ltd.	SGPL	U-1	660	12.11.2016
AP	Sembcorp Gayatri Pvt. Ltd.	SGPL	U-2	660	15.02.2017
	Sub Total :			2640	
	Total (16-17)			6360	
	Total (12th Plan):			35410	
	Total (upto 31.03.17):			41490	

11. Details of Expenditure of Thermal Power Projects Under Construction							
State	Project Name	Impl Agency	Main Equipmt. Supplier	Unit No	Cap. (MW)	Total Exp incurred (Cr.s.)	Till (Month/ Year)
	CENTRAL SECTOR						
Assam	Bongaigaon TPP	NTPC	BHEL	U-3		6405.00	1/17
Bihar	Barh STPP- I	NTPC	Others	U-1	660	12694.00	1/17
				U-2	660		
				U-3	660		
Bihar	Nabi Nagar TPP	NTPC	BHEL	U-2	250	6266.92	01/17
				U-3	250		
				U-4	250		
Bihar	New Nabi Nagar STPP	NTPC	BHEL	U-1	660	7727.00	11/16
				U-2	660		
				U-3	660		
Chhattisgarh	Lara TPP	NTPC	Boiler-Doosan, TG- BGR	U-1	800	7539.00	1/17
Chhattisgarh	Lara TPP	NTPC		U-2	800		
Jharkhand	North Karnpura TPP	NTPC	BHEL	U-1	660	3934.00	1/17
				U-2	660		
				U-3	660		
Karnataka	Kudgi STPP Ph-I	NTPC	Others	U-3	800	12777.00	1/17
Maharashtra	Solapur STPP	NTPC	SG-BGR, SGT- Alsthom	U-1	660	7337.00	01/17
Maharashtra	Solapur STPP	NTPC		U-2	660		
MP	Gadarwara STPP	NTPC	BHEL	U-1	800	6888.00	1/17
				U-2	800		
MP	Khargon TPP	NTPC	L&T	U-1	660	2209.00	1/17
				U-2	660		
Odisha	Darlipalli STPP	NTPC	SG-BHEL, SGT- Toshiba	U-1	800	4863.00	1/17
				U-2	800		
Telangana	Telangana Ph-I	NTPC	SG-BHEL, SGT- Alsthom	U-1	800	590.00	1/17
				U-2	800		
TN	Neyveli New TPP	NLC	BHEL	U-1	500	3721.2	2/17
				U-2	500		
UP	Ghatampur TPP	JV of NLC&UPSEB		U-1	660	786.99	2/17
				U-2	660		
				U-3	660		
UP	Meja STPP	NTPC	SG-BGR, SGT- Toshiba	U-1	660	5793.63	10/16
UP	Meja STPP	NTPC		U-2	660		
UP	Tanda TPS II	NTPC	BHEL	U-1	660	2172.00	1/17
				U-2	660		
Total Central Sector					22400.0		
	STATE SECTOR						
AP	Dr. NT Rao TPS St-V	APGENCO		U-1	800	437	01/17
AP	Rayalseema St-III U-6	APGENCO	BHEL	U-6	600	3437.57	2/17
AP	Sri Damodaran Sanjeevaiah TPS St-II	APGENCO		U-1	800	199.20	05/16
Assam	Namrup CCGT	APGCL	BHEL	ST	36.15	487.3	12/16
Bihar	Barauni TPS Extn	BSPGCL	BHEL	U-8	250	4857.21	2/17
				U-9	250		
Chhattisgarh	Marwa TPP	CSPGCL	BHEL	U-2	500	8214.45	07/16
Gujarat	Wanakbori TPS Extn.	GSECL		U-8	800	1465.51	12/16

Karnataka	Yelahanka CAPP	KPCL		GT+ST	370	178.06	2/17
MP	Shri Singhaji TPP	MPPGCL	L&T	U-3	660	2450.24	2/17
				U-4	660		
Odisha	Ib valley TPP		BHEL	U-3	660	3980.53	1/17
				U-4	660		
Rajasthan	Chhabra Super Critical TPP	RRVUNL	L&T-MHI	U-5	660	5140.75	07/16
				U-6	660		
Rajasthan	Suratgarh TPS	RRVUNL	BHEL	U-7	660	6192.37	2/17
				U-8	660		
Telangana	Kothagudem TPS St-VII	TSGENCO	BHEL	U-1	800	1945.98	02/17
Telangana	Bhadradri TPP/	TSGENCO		U-1	270	1000.00	12/15
				U-2	270		
				U-3	270		
				U-4	270		
TN	Ennore SCTPP	TANGEDCO	BHEL	U-1	660	448.6	10/16
				U-2	660		
TN	Ennore TPP Exp. SC ()	TANGEDCO/ Lanco	LANCO	U-1	660	791.4	2/17
TN	North Chennai St-III	TANGEDCO		U-1	800	147.41	10/16
TN	Upper Super Critical TPP	TANGEDCO		U-1	800	10.01	10/16
				U-2	800		
UP	Harduaganj Exp.-II TPP	UPRVUNL	BHEL	U- 1	660	291.73	2/17
UP	Obra-C TPP	UPRVUNL		U-1	660	8.5	1/17
				U-2	660		
UP	Jawaharpur TPP	UPRVUN		U-1	660	7.0	1/17
				U-2	660		
	Total State Sector				18746.15		
	PRIVATE SECTOR						
AP	Bhavanpadu TPP	M/s East Coast Energy Ltd.	Chinese	U-1	660	3785.60	01/16
				U-2	660		
AP	Thamminapatnam TPP-II	Meenaksha Energy Ltd.	Chinese	U-3	350	5119.98	1/17
				U-4	350		
Bihar	Siriya TPP	Jas Infrastructure	Chinese	U-1	660	NA	
				U-2	660		
				U-3	660		
				U-4	660		
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	Chinese	U-3	600	17041.06 (for 6units)	09/16
			U-4	600			
			U-5	600			
			U-6	600			
Chhattisgarh	Binjkote TPP	M/s SKS Power Generation (Chhattisgarh) Ltd.	Chinese	U-1	300	3828.00	06/15
				U-2	300		
				U-3	300		
				U-4	300		
Chhattisgarh	Devari TPP	Visa Power Ltd	BHEL	U-1	600	2077.23	11/15
Chhattisgarh	Lanco Amarkantak TPS-II	LAP Pvt. Ltd.	Chinese	U-3	660	8629.00	08/16
				U-4	660		

Chhattisgarh	Nawapura TPP	M/s TRN Energy Pvt. Ltd.	Chinese	U-2	300	3466.55	01/16
Chhattisgarh	Salora TPP	M/s Vandana Vidyut	Chinese	U-2	135	2386.89	03/15
Chhattisgarh	Singhitarai TPP	Athena Chhattisgarh Power Ltd.	Chinese	U-1	600	6092.28	08/16
				U-2	600		
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	Chinese	U-3	360	10671.51 (for 4units)	12/16
				U-4	360		
Jharkhand	Matrishi TPP-Ph-I	M/s Corporate Power Ltd	BHEL	U-1	270	3120.00	11/12
				U-2	270		
Jharkhand	Matrishi TPP-Ph-II	Corporate Power Ltd	BHEL	U-3	270	2207.00	09/12
				U-4	270		
Jharkhand	Tori TPP Ph-I	Essar Power	Chinese	U-1	600	4639.65	09/16
				U-2	600		
Jharkhand	Tori TPP Ph-II	Essar Power	Chinese	U-3	600	246.65	03/15
Maharashtra	Amravati TPP Ph-II	Ratan India Power Ltd.	BHEL	U-1	270	763.80	03/15
				U-2	270		
				U-3	270		
				U-4	270		
				U-5	270		
Maharashtra	Bijora Ghanmukh TPP	Jinbhuvish Power Generation Pvt. Ltd.	Chinese	U-1	300	422.27	03/15
				U-2	300		
Maharashtra	Lanco Vidarbha TPP	Lanco Vidarbha	Chinese	U-1	660	5215.00	1/17
				U-2	660		
Maharashtra	Nasik TPP Ph-I	Ratan India Power Ltd	BHEL	U-3	270	6613.12	02/16
				U-4	270		
				U-5	270		
Maharashtra	Nasik TPP Ph-II	Ratan India Power Ltd.	BHEL	U-1	270	711.81	03/15
				U-2	270		
				U-3	270		
				U-4	270		
				U-5	270		
MP	Gorgi TPP (DB Power)	DB Power	BHEL	U-1	660	475.79	09/15
MP	Mahan TPP	Essar Power MP Ltd	Chinese	U-2	600	7969.56	01/17
MP	NiwariTPP	BLA Power	L&T	U-2	45	290.00	03/15
Orissa	Ind Barat TPP (Orissa)	Ind. Barath	Chinese	U-2	350	4253.00	2/17
Orissa	KVK Nilanchal TPP	KVK Nilachal	Chinese	U-1	350	1708.36	03/15
				U-2	350		
				U-3	350		
Orissa	Lanco Babandh TPP	Lanco Babandh Power Ltd	Chinese	U-1	660	7588.00	01/17
				U-2	660		
Orissa	Malibrahmani TPP (Monnet Ispat)	MPCL	BHEL	U-1	525	5329.75	12/14
				U-2	525		
TN	Tuticorin TPP St-IV	SEPC	BHEL	U-1	525	491.42	09/16
TN	Tuticorin TPP(Ind Barath)	IBPIL	Chinese	U-1	660	2000.00	05/15
UP	Prayagraj (Bara) TPP	J.P.Power Ventures	BHEL	U-3	660	14613.43	12/16
WB	India Power TPP.	Haldia Energy Ltd	BTG-BHEL	U-1	150	3209.16	2/17
				U-2	150		
				U-3	150		
	Total Private Sector				28515.0		
	Grand Total				69661.15		
