



देश में कार्यान्वित तापीय विद्युत परियोजनाओं की प्रगति का पुनर्वलोकन
Review of Progress of Thermal Power Projects under execution in the Country



170वाँ त्रैमासिक पुनर्वलोकन (जनवरी-मार्च '2020)

(विद्युत अधिनियम, २००३ की धारा ७३ (एफ) के तहत के.वि.प्रा. के दायित्व की पूर्णता के लिये संकलित)
(In fulfillment of CEA's obligation under section 73(f) of Electricity)

*170th QUARTERLY REVIEW
(January-March '2020)*

भारत सरकार
GOVERNMENT OF INDIA
विद्युत मंत्रालय
MINISTRY OF POWER
केन्द्रीय विद्युत प्राधिकरण
CENTRAL ELECTRICITY AUTHORITY
नई दिल्ली
NEW DELHI

FORWARD

Central Electricity Authority (CEA) has brought out Quarterly Review of the Progress of works on various sanctioned (for the period January – March 2020) give the details of thermal power projects commissioned during 12th Plan and onwards along with quarter-wise details of the projects for the 2019-20. This review also provides information in respect of thermal power projects under construction for commissioning beyond 2019-20 also.

The Quarterly Review has been brought out by CEA on the basis of data received from various power project authorities, visits made by CEA officers to various power projects and discussions held with the existing agencies and suppliers of equipment from time to time. Project authorities are requested to intimate the latest status of their projects in case the status indicated in this review has changed in any manner so that the same could be incorporated in the subsequent issue.

CEA whole heartedly welcomes suggestions / feed back from various stake holders for further improvement in the Quarterly Review.


(M. P. Singh)
Chief Engineer (TPM)

Index

Sl.No.	CONTENTS	PAGE Nos.
1.0	Executive Summary	03-04
2.0	Generation capacity addition target((RFD) /achievement for the year 2019-20 Bar Chart showing Thermal Capacity Addition Target/Achievement during the year 2019-20	05-06
3.0	Year wise Thermal Capacity Addition in the Country during 12 th Plan	07-19
3.1	Thermal Capacity Addition Target/ Achievement for the Year 2012-13	07-08
3.2	Thermal Capacity Addition Target/ Achievement for the Year 2013-14	09-10
3.3	Thermal Capacity Addition Target/ Achievement for the Year 2014-15	11-12
3.4	Thermal Capacity Addition Target/ Achievement for the Year 2015-16	13-14
3.5	Thermal Capacity Addition Target/ Achievement for the Year 2016-17	15-16
4.0	Thermal Capacity Addition Target/ Achievement for the Year 2017-18	17-18
5.0	Thermal Capacity Addition Target/ Achievement for the Year 2018-19	19-19
6.0	Details of Thermal Power Projects under construction in the country	20-23
7.0	Thermal Power Projects visited during the 4 th quarter (January – March, 2020)	24-24
8.0	Supercritical Units commissioned during 11 th Plan and beyond	25-29
9.0	Plan/Year wise Thermal Capacity Targets / Achievements	30-33
10.0	Power Generating Capacity of Thermal Units in the country since inception of 1st five year plan	34-34
10.1	Bar Chart representing Plan wise Growth of Thermal Installed Capacity in MW	35-35

1. Executive Summary

1.1 Original Targeted Capacity Addition Programme during 12th Plan.

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	14877.6	6004	5300	26181.6
STATE	13922	1608	0	15530
PRIVATE	43540	3285	0	46825
TOTAL	72339.6	10897	5300	88536.6

1.2 Actual Achievement against Targeted Capacity Addition during 12th Plan

Thermal Capacity Addition (Year wise/Sector wise) during 12th Plan (MW)													
Year	Central				State			Private			Grand Total	Revised Target	% Ach
	Thermal	Hydro	Nuclear	Total	Thermal	Hydro	Total	Thermal	Hydro	Total			
2012-13	5023.3	374	-	5397.3	3911	66	3977	11187.5	70	11257.5	20631.8	15154.3	136.14%
2013-14	1660	914	-	2574	3322	45	3367	11785	99	11884	17825	15234.3	117.01%
2014-15	2659.2	736.01	1000	4395.21	4886.1	0	4886.1	13285	0	13285	22566.31	14988.3	150.56%
2015-16	3295.6	480	-	3775.6	6460	610	7070	12705	426	13131	23976.6	17346.1	138.22%
2016-17	3230.5	80	1000	4310.5	3622.25	1555	5177.25	4698	24	4722	14209.75	13440.5	105.72%
Total	15868.6	2584.01	2000	20452.6	22201.4	2276	24477	53660.5	619	54279.5	99209.46	76163.5	130.26%

1.3 Thermal Capacity Addition during FY 2017-18, FY 2018-19 & 2019-20

Thermal capacity addition after 12th Plan (from 01.04.2017 onwards)						
Sector	2017 - 18 (MW)		2018-19 (MW)		2019-20 (MW)	
	Target (MW)	Achievement (MW)	Target (MW)	Achievement (MW)	Target (MW)	Achievement (MW)
Central	48800	3170	2760	1300	6040	3940
State	3546.15	1260	4506.15	2780	4256.15	2780
Private	2940	2280	Nil	Nil	0	0
Total	11366.15	6710	7266.15	4080	10296.15	6720
Additional Thermal Capacity included in Capacity Addition						
Central	-	-	-	660	-	-
State	-	500	-	69.755	-	-
Private	-	1500	-	972	-	-
Total	-	200	-	1701.755	-	45
Grand Total	11366.15	8710	7266.16	5781.755	10296.15	6765


1.4 Summary of Super Critical and Sub Critical Units under construction in the country (As on 31st March, 2020)

Sector	Super Critical (MW)	Sub-Critical (MW)	Total (MW)	No. of Super Critical Units	No. of Sub Critical Units	No. of Super Critical Projects	No. of Sub Critical Projects	Total No. of Projects
Central	17620	1500	19120	25	5	11	7	18
State	16580	1486.15	18066.15	23	6	17	0	17
Private	9240	14490	23730	14	39	7	19	26
Total	43440	17476.15	60916.15	62	50	35	26	61

2. RFD FOR THE YEAR 2019-20

S. No.	Project Name	LOA Date	Unit No	Fuel	Targeted Cap. (MW)	Org. Comm. Sched.	Ant. Trial Run/ COD at the Beginning of the year	Achieved Cap. (MW)	Actual/ Ant. Date of Cap. Addition	Remarks
	CENTRAL SECTOR									
1	Nabi Nagar STPP	Jan-13	U-1	Coal	660	Jan-17	May-19	660	12.07.2019(A)	TR completed on 12.07.2019
2	Lara STPP	Dec-12	U-2	Coal	800	May-17	Dec-19	-	Slipped	-
3	Gadarwara STPP	Mar-13	U-2	Coal	800	Sep-17	Dec-19	-	Slipped	-
4	Khargone STPP St-I	Mar-15	U-1	Coal	660	Mar-19	Aug-19	660	29.09.2019 (A)	TR completed on 29.09.2019
		Mar-15	U-2	Coal	660	Sep-19	Feb-20	660	24.03.2020 (A)	TR completed on 24.03.2020.
5	Darlipalli STPP St-I	Feb-14	U-1	Coal	800	Feb-18	Aug-19	800	30.12.2019 (A)	TR completed on 29.12.2019 at 24:00 Hrs
6	Tanda TPP St- II	Sep-14	U-5	Coal	660	Sep-17	Sep-19	660	28.09.2019 (A)	TR completed on 28.09.2019
7	Neyveli New TPP	Jun-11	U-1	Lignite	500	Mar-18	Apr-19	500	20.12.2019 (A)	TR completed on 20.12.2019
		Jun-11	U-2	Lignite	500	Sep-18	Oct-19	-	Slipped	-
	Total Central Sector				6040			3940		
	STATE SECTOR									
1	Dr.Narla Tata Rao TPS Stage-V	Dec-15	U-8	Coal	800	Jun-19	Feb-20	-	Slipped	-
2	Namrup CCGT	Feb-09	ST	Gas	36.15	Jan-12	Nov-19	-	Slipped	-
3	Wanakbori TPS Extn.	Oct-14	U-8	Coal	800	Oct-18	Nov-19	800	12.10.2019 (A)	TR completed on 12.10.2019
4	Yelahanka CCPP	Nov-15	GT+ST	Gas	370	Mar-18	Nov-19	-	Slipped	-
5	Ib valley TPP	Mar-14	U-3	Coal	660	Aug-17	Apr-19	660	01.07.2019 (A)	TR completed on 01.07.2019.
		Mar-14	U-4	Coal	660	-	Jul-19	660	17.08.2019 (A)	TR completed on 17.08.2019.
6	Suratgarh SCTPP	Mar-13	U-7	Coal	660	Jul-16	Nov-19	660	15.03.2020 (A)	TR completed on 15.03.2020.
7	Bhadradi TPP	Mar-15	U-1	Coal	270	Mar-17	Jan-20	-	Slipped	-
Total Sector Sector					4256.15				2780	
TOTAL THERMAL CAPACITY ADDITION					10296.15				6720	
	ADDITIONAL PROJECTS									
	PRIVATE SECTOR									
1	BLA Power Pvt. Ltd (Niwari) TPP	Apr-11	U-2	Coal	-	-	-	45	06.06.2019 (A)	COD on 20.03.2017, but information received late. Capacity addition on 06.06.2019 after approval of Chairperson, CEA.
Total Additional Capacity								45		
GRAND TOTAL - THERMAL CAPACITY ADDITIO								6765		

Bar Chart showing Thermal Capacity Addition Target/Achievement during the year 2019-20(MW)

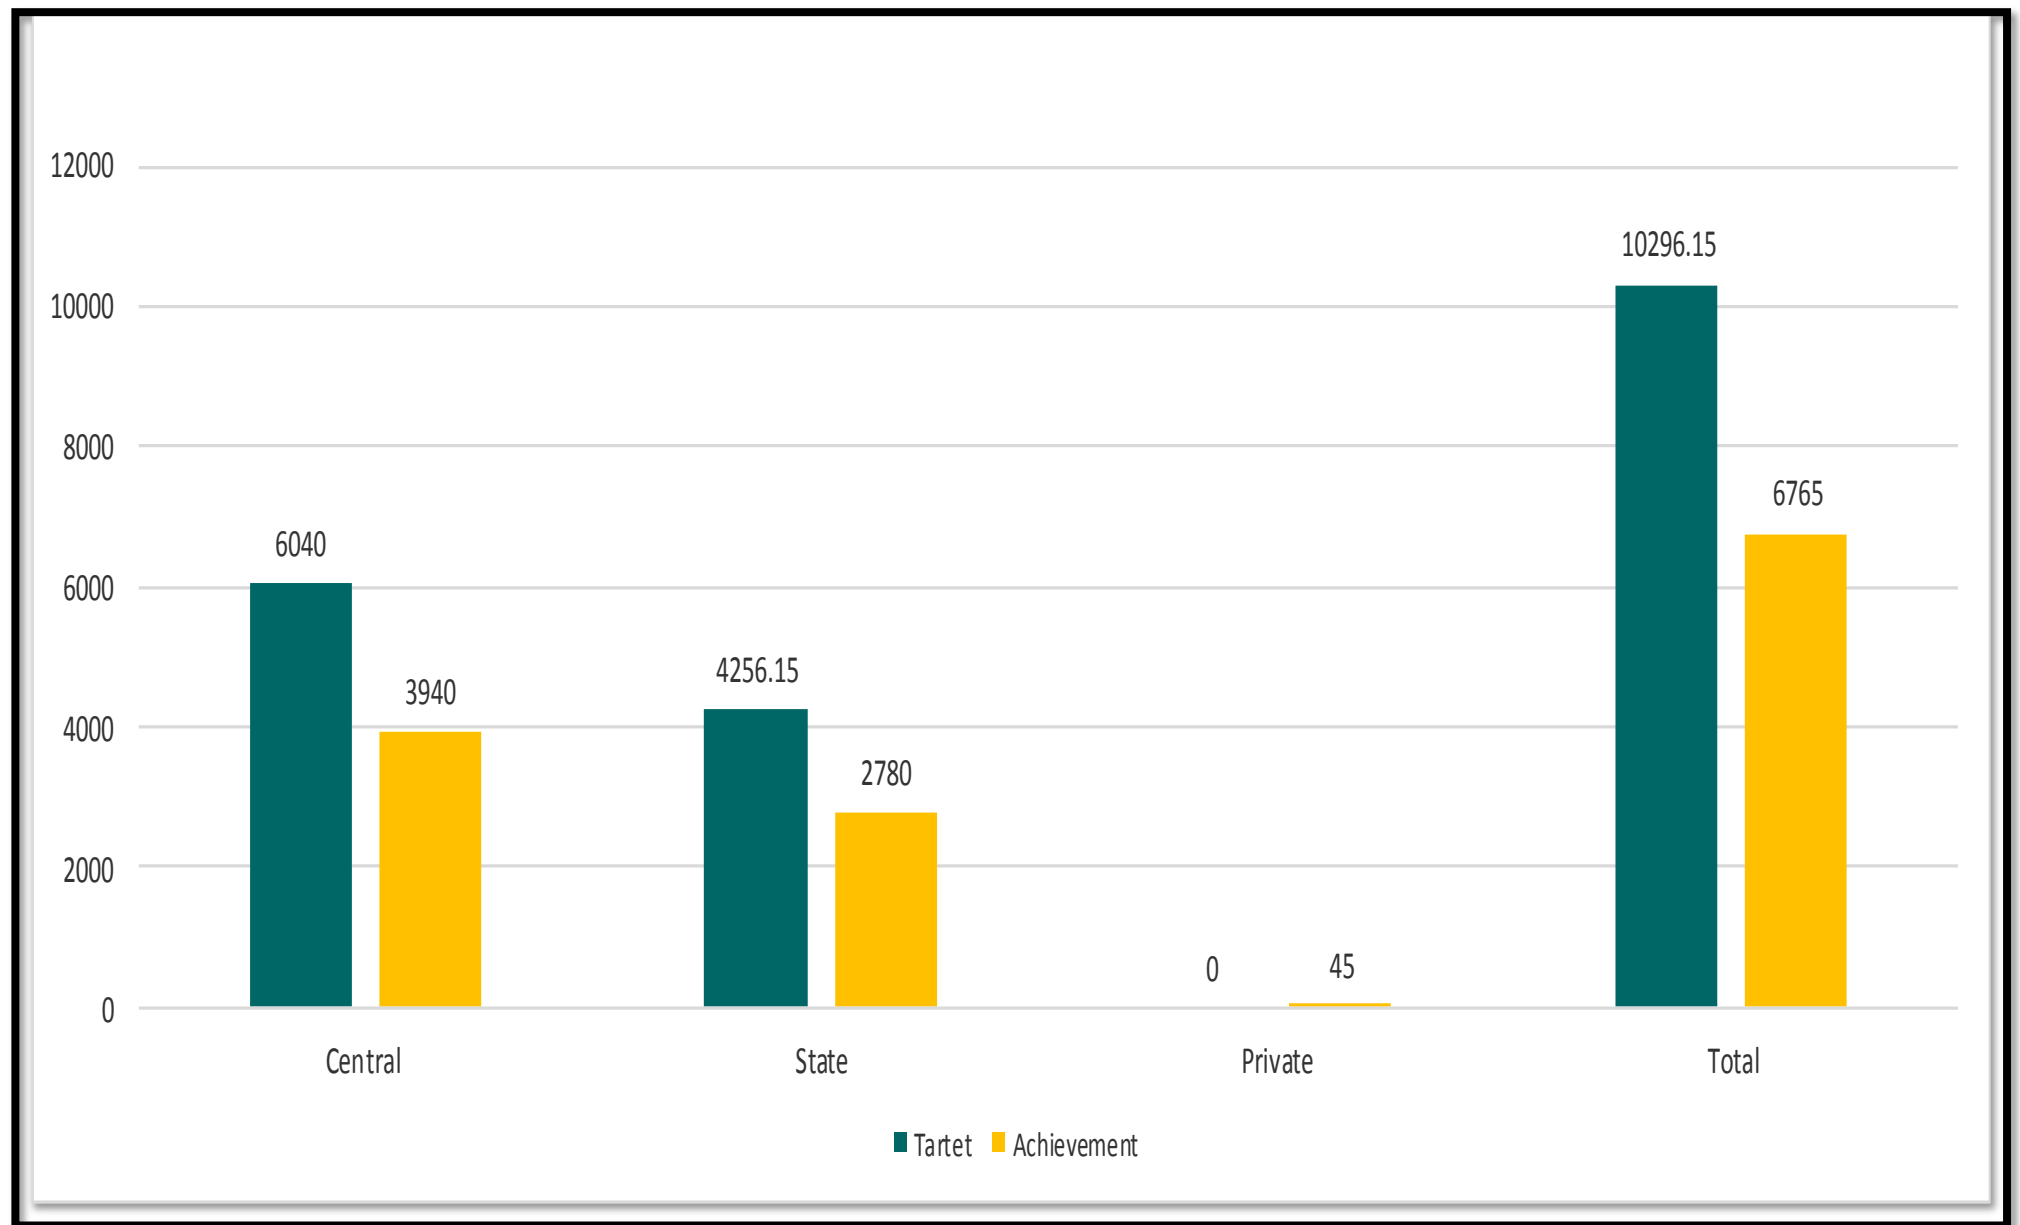

3. Year Wise Thermal Capacity Additional in the Country during 12th Plan

3.1 Thermal Capacity Addition Target/ Achievement for the Year 2012-13

State	Project Name	Impl Agency	Unit No	LOA Date	BTG Supplier	Targeted Cap. (MW)	Actual Cap. comm. (MW)	Comm. Date		COD
								Envisaged at the beginning of year	Ant. /Act(A)	
CENTRAL SECTOR										
Chhattisgarh	Sipat -I	NTPC	U-3	Apr-04	Others	660	660	06/12	02.06.12(A)	01.08.2012
Haryana	Indira Gandhi TPP	APCPL	U-3	Jul-07	BHEL	500	500	12/12	07.11.12(A)	26.04.2013
Jharkhand	Kodarma TPP	DVC	U-2	Jun-07	BHEL	500	500	12/12	15.02.13(A)	14.06.2014
Maharashtra	Mouda TPP	NTPC	U-1	Nov-08	BHEL	500	500	07/12	19.04.12(A)	13.03.2013
Maharashtra	Mouda TPP	NTPC	U-2	Nov-08	BHEL	-	500	-	29.03.13(A)	March 14
MP	Vindhyachal TPP-IV	NTPC	U-11	Jan-09	BHEL	500	500	07/12	14.06.12(A)	01.03.2013
MP	Vindhyachal TPP-IV	NTPC	U-12	Jan-09	BHEL	-	500	-	22.03.13(A)	March 14
TN	Vallur TPP Ph-I	NTECL	U-2	Aug-07	BHEL	500	500	02/13	28.02.13(A)	25.08.2013
Tripura	Tripura Gas	ONGC	Module-1	Jun-08	BHEL	363.3	363.3	11/12	03.01.13 (A)	04.01.2014
UP	Rihand TPP-III	NTPC	U-5	Feb-09	BHEL	500	500	06/12	25.05.12(A)	19.11.2012
Total Central Sector						4023.3	5023.3			
STATE SECTOR										
Chhattisgarh	Korba West Extn.St.III TPP	CSEB	U-5	-	BEHL	-	500	-	22.03.13(A)	05.09.2013
Chhattisgarh	Marwa TPP	CSEB	U-1	Apr-08	BHEL	500	-	02/13	Slipped	-
Delhi	Pragati CCGT - III	PPCL	GT-3	May-08	BHEL	250	250	08/12	27.06.12(A)	28.10.2013
Gujarat	Pipavav CCPP	GSECL	Block-2	Dec-07	BHEL	351	351	01/13	27.03.13(A)	27.03.2013
	Ukai TPP Extn	GSECL	U-6	Sep-07	BHEL	490	490	12/12	05.03.13(A)	08.06.2013
Rajasthan	Ramgarh CCGT	RRVUNL	GT	Aug-09	BHEL	110	110	01/13	20.03.13(A)	06.12.2013
	Ramgarh CCGT	RRVUNL	ST-1		BHEL	50	-	02/13	Slipped	-
MP	Satpura TPP Extn.	MPPGCL	U-10	Mar-08	BHEL	250	250	02/13	22.03.13(A)	18.08.2013
TN	Mettur TPP Ext	TNEB	U-1	Aug-08	Chinese	600	600	06/12	11.10.12(A)	12.10.2013
	North Chennai Extn.	TNEB	U-2	Aug-08	BHEL	600	600	03/13	09.03.13(A)	08.05.2014
UP	Harduaganj Ext	UPRVUNL	U-9	Jun-06	BHEL	250	250	05/12	25.05.12(A)	10.10.2013
	Parichha Extn	UPRVUNL	U-5	Jun-06	BHEL	250	250	06/12	24.05.12(A)	17.07.2012
	Parichha Extn	UPRVUNL	U-6			250	250	09/12	11.03.13(A)	18.04.2013
Total -State Sector						3951	3911			
PRIVATE SECTOR										
AP	Simhapuri TPP Ph-1	Madhucon Projects Ltd.	U-2	Jan-09	Chinese	150	150	09/12	02.07.12(A)	15.07.2012
	Thamminapatnam TPP-I	Meenakshi Energy Pvt. Ltd.	U-1	Aug-09	Chinese	150	150	08/12	09.09.12(A)	07.10.2012
	Thamminapatnam TPP-I	Meenakshi Energy Pvt. Ltd.	U-2			150	-	11/12	Slipped	-
Chhattisgarh	Kasaipalli TPP	M/s ACB (India)	U-2	Nov-08	Chinese	135	135	06/12	21.06.12(A)	21.06.2012
	Salora TPP	M/s Vandna Vidyut	U-1	Nov-08	Chinese	135	-	12/12	Slipped	-
	Swastik Korba TPS	ACB	U-1	-	Others	25	-	06/12	Slipped	-
	Ratija TPP	SCPL	U-1	-	Chinese	-	50	-	04.02.13(A)	27.02.2013
Gujarat	Mundra Ultra Mega TPP	Tata Power Co.	U-2	May-07	Others	800	800	12/12	25.07.12(A)	28.07.2012
	Mundra Ultra Mega TPP	Tata Power Co.	U-3	May-07	Others	-	800	-	16.10.12(A)	27.10.2012
	Mundra Ultra Mega TPP	Tata Power Co.	U-4	May-07	Others	-	800	-	16.01.13(A)	21.01.2013
	Mundra Ultra Mega TPP	Tata Power Co.	U-5	Jun-07	Others	-	800	-	18.03.13(A)	22.03.2013
	UNO-SUGEN CCPP	Torrent Power Ltd.	Mod-1	-	Others	-	382.5	-	20.01.13(A)	04.04.2013
Haryana	Salaya TPP	ESSAR	U-2	Nov-07	Chinese	600	600	08/12	13.06.12(A)	15.06.2012
	Jhajjar TPP (Mahatma Gandhi TPP)	CLP Power India Pvt. Ltd.	U-2	Jan-09	Chinese	660	660	04/12	11.04.12(A)	19.07.2012

State	Project Name	Impl Agency	Unit No	LOA Date	BTG Supplier	Targeted Cap. (MW)	Actual Cap. comm. (MW)	Comm. Date		COD
								Envisaged at the beginning of year	Ant. /Act(A)	
Jharkhand	Adhunik Power TPP	Adhunik Power Co. Ltd.	U-1	May-09	BHEL	270	270	09/12	19.11.12(A)	21.01.2013
	Adhunik Power TPP	Adhunik Power Co. Ltd.	U-2	May-09	BHEL	-	270	-	29.03.13(A)	19.05.2013
	Corporate Power Ltd Ph-I (Maitrishi Usha)	M/s Corporate Power Ltd.	U-1	Dec-09	BHEL	270	-	12/12	Slipped	-
Maharashtra	Bela TTP-I	IEPL	U-1	Dec-08	BHEL	270	270	09/12	20.03.13(A)	18.07.2013
	Butibori TPP	Vidarbha Industries Power	U-2	Dec-09	Chinese	300	300	08/12	17.08.12 (A)	04.04.2013
	EMCO Warora TPP	EMCO Energy Ltd. (GMR)	U-1	Sep-09	Chinese	300	300	11/12	07.02.13(A)	19.03.2013
	Tirora TPP Ph-I	Adani Power Ltd	U-1	Feb-08	Chinese	660	660	08/12	11.09.12(A)	23.09.2012
	Tirora TPP Ph-I	Adani Power Ltd	U-2			660	660	11/12	25.03.13(A)	30.03.2013
	Tirora TPP Ph-II	Adani Power Ltd	U-1			660	-	02/13	Slipped	-
	GEPL TPP	GEPL Pvt. Ltd.	U-2	Mar-09	Chinese	-	60	-	28.04.12(A)	-
	GEPL TPP	GEPL Pvt. Ltd.	U-1	-	Chinese	-	60	-	08.09.12(A)	09.05.2012
	Amaravathi TPP Ph-I	Indiabulls	U-1	-	BHEL	-	270	-	25.03.13(A)	03.06.2013
MP	Bina TPP	Bina Power Ltd.	U-1	Sep-08	BHEL	250	250	09/12	12.08.12(A)	30.08.2012
	Bina TPP	Bina Power Ltd.	U-2	Sep-08	BHEL		250	-	31.03.13(A)	07.04.2013
	Mahan	Essar Power Ltd.	U-1	-	Chinese		600	-	24.02.13(A)	29.04.2013
Orissa	Sterlite TPP	Sterlite Energy Ltd.	U-4	Sep-08	Chinese	600	600	06/12	25.04.12(A)	26.04.2012
	Kamalanga TPP		U-1	-	Chinese		350	-	29.03.13(A)	25.03.2014
Rajasthan	Jallipa- Kapurdi TPP	Raj west power Ltd (JSW)	U-5	Mar-07	Chinese	135	135	03/13	05.02.13(A)	05.02.2013
			U-6	Apr-07	Chinese	-	135	-	03.03.13(A)	03.03.2013
			U-7	Jun-07	Chinese	-	135	-	16.03.13(A)	16.03.2013
			U-8	May-07	Chinese	-	135	-	28.02.13(A)	28.02.2013
TN	Tuticorin TPP	Ind Barath	U-1	-	Chinese	-	150	-	10.03.13(A)	07.02.2013
Total -Private Sector						7180	11187.5			
Total for the year 2012-13						15154.3	20121.8			

3.2 Thermal Capacity Addition Target/ Achievement for the Year 2013-14

As on 31.03.14										
State	Project Name	Impl Agency	Unit No	LOA Date	BTG Supplier	Targeted Cap. (MW)	Actual Cap. comm. (MW)	Actual Comm. Date	At the beginning of the year	COD
CENTRAL SECTOR										
Bihar	Barh STPP St-II	NTPC	4	03/08 & 10/08	BHEL	660	660	30/11/13	12/13	15.11.2014
TN	Vallur TPP Ph-I	NTPC/ NTECL/ TNEB-JV	3	07/09	BHEL	500	500	28.02.2014	03/14	26.02.2015
TN	Tuticorin TPP	NLC/ TNEB-JV	1	01/09	BHEL	500	-	Slipped	03/14	-
Tripura	Tripura CCGT	ONGC JV	Blk-2	06/08	BHEL	363.3	-	Slipped	09/13	-
UP	Rihand STPP St-III	NTPC	6	02/09	BHEL	500	500	7/10/2013	12/13	March 2014
WB	Raghunathpur TPP	DVC	1	12/07	CHINA	600	-	Slipped	03/14	-
Total Central Sector						3123.3	1660			
STATE SECTOR										
Chhattisgarh	Marwa TPP	CSEB	1	04/08	BHEL	500	500	30.03.2014	09/13	-
Delhi	Pragati St-III CCGT	PPCL	GT-4	05/08	BHEL	250	250	7/5/2013	06/13	27.02.2014
Delhi	Pragati St-III CCGT	PPCL	ST-2	05/08	BHEL	250	250	26.02.2014	09/13	27.03.2014
Gujarat	Pipavav JV CCGT	GSECL	Block-1	12/07	BHEL	351	351	05/02/2013	09/13	-
MP	Shree Singaji TPP(Malwa TPP)	MPPGCL	1	12/08	BHEL	600	600	18/11/2013	06/13	February 2014
MP	Satpura TPS Extn.	MPPGCL	11	03/08	BHEL	250	250	25/12/2013	10/13	16.03.2014
Maha-rashtra	Chandrapur TPS Extn.	MAHAGENCO	8	07/08	BHEL	500	-	Slipped	12/13	-
Rajasthan	Kalisindh TPP	RRVUNL	1	07/08	SEPCO, CHINA	600	-	Slipped	12/13	-
Rajasthan	Chhabra TPS Extn.	RRVUNL	3	08/08	BHEL	250	250	14/09/13	06/13	19.12.2013
Rajasthan	Chhabra TPS Extn.	RRVUNL	4	08/08	BHEL	250	-	Slipped	01/14	-
Rajasthan	Ramgarh CCGP	RRVUNL	ST	08/09	BHEL	50	-	Slipped	12/13	--
TN	North Chennai TPS Extn.	TNEB	1	08/08	BHEL	600	600	13/09/13	09/13	20.03.2014
Total -State Sector						4451	3051			
PRIVATE SECTOR										
AP	Vizag TPP	Hinduja	1	03/10	BHEL	520	-	-	03/14	-
AP	Thammina-patnam TPP	Meena-kshi Energy	2	08/09	Chinese	150	150	17/04/13	09/13	30.04.2013
Chhattis-garh	Tamnar TPP	Jindal Power	1	12/08	BHEL	600	600	10.03.2014	03/14	14.03.2014
Chhattis-garh	Vandana Vidyut TPP	Vandana Vidyut TPP	1	05/08	BOILER: CETHAR VESSELS LTD TG: CNAIC, CHINA	135	-	Slipped	06/13	-
Chhattis-garh	DB Power TPP	DB Power Ltd	1	05/10	BHEL	600	600	23.02.2014	12/13	03.11.2014
Chhattis-garh	Swastik Korba TPP	ACB	1	02/10	BOILER: IJT; TURBINE: SIEMENS	25	-	Slipped	12/13	
Chhattis-garh	Akaltara TPP	KSK Mahanadi	1	04/09	SEC,CHIINA	600	600	13/08/13	09/13	14.08.2013
MP	Sasan UMPP	Reliance Power	3	06/08	SEC, CHINA	660	660	30/5/13	05/13	
MP	Sasan UMPP	Reliance Power	2	06/08	SEC, CHINA	660	660	18/12/13	09/13	
Maha-rashtra	Nasik TPP Ph-I	India Bulls	1	11/09	BHEL	270	270	25.02.2014	09/13	29.03.2014
Maha-rashtra	Dhariwal Infrastructure (P) Ltd.TPP	Dhariwal Infra-structure (P) Ltd.	1	04/10	SEC, CHINA	300	300	3/11/2013	06/13	13.02.2014
Maha-rashtra	Dhariwal Infrastructure (P) Ltd.TPP	Dhariwal Infra-structure (P) Ltd.	2	04/10	SEC, CHINA	300	-	Slipped	12/13	
Maha-rashtra	EMCO Warora TPP	GMR EMCO Energy Ltd.	2	09/09	SEC, CHINA	300	300	27/08/2013	06/13	01.09.2013

State	Project Name	Impl Agency	Unit No	LOA Date	BTG Supplier	Targeted Cap. (MW)	Actual Cap. comm. (MW)	Actual Comm. Date	At the beginning of the year	COD
Maha-rashtra	Tirora TPP Ph-II	Adani Power	1	02/08	SCMEC, CHINA	660	660	10/6/2013	06/13	14.06.2013
Orissa	Derang TPP	Jindal India Thermal Power	1	07/09	BHEL	600	-	Slipped	12/13	-
Orissa	Kamalang TPP	GMR Energy	2	08/08	SEPCO III, CHNA	350	350	28/09/13	09/13	12.11.2013
Punjab	Goindwal Sahib TPP	GVK Industries	1	02/09	BHEL	270	-	Slipped	06/13	-
Punjab	Talwandi Sahib TPP	Sterlite	1	07/09	SEPCO I, CHINA	660	-	Slipped	01/14	-
Total -Private Sector						7660	5150			
Total for during the year 2013-14						15234.3	9861			
Additional Capacity Commissioned										
Rajasthan	Kawai TPP	Adani Power Rajasthan Ltd.	1	04/10	Chinese	-	660	28/05/2013	-	31.05.2013
Tripura	Rokhia GT	Tripura State Electricity Corporation Ltd.)	9	-	BHEL	-	21	31/08/2013	-	-
Rajasthan	Kawai TPP	Adani Power Rajasthan Ltd.	2	04/10	Chinese	-	660	24/12/2013	-	31.05.2014
MP	BLA Power(Niwari) TPP	BLA Power Pvt.Ltd	1	-	Boiler –ISGEC Turbine- SIEMENS	-	45	24/03/2012	-	03.04.2012
TN	Tuticorin Indbarath	Indbarath Ltd	2		Chinese	-	150	30/12/2013	-	15.03.2014
Punjab	Rajpura TPP	Nabha Power	1	Jul-10	L&T	-	700	24/01/2014	-	01.02.2014
Gujarat	Dgen CCPP	Torrent Power	Block-I	Jul-10	Siemens Germany	-	400	12/01/2014	-	-
Maharashtra	Amaravati TPP Ph-I	India bulls Power Ltd	2	Nov-09	BHEL	-	270	17.02.2014	-	28.03.2014
AP	Simhapuri TPS Ph-II	Simhapuri Energy Pvt Ltd	3	Mar-10	Chinese	-	150	21.02.2014	-	26.02.2014
Gujarat	Dgen CCPP	Torrent Power	Block-3	Jul-10	Siemens Germany	-	400	09/03/2014	-	
Orissa	Kamalang TPP	GMR Energy	3	08/08	SEPCO III, CHNA	-	350	21/03/14	-	25.03.2014
Maha-rashtra	Tirora TPP Ph-II	Adani Power	2	02/08	SCMEC, CHINA	-	660	23/3/2014	-	31.03.2014
MP	Sasan UMPP	Reliance Power	4	06/08	SEC, CHINA	-	660	25/03/14	-	12.04.2014
Chhattis-garh	Tamnar TPP	Jindal Power	2	12/08	BHEL	-	600	30.03.2014	-	31.03.2014
Chhattis-garh	Chakabura TPP	ACBIL	1	-	Chinese	-	30	28.03.2014	-	30.03.2014
West Bengal	Durgapur TPS Extn	DPL	8	-	BHEL	-	250	31.03.2014	-	-
Chhattis-garh	Avantha Bhandar TPP	KWPCL	1	-	BHEL	-	600	31.03.2014	-	01.04.2014
Maha-rashtra	Butibori TPP Ph-II	Vidarbha Industries Power Ltd	1	-	Chinese	-	300	19.03.2013	-	28.03.2014
Total Addl.Capacity							6906			
Total for the Year 2013-14							16767			

3.3 Thermal Capacity Addition Target/ Achievement for the Year 2014-15

State	Project Name	Impl Agency	Equip. Supplier	Fuel	Unit No	LOA date	Targeted Cap. (MW)	Actual Cap .comm. (MW)	Actual Comm. Date	At the beginning of the year	COD
CENTRAL SECTOR											
Bihar	Barh STPP-II	NTPC	BHEL	Coal	U-5	SG:03/2008 TG:10/2008	660	660	04.03.2015	Feb-15	18.02.2016
	Muzaffarpur TPS Exp	KBUNL (JV of NTPC & BSEB)	BHEL	Coal	U-3	03/2010	195	195	31.03.2015	Mar-15	18.03.2017
TN	Tuticorin TPP	NTPL(JV of NLC & TANGEDCO)	BHEL	Coal	U-1	28.01.09	500	500	10.03.2015	Oct-14	18.06.2015
			BHEL	Coal	U-2		500		Feb-15	-	
Tripura	Palatana CCPP	OTPC (JV of ILFS, ONGC & Tripura Govt)	BHEL	Gas	BLK-2	23.06.08	363.3	363.3	16.11.2014	Aug-14	-
WB	Raghunathpur TPP, Ph-I	DVC	Chinese	Coal	U-1	14.12.2007	600	600	24.08.2014	Aug-14	31.03.2016
Total Central Sector							2818.3	2318.3			
STATE SECTOR											
AP	Damodaram Sanjeevaiah TPP	APPDCL	Blr- BHEL TG- L&T	Coal	U-1	SG:08/2008 TG:09/2008	800	800	28.08.2014	Jun-14	05.02.2015
					U-2		800	800	17.03.2015	Jan-15	24.08.2015
Chhattisgarh	Marwa TPP	CSPGCL	BHEL	Coal	U-2	11.04.08	500	-	Slipped	Dec-14	-
Maharashtra	Chandrapur TPS	MSPGCL	BHEL	Coal	U-8	25.07.08	500	500	29.03.2015	Oct-14	04.06.2016
	Koradi TPS Expn.	MSPGCL	L&T	Coal	U-8	23.09.09	660	660	30.03.2015	Oct-14	16.12.2015
	Koradi TPS Expn.	MSPGCL	L&T	Coal	U-9		660	-	Slipped	Jan-15	-
	Parli TPS Expn.	MSPGCL	BHEL	Coal	U-8	21.01.09	250	-	Slipped	Nov-14	-
MP	Malwa TPP (Shree Singaji)	MPPGCL	BHEL	Coal	U-2	12.12.08	600	600	15.10.2014	Sep-14	01.01.2015
Rajasthan	Kalisindh TPP	RRVUNL	Chinese	Coal	U-1	09.07.08	600	600	02.05.2014	Jun-14	01.06.2014
	Kalisindh TPP		Chinese	Coal	U-2		600	-	Slipped	Jan-15	-
	Ramgarh CCPP		BHEL	Gas	ST	18.08.09	50	50	01.05.2014	Jul-14	-
	Chhabra TPP		BHEL	Coal	U-4	20.08.08	250	250	30.06.2014	Jun-14	30.12.2014
UP	Anpara-D TPS	UPRVUNL	BHEL	Coal	U- 6	27.10.07	500	-	Slipped	Mar-15	-
Total State Sector							6770	4260			
PRIVATE SECTOR											
AP	Painampuram TPP	Thermal Power Tech Corp.Ltd	Chinese	Coal	U-1	09/2010	660	660	07.02.2015	Dec-14	02.03.2015
	Vizag TPP	Hinduja National Power Corp.Ltd	BHEL	Coal	U-1	03/2010	520	-	Slipped	Oct-14	-
Chhattisgarh	Swastic Korba TPP	ACB India Ltd.	Blr:ISGEC India TG:Siemens	Coal	U-1	29.03.10	25	25	31.03.2015	Nov-14	-
	Salora TPP	Vandana Vidyut Ltd	Chinese	Coal	U-1	11/2008	135	135	10.04.2014	Sep-14	01.05.2014
	Bandakhar TPP	Maruti Clean coal	Chinese	Coal	U-1	-	300	-	Slipped	Jan-15	-
Maharashtra	Amravati TPP Ph-I	India Bulls Power Ltd	BHEL	Coal	U-3	30.11.09	270	270	29.01.2015	Oct-14	03.02.2015
Maharashtra	Nasik TPP Ph-I	India Bulls Realtech	BHEL	Coal	U-2	24.11.09	270	-	Slipped	Jul-14	-
Maharashtra	Dhariwal TPP	Dhariwal Infrastruecture Ltd	Chinese	Coal	U-2	28.04.10	300	300	28.05.2014	Jun-14	02.08.2014
Orissa	Derang TPP	JIPL	BHEL	Coal	U-1	26.07.09	600	600	10.05.2014	Jun-14	06.06.2014
Punjab	Rajpura TPP (Nabha)	Nabha Power Ltd	L&T	Coal	U-2	16.07.10	700	700	06.07.2014	Jul-14	01.08.2014
Punjab	Talwandi Sabo TPP	M/s Sterlite	Chinese	Coal	U-1	18.07.09	660	660	17.06.2014	May-14	01.08.2014
Punjab	Talwandi Sabo TPP	M/s Sterlite	Chinese	Coal	U-2	18.07.09	660	-	Slipped	Sep-14	-
WB	Haldia TPP	M/s Haldia Energy Ltd.	Chinese	Coal	U-1	14.09.11	300	300	14.01.2015	Dec-14	28.01.2015
Total Private Sector							5400	3650			
Total target during 2014-15							14988.3	10228.3			

Additional Capacity Commissioned											
State	Project Name	Impl Agency	Equip. Supplier	Fuel	Unit No	LOA date	Targeted Cap. (MW)	Actual Cap .comm. (MW)	Actual Comm. Date	At the beginning of the year	COD
Gujarat	D gen CCGP	Torrent Power	Siemens Germany	gas	Block-II	02.07.2010	-	400	23.04.2014	-	-
Gujarat	Dhuvaran CCGP	GSECL	Siemens Germany	gas	Unit 1		-	376.1	21.05.2014	-	-
MP	Sasan UMPP	SPL	Chinese	Coal	4th Unit (Unit-1)		-	660	21.05.2014	-	27.05.2014
MP	Sasan UMPP	SPL	Chinese	Coal	Unit-5		-	660	24.08.2014	-	26.12.2014
Chhattisgarh	Akaltara TPP	KSK	Chinese	Coal	Unit-2		-	600	22.08.2014	-	26.08.2014
MP	Nigrie TPP	JPVL	L&T	Coal	Unit-1		-	660	29.08.2014	-	03.09.2014
Maharashtra	Tirora TPP Ph-II	Adani Power Maharashtra Pvt Ltd	Chinese	Coal	Unit-3	05.11.2009	-	660	25.09.2014	-	11.10.2014
TN	Mutiara TPP	Coastal Energen	Chinese	Coal	Unit-1	25.02.2009	-	600	02.12.2014	-	23.12.2014
Chhattisgarh	Tamnar TPP (Raigarh)	Jindal Power	BHEL	Coal	Unit-3		-	600	07.01.2015	-	15.01.2015
Orissa	Derang TPP	JIPL	BHEL	Coal	U-2		-	600	24.01.2015	-	12.02.2015
TN	Neyveli TPS Ph-II Exp	NLC	BHEL	Coal	U-2		-	250	24.01.2015	-	22.04.2015
WB	Haldia TPP	M/s Haldia Energy Ltd.	Chinese	Coal	U-2		-	300	16.02.2015	-	21.02.2015
MP	Nigrie TPP	JP Ventures Ltd	Non-BHEL	Coal	U-2		-	660	17.02.2015	-	21.02.2015
Chhattisgarh	Raikhera TPP	GMR	Chinese	Coal	U-1		-	685	27.02.2015	-	01.06.2015
Maharashtra	Amravati TPP Ph-I	India Bulls Power Ltd	BHEL	Coal	U-4	30.11.09	-	270	04.03.2015	-	08.03.2015
AP	Simhapuri	Simhapuri Energy Pvt Ltd	Chinese	Coal	U-4		-	150	07.03.2015	-	31.03.2015
Maharashtra	Amravati TPP Ph-I	India Bulls Power Ltd	BHEL	Coal	U-5	30.11.09	-	270	12.03.2015	-	13.03.2015
MP	Sasan UMPP	SPL	Chinese	Coal	Unit-6		-	660	19.03.2015	-	27.03.2015
Tripura	Agartala CCGP	NEEPCO	Thermax	gas	ST-2		-	25.5	22.03.2015	-	-
Chhattisgarh	DB Power TPP	DB Power Ltd	BHEL	Coal	Unit-2		-	600	24.03.2015	-	-
Chhattisgarh	Tamnar TPP (Raigarh)	Jindal Power	BHEL	Coal	Unit-4		-	600	26.03.2015	-	-
Gujarat	Sikka TPP Extn	GSECL	BHEL	Coal	U-3		-	250	28.03.2015	-	14.09.2015
Tripura	Monarchak gas power project	NEEPCO	BHEL	Gas	GT		-	65.4	30.03.2015	-	-
Additional Capacity Commissioned								10602			
								20830.3			

3.4 Thermal Capacity Addition Target/ Achievement for the Year 2015-16

State	Project Name	Impl Agency	Unit No	BTG Supplier	Cap. (MW)	Anti. Comm. (beginning of the year)	Now Anti. Comm.	Cap. Add (MW)	Actual Date of Comm.	COD
CENTRAL SECTOR										
Assam	Bongaigaon TPP	NTPC	U-1	BHEL	250	06/2015	-	250	22.06.15(A)	01.04.2016
Bihar	Muzafferpur	NTPC	U-4	BHEL	195	02/2016	03/2016	-	-	-
Bihar	Nabi Nagar TPP	NTPC	U-1	BHEL	-	-	-	250	20.03.16(A)	15.01.2017
Jharkhand	Bokaro TPS "A" Exp.	DVC	U-1	BHEL	-	-	-	500	22.03.16(A)	23.02.2017
Maharashtra	Mouda STPP-II	NTPC	U-3	BHEL	-	-	-	660	28.03.16(A)	01.02.2017
MP	Vindhyachal TPP-V	NTPC	U-13	BHEL	500	12/2015	-	500	06.08.15(A)	30.10.2015
Tripura	Agratala STG	NEEPCO	ST-2	Thermax	25.5	05/2015	01/2016	-	-	-
Tripura	Monarchak CCPP	NEEPCO	ST	BHEL	35.6	08/2015	-	35.6	14.01.16(A)	-
TN	Tuticorin TPP	NLC	U-2	BHEL	500	07/2015	-	500	09.07.15(A)	29.08.2015
WB	Raghunathpur TPP, Ph-I	DVC	U-2	Chinese	600	01/2016	-	600	18.01.16(A)	31.03.2016
Total Central Sector					2106.1			3295.6		
STATE SECTOR										
Chhattisgarh	Marwa TPP	CSPGCL	U-2	BHEL	500	09/2015	02/2016	-	-	-
Gujarat	Sikka TPS	GSECL	U-4	BHEL	250	12/2015	-	250	25.09.15(A)	28.12.2015
Karnataka	Bellary TPS St-III	KPCL	U-3	BHEL	700	12/2015	01/2016	700	01.03.16(A)	16.09.2017
Karnataka	Yermarus TPP	KPCL	U-1	BHEL	800	01/2016	02/2016	800	29.03.16(A)	07.03.2017
Maharashtra	Chandrapur TPS	MSPGCL	U-9	BHEL	500	10/2015	02/2016	500	21.03.16(A)	24.11.2016
Maharashtra	Koradi TPS Expn.	MSPGCL	U-9	L&T	660	09/2015	02/2016	660	15.03.16(A)	22.11.2016
Maharashtra	Koradi TPS Expn.	MSPGCL	U-10	L&T	660	02/2016	05/2016	-	-	-
Maharashtra	Parli TPS	MSPGCL	U-8	BHEL	250	01/2016	03/2016	250	30.03.16(A)	30.11.2016
Rajasthan	Kalisindh TPP	RVUNL	U-2	Chinese	600	05/2015	-	600	06.06.15(A)	25.07.2015
Telangana	Singareni TPP	Singareni Collieries Co Ltd	U-1	BHEL	600	01/2016	03/2016	600	13.03.16(A)	25.09.2016
Telangana	Kakatiya TPS Extn.	T GENCO	U-1	BHEL	600	12/2015	12/2015	600	31.12.15(A)	24.03.2016
UP	Anpara-D TPS	UPRVUNL	U- 6	BHEL	500	06/2015	-	500	06.06.15(A)	08.05.2016
UP	Anpara-D TPS	UPRVUNL	U- 7	BHEL	500	12/2015	02/2016	500	06.03.16(A)	18.10.2016
WB	Sagardighi TPS-Extn	West Bengal	U-3	BHEL	500	09/2015	12/2015	500	14.12.15(A)	-
WB	Sagardighi TPS-Extn	West Bengal	U-4	BHEL	500	01/2016	06/2016	-	-	-
Total State Sector					8120			6460		
PRIVATE SECTOR										
AP	Painampuram TPP	Thermal Power Tech Corporation Ltd	U-2	Chinese	660	08/2015	-	660	03.09.15(A)	15.09.2015
AP	Vizag TPP	Hinduja National Power Corp. Ltd	U-1	BHEL	520	10/2015	02/2015	520	27.12.15(A)	11.01.2016
AP	Lanco Kondapalli Extn. Ph-III (PS)	Lanco Kondapalli Power Co.Ltd	Block-I	Others	-	-	-	371	07.08.15(A)	-
AP	Lanco Kondapalli Extn. Ph-III (PS)	Lanco Kondapalli Power Co.Ltd	Block-II	Others	-	-	-	371	05.09.15(A)	-
AP	Vemagiri CCPP-II (PS)	GMR Rajahmundry Energy Ltd.	Block-I	Others	-	-	-	384	12.09.15(A)	-
AP	Vemagiri CCPP-II (PS)	GMR Rajahmundry Energy Ltd.	Block-II	Others	-	-	-	384	05.10.15(A)	-
AP	Vizag TPP	Hinduja National Power Corp. Ltd	U-2	BHEL	-	-	-	520	30.03.16(A)	03.07.2016
Chhattisgarh	Bandakhar TPP	M/s Maruti Clean (Chhattisgarh) Ltd.	U-1	Chinese	300	06/2015	-	300	19.06.15(A)	-
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	U-1	Chinese	360	06/2015	-	360	28.10.15(A)	27.11.2015
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	U-2	Chinese	-	-	-	360	28.01.16(A)	12.02.2016
Chhattisgarh	BALCO TPP	BALCO Pvt Ltd	U-1	Chinese	300	06/2015	-	300	05.06.15(A)	11.07.2015
Chhattisgarh	BALCO TPP	BALCO Pvt Ltd	U-2	Chinese	300	09/2015	02/2016	300	24.03.16(A)	30.03.2016
Chhattisgarh	Raikheda TPP	GMR	U-2	Doosan (Non-BHEL)	685	12/2015	02/2016	685	28.03.16(A)	

State	Project Name	Impl Agency	Unit No	BTG Supplier	Cap. (MW)	Anti. Comm. (beginning of the year)	Now Anti. Comm.	Cap. Add (MW)	Actual Date of Comm.	COD
Chhattisgarh	Salora	Vandana Vidyut	U-2	Chinese	135	09/2015	2016-17	-	-	-
Maharashtra	Nasik TPP Ph-I	Ratan India (Nasik) Power Ltd	U-2	BHEL	270	01/2016	03/2016	-	-	-
MP	Anuppur TPP Ph-I	MB Power(MP)	U-1	Chinese	600	06/2015	-	600	20.04.15(A)	20.05.2015
M.P	Seioni TPP Ph-I	Jhabua Power Ltd	U-1	BHEL	-	-	-	600	22.03.16(A)	03.05.2016
MP	Anuppur TPP Ph-I	MB Power(MP)	U-2	Chinese	-	-	-	600	30.03.16(A)	07.04.2016
Orissa	Ind Bharat TPP (Orissa)	Ind Barath	U-1	Chinese	350	10/2015	01/2016	350	25.02.16(A)	20.07.2016
Punjab	Talwandi Sabo TPP	Talwandi Sabo Power Ltd	U-2	Chinese	660	06/2015	-	660	30.10.15(A)	25.11.2015
Punjab	Talwandi Sabo TPP	Talwandi Sabo Power Ltd	U-3	Chinese	660	12/2015	03/2016	660	29.03.16(A)	25.08.2016
Punjab	Goindwal Sahib TPP	GVK Power	U-1	BHEL	-	-	-	270	14.02.16(A)	06.04.2016
Punjab	Goindwal Sahib TPP	GVK Power	U-2	BHEL	-	-	-	270	15.03.16(A)	16.04.2016
TN	ITPCL TPP	IL&FS TN PC.Ltd	U-1	Chinese	-	-	-	600	19.09.2015	29.09.2015
TN	Melamaruthur (Mutiara)	Coastal Energen	U-2	Chinese	-	-	-	600	02.01.16(A)	15.01.2016
UP	Lalitpur TPP	Lalitpur power Generation Co. Ltd	U-1	BHEL	660	-	-	660	26.03.16(A)	01.10.2015
UP	Lalitpur TPP	Lalitpur power Generation Co. Ltd	U-2	BHEL	-	09/2015	-	660	08.01.16(A)	14.10.2016
UP	Prayagraj (Bara) TPP	Prayagraj power Gen. Co. Ltd(J.P.Power Ventures)	U-1	BHEL	660	10/2015	-	660	25.12.15(A)	29.02.2016
Total Private Sector					7120			12705		
Grand Total					17346.1			22460.6		

3.5 Thermal Capacity Addition Target/ Achievement for the Year 2016-17

State	Project	Unit	Imp Agency	BTG Supplier	Capacity (MW)	Anticipated Commng. Schedule	Actual date of comm.	Capacity Achieved	COD
<u>CENTRAL SECTOR</u>									
Bihar	Nabinagar TPP	U-2	NTPC	BHEL	250	12-2016	-	-	-
Bihar	Kanti TPS St-II	U-4	NTPC	BHEL	195	09-2016	24.03.2017	195.0	01.07.2017
Chhattisgarh	Lara STPP	U-1	NTPC	NON BHEL	800	01-2017	-	-	-
Karnataka	Kudgi TPP	U-1	NTPC	NON BHEL	800	11-2016	25.12.2016	800.0	31.07.2017
Maharashtra	Mauda STPP-II	U-4	NTPC	BHEL	660	12-2016	18.03.2017	660.0	18.09.2017
Tripura	Agartala Gas Based Power Project	ST-1	NEEPCO	NON BHEL	25.5	06-2016	23.08.2016	25.5	-
Total Central					2730.5			1680.5	
<u>STATE SECTOR</u>									
Assam	Namrup CCGT	GT	APGCL	BHEL	70	09-2016	11.01.2017	62.25	-
Assam	Namrup CCGT	ST	APGCL	BHEL	30	09-2016	-	-	-
Bihar	Barauni TPP,	U-8	BSEB	BHEL	250	12-2016	-	-	-
Chhattisgarh	Marwa TPS	U-2	CSPGCL	BHEL	500	06-2016	15.07.2016	500.0	31.07.2016
Gujarat	Bhavnagar TPP	U-1	BECL	BHEL	250	06-2016	16.05.2016	250.0	-
Gujarat	Bhavnagar TPP	U-2	BECL	BHEL	250	08-2016	27.03.2017	250.0	-
Karnataka	Yermarus TPP	U-2	KPCL	BHEL	800	07-2016	29.03.2017	800.0	06.04.2017
Maharashtra	Koradi TPP	U-10	MSPGCL	NON BHEL	660	08-2016	28.12.2016	660.0	17.01.2017
Telangana	Singreni TPP	U-2	SCCL	BHEL	600	06-2016	25.11.2016	600.0	02.12.2016
West Bengal	Sagardighi TPS-II	U-4	WBPCL	BHEL	500	09-2016	15.12.2016	500.0	-
Total State					3910			3622.25	
<u>PRIVATE SECTOR</u>									
Andhra pradesh	Sembcorp Gayatri Pvt.ltd.(NCC TPP)	U-1	SGPL	NON BHEL	660	09-2016	12.11.2016	660.0	17.11.2016
Andhra pradesh	Sembcorp Gayatri Pvt.ltd.(NCC TPP)	U-2	SGPL	NON BHEL	660	12-2016	15.02.2017	660.0	21.02.2017
Chhattisgarh	Nawapara TPP	U-1	TRN	CHINESE	300	05-2016	14.08.2016	300.0	19.08.2016
Chhattisgarh	Nawapara TPP	U-2	TRN	CHINESE	300	11-2016	-	-	-
Chhattisgarh	Ucchpinda TPP	U-3	RKM	CHINESE	360	07-2016	-	-	-
Chhattisgarh	Binjkote TPP	U-1	SKS	NON BHEL	300	11-2016	-	-	-
Chhattisgarh	Athena Singhitarai TPP	U-1	Athena Chhattisgarh	NON BHEL	600	10-2016	-	-	-
Maharashtra	Nashik TPP, Ph-I	U-2	Rattan Power	BHEL	270	06-2016	15.02.2017	270.0	-
Maharashtra	Nashik TPP, Ph-I	U-3	Rattan Power	BHEL	270	12-2016	-	-	-
Orissa	Utkal TPP	U-2	Ind Barath	NON BHEL	350	07-2016	-	-	-
Orissa	Lanco Babandh TPP	U-1	Lanco Babandh	NON BHEL	660	02-2017	-	-	-
Tamilnadu	ITPCL TPP	U-2	ILFS	NON BHEL	600	05-2016	18.04.2016	600.0	30.04.2016

State	Project	Unit	Imp Agency	BTG Supplier	Capacity (MW)	Anticipated Commng. Schedule	Actual date of comm.	Capacity Achieved	COD
Uttar pradesh	Bara TPP	U-2	Jaypee	BHEL	660	07-2016	06.09.2016	660.0	10.09.2016
Uttar pradesh	Lalitpur TPP	U-3	LPGCL	BHEL	660	04-2016	01.04.2016	660.0	23.12.2016
West Bengal	Haldia TPP	U-1	India Power	BHEL	150	07-2016	-	-	-
Total Private					6800			3810.0	
Total Thermal					13440.5			9112.75	
ADDITIONAL PROJECTS COMMISSIONED IN RFD 2016-17									
<i>CENTRAL SECTOR</i>									
Assam	Bongaigaon TPP	U-2	NTPC	BHEL	-	-	22.03.2017	250.0	01.11.2017
Karnataka	Kudgi TPP	U-2	NTPC	NON BHEL	-	-	23.03.2017	800.0	31.12.2017
Uttar Pradesh	Unchahar TPS ST-IV	U-6	NTPC	BHEL	-	-	31.03.2017	500.0	-
<i>PRIVATE SECTOR</i>									
Chhattisgarh	Ratija TPP -II	U-2	Spectrum Coal&Power Ltd	Non-BHEL	-	-	10.11.2016	50.0	-
Uttrakhand	GAMA CCPP	Module-1 (GT1&2+ST)	M/s GAMA Infraprop Ltd.	Others	-	-	25.04.2016	225.0	-
Uttrakhand	Kashipur CCPP	Blk-I	Srawanthi Energy Pvt.Ltd	Others	-	-	20.11.2016	225.0	-
Maharashtra	Mangaon CCPP	Block-I	M/s PGPL	Others	-	-	14.07.2016	388.0	-
Total Additional								2438.0	
Total Grand Thermal Capacity					13440.5			11550.75	

4. Thermal Capacity Addition Target/ Achievement for the Year 2017-18

State	Project Name	Impl Agency	Equipment Supplier	Unit No.	Targeted Cap. (MW)	Anti. Comm Date at beginning of year	Anti. Comm Date (At present)	Actual Date of Comm	Capacity Achieved (MW)	COD
CENTRAL SECTOR										
Assam	Bongaigaon TPP	NTPC	BHEL	3	250	Dec-17	Apr-18	-	-	-
Bihar	Nabi Nagar TPP	JV of NTPC & Rly	BHEL	2	250	Apr-17	-	03.04.2017	250.00	10.09.2017
Bihar	New Nabi Nagar TPP	JV of NTPC & BSPGCL	NON BHEL	1	660	Aug-17	Mar-18	-	-	-
Chhattisgarh	Lara TPP	NTPC	NON BHEL	1	800	Oct-17	-	23.03.2018	800.00	-
Karnataka	Kudgi STPP Ph-I	NTPC	NON BHEL	3	800	Aug-17	-	12.03.2018	800.00	-
MP	Gadarwara STPP,St-I	NTPC	BHEL	1	800	Jan-18	Mar-18	-	-	-
Maharashtra	Solapur STPP	NTPC	NON BHEL	1	660	Apr-17	-	07.04.2017	660.00	25.09.2017
UP	Meja STPP	JV of NTPC & UPRVUNL	NON BHEL	1	660	Oct-17	-	31.03.2018	660.00	-
TOTAL CENTRAL SECTOR					4880				3170.00	
STATE SECTOR										
AP	Royal seema TPP	APGENCO	BHEL	6	600	Aug-17	-	12.03.2018	600.00	29.03.2018
Assam	Namrup	APGCL	BHEL	ST	36.15	Feb-18	Mar-18	-	-	-
MP	Shree Singaji TPP, St-II	MPPGCL	NON BHEL	3	660	Dec-17	Jun-18	-	-	-
Rajasthan	Suratgarh TPS	RRVUNL	BHEL	7	660	Nov-17	Feb-18	-	-	-
Rajasthan	Chhabra SCTPP	RRVUNL	L&T & MHI	5	660	Apr-17	-	04.04.2017	660.00	-
Rajasthan	Chhabra SCTPP	RRVUNL	L&T & MHI	6	660	Jan-18	Feb-18	-	-	-
Telangana	Bhadradi TPP	TGENCO	BHEL	1	270	Mar-18	May-19	-	-	-
TOTAL STATE SECTOR					3546.15				1260.00	
PRIVATE SECTOR										
Chhattisgarh	Akaltara (Naiyara) TPP	KSK Mahandi Power Company Ltd	CHINESE	3	600	Nov-17	-	18.01.2018	600.00	28.02.2018
Chhattisgarh	Binjkote TPP	SKS Power Generation (Chhattisgarh) Ltd	CHINESE	1	300	May-17	-	25.04.2017	300.00	-
Chhattisgarh	Nawapara TPP	TRN Energy	CHINESE	2	300	May-17	-	18.04.2017	300.00	01.05.2017
Chhattisgarh	Lanco Amarkantak TPS-II	LAP Pvt. Ltd.	CHINESE	3	660	Nov-17	Mar-18	-	-	-
Maharashtra	Nasik TPP Ph-I	RattanIndia Nasik Power Ltd	BHEL	3	270	May-17	-	14.04.2017	270.00	-
UP	Bara TPP	Prayagraj Power Generation Co.Ltd.	BHEL	3	660	Aug-17	-	22.05.2017	660.00	26.05.2017
WB	India Power TPP (Haldia)	Indian Energy Ltd (Haldia)	BHEL	1	150	Apr-17	-	07.06.2017	150.00	-
TOTAL PRIVATE SECTOR					2940				2280.00	

ADDITIONAL PROJECTS COMMISSIONED										
State	Project Name	Impl Agency	Equipment Supplier	Unit No.	Targeted Cap. (MW)	Anti. Comm Date at beginning of year	Anti. Comm Date (At present)	Actual Date of Comm	Capacity Achieved (MW)	COD
PRIVATE SECTOR										
Maharashtra	Nasik TPP Ph-I	RattanIndia Nasik Power Ltd	BHEL	4	-	-	-	19.05.2017	270.00	-
Maharashtra	Nasik TPP Ph-I	RattanIndia Nasik Power Ltd	BHEL	5	-	-	-	30.05.2017	270.00	-
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt.Ltd.	Chinese	3	-	-	-	12.09.2017	360.00	-
Maharashtra	Shirpur TPP	Shirpur Power Pvt. Ltd.	BHEL	1	-	-	-	28.09.2017	150.00	-
WB	India Power TPP (Haldia)	Indian Energy Ltd (Haldia)	BHEL	2	-	-	-	31.12.2017*	150.00	-
Bihar	Barauni Ext.	BSEB	BHEL	8	-	-	-	11.01.2018	250.00	-
Chhattisgarh	Binjkote TPP	SKS Power Generation (Chhattisgarh) Ltd	CHINESE	2	-	-	-	28.03.2018	300.00	-
Bihar	Barauni Ext.	BSEB	BHEL	9	-	-	-	31.03.2018	250.00	-
TOTAL ADDITIONAL PRIVATE SECTOR									2000.00	
TOTAL THERMAL CAPACITY					11366.15				8710.00	

5. Thermal Capacity Addition Target/ Achievement for the Year 2018-19

State	Project Name	Impl Agency	Equipment Supplier	Unit No.	Targeted Cap. (MW)	Anti. Comm Date at beginning of year	Anti. Comm Date (At present)	Actual Date of Comm	Capacity Achieved (MW)	COD
CENTRAL SECTOR										
Assam	Bongaigaon TPP	NTPC	BHEL	3	250	Sept - 18	-	26.03.2019	250	-
Bihar	Nabi Nagar TPP	JV of NTPC & Rly	BHEL	3	250	Dec - 18	-	26.02.2019	250	-
Bihar	New Nabi Nagar TPP	NTPC	Alstom-Bharat Forge	1	660	Jan - 19	Jun - 19	-	-	-
MP	Gadarwara TPP	NTPC	BHEL	1	800	Nov - 18		29.03.2019	800	-
Odisha	Darlipalli STPP	NTPC		1	800	Mar - 19	Sept - 19	-	-	-
Total Central Sector					2760				1300	
STATE SECTOR										
Assam	Namrup CCGT	APGCL	BHEL	ST	36.15	Feb - 19	Sept - 19	-	-	-
MP	Shri Singhaji TPP St-II	MPPGCL	L&T	3	660	Sept - 18	-	18.11.2018	660	-
MP	Shri Singhaji TPP St-II	MPPGCL	L&T	4	660	Feb - 19	-	27.03.2019	660	-
Odisha	Ib valley TPP	OPGC	BHEL	3	660	Mar - 19	Jun - 19	-	-	-
Rajasthan	Chhabra TPP Extn	RRVUNL	L&T	6	660	Dec - 18	-	29.03.2019	660	-
Rajasthan	Suratgarh SCTPP	RRVUNL	BHEL	7	660	Dec - 18	Aug - 19	-	-	-
Karnataka	Yelahanka CCPP	KPCL	BHEL	GT+ST	370	Oct - 18	Aug - 19	-	-	-
Telangana	Kothagudem TPS St-VII	TSGENCO	BHEL	1	800	Dec - 18	-	26.12.2019	800	-
Total State Sector					4506.15				2780	
PRIVATE SECTOR					0				0	
TOTAL THERMAL CAPACITY ADDITION					7266.15				4080	

ADDITIONAL PROJECTS

CENTRAL SECTOR										
Maharashtra	Solapur STPP	NTPC	BGR	2	-	-	-	29.03.2019	660	-
Total Central Sector									660	
STATE SECTOR										
Assam	Lakwa Replacement Power Project.	APGCL	Others	1 to 7	-	-	-	26.04.2018	69.755	-
Total State Sector									69.755	
PRIVATE SECTOR										
MP	Mahan TPP	ESSAR	Chinees	2	-	-	-	07.10.2018	600	-
Chhattisgarh	Uchpinda TPP	R K M POWERGEN	Chinees	4	-	-	-	20.03.2019	360	-
WB	Dishergarh TPS	IPCL	Others	-	-	-	-	27.03.2019	12	-
Total Private Sector									972	
Total Additional Capacity									1701.755	
TOTAL GRAND THERMAL CAPACITY ADDITION					7266.15				5781.755	
Reamrks: Lakwa Replacement Power Project (69.755 MW) had achieved COD on 26.04.18 but the intimation regarding COD was received in Oct'18.										
Mahan TPP (600MW) was a stressed project.										

6. Details of Under Construction Thermal Power Projects in country

S. No.	State	Project Name / Impl. Agency/ EPC or BTG	LOA Date/	Unit No	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Ant. Trial Run / COD	Exp. In crores.	Till Date
CENTRAL SECTOR										
1.	Bihar	Barh STPP-I /NTPC/Others	Mar-05	U-1	660	May-17	Oct-20	Nov-20	16576.34	Oct-19
			Mar-05	U-2	660	Nov-17	Mar-21	Apr-21		
			Mar-05	U-3	660	May-18	Sep-21	Oct-21		
2.	Bihar	Nabi Nagar TPP / JV of NTPC & Rlys/BHEL	Jan-08	U-4	250	Nov-13	Dec-20	Feb-21	8078.42	Feb-2019
3.	Bihar	New Nabi Nagar TPP / JV of NTPC & BSPGCL TG-Alstom & Bharat Forge, SG-BHEL	Jan-13	U-2	660	Jul-17	Dec-20	Jan-21	14408.86	Feb-20
			Jan-13	U-3	660	Jan-18	Jul-21	Aug-21		
4.	Bihar	Buxar TPP	Jun-19	U-1	660	Jul-23	Jun-23	Jul-23	882.92	Feb-20
			Jun-19	U-2	660	Jan-24	Jan-24	Jan-24		
5.	Chhatisgarh	Lara STPP / NTPC / SG-Dooson TG-BGR Hitachi	Dec-12	U-2	800	May-17	Jul-20	Aug-20	12607.28	Oct-19
6.	Jharkhand	North Karanpura STPP/ NTPC / BHEL	Feb-14	U-1	660	Feb-18	May-21	Jun-21	9568.76	Oct-19
			Feb-14	U-2	660	Aug-18	Nov-21	Dec-21		
			Feb-14	U-3	660	Feb-19	May-22	Jun-22		
7.	MP	Gadarwara STPP / NTPC / BTG-BHEL	Mar-13	U-2	800	Sep-17	Aug-20	Sep-20	12292.03	Oct-19
8.	Odisha	Darlipalli STPP / NTPC / SG- BHEL TG-JSW & Toshiba	Feb-14	U-2	800	Jun-18	Oct-20	Nov-20	9869.68	Oct-19
9.	Rajasthan	Barsingar TPP ext/NLC/Reliance Infra	Nov-16	U-1	250	May-20	Hold	Hold	159.0581	Mar-20
10.	Rajasthan	Bithnok TPP / NLC / Reliance Infra	Nov-16	U-1	250	May-20	Hold	Hold	174.6634	Mar-20
11.	Telangana	Telangana STPP St- I / NTPC / SG- BHEL TG- Alstom & Bharatforge	Feb-16	U-1	800	Jan-20	Apr-21	May-21	5647.81	Oct-19
			Feb-16	U-2	800	Jul-20	Oct-21	Nov-21		
12.	TN	Neyveli New TPP / NLC / BHEL	Dec-13	U-2	500	Mar-18	Sep-20	Oct-20	6265.1603	Feb-20
13.	UP	Meja STPP / JV of NTPC & UPRVUNL / SG-BGR TG-Toshiba	Apr-12	U-2	660	Dec-16	Sep-20	Oct-20	9980	Oct-19
14.	UP	Ghatampur TPP / JV of NLC & UPRVUNL / MHPS Boiler Pvt. Ltd.	Aug-16	U-1	660	Apr-20	Feb-21	Apr-21	8844.35	Feb-20
			Aug-16	U-2	660	Oct-20	Aug-21	Oct-21		
			Aug-16	U-3	660	Oct-20	Jan-22	Mar-22		
15.	UP	Tanda TPP St II / NTPC / SG: L&T / TG: Alstom	Sep-14	U-6	660	Feb-20	Nov-20	Dec-20	6571.40	Oct-19
16.	UP	Khurja SCTPP	Mar-19	U-1	660	Mar-23	Apr-23	Apr-23	521.82	Sep-19
			Mar-19	U-2	660	Sep-23	Sep-23	Sep-23		
17.	Jharkand	Patratu STPP / JV of NTPC & Jharkhand Bidyut Vitran Nigam Ltd.	Mar-18	U-1	800	Mar-22	Mar-22	Mar-22	2078.5	Oct-19
			Mar-18	U-2	800	Sep-22	Sep-22	Sep-22		
			Mar-18	U-3	800	Mar-23	Mar-23	Mar-23		
18.	Odisha	Rourkela PP-II Expansion / NTPC-Sail Power Co Ltd (NSPCL) (JV of NTPC & SAIL) / BHEL	May-16	U-1	250	Dec-18	Feb-21	Apr-21	1414	Sept-19
TOTAL CENTRAL SECTOR					19120					
STATE SECTOR										

S. No.	State	Project Name / Impl. Agency/ EPC or BTG	LOA Date/	Unit No	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Ant. Trial Run / COD	Exp. In crores.	Till Date
1.	A.P	Dr.Narla Tata Rao TPS St-V / APGENCO / BTG- BHEL	Oct-15	U-1	800	Jun-19	Oct-20	Nov-20	4639.42	Sept-19
2.	A.P	Sri Damodaran Sanjeevaiah TPP St-II / APGENCO / BTG- BHEL	Nov-15	U-1	800	Mar-19	Nov-20	Dec-20	5928	Feb-20
3.	Assam	Namrup CCGT / APGCL / BHEL	Feb-09	ST	36.15	Jan-12	06.03.2020	Jun-20	581.48	Jun-19
4.	Karnataka	Yelahanka CCPP BY KPCL / BHEL	Nov-15	GT+ST	370	Mar-18	Oct-20	Nov-20	1578.8517	Feb-20
5.	Maharashtra	Bhusawal TPS / MAHAGENCO	Jan-18	U-6	660	Mar-22	Apr-22	Jun-22		
6.	Rajasthan	Suratgarh SCTPP / RRVUNL / BHEL	May-13	U-8	660	Dec-16	Jun-20	Dec-20	9303.23	Feb-20
7.	Telangana	Bhadradri TPP / TSGENCO / BHEL	Mar-15	U-1	270	Mar-17	20.03.2020	Jun-20	6325.52	13.03.2020
			Mar-15	U-2	270	May-17	Jul-20	Aug-20		
			Mar-15	U-3	270	Jul-17	Dec-20	Jan-21		
			Mar-15	U-4	270	Sep-17	May-21	Jun-21		
8.	TN	Ennore exp. SCTPP (Lanco) / TANGEDCO / BTG-BGR	May-14	U-1	660	Jan-18	Nov-23	Dec-23	791.4	Dec-17
9.	TN	Ennore SCTPP / TANGEDCO / BHEL	Sep-14	U-1	660	Jan-18	Jul-21	Aug-21	3555.68	May-19
			Sep-14	U-2	660	Mar-18	Oct-21	Nov-21		
10.	TN	North Chennai TPP St-III / TANGEDCO / BHEL	Jan-16	U-1	800	Mar-19	Nov-20	Jan-21	5304.14	Feb-20
11.	TN	Udangudi STPP Stage I / TANGEDCO / EPC-BHEL	Dec-17	U-1	660	Feb-21	Jan-23	Mar-23	979.1192	Feb-20
				U-2	660	Feb-21	Jul-23	Sep-23		
12.	TN	Uppur Super Critical TPP TANGEDCO / BHEL	Feb-16	U-1	800	Mar-19	Jan-23	Mar-23	2665.45	Feb-20
			Feb-16	U-2	800	Oct-19	Jul-23	Sep-23		
13.	UP	Harduaganj TPS Exp-II / UPRVUNL / Toshiba JSW	Sep-15	U-1	660	Jun-19	Jun-20	Sept-20	2855.27	Sept-19
14.	Telangana	Yadadri TPS / TSGENCO / BHEL	Oct-17	U-1	800	Oct-20	Sep-22	Oct-22	5861.88	Nov-19
				U-2	800	Oct-20	Sep-22	Oct-22		
				U-3	800	Oct-21	May-23	Jun-23		
				U-4	800	Oct-21	May-23	Jun-23		
				U-5	800	Oct-21	Sep-23	Oct-23		
15.	UP	Jawaharpur STPP / UPRVUNL / Doosan	Dec-16	U-1	660	Sep-20	Sept-21	Dec-21	3968.2	Feb-20
			Dec-16	U-2	660	Jan-21	Feb-22	Jun-22		
16.	UP	Panki TPS Extn. / URVUNL	Mar-18	U-1	660	Dec-21	Dec-21	Jan-22	16	Apr-18
17.	UP	Obra-C STPP / UPRVUNL / Doosan	Dec-16	U-1	660	Sep-20	Apr-21	Jun-21	2782.48	Nov-19
			Dec-16	U-2	660	Dec-20	Jul-21	Nov-21		
TOTAL STATE SECTOR					18066.15					
PRIVATE SECTOR										

S. No.	State	Project Name / Impl. Agency/ EPC or BTG	LOA Date/	Unit No	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Ant. Trial Run / COD	Exp. In crores.	Till Date
1.	AP	Bhavanapadu TPP Ph-I / East Coast Energy Ltd. BTG-Chinese	Sep-09	U-1	660	Oct-13	Uncertain*	Uncertain*	3785.6	Jan-16
			Sep-09	U-2	660	Mar-14	Uncertain*	Uncertain*		
2.	AP	Thamminapatnam TPP stage -II / Meenakshi Energy Pvt. Ltd. / SG-Cether vessels TG-Chinese	Dec-09	U-3	350	May-12	Stressed	Stressed	5414.4	Feb-19
			Dec-09	U-4	350	Aug-12	Stressed	Stressed		
3.	Bihar	Siriya TPP (Jas Infra. TPP) / JICPL / BTG-Chinese	Mar-11	U-1	660	Aug-14	Uncertain*	Uncertain*	NA	
			Mar-11	U-2	660	Dec-14	Uncertain*	Uncertain*		
			Mar-11	U-3	660	Apr-15	Uncertain*	Uncertain*		
			Mar-11	U-4	660	Aug-15	Uncertain*	Uncertain*		
4.	Chhattisgarh	Akaltara TPP (Naiyara) / KSK Mahandi Power Company Ltd./ Chinese	Apr-09	U-4	600	Apr-13	Stressed	Stressed	18730.00	Dec-16
			Apr-09	U-5	600	Aug-13	Uncertain	Uncertain		
			Apr-09	U-6	600	Dec-13	Uncertain	Uncertain		
5	Chhattisgarh	Binjkote TPP / SKS Power Generation (Chhattisgarh) Ltd. SG-Cethar Vessels TG-Harbin China	Mar-11	U-3	300	Mar-14	Uncertain	Uncertain	3828	Jun-15
			Mar-11	U-4	300	Jun-14	Uncertain	Uncertain		
5.	Chhattisgarh	Lanco Amarkantak TPP-II / LAP Pvt. Ltd. BTG-DEC	Nov-09	U-3	660	Jan-12	Uncertain	Uncertain	9537.79	Dec-16
			Nov-09	U-4	660	Mar-12	Uncertain	Uncertain		
6.	Chhattisgarh	Singhitarai TPP / Athena Chhattisgarh Power Ltd. BTG –DECL	Dec-09	U-1	600	Nov-14	Uncertain	Uncertain	6408.47	May-17
			Dec-09	U-2	600	Feb-15	Uncertain	Uncertain		
7.	Chhattisgarh	Salora TPP / Vandana Vidyut / BTG-Cether Vessles	Sep-09	U-2	135	Sep-11	Uncertain*	Uncertain*	2386.89	Mar-15
8.	Chhattisgarh	Deveri (Visa) TPP / Visa Power Ltd. BTG-BHEL	Jun-10	U-1	600	Aug-13	Uncertain*	Uncertain*	2077.23	Nov-15
9.	Jharkhand	Matrishri Usha TPP Ph-I / Corporate Power Ltd. EPC-BHEL	Dec-09	U-1	270	Apr-12	Uncertain*	Uncertain*	3120	Nov-12
			Dec-09	U-2	270	May-12	Uncertain*	Uncertain*		
10.	Jharkhand	Matrishri Usha TPP Ph-II / Corporate Power Ltd. EPC-BHEL	Mar-11	U-3	270	Oct-12	Uncertain*	Uncertain*	2207	Sep-12
			Mar-11	U-4	270	Jan-13	Uncertain*	Uncertain*		
11.	Jharkhand	Tori TPP Ph-I / Essar Power Ltd. / BTG-China	Aug-08	U-1	600	Jul-12	Uncertain*	Uncertain*	4757.92	Jun-17
			Aug-08	U-2	600	Sep-12	Uncertain*	Uncertain*		
12.	Jharkhand	Tori TPP Ph-II / Essar Power Ltd. /		U-3	600	Dec-15	Uncertain*	Uncertain*	246.65	Mar-15
13.	Maharashtra	Amravati TPP Ph-II / Ratan India Power Pvt. Ltd. / BTG-BHEL	Oct-10	U-1	270	Jul-14	Uncertain*	Uncertain*	763.8	Mar-15
			Oct-10	U-2	270	Sep-14	Uncertain*	Uncertain*		
			Oct-10	U-3	270	Nov-14	Uncertain*	Uncertain*		
			Oct-10	U-4	270	Jan-15	Uncertain*	Uncertain*		
			Oct-10	U-5	270	Mar-15	Uncertain*	Uncertain*		
14.	Maharashtra	Lanco Vidarbha TPP / LVP Pvt. Ltd. / EPC-LANCO	Nov-09	U-1	660	Jul-14	Uncertain*	Uncertain*	5338	Apr-17

S. No.	State	Project Name / Impl. Agency/ EPC or BTG	LOA Date/	Unit No	Cap. (MW)	Org. Comm. Sched.	Ant. Comm. Sched.	Ant. Trial Run / COD	Exp. In crores.	Till Date
	<i>a</i>		Nov-09	U-2	660	Nov-14	Uncertain*	Uncertain*		
15.	<i>Maharashtra</i>	Nasik TPP Ph-II / Ratan India Nasik Power Pvt. Ltd. / BTG-BHEL	Nov-09	U-1	270	Apr-13	Uncertain	Uncertain	711.81	Mar-15
			Nov-09	U-2	270	Jun-13	Uncertain	Uncertain		
			Nov-09	U-3	270	Aug-13	Uncertain	Uncertain		
			Nov-09	U-4	270	Oct-13	Uncertain	Uncertain		
			Nov-09	U-5	270	Dec-13	Uncertain	Uncertain		
16.	<i>Maharashtra</i>	Bijora Ghanmukh TPP / Jinbhuvish Power Generation Pvt. Ltd. / BTG-Chinese	Sep-11	U-1	300	Dec-16	Uncertain	Uncertain	422.27	Mar-15
			Sep-11	U-2	300	Mar-17	Uncertain	Uncertain		
17.	<i>Maharashtra</i>	Shirpur TPP, Shirpur Power Pvt. Ltd. / BHEL	Nov-11	U-2	150	Apr-15	Uncertain	Uncertain	2277.94	Apr-17
18.	<i>MP</i>	Gorgi TPP / D.B. Power (MP) Ltd. / BTG-BHEL	Mar-11	U-1	660	Jun-13	Uncertain	Uncertain	475.79	Sep-15
19.	<i>Odisha</i>	Ind Barath TPP (Odisha) / Ind Barath / BTG-Cethar Vessels	May-09	U-2	350	Dec-11	Uncertain	Uncertain	4254	Apr-17
20.	<i>Odisha</i>	KVK Nilanchal TPP/ KVK Nilanchal / BTG-Harbin China	Nov-09	U-1	350	Dec-11	Uncertain*	Uncertain*	1708.36	Mar-15
			Nov-09	U-2	350	Feb-12	Uncertain*	Uncertain*		
			Nov-09	U-3	350	Feb-12	Uncertain*	Uncertain*		
21.	<i>Odisha</i>	Lanco Babandh TPP / LBP Ltd. / BTG-Chinese	Nov-09	U-1	660	Apr-13	Uncertain*	Uncertain*	7615	Mar-17
			Nov-09	U-2	660	Aug-13	Uncertain*	Uncertain*		
22.	<i>Odisha</i>	Malibrahmani TPP / MPCL / BTG-BHEL	Jun-10	U-1	525	Dec-12	Uncertain*	Uncertain*	5329.75	Dec-14
			Jun-10	U-2	525	Feb-13	Uncertain*	Uncertain*		
23.	<i>TN</i>	Tuticorin TPP (Ind- Barath) / IBPIL / BTG-Chinese	May-10	U-1	660	May-12	Uncertain*	Uncertain*	2000	May-15
24.	<i>TN</i>	Tuticorin TPP St-IV / SEPC / EPC-MEIL (BTG-BHEL)	Jan-14	U-1	525	Sep-18	Apr-20	Apr-20	2436.53	Nov-19
25.	<i>WB</i>	Hiranmaye Energy Ltd (India Power corporation (Haldia) TPP / BTG-BHEL.	Sep-10	U-3	150	May-16	Uncertain*	Uncertain*	3263.05	Oct-17
Total Private Sector					23730					
GRAND TOTAL					60916.15					

* Presently work at site is on hold.

7. Thermal Power Projects visited during Fourth Quarter (January – March) of 2019-20

Following under construction thermal power projects in country were visited by officers of TPM Division to review the status of progress of ongoing construction activities at project sites:

Sl. No.	Name of Project with capacity	State
01.	Telangana STPP Stage-I (2 x 800 MW)	Andhra Pradesh
02.	Ghatampur STPP (3 x 660 MW)	Uttar Pradesh
03.	Tuticorin Stage IV (525 MW)	Tamil Nadu
04.	Yelahanka CCPP (370 MW)	Karnataka

8. Details of Super Critical Units Commissioned in the country as on 31st March 2020

State	Project Name	Impl Agency/ Make	Unit No	Cap. MW	Actual Comm. Date	BHEL	L&T	Chinese	Russia	Others	Doosan Power System India.
Commissioned during 11th Plan											
CENTRAL SECTOR											
Chhattisgarh	Sipat-I	NTPC	U-1	660	28.06.11	-	-	-	660	-	-
Chhattisgarh	Sipat-I	TG-Power M/C, Russia. SG-Dussan,Korea	U-2	660	24.12.11	-	-	-	660	-	-
Total Central Sector				1320		0	0	0	1320	0	0
PRIVATE SECTOR											
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-1	660	26.12.10	-	-	660	-	-	-
Gujarat	Mundra TPP Ph-II	Boiler : Harbin, China & TG:M/s DEC, China	U-2	660	20.07.11	-	-	660	-	-	-
Gujarat	Mundra TPP Ph-III	Adani Power Ltd	U-1	660	07.11.11	-	-	660	-	-	-
Gujarat	Mundra TPP Ph-III	Boiler : Harbin, China & TG:M/s DEC, China	U-2	660	03.03.12	-	-	660	-	-	-
Gujarat	Mundra TPP Ph-III	Boiler : Harbin, China & TG:M/s DEC, China	U-3	660	09.03.12	-	-	660	-	-	-
Gujarat	Mundra UMTTP	Tata Power Co. Boiler: DOOSAN, KOREA TG: TOSHIBA, JAPAN	U-1	800	25.02.12	-	-	-	-	800	-
Haryana	Jajjar TPP (Mahatama Gandhi TPP)	CLP Power India Pvt. Ltd Boiler: Harbin, China & TG:M/s DEC, China	U-1	660	12.01.12	-	-	660	-	-	-
Total Private Sector				4760		0	0	3960	0	800	0
Grand Total in 11th Plan Commissioned				6080		0	0	3960	1320	800	0
Commissioned during 12th Plan (Targeted)											
CENTRAL SECTOR											
Chhattisgarh	Sipat-I		U-3	660	02.06.12	-	-	-	660	-	-
Bihar	Barh -II	NTPC	U-4	660	30.11.13	660	-	-	-	-	-
Bihar	Barh -II	NTPC	U-5	660	04.03.15	660	-	-	-	-	-
Total Central Sector				1980		1320	0	0	660	0	0
STATE SECTOR											
AP	Damodaram Sanjeevaiah TPS	APPDL	U-1	800	28.08.14	-	800	-	-	-	-
AP	Damodaram Sanjeevaiah TPS	Boiler-BHEL, TG- L&T	-	-	-	-	-	-	-	-	-
AP	Damodaram Sanjeevaiah TPS	Boiler-BHEL, TG- L&T	U-2	800	17.03.15	-	800	-	-	-	-
Maharashtra	Koradi TPS Expn.	MSPGCL	U-8	660	30.03.15	-	660	-	-	-	-
Total Statal Sector				2260		0	2260	0	0	0	0
PRIVATE SECTOR											
AP	Painampuram TPP	Thermal Power Tech Corp. Ltd	U-1	660	07.02.15	-	-	660	-	-	-

State	Project Name	Impl Agency/ Make	Unit No	Cap. MW	Actual Comm. Date	BHEL	L&T	Chinese	Russia	Others	Doosan Power System India.
AP	Painampuram TPP	Thermal Power Tech Corp. Ltd	U-2	660	05.09.15	-	-	660	-	-	-
AP	NCC TPP	NCC Power Projects Ltd	U-1	660	12.11.16	-	-	660	-	-	-
AP	NCC TPP	NCC Power Projects Ltd	U-2	660	15.02.17	-	-	660	-	-	-
Gujarat	Mundra UMTPP	Tata Power Co.	U-2	800	25.07.12	-	-		-	800	-
Haryana	Jajjar TPP (Mahatama Gandhi TPP)	CLP Power India Pvt. Ltd	U-2	660	11.04.12	-	-	660	-	-	-
Maharashtra	Tirora TPP Ph-I	Adani Power Ltd	U-1	660	11.09.12	-	-	660	-	-	-
Maharashtra	Tirora TPP Ph-I	Boiler : BABCOCK, China & TG: BSTG China	U-2	660	25.03.13	-	-	660	-	-	-
Maharashtra	Tirora TPP Ph-II	Adani Power Ltd	U-1	660	10.06.13	-	-	660	-	-	-
MP	Sasan UMPP	Reliance Power Ltd.	U-3	660	30.05.13	-	-	660	-	-	-
MP	Sasan UMPP	BTG: M/s Shanghai Elec Corp., China	U-2	660	18.12.13	-	-	660	-	-	-
Punjab	Rajpura TPP (Nabha)	Nabha Power Ltd	U-1	700	24.01.14	-	700	-	-	-	-
Punjab	Rajpura TPP (Nabha)	BTG:L&T	U-2	700	06.07.14	-	700	-	-	-	-
Punjab	Talwandi Sabo TPP	M/s Sterlite	U-1	660	17.06.14	-	-	660	-	-	-
Punjab	Talwandi Sabo TPP	M/s Sterlite	U-2	660	30.10.15	-	-	660	-	-	-
Punjab	Talwandi Sabo TPP	M/s Sterlite	U-3	660	29.03.16	-	-	660	-	-	-
U.P	Prayagraj (Bara) TPP	Prayagraj power Gen. Co.Ltd (J.P.Power Ventures)	U-1	660	25.12.15	660	-	-	-	-	-
			U-2	660	06.09.16	660	-	-	-	-	-
Total Private Sector				12100		1320	1400	8580	0	800	0
Total 12th Plan Target Commissioned				16340		2640	3660	8580	660	800	0

Additional Units Commissioned , Not in the 12th Plan Target											
Central Sector											
Karnataka	Kudgi STPP Ph-I	NTPC	U-1	800	25.12.2016	-	-	-	-	-	800
Karnataka	Kudgi STPP Ph-I	NTPC	U-2	800	23.03.2017	-	-	-	-	-	800
Maharashtra	Mouda STPP -II	NTPC	U-3	660	28.03.16	660	-	-	-	-	-
Maharashtra	Mouda STPP-II	NTPC	U-2	660	18.03.2017	660	-	-	-	-	-
Sub-Total				2920		1320	0	0	0	0	1600
State Sector											
Karnataka	Bellary TPS- St-III	KPCL	U-3	700	01.03.16	700	-	-	-	-	-
Karnataka	Yermaus TPP	KPCL	U-1	800	29.03.16	800	-	-	-	-	-
Karnataka	Yermaus TPP	KPCL	U-2	800	29.03.17	800	-	-	-	-	-
Maharashtra	Koradi TPS Expn.	MSPGCL	U-9	660	28.03.16	-	660	-	-	-	-
Maharashtra	Koradi TPS Expn.	MSPGCL	U-10	660	28.12.16	-	660	-	-	-	-
Sub-Total				3620		2300	1320	0	0	0	0
Private Sector											
Chhattisgarh	Raikheda TPP	GMR Chhattisgarh Energy Ltd.	U-1	685	27.02.15	-	-	-	-	-	685
		BTG: Doosan Power System India.	U-2	685	28.03.16	-	-	-	-	-	685
Gujarat	Mundra UMTTP	Tata Power Co.	U-3	800	16.10.12	-	-	-	-	800	-
Gujarat	Mundra UMTTP	Tata Power Co.	U-4	800	16.01.13	-	-	-	-	800	-
Gujarat	Mundra UMTTP	Tata Power Co.	U-5	800	18.03.13	-	-	-	-	800	-
Maharashtra	Tirora TPP Ph-II	Adani Power Ltd	U-2	660	23.03.14	-	-	660	-	-	-
		Boiler : BABCOCK, China & TG: BSTG, China	-	-	-	-	-	-	-	-	-
Maharashtra	Tirora TPP Ph-II	Adani Power Ltd	U-3	660	25.09.14	-	-	660	-	-	-
Rajasthan	Kawai TPP	Adani Power Ltd.	U-1	660	28.05.13	-	-	660	-	-	-
		BTG: M/s Shanghai Elec Corp., China	U-2	660	24.12.13	-	-	660	-	-	-
MP	Sasan UMPP	Reliance Power Ltd.	U-4	660	25.03.14	-	-	660	-	-	-
MP	Sasan UMPP	BTG: M/s Shanghai Elec Corp., China	U-1	660	21.05.14	-	-	660	-	-	-
MP	Sasan UMPP		U-5	660	24.08.14	-	-	660	-	-	-
MP	Sasan UMPP		U-6	660	19.03.15	-	-	660	-	-	-
	Nigri TPP	Jaiprakash Power ventures Ltd	U-1	660	29.08.14	-	660	-	-	-	-
		BTG:L&T	U-2	660	17.02.15	-	660	-	-	-	-
UP	Lalitpur TPP	Lalitpur power Generation Co. Ltd	U-2	660	08.01.16	660	-	-	-	-	-
UP	Lalitpur TPP	Lalitpur power Generation Co. Ltd	U-1	660	26.03.16	660	-	-	-	-	-
UP	Lalitpur TPP	Lalitpur power Generation Co. Ltd	U-3	660	01.04.16	660	-	-	-	-	-
Total Private Sector				12350		1980	1320	5280	0	2400	1370
Total Additional				18890		5600	2640	5280	0	2400	2970

Super critical Units Commissioned during the year 2017-18											
State	Project Name	Impl Agency/ Make	Unit No	Cap. MW	Actual Comm. Date	BHEL	L&T	Chinese	Russia	Others	Doosan Power System India.
Central Sector											
Maharashtra	Solapur STPP	NTPC	U-1	660	07.04.2017	-	-	-	-	660	-
Karnataka	Kudgi STPP Ph-I	NTPC	U-3	800	12.03.2018	0	0	0	0	800	0
Uttar Pradesh	Meja STPP	JV of NTPC & UPRVUNL	U-1	660	31.03.2018	0	0	0	0	660	0
Chhattisgarh	Lara TPP	NTPC	U-1	800	23.03.2018	0	0	0	0	800	0
Total Central Sector				2920		0	0	0	0	2920	0
State Sector											
Rajasthan	Chhabra SCTPP	RRVUNL	U-5	660	04.04.2017	0	660	0	0	0	0
Total State Sector				660		0	660	0	0	0	0
Private Sector											
UP	Paryagraj(Bara) TPP	Prayagraj Power Gen Co. Ltd	U-3	660	22.05.2017	660	0	0	0	0	0
Total Private Sector				660		660	0	0	0	0	0
Total Commissioned in 2017-18				4240		660	660	0	0	2920	0

Super Critical Units Commissioned during the year 2018-19											
State	Project Name	Impl Agency/ Make	Unit No	Cap. MW	Actual Date of Cap. Add.	BHEL	L&T	Chinese	Russia	Others	Doosan Power System India.
Central Sector											
MP	Gadarwara TPP	NTPC	U-1	800	29.03.2019	800	0	0	0	-	0
Maharashtra	Solapur STPP	NTPC	U-2	660	29.03.2019	0	0	0	0	660	0
Total Central Sector				1460		0	0	0	0	1460	0
State Sector											
MP	Shri Singhaji TPP St-II	MPPGCL	U-3	660	18.11.2018	0	660	0	0	-	0
MP	Shri Singhaji TPP St-II	MPPGCL	U-4	660	27.03.2019	0	660	0	0	-	0
Rajasthan	Chhabra TPP Extn	RRVUNL	U-6	660	29.03.2019	0	660	0	0	-	0
Telangana	Kothagudem TPS St-VII	TSGENCO	U-1	800	26.12.2018	800	-	-	-	-	-
Total State Sector				2780		800	0	0	0	1980	0
Private Sector											
Total Private Sector				0		0	0	0	0	0	0
Total Commissioned in 2018-19				4240		2400	1980	0	0	4100	0

Super critical Units Commissioned during the year 2019-20 up to 31st March, 2020											
State	Project Name	Impl Agency/ Make	Unit No	Cap. MW	Actual Date of Cap. Add.	BHEL	L&T	Chinese	Russia	Others	Doosan Power System India.
Central Sector											
Bihar	Nabi Nagar STPP	NTPC	1	660	12.07.2019	660	0	0	0	0	0
M.P.	Khargone STPP St-I	NTPC	1	660	29.09.2019	0	660	0	0	0	0
U.P.	Tanda TPP St-II	NTPC	5	660	28.09.2019	0	660	0	0	0	0
Odisha	Darlipali STPP	NTPC	1	800	30.12.2019	0	0	0	0	800	0
M.P.	Khargone STPP St-I	NTPC	2	660	24.03.2020	0	660	0	0	0	0
Total Central Sector				3440		660	1320	0	0	800	0
State Sector											
Odisha	Ib Valley TPP	OPGC	3	660	01.07.2019	660	0	0	0	0	0
Odisha	Ib Valley TPP	OPGC	4	660	17.08.2019	660	0	0	0	0	0
Gujarat	Wanakbori TPP Ext.	GSECL	8	800	12.10.2019	800	0	0	0	0	0
Rajasthan	Suratgarh SCTPP	RRVUNL	7	660	15.03.2020	660	0	0	0	0	0
Total State Sector				2780		2780	0	0	0	0	0
Private Sector											
Total Private Sector				0							
GRANT TOTAL IN 2019-20				6220							

9. Year/Plan wise Thermal Capacity Addition in the Country

Sl. No.	Year	Capacity Addition (MW)	Target (MW)	% Achievement
1st Five Year Plan (1.1.51 to 31.12.55)				
1	1951	107.02	-	-
2	1952	86.33	-	-
3	1953	227.43	-	-
4	1954	126.64	-	-
5	1955	54.69	-	-
	Total :	<u>602.11</u>	-	-
2nd Five Year Plan (1.1.56 to 31.03.61)				
6	1956-57	69.36	-	-
7	1957-58	184.49	-	-
8	1958-59	140.65	-	-
9	1959-60	193.18	-	-
10	1960-61	<u>393.37</u>	-	-
	Total :	<u>981.05</u>	-	-
3rd Five Year Plan (1.4.61 to 31.03.66)				
11	1961-62	63.33	-	-
12	1962-63	65.12	-	-
13	1963-64	544.08	-	-
14	1964-65	599.02	-	-
15	1965-66	<u>895.34</u>	-	-
	Total :	<u>2166.89</u>	-	-
Annual Plans (1966-67, 67-68, 68-69)				
16	1966-67	431.67	-	-
17	1967-68	1061.29	-	-
18	1968-69	654.12	-	-
	Total :	<u>2147.08</u>	-	-

Sl. No.	Year	Capacity Addition (MW)	Target (MW)	% Achievement
4th Five Year Plan (1.4.69 to 31.03.74)				
19	1969-70	497.32	-	-
20	1970-71	358.04	-	-
21	1971-72	317.04	-	-
22	1972-73	653.54	-	-
23	1973-74	181.96	-	-
	Total :	<u>2007.9</u>	5746	34.94
5th Five Year Plan (1.4.74 to 31.03.79)				
24	1974-75	1089.18	-	-
25	1975-76	866.02	-	-
26	1976-77	790.23	-	-
27	1977-78	1204.8	-	-
28	1978-79	<u>2198.5</u>	-	-
	Total :	<u>6148.73</u>	7845	78.38
29	1979-80	1216.87	2265	53.72
6th Five Year Plan (1.4.80 to 31.03.85)				
30	1980-81	1138.6	-	-
31	1981-82	1749.82	-	-
32	1982-83	2135.13	-	-
33	1983-84	2940.89	-	-
34	1984-85	2641.4	-	-
	Total :	<u>10605.84</u>	14898	71.19
7th Five Year Plan (1.4.85 to 31.03.90)				
35	1985-86	2977	-	-
36	1986-87	1920	-	-
37	1987-88	3912	-	-
38	1988-89	4117.3	-	-
39	1989-90	4167	-	-
	Total :	<u>17093.3</u>	15999	106.84

Sl. No.	Year	Capacity Addition (MW)	Target (MW)	% Achievement
Annual Plans (1990-91, 91-92)				
40	1990-91	2364	3962	59.67
41	1991-92	2370.5	4512	52.54
8th Five Year Plan (1.4.92 to 31.03.97)				
42	1992-93	2944.32	-	-
43	1993-94	3741.6	-	-
44	1994-95	3928.5	-	-
45	1995-96	1976.5	-	-
46	1996-97	963	-	-
	Total :	<u>13553.92</u>	20156	67.25
9th Five Year Plan (1.4.97 to 31.03.2002)				
47	1997-98	2993.5	-	-
48	1998-99	3724.5	-	-
49	1999-2000	2696	-	-
50	2000-01	2277.9	-	-
51	2001-02	2009	-	-
	Total :	<u>13700.9</u>	29550.7	46.36
10th Five Year Plan (1.4.02 to 31.03.07)				
52	2002-03	2223.1	-	-
53	2003-04	1361.6	-	-
54	2004-05	2933.92	-	-
55	2005-06	1588.8	-	-
56	2006-07	4006.8	-	-
	Total :	<u>12114.22</u>	25416.2	47.66


Sl. No.	Year	Capacity Addition (MW)	Target (MW)	% Achievement
11th Five Year Plan (1.4.07 to 31.03.12)				
57	2007-08	6620	-	-
58	2008-09	2484.7	-	-
59	2009-10	9106	-	-
60	2010-11	11250.5	-	-
61	2011-12	19078.7	-	-
	Total	<u>48539.9</u>	59693	81.32
12th Five Year Plan (01.04.12 to 31.03.17)				
62	2012-13	20121.8	15154.3	132.78
63	2013-14	16767	15234.3	110.06
64	2014-15	20830.3	14988.3	138.98
65	2015-16	22460.6	17346.1	129.49
65	2016-17	11550.75	13440.5	85.94
	Total	<u>91730.45</u>	76163.5	120.44
Annual Plan (2017-18)				
66	2017-18	<u>8710</u>	11366.15	76.63
Annual Plan (2018-19)				
67	2018-19	<u>5781.76</u>	7266.15	79.57
Annual Plan (2019-20)				
68	2019-20	<u>6765</u>	10296.15	65.7

10. Thermal Generating Capacity in the Country since inception of 1st Five Year Plan

Plan/ Duration	Capacity Addition (MW)	Cumulative (MW)
1st Plan (1.1.51 to 31.3.56)	602.11	1755
2nd Plan (1956-61)	981.05	2736
3rd Plan (1961-66)	2166.89	4903
Annual Plan (1966-67)	431.67	5335
Annual Plan (1967-68)	1061.29	6396
Annual Plan (1968-69)	654.12	7050
4th Plan (1969-74)	2007.9	9058
5th Plan (1974-79)	6148.73	15207
Annual Plan (1979-80)	1216.87	16424
6th Plan (1980-85)	10606	27030
7th Plan (1985-90)	17093.3	44123
Annual Plan (1990-91)	2364	46487
Annual Plan (1991-92)	2370.5	48858
8th Plan (1992-97)	13554.82	62412
9th Plan (1997-2002)	13700.9	76113
10th Plan (2002-07)	12114.24	88228
11th Plan (2007-12)	48539.9	136768
12th Plan (2012-17)	91730.45	228498
Annual Plan (2017-18)	8710	237208
Annual Plan (2018-19)	5781.76	242990
Annual Plan (2019-20)	6765	249755

10.1

Bar Chart representing Plan-wise Growth of Thermal Capacity

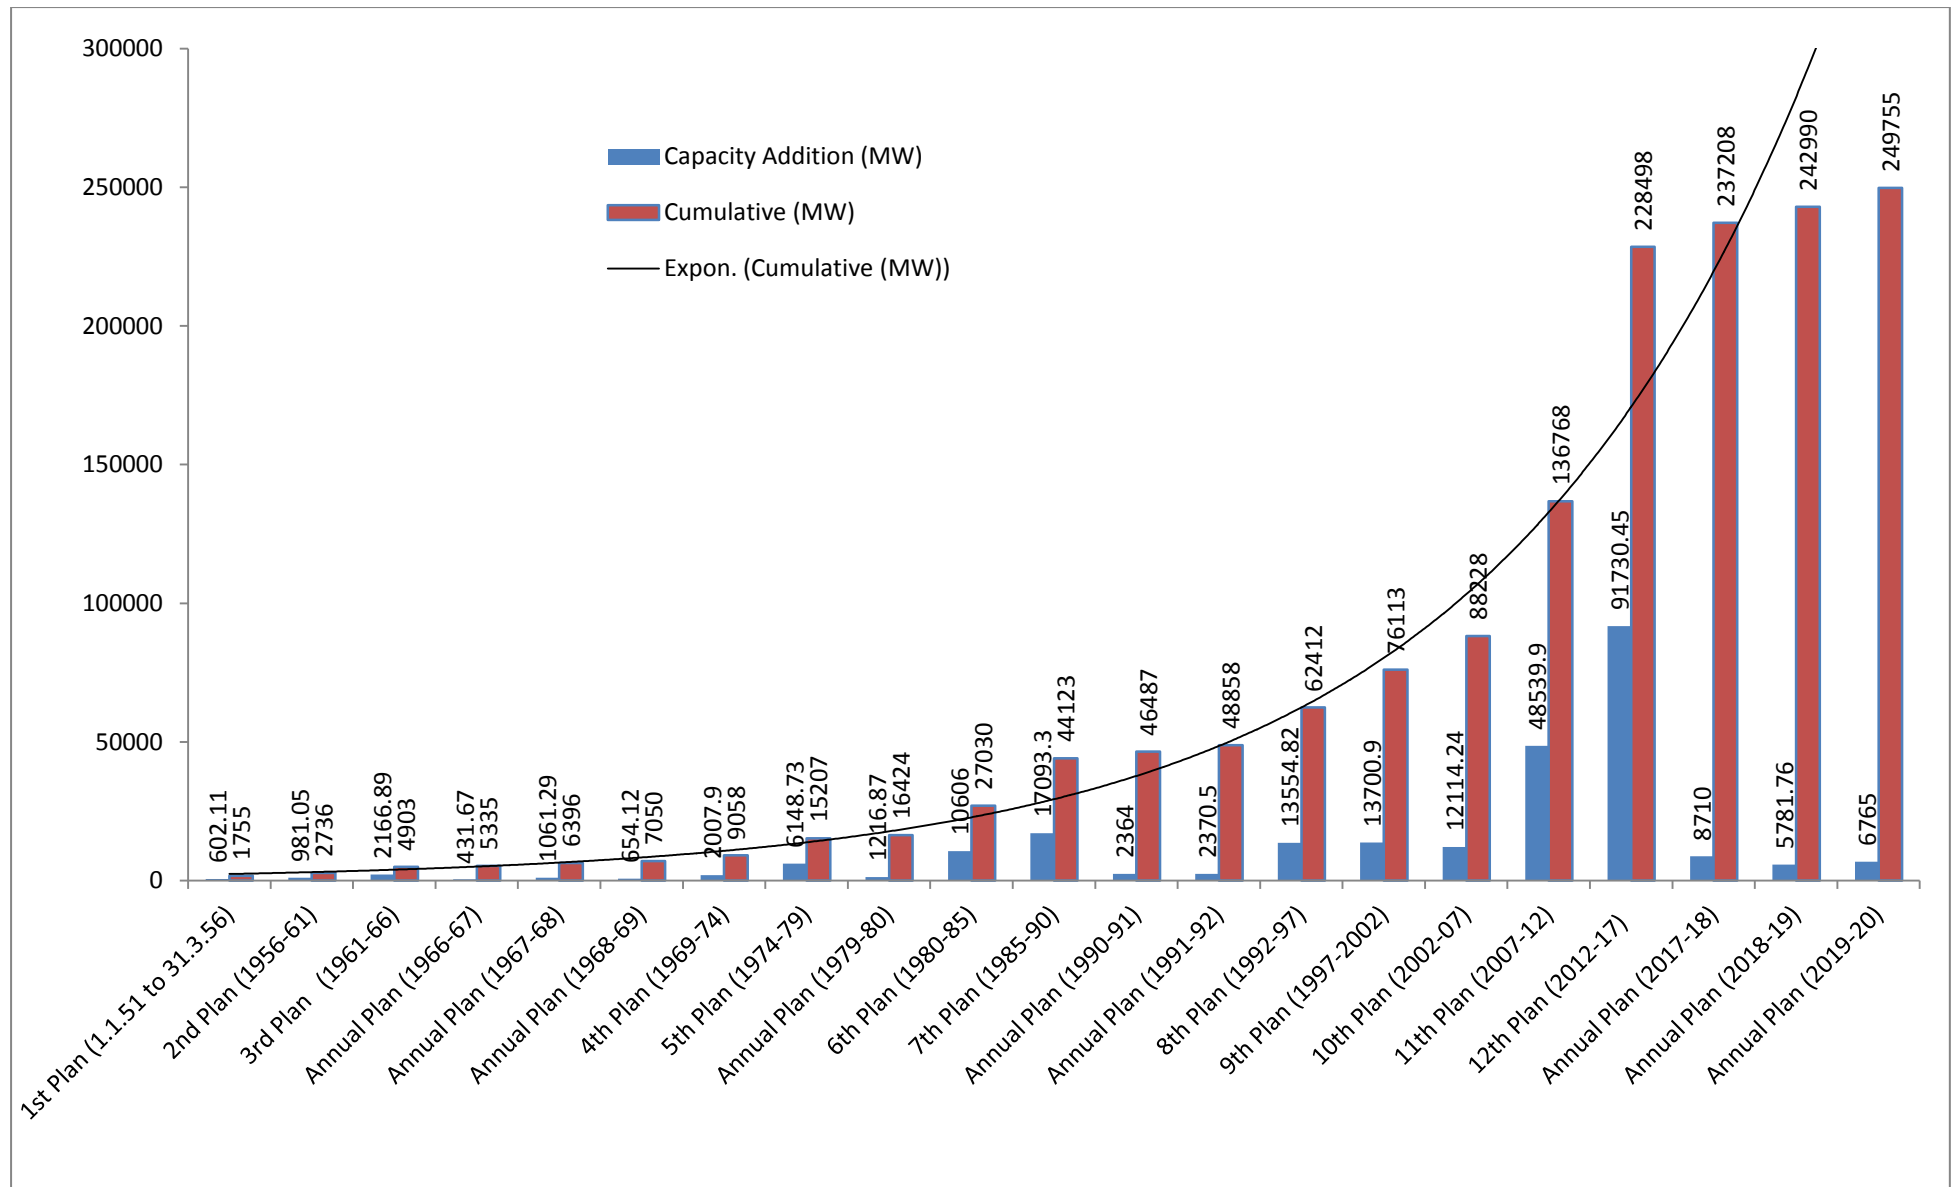

देश में कार्यान्वित तापीय विद्युत परियोजनाओं की प्रगति का पुनर्वालोचन

Review of Progress of Thermal Power Projects under execution in the Country

170 वाँ त्रैमासिक पुनर्वालोचन
(जनवरी-मार्च, 2020)

Quarterly Review

(January-March'2020)

Central Electricity Authority

Ministry of Power

Government of India

Thermal Project Monitoring Division

9th Floor(S), Sewa Bhawan, R.K. Puram,

New Delhi – 110 066

Phone: 011-26732996, 2610 5075 (Fax)

E mail: cea-tmd@nic.in
