



देश में कार्यान्वित ताप विद्युत परियोजनाओं
की प्रगति का पुनर्वलोकन



REVIEW OF PROGRESS OF THERMAL POWER PROJECTS
UNDER EXECUTION IN THE COUNTRY

139 वाँ त्रैमासिक पुनर्वलोकन
(अप्रैल-जून, 2012)

139th QUARTERLY REVIEW
(April to June, 2012)

केन्द्रीय विद्युत प्राधिकरण
विद्युत मंत्रालय
भारत सरकार
नई दिल्ली

CENTRAL ELECTRICITY AUTHORITY
MINISTRY OF POWER
GOVERNMENT OF INDIA
NEW DELHI

जुलाई - 2012

July, 2012

(विद्युत अधिनियम, 2003 की धारा 73 (एफ) के तहत के.वि.प्रा. के दायित्व की पूर्णता के लिये संकलित)

(In fulfillment of CEA's obligation under section 73(f) of Electricity Act, 2003)

FOREWORD

Central Electricity Authority (CEA) has been bringing out Quarterly Review of the progress of works on various sanctioned thermal power projects under implementation in the country. The present quarterly review, 139th in the series (for the period April, 2012 -June, 2012) gives the details of thermal power projects commissioned during 11th plan and 1st Qtr of the First year of 12th Plan in the country. This review provides information in respect of thermal power projects under construction for commissioning during 12th plan and beyond.

CEA has been rendering assistance to various stake holders in timely commissioning of the project and even in pre-ponement of the project commissioning. We would like to welcome you for sharing your experiences, high standards of achievements and the constraints in project implementation. We shall endeavour to resolve the issues to the benefit of the project and therefore, request you to feel free in reporting the same for initiating the suitable remedial measures.

The quarterly review has been brought out by CEA on the basis of data received from various project authorities, visits made by the CEA engineers to different power projects and discussions held with the executing agencies and suppliers of equipments from time to time. Project authorities are requested to intimate the latest status of their projects in case the status indicated in this review has changed in any manner so that the same could be incorporated in the subsequent issues.

We whole-heartedly welcome suggestions / feed back for further improvement in the quarterly review.

(Mam Chand)
Chief Engineer I/C (TPM)

Index

Sl.NO	CONTENTS	PAGE NO
1.0	Executive Summary	
1.2.1	11 th Plan Capacity Addition Target	
1.2.2	Sector-wise / Fuel-wise thermal capacity addition target during 11 th Plan	
1.2.3	Total thermal capacity commissioned during 11 th Plan	
1.3.1	12 th Plan Capacity Addition Target	
2	Plan wise Thermal Capacity Targets / Achievements	
2.1	Year/Plan wise Thermal Capacity Addition in the Country	
3.	Thermal Projects commissioned during the 1 st quarter (April – June) of the year 2012	
4.	Thermal Power Projects Commissioned during 11 th Plan	
5.	Thermal Power Projects slipped from 11 th Plan Original Target	
6.	Thermal Units slipped from 11 th Plan Mid Term Appraisal Target	
7	Thermal Power Projects which are under construction and likely to be commissioned during 12 th Plan and beyond - Make- BHEL/ Non-BHEL (Indian)/ Chinese/Others (Expt. Chinese)	
8.	Thermal Capacity Addition Target/Achievement for the Year 2012-13	
9.	Thermal Power Projects visited during the quarter (April – June, 2012)	
10.	Trend of Capacity addition as % of Total (Thermal, Hydro and Nuclear mix)	
11.	(a) Growth of Thermal Capacity in MW (b) Growth of Installed Capacity in MW	
12.	Supercritical Units commissioned during 11 th Plans	
13	Details of Expenditure of Thermal Power Projects under construction	

1. Executive Summary

1.1 Trend of Thermal Hydro, Renewable Energy Sources (RES) Mix as on 30.04.2012

Mode wise	As on 31.03.2012	Capacity Addition during Q1	As on 30.06.2012
Thermal	131353.18 MW	4965 MW	136318.18 MW
Hydro	38990.40 MW	301 MW	39291.40 MW
Nuclear	4780.00 MW	0	4780.00 MW
RES	24503.45 MW	0	24503.45 MW
Total	199627.03 MW	5266	204893.03 MW

1.2.1 TOTAL CAPACITY ADDITION (MW) PROGRAMME DURING 11TH PLAN (AS PER ORIGINAL TARGET) (MW)

Thermal	59693
Hydro	15627
Nuclear	3380
Total	78700

1.2.2 TOTAL CAPACITY ADDITION (MW) PROGRAMME DURING 11TH PLAN (AS PER MID TERM TARGET) (MW)

SECTOR	THERMAL		HYDRO		NUCLEAR		TOTAL	
	Target	Achieved	Target	Achieved	Target	Achieved	Target	Achieved
CENTRAL	14920.0	12790.0	2922	1550	3380	880	21222.0	15220.0
STATE	18501.4	14030.4	2854	2702	0	0	21355.4	16732.4
PRIVATE	17335.5	21719.5	2461	1292	0	0	19796.5	23011.5
TOTAL	50756.9	48539.9	8237	5544	3380	880	62373.9	54963.9

1.2.3 Total Capacity addition during 11th Plan

1.2.3a TOTAL CAPACITY COMMISSIONED DURING 2007-08 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	1990	1030	220	3240
STATE	3880	1393	-	5273
PRIVATE	750	-	-	750
TOTAL	6620	2423	220	9263

1.2.3b TOTAL CAPACITY COMMISSIONED DURING 2008-09 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	750	-	-	750
STATE	852.2	969	-	1821.2
PRIVATE	882.5	-	-	882.5
TOTAL	2484.7	969	-	3453.7

1.2.3c TOTAL CAPACITY COMMISSIONED DURING 2009-10 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	1740		440	2180
STATE	3079	39		3118
PRIVATE	4287	-	-	4287
TOTAL	9106	39	440	9585

1.2.3d TOTAL CAPACITY COMMISSIONED DURING 2010-11 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	3740.0	320	220	4280.0
STATE	2581.0	178		2759.0
PRIVATE	4929.5	192	-	5121.5
TOTAL	11250.5	690	220	12160.5

1.2.3e TOTAL CAPACITY COMMISSIONED DURING 2011-12 (MW)

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	4570.0	200	-	4770.0
STATE	3638.2	123	-	3761.2
PRIVATE	10870.5	1100	-	11970.5
TOTAL	19078.7	1423	-	20501.7

**1.3.1 TOTAL CAPACITY ADDITION (MW) PROGRAMME DURING 12TH PLAN
(As per working group) (MW)**

SECTOR	THERMAL	HYDRO	NUCLEAR	TOTAL
CENTRAL	11426	5632	2800	19858
STATE	12340	1456	00	13796
PRIVATE	40015	2116	00	42131
TOTAL	63781	9204	2800	75785

2. Plan wise Thermal Capacity Targets / Achievements
(from 4th Plan onwards)

Plan	Target (MW) (Original)	Capacity (MW) Addition	%Achieved
4th Plan (1969-74)	5746	2007.9	34.94
5th Plan (1974-79)	7845	6148.73	78.38
Annual Plan (1979-80)	2265	1216.87	53.72
6th Plan (1980-85)	14898	10605.84	71.19
7th Plan (1985-90)	15999	17093.4	106.84
Annual Plan (1990-91)	3962	2364	64.03
Annual Plan (1991-92)	4512	2370.5	52.54
8th Plan (1992-97)	20156	13554.9	67.2
9th Plan (1997-02)	29550.7	13800.9	46.71
10th Plan (2002-07)	25416.2	12114.24	47.66
11th Plan (2007-12)	59693	48539.9	81.32

2.1 Year/Plan wise Thermal Capacity Addition in the Country

Sl. No.	Year	Capacity Addition (MW)	Remarks
1st Five Year Plan (1.1.51 to 31.12.55)			
1	1951	107.02	
2	1952	86.33	
3	1953	227.43	
4	1954	126.64	
5	1955	<u>54.69</u>	
	Total :	<u>602.11</u>	
2nd Five Year Plan (1.1.56 to 31.03.61)			
6	1956-57	69.36	
7	1957-58	184.49	
8	1958-59	140.65	
9	1959-60	193.18	
10	1960-61	<u>393.37</u>	
	Total :	<u>981.05</u>	
3rd Five Year Plan (1.4.61 to 31.03.66)			
11	1961-62	63.33	
12	1962-63	65.12	
13	1963-64	544.08	
14	1964-65	599.02	
15	1965-66	<u>895.34</u>	
	Total :	<u>2166.89</u>	
Annual Plans (1966-67, 67-68, 68-69)			
16	1966-67	431.67	
17	1967-68	1061.29	
18	1968-69	654.12	
		<u>2147.08</u>	
4th Five Year Plan (1.4.69 to 31.03.74)			
19	1969-70	497.32	
20	1970-71	358.04	
21	1971-72	317.04	
22	1972-73	653.54	
23	1973-74	<u>181.96</u>	
	Total :	<u>2007.9</u>	
5th Five Year Plan (1.4.74 to 31.03.79)			
24	1974-75	1089.18	
25	1975-76	866.02	
26	1976-77	790.23	
27	1977-78	1204.8	
28	1978-79	<u>2198.5</u>	
	Total :	<u>6148.73</u>	
Annual Plan (1979-80)			
29	1979-80	1216.87	

6th Five Year Plan (1.4.80 to 31.03.85)

30	1980-81	1138.6
31	1981-82	1749.82
32	1982-83	2135.13
33	1983-84	2940.89
34	1984-85	<u>2641.4</u>
Total :		<u>10605.84</u>

7th Five Year Plan (1.4.85 to 31.03.90)

35	1985-86	2977.00
36	1986-87	1920.00
37	1987-88	3912.00
38	1988-89	4117.30
39	1989-90	<u>4167.00</u>
Total :		<u>17093.30</u>

Annual Plans (1990-91, 91-92)

40	1990-91	2364.00
41	1991-92	2370.50

8th Five Year Plan (1.4.92 to 31.03.97)

42	1992-93	2944.32
43	1993-94	3741.6
44	1994-95	3928.5
45	1995-96	1976.5
46	1996-97	<u>963.00</u>
Total :		<u>13553.92</u>

9th Five Year Plan (1.4.97 to 31.03.2002)

47	1997-98	2993.50
48	1998-99	3724.50
49	1999-2000	2696.00
50	2000-01	2277.90
51	2001-02	<u>2009.00</u>
Total :		<u>13700.9</u>

10th Five Year Plan (1.4.02 to 31.03.07)

52	2002-03	2223.10
53	2003-04	1361.60
54	2004-05	2933.92
55	2005-06	1588.80
56	2006-07	<u>4006.80</u>
Total :		<u>12114.22</u>

11th Five Year Plan (1.4.07 to 31.03.12)

57	2007-08	6620	2nd Highest.
58	2008-09	2484.7	
59	2009-10	9106	
60	2010-11	11250.5	
61	2011-12	<u>19078.7</u>	Highest till date.
Total		<u>48539.90</u>	

Note: Figures from 1951 to 1984-85 indicate uprated/derated capacities

3. Thermal Projects Commissioned During the 1st Quarter (April-June) of the year 2012

S.No	Project Name & Unit No./Implementing Agency	Cap. (MW)	Date of Commissioning
Central Sector			
1	Mouda TPP, U-1, NTPC	500	19.04.12(A)
2	Rihand STPS-III, U-5, NTPC	500	25.05.12(A)
3	Sipat TPP, U-3, NTPC	660	02.06.12(A)
4	Vindhyachal U - 11	500	14.06.12(A)
	Total Central Sector	2160	
State Sector			
5	Paricha Extn., U-5, UPRVUNL	250	24.05.12(A)
6	Harduaganj., U-9, UPRVUNL	250	25.05.12(A)
7	Pragati CCGT - III , GT-3, PPCL	250	27.06.12(A)
	Total of State Sector	750	
Private Sector			
8	Jajjar TPS(Mahatma Gandhi TPP), U-2, CLP Power	660	11.04.12(A)
9	Sterlite TPP, U-4, Sterlite Energy	600	25.04.12(A)
10	GEPL TPP, U-1, GEPL(Not targeted in 12-13)	60	28.04.12(A)
11	Salaya TPP, U-2, Essar Power	600	13.6.12(A)
12	Kasaipalli TPS, U-2, ACB India	135	21.6.12(A)
	Total of Private Sector	2055	
	Total in Q-1	4965	

4 THERMAL POWER PROJECTS COMMISSIONED DURING 11TH PLAN

Sector State	Project Name	Impl. Agency	Unit No.	Cap. (MW)	Actual. Comm. Date
2007-08					
CENTRAL SECTOR					
Bihar	Kahalgaon St-2,Ph-1	NTPC	U-6	500	16-03-08
Chhattisgarh	Sipat-II	NTPC	U-4	500	27-05-07
Maharashtra	Ratnagiri(Dhabol) Ph-II	RGPPL	Block-3	740	28-10-07
WB	Mejia TPS	DVC	U-6	250	01-10-07
Sub Total :				1990	
STATE SECTOR					
AP	Rayalseema TPP St-II	APGENCO	U-4	210	20-11-07
Chhattisgarh	Korba East TPP St-V	CSEB	U-2	250	11-12-07
Gujarat	Dhuvaran CCPP Extn.	GSECL	ST	40	13-08-07
Haryana	Yamuna Nagar TPP	HPGCL	U-1	300	13-11-07
			U-2	300	29-03-08
Karnataka	Bellary TPP	KPCL	U-1	500	03-12-07
Maharashtra	Paras TPS Expn,U-1	MSPGCL	U-1	250	31-05-07
MP	Sanjay Gandhi TPP Extn.-III	MPPGCL	U-5	500	18-06-07
Punjab	Guru Har Govind TPS-II	PSEB	U-3	250	03-01-08
Rajasthan	Dholpur CCGT	RRVUNL	GT-2	110	16-06-07
			ST	110	27-12-07
WB	Bakereshwar TPS	WBPDC	U-4	210	23-12-07
WB	Durgapur TPS Extn	DPL	U-7	300	24-11-07
WB	Sagardighi TPP	WBPDC	U-1	300	21-12-07
WB	Santaldih TPP Extn Ph-I	WBPDC	U-5	250	07-11-07
Sub Total :				3880	
PRIVATE SECTOR					
Chhattisgarh	O.P.Jindal STPP	Jindal Power Ltd.	U-1	250	02-09-07
			U-2	250	06-03-08
			U-3	250	10-02-08
Sub Total :				750	
Total :				6620	
2008-09					
CENTRAL SECTOR					
Chhattisgarh	Bhilai TPP Expn	NSPCL	U-1	250	20-04-08
Chhattisgarh	Sipat-II	NTPC	U-5	500	27-12-08
Sub Total :				750	
STATE SECTOR					
MP	Amarkantak TPP	MPPGCL	U-5	210	15-06-08
Punjab	Guru Har Govind TPS-II	PSEB	U-4	250	31-07-08
TN	Valuthur CCPP Extn.	TNEB	GT	59.8	06-05-08
			ST	32.4	16-02-09
WB	Sagardighi TPP	WBPDC	U-2	300	20-07-08
Sub Total :				852.2	
PRIVATE SECTOR					
Chhattisgarh	O.P.Jindal STPP	Jindal Power Ltd.	U-4	250	17-06-08
Page 1 of 5					
Gujarat	Sugen CCPP(Akhakhol)	Torrent Power Gen. Ltd.	Blk-I	382.5	04-02-09
Maharashtra	Trombay TPS Extn	Tata Power Company	U-8	250	26-03-09
Sub Total :				882.5	
Total :				2484.7	

<i>Sector State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>Cap. (MW)</i>	<i>Actual. Comm. Date</i>
2009-10					
<u>CENTRAL SECTOR</u>					
Bihar	Kahalgao St-2,Ph-2	NTPC	U-7	500	31-07-09
Chhattisgarh	Bhilai TPP Expn	NSPCL	U-2	250	12-07-09
Jharkhand	Chandrapura TPS Extn.	DVC	U-7	250	04-11-09
			U-8	250	31-03-10
UP	NCP Project St-II, U-5	NTPC	U-5	490	29-01-10
Sub Total :				1740	
<u>STATE SECTOR</u>					
AP	Vijayawada TPP -IV	APGENCO	U-1	500	08-10-09
Gujarat	Kutch Lignite TPS Extn	GSECL	U-4	75	01-10-09
Gujarat	Utran CCPP Extn	GSECL	GT	240	08-08-09
			ST	134	10-10-09
Haryana	Rajiv Gandhi TPS,Hissar	HPGCL	U-1	600	31-03-10
Maharashtra	New Parli TPP	MSPGCL	U-2	250	10-02-10
Maharashtra	Paras TPS Expn,U-2	MSPGCL	U-2	250	27-03-10
Rajasthan	Chhabra TPS	RRVUNL	U-1	250	30-10-09
Rajasthan	Giral Lignite-II	RRVUNL	U-2	125	06-11-09
Rajasthan	Kota TPP	RRVUNL	U-7	195	31-08-09
Rajasthan	Suratgarh TPP	RRVUNL	U-6	250	29-08-09
WB	Bakereshwar TPS	WBPCL	U-5	210	07-06-09
Sub Total :				3079	
<u>PRIVATE SECTOR</u>					
AP	Gautami CCPP	Gautami Power Ltd	GT-1	145	03-05-09
			GT-2	145	03-05-09
			ST	174	03-05-09
AP	Konaseema CCPP	Konaseema gas Power Ltd.	GT-1	140	01-05-09
			GT-2	140	01-05-09
AP	Lanco Kondapalli Ph-II (GT)	Lanco Kondapalli	GT	233	05-12-09
Chhattisgarh	Lanco AmarkantakTPS Ph-1,U-1	Lanco Amarkantak Power Pvt. Ltd.	U-1	300	04-06-09
Chhattisgarh	Lanco AmarkantakTPS Ph-1,U-2	Lanco Amarkantak Power Pvt. Ltd	U-2	300	26-03-10
Gujarat	Mundra TPP Ph-1(U-1&2)	Adani Power Ltd	U-1	330	04-08-09
			U-2	330	17-03-10
Gujarat	Sugen CCPP(Akhakhol)	Torrent Power Gen. Ltd.	Blk-II	382.5	07-05-09
			Blk-III	382.5	08-06-09
Karnataka	Toranagallu TPP	JSW Energy(Vijayanagar)	U-1	300	27-04-09
			U-2	300	24-08-09
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	U-1	135	16-10-09
UP	Rosa TPP Ph-I	Rosa Power Supply Co.Ltd.-	U-1	300	10-02-10
		Reliance Energy			
WB	Budge-Budge- III	CESC	U-3	250	29-09-09
Sub Total :				4287	
Total :				9106	

Sector State	Project Name	Impl. Agency	Unit No.	Cap. (MW)	Actual. Comm. Date
2010-11					
CENTRAL SECTOR					
AP	Simhadri STPP Extn.	NTPC	U-3	500	31-03-11
Chhattisgarh	Korba STPP	NTPC	U-7	500	26-12-10
Haryana	Indira Gandhi TPP	APCPL	U-1	500	31-10-10
Rajasthan	Barsingsar Lignite	NLC	U-1	125	28-06-10
			U-2	125	25-01-11
UP	NCP Project St-II	NTPC	U-6	490	30-07-10
WB	Farakka STPS- III	NTPC	U-6	500	23-03-11
WB	Mejia TPS Extn	DVC	U-1	500	30-09-10
			U-2	500	26-03-11
			Sub Total :	3740	
STATE SECTOR					
AP	Kakatiya TPP	APGENCO	U-1	500	27-05-10
AP	Rayalseema TPP St-III	APGENCO	U-5	210	31-12-10
Delhi	Pragati CCGT - III	PPCL	GT-1	250	24-10-10
			GT2	250	16-02-11
Gujarat	Surat Lignite TPP Extn.	GIPCL	U-3	125	12-04-10
			U-4	125	23-04-10
Haryana	Rajiv Gandhi TPS,Hissar	HPGCL	U-2	600	01-10-10
Karnataka	Raichur U-8	KPCL	U-8	250	26-06-10
Rajasthan	Chhabra TPS	RRVUNL	U-2	250	04-05-10
Tripura	Baramura GT Extn.	TSECL	U-5	21	03-08-10
			Sub Total :	2581	
PRIVATE SECTOR					
AP	Konaseema CAPP	Konaseema gas Power Ltd.	ST	165	30-06-10
AP	Lanco Kondapalli Ph-II (ST)	Lanco Kondapalli	ST	133	19-07-10
Delhi	Rithala CAPP	NDPL	GT-1	35.75	09-12-10
			GT-2	35.75	04-10-10
Gujarat	Mundra TPP Ph-I(U-3&4)	Adani Power Ltd	U-3	330	02-08-10
			U-4	330	20-12-10
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-1	660	26-12-10
Karnataka	Udupi TPP	UPCL	U-1	600	23-07-10
Maharashtra	JSW Ratnagiri TPP	JSW Energy(Ratnagiri) Ltd	U-1	300	24-08-10
			U-2	300	09-12-10
Maharashtra	Wardha Warora TPP	WPCL	U-1	135	05-06-10
			U-2	135	10-10-10
			U-3	135	13-01-11
Orissa	Sterlite TPP	Sterlite Energy Ltd.	U-1	600	14-10-10
			U-2	600	29-12-10
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	U-2	135	08-07-10
UP	Rosa TPP Ph-I	Rosa Power Supply Co.Ltd.- Reliance Energy	U-2	300	28-06-10
			Sub Total :	4929.5	
			Total :	11250.5	

2011-12

CENTRAL SECTOR

<i>Sector State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>Cap. (MW)</i>	<i>Actual. Comm. Date</i>
<u>CENTRAL SECTOR</u>					
AP	Simhadri STPP Extn.	NTPC	U-4	500	30-03-12
Chhattisgarh	Sipat-I	NTPC	U-1	660	28-06-11
			U-2	660	24-12-11
Haryana	Indira Gandhi TPP	APCPL	U-2	500	05-11-11
Jharkhand	Kodarma TPP	DVC	U-1	500	20-07-11
TN	Neyveli TPS-II Exp.	NLC	U-1	250	04-01-12
TN	Vallur TPP Ph I	NTECL	U-1	500	28-03-12
WB	Durgapur Steel TPS	DVC	U-1	500	29-07-11
			U-2	500	23-03-12
Sub Total :				4570	
<u>STATE SECTOR</u>					
AP	Kothagudem TPP -VI	APGENCO	U-1	500	26-06-11
Assam	Lakwa Waste Heat Unit	APGCL	ST	37.2	24-12-11
Delhi	Pragati CCGT - III	PPCL	ST-1	250	29-02-12
Gujarat	Hazira CCPP Extn.	GSECL	GT+ST	351	18-02-12
Karnataka	Bellary TPP St-II	KPCL	U-2	500	23-03-12
Maharashtra	Bhusawal TPS Expn.	MSPGCL	U-4	500	07-03-12
			U-5	500	30-03-12
Maharashtra	Khaperkheda TPS Expn.	MSPGCL	U-5	500	05-08-11
UP	Harduaganj Ext	UPRVUNL	U-8	250	27-09-11
WB	Santalidih TPP Extn Ph-II	WBPCL	U-6	250	29-06-11
Sub Total :				3638.2	
<u>PRIVATE SECTOR</u>					
AP	Simhapuri Energy Pvt.Ltd	Madhucon Projects Ltd	U-1	150	24-03-12
Chhattisgarh	Kasaipalli TPP	ACB India Ltd.	U-1	135	13-12-11
Chhattisgarh	Katghora TPP	Vandana Energy & Steel Ltd	U-1	35	14-02-12
Chhattisgarh	SV Power TPP	SV Power Pvt Ltd	U-1	63	07-12-11
Delhi	Rithala CCPP	NDPL	ST	36.5	04-09-11
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-2	660	20-07-11
Gujarat	Mundra TPP Ph-III	Adani Power Ltd	U-1	660	07-11-11
			U-2	660	03-03-12
			U-3	660	09-03-12
Gujarat	Mundra UMTTP	Tata Power Co.	U-1	800	25-02-12
Gujarat	Salaya TPP	Essar Power Gujarat Ltd.	U-1	600	22-02-12
Haryana	Jajjar TPP (Mahatma Gandhi TPP)	CLP Power India Pvt. Ltd	U-1	660	12-01-12
Jharkhand	Maithon RB TPP	DVC	U-1	525	30-06-11
			U-2	525	23-03-12
Karnataka	Udupi TPP	UPCL	U-2	600	17-04-11
Maharashtra	JSW Ratnagiri TPP	JSW Energy(Ratnagiri) Ltd	U-3	300	06-05-11
			U-4	300	08-10-11
Maharashtra	Mihan TPS	Abhijeet MADC Nagpur Energy Pvt Ptd	U-1	61.5	09-02-12
			U-2	61.5	09-02-12
			U-3	61.5	09-02-12
			U-4	61.5	09-02-12
Maharashtra	Wardha Warora TPP	WPCL	U-4	135	30-04-11
Orissa	Sterlite TPP	Sterlite Energy Ltd.	U-3	600	16-08-11
Rajasthan	Jallipa-Kapardi TPP	Raj West Power Ltd.(JSW)	U-3	135	02-11-11

<i>Sector State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No</i>	<i>Capacity. (MW)</i>	<i>Actual. Comm. Date</i>
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	U-4	135	23-11-11
UP	Anpara-C	Lanco Anpara Power Pvt. Ltd.	U-1	600	15-11-11
			U-2	600	12-11-11
UP	Barkhera TPP	Bajaj Energy Pvt. Ltd	U-1	45	06-11-11
			U-2	45	28-01-12
UP	Khamberkhera TPP	Bajajb Energy Pvt. Ltd	U-1	45	17-10-11
			U-2	45	28-11-11
UP	Kundarki TPP	Bajaj Energy Pvt. Ltd	U-1	45	10-01-12
			U-2	45	29-02-12
UP	Maqsoodpur TPP	Bajaj Energy Pvt Ltd	U-1	45	03-11-11
			U-2	45	21-01-12
UP	Rosa TPP Ph-II	Reliance Power Ltd.	U-3	300	27-12-11
			U-4	300	28-03-12
UP	Utrala TPP	Bajaj Energy Pvt. Ltd	U-1	45	21-02-12
			U-2	45	19-03-12
Sub Total :				10870.5	
Total :				19078.7	
Total (11thPlan):				48539.9	

5.0 Thermal Power Projects slipped from 11th Plan Original Target

State	Project Name	Impl Agency	Main Plant Equipment Supplier	Unit No	Cap. (MW)	Reasons of delay
<u>Central Sector</u>						
Assam	Bongaigaon TPP	NTPC	BHEL	U-1	250	Frequent bandhs, Heavy monsoon, poor performance of main civil agency M/s SPML.
Assam	Bongaigaon TPP	NTPC	BHEL	U-2	250	Frequent bandhs, Heavy monsoon, poor performance of main civil agency M/s SPML.
Assam	Bongaigaon TPP	NTPC	BHEL	U-3	250	Boiler and TG erection yet to start. Reasons of delay: Frequent bandhs, Heavy monsoon, poor performance of main civil agency M/s SPML.
Bihar	Barh STPP- I	NTPC	Others	U-1	660	Delay due to contractual dispute between NTPC and Power machine and Technoprome Russia. Finalisation of agency for erection
Bihar	Barh STPP- I	NTPC	Others	U-2	660	Delay due to contractual dispute between NTPC and Power machine and Technoprome Russia for finalisation of agency for erection.
Bihar	Barh STPP- I	NTPC	Others	U-3	660	Delay due to contractual dispute between NTPC and Power machine and Technoprome Russia
Bihar	Barh STPP-II	NTPC	BHEL	U-4	660	Delay in Placement of main Plant Order. Delay in supply of material by BHEL for boiler and TG
Bihar	Nabi Nagar TPP	NTPC	BHEL	U-1	250	Delay due to land acquisition
Bihar	Nabi Nagar TPP	NTPC	BHEL	U-2	250	Delay due to land acquisition
Bihar	Nabi Nagar TPP	NTPC	BHEL	U-3	250	Delay due to land acquisition
Chhattisgarh	Sipat-I	NTPC	Others	U-3	660	Due to extra claims raised by M/s. Power Machine, Russia for price escalations beyond contractual provisions. Due to IP & HP turbine modification suggested by M/s PM and delay in supply of canalised items, etc.
Haryana	Indira Gandhi TPP	APCPL	BHEL	U-3	500	Delay due to slow civil works of TG deck access floors and other floors of TG Hall and ID fan Foundation. Delay in supply of TG material.
Jharkhand	Koderma TPP	DVC	BHEL	U-2	500	Delay in supply of Boiler and TG materials. Delay in TG erection start.
Jharkhand	BokaroTPS "A"Exp.	DVC	BHEL	U-1	500	Delay in shifting of switchyard (charged). Delay in removal of existing CW underground facilities. Delay in supply of material by BHEL.
Maharashtra	Mouda TPP	NTPC	BHEL	U-1	500	Synchronised in April, 12
Maharashtra	Mouda TPP	NTPC	BHEL	U-2	500	Delay in placement of main plant order. Delay due to readiness of BoP and completion of civil works.
TN	Neyveli TPS-II Exp.	NLC	BHEL	U-2	250	Slow progress of refractory work
TN	Vallur TPP Ph I	NTECL	BHEL	U-2	500	Poor mobilization by civil agency resulting in delay in handing over of fronts. Delay in supply of Blrs & TG Materials. Completion of P-91 welding joints and boiler ducting.
TN	Tuticorin TPP	NLC	BHEL	U-1	500	Delay in placement of main plant order. Slow progress of works and change in design by the main plant contractor.
TN	Tuticorin TPP	NLC	BHEL	U-2	500	Delay in placement of main plant order. Slow progress of works and change in design by the main plant contractor.
Tripura	Tripura CCGT	OTPC	BHEL	Module-1 (363.3)	375	Delay in award of logistic by BHEL. Slow progress of work. Delay in forest clearance from MOE&F for erection of transmission lines. Delay in widening of heavy equipments .
Tripura	Tripura CCGT	OTPC	BHEL	Module-II (363.3)	375	Delay in award of logistic by BHEL. Slow progress of work. Delay in forest clearance from MOE&F for erection of transmission lines. Delay in widening of heavy equipments .
WB	Raghunathpur TPP, Ph-I	DVC	Chinese	U-1	600	Delay in Land acquisition for water & Rail corridor. Delay in erection of main plant equipment by M/s RIL. Slow progress of CHP by M/s TRF. Law & Order Problem. TG erection delayed due to civil works / non-availability of EOT crane. . Law & Order Problem.

WB	Raghnunathpur TPP, Ph-I	DVC	Chinese	U-2	600	Delay in Land acquasation for water & Rail corridor. Delay in erection of main plantequipment by M/s RIL, Slow progress of CHP by M/s TRF. Law & Order Problem.
		Total-Central			11000	
State Sector						
AP	Kakatiya TPP Extn	APGENCO	BHEL	U-2 (600)*	500	Delay in placement of main plant order. Due to delay in start of civil works.
Chhattisgarh	Korba West St-III.	CSEGL	BHEL	U-5	500	Delay in placement of main plant order. Delay in placement of civil works orders.
Chhattisgarh	Marwa TPP	CSEGL	BHEL	U-1	500	Delay in placement of main plant order. Delay in placement of civil works orders.
Chhattisgarh	Marwa TPP	CSEGL	BHEL	U-2	500	Delay in placement of main plant order. Delay in placement of civil works order.
Delhi	Pragati CCGT – III	PPCL	BHEL	GT-3	250	Delay in completion of civil works.
Delhi	Pragati CCGT – III	PPCL	BHEL	GT-4	250	Delay in supply of GT-4
Delhi	Pragati CCGT – III	PPCL	BHEL	ST-2	250	Delay in completion of civil works
Gujarat	Pipavav CCPP	GSECL	BHEL	Block-1	351	Delay in civil works and delay in supplies.
Gujarat	Pipavav CCPP	GSECL	BHEL	Block-2	351	Delay in civil works and delay in supplies.
Gujarat	Ukai TPS Extn.	GSECL	BHEL	U-6	490	Delay in civil works and supply of main plant equipment. Delay in readiness of CHP & AHP
Gujarat	Sikka TPS Extn.	GSECL	BHEL	U-3	250	Delay due to conditional environment clearance by MOE&F. Delay in placement of main plant order.
Gujarat	Sikka TPS Extn.	GSECL	BHEL	U-4	250	Delay due to conditional environment clearance by MOE&F. Delay in placement of main plant order.
MP	Malwa TPP (Shree Singati TPP)	MPGENCO	BHEL	U-1 (600)*	500	Delay in placement of main plant order. Delay in boiler pressure part supply/erection.slow progress of work.
		MPGENCO	BHEL	U-2 (600)*	500	Delay in placement of main plant order. Delay in boiler pressure part supply/erection.slow progress of work.
MP	Satpura TPS Extn	MPPGCL	BHEL	U-11	250	Delay in placement of main plant order and BoPs. Delay in supply of pressure parts. Slow progress of work.
MP	Satpura TPS Extn	MPPGCL	BHEL	U-10	250	Delay in supply of pressure parts. Slow progress of TG erection.
Rajasthan	Kalisindh TPS	RRVUNL	Chinese	U-1 (600)*	500	Delay in placement of Main Plant and BoPs. Delay in supplies including Generator Transformer.
TN	Mettur TPP Ext	TNEB	Chinese	U-1 (600)*	500	Slow progress of works.
TN	North Chennai TPS St-II, U-1	TNEB	BHEL	U-1	600	Reasons of delay: Delay in supply by BHEL.
UP	Harduaganj Ext	UPRVUNL	BHEL	U-9	250	Delay in TG erection. Readiness of mills
UP	Parichha Extn	UPRVUNL	BHEL	U-5	250	Delay due to collapse of chimney
UP	Parichha Extn	UPRVUNL	BHEL	U-6	250	Delay due to collapse of chimney
U.P	Anpara-D	UPRVUNL	BHEL	U-6	500	Delay in finalisation of Agency for civil works and delay in civil works.
UP	Anpara-D	UPRVUNL	BHEL	U- 7	500	Delay in civil works.
-		Total - State			9292	
-	Private Sector					
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-5	135	Due to delay in developemnt of Jalipa mine. Non availability of permanent 33KV supply for pumping stations to operate at full load.
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-6	135	Due to delay in developemnt of Jalipa mine. Non availability of permanent 33KV supply for pumping stations to operate at full load.
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-7	135	Due to delay in developemnt of Jalipa mine. Non availability of permanent 33KV supply for pumping stations to operate at full load.
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-8	135	Due to delay in developemnt of Jalipa mine. Non availability of permanent 33KV supply for pumping stations to operate at full load.
-		Total Private			540	
-	Total Slipped from the Original 11th Plan				20832	

6. Thermal Units Slipped From 11th Plan Mid Term Appraisal Target

Sector/ State	Project Name	Impl Agency	Main Plant Supplier	Unit No	Cap. (MW)	Reasons for slippage
<u>Central Sector</u>						
Assam	Bongaigaon TPP	NTPC	BHEL	U-1	250	Frequent bandhs, Heavy monsoon and delay in main civil works by M/s SPML.
Assam	Bongaigaon TPP	NTPC	BHEL	U-2	250	
Haryana	Indira Gandhi TPP	APCPL	BHEL	U-3	500	Delay in civil works of TG deck access floors, other floors of TG Hall and ID fan Foundation. Delay in supply of TG material.
Jharkhand	Koderma TPP	DVC	BHEL	U-2	500	Delay in supply of Boiler and TG materials. Delay in TG erection start.
TN	Neyveli TPS-II Exp.	NLC	BHEL	U-2	250	Slow progress of refractory work
TN	Vallur TPP Ph I	NTECL	BHEL	U-2	500	Poor mobilization by civil agency resulting in delay in handing over of fronts. Delay in supply of TG Materials. Completion of P-91 welding joints and boiler ducting.
WB	Raghunathpur TPP, Ph-I	DVC	Chinese	U-1	600	Delay in Land acquisition for water & Rail corridor. Delay in erection of main plant equipments by M/s RIL. Slow progress of CHP by M/s TRF. Law & Order Problem. TG erection delayed due to civil works / non-availability of EOT crane.
WB	Raghunathpur TPP, Ph-I	DVC	Chinese	U-2	600	
-			Total- Central		3450	
<u>State Sector</u>						
Delhi	Pragati CCGT - III	PPCL	BHEL	GT-3	250	Delay in completion of civil works.
Delhi	Pragati CCGT - III	PPCL	BHEL	GT-4	250	Delay in supply of GT-4
Delhi	Pragati CCGT - III	PPCL	BHEL	ST-2	250	Delay in completion of civil works
Gujarat	Pipavav CCGT	GSECL	BHEL	Block-1	351	Delay in civil works and delay in supplies.
Gujarat	Pipavav CCGT	GSECL	BHEL	Block-2	351	Delay in civil works and delay in supplies.
Gujarat	Ukai TPS Extn.	GSECL	BHEL	U-6	490	Delay in civil works and supply of main plant equipments. Delay in readiness of CHP & AHP
TN	Mettur TPP Ext	TNEB	Chinese	U-1	600	Non-readiness of AHP and CHP.
TN	North Chennai TPS St-II, U-1	TNEB	BHEL	U-1	600	Delay in supply of generator stator by BHEL due to fall of the same in the river.
TN	North Chennai TPS St-II, U-2	TNEB	BHEL	U-2	600	Delay in supply by BHEL.
UP	Harduaganj Ext	UPRVUNL	BHEL	U-9	250	Delay in TG erection and readiness of mills
UP	Parichha Extn	UPRVUNL	BHEL	U-5	250	Delay due to collapse of chimney
UP	Parichha Extn	UPRVUNL	BHEL	U-6	250	
-			Total - State		4492	
Private Sector						
Maharashtra	Tirora TPP Ph-I	Adani Power Ltd	Chinese	U-1	660	Delay due to non readiness of power evacuation system readiness.

<i>Rajasthan</i>	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-5	135	Delay in developemnt of Jalipa mine. Non availability of permanent 33KV supply for pumping stations to operate at full load.
<i>Rajasthan</i>	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-6	135	
<i>Rajasthan</i>	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-7	135	
<i>Rajasthan</i>	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-8	135	
-		Total Private			1200	
-			Total Slipped:		9142	

7.0 THERMAL PROJECTS WHICH ARE UNDER CONSTRUCTION AND LIKELY TO BE COMMISSIONED DURING 12TH PLAN AND BEYOND -- TG MAKE- BHEL/ NON-BHEL(INDIAN)/ CHINESE/OTHERS (Expt. CHINESE)

<i>State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>CAPACITY (MW)</i>	<i>BHEL Cap. (MW)</i>	<i>NON-BHEL (Indian) Cap.(MW)</i>	<i>CHINESE Cap. (MW)</i>	<i>OTHERS Cap. (MW)</i>
<u>CENTRAL SECTOR</u>								
Assam	Bongaigaon TPP	NTPC	U-1	250	250	---	---	---
			U-2	250	250	---	---	---
			U-3	250	250	---	---	---
			U-4	250	250	---	---	---
Bihar	Barh STPP- I		U-1	660	---	---	---	660
			U-2	660	---	---	---	660
			U-3	660	---	---	---	660
	Barh STPP-II		U-1	660	660	---	---	---
			U-2	660	660	---	---	---
	Muzaffarpur TPP Exp		U-3	195	195	---	---	---
			U-4	195	195	---	---	---
	Nabi Nagar TPP		U-1	250	250	---	---	---
			U-2	250	250	---	---	---
			U-3	250	250	---	---	---
			U-4	250	250	---	---	---
Haryana	Indira Gandhi TPP	APCPL	U-3	500	500	---	---	---
Jharkhand	BokaroTPS "A"Exp.	DVC	U-1	500	500	---	---	---
	Kodarma TPP		U-2	500	500	---	---	---
Maharashtra	Mouda TPP	NTPC	U-2	500	500	---	---	---
MP	Vindhyachal TPP-IV		U-12	500	500	---	---	---
TN	Neyveli TPS-II Exp.	NLC	U-2	250	250	---	---	---
	Tuticorin JV		U-1	500	500	---	---	---
			U-2	500	500	---	---	---
	Vallur TPP Ph I	NTECL	U-2	500	500	---	---	---
	Vallur TPP-II		U-3	500	500	---	---	---
	Monarchak CCPP	NEEPCO	GT+ST	101	101	---	---	---
Tripura	Tripura Gas	ONGC	Module-1	363.3	363.3	---	---	---
			Module-2	363.3	363.3	---	---	---

<i>State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>CAPACITY (MW)</i>	<i>BHEL Cap. (MW)</i>	<i>NON-BHEL (Indian) Cap.(MW)</i>	<i>CHINESE Cap. (MW)</i>	<i>OTHERS Cap. (MW)</i>
UP	Rihand TPP- III	NTPC	U-6	500	500	---	---	---
WB	Raghunathpur TPP, Ph-I	DVC	U-1	600	---	---	600	---
			U-2	600	---	---	600	---
Sub-Total :				12717.6	9537.6	0	1200	1980
STATE SECTOR								
AP	Damodaram Sanjeevaiah TPS	APPDL	U-1	800	---	800	---	---
			U-2	800	---	800	---	---
	Kakatiya TPP Extn	APGENCO	U-1	600	600	---	---	---
	Rayalseema St-III U-6	BHEL	U-6	600	600	---	---	---
Assam	Namrup CCGT	APGCL	GT	70	70	---	---	---
			ST	30	30	---	---	---
Chhattisgarh	Korba West St-III.	CSPGCL	U-5	500	500	---	---	---
	Marwa TPP		U-1	500	500	---	---	---
			U-2	500	500	---	---	---
Delhi	Pragati CCGT - III	PPCL	GT-4	250	250	---	---	---
			ST-2	250	250	---	---	---
Gujarat	Pipavav CCGP	GSECL	Block-1	351	351	---	---	---
			Block-2	351	351	---	---	---
	Sikka TPP Extn.		U-3	250	250	---	---	---
			U-4	250	250	---	---	---
	Ukai TPP Extn.		U-6	490	490	---	---	---
Maharashtra	Chandrapur TPS	MSPGCL	U-8	500	500	---	---	---
			U-9	500	500	---	---	---
	Koradi TPP Expn.		U-10	660	---	660	---	---
			U-8	660	---	660	---	---
			U-9	660	---	660	---	---
	Parli TPP Expn.		U-8	250	250	---	---	---
MP	Malwa TPP (Shree Singati TPP)	MPGENCO	U-1	600	600	---	---	---
			U-2	600	600	---	---	---

<i>State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>CAPACITY (MW)</i>	<i>BHEL Cap. (MW)</i>	<i>NON-BHEL (Indian) Cap.(MW)</i>	<i>CHINESE Cap. (MW)</i>	<i>OTHERS Cap. (MW)</i>
MP	Satpura TPP Extn	MPPGCL	U-10	250	250	---	---	---
			U-11	250	250	---	---	---
Rajasthan	Chhabra TPP Extn.	RRVUNL	U-3	250	250	---	---	---
			U-4	250	250	---	---	---
	Kalisindh TPS		U-1	600	---	---	600	---
			U-2	600	---	----	600	---
	Ramgarh CCPP Extn. -III		GT	110	110	---	---	---
			ST	50	50	---	---	---
TN	Mettur TPP Ext	TNEB	U-1	600	---	---	600	---
	North Chennai Extn, U-1		U-1	600	600	---	---	---
	North Chennai Extn, U-2		U-2	600	600	---	---	---
UP	Anpara-D	UPRVUNL	U- 6	500	500	---	---	---
			U-7	500	500	---	---	---
	Parichha Extn		U-6	250	250	---	---	---
WB	Durgapur TPS Extn	DPL	U-8	250	---	---	250	---
Sub-Total :				16682	11052	3580	2050	0
<u>PRIVATE SECTOR</u>								
AP	Bhavanpadu TPP	M/s East Coast Energy Ltd.	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
	Painampuram TPP	Thermal Power Tech Corporation Ltd	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
	Simhapuri Energy Pvt Ltd Ph-II	Madhucon Projects Ltd.	U-3	150	---	---	150	---
			U-4	150	---	---	150	---
	Thamminapatnam TPP-I	Meenakshi Energy Pvt. Ltd	U-1	150	---	---	150	---
			U-2	150	---	---	150	---
	Thamminapatnam TPP-II	Meenaksha Energy Ltd.	U-3	350	---	---	350	---
			U-4	350	---	---	350	---
	Vizag TPP	Hinduja National Power Corp. Ltd	U-1	520	520	---	---	---
			U-2	520	520	---	---	---

<i>State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>CAPACITY (MW)</i>	<i>BHEL Cap. (MW)</i>	<i>NON-BHEL (Indian) Cap.(MW)</i>	<i>CHINESE Cap. (MW)</i>	<i>OTHERS Cap. (MW)</i>
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	U-1	600	---	---	600	---
			U-2	600	---	---	600	---
			U-3	600	---	---	600	---
			U-4	600	---	---	600	---
	Avantha Bhandar TPS, U-1	Korba West Power Co. Ltd.	U-1	600	600	---	---	---
	Badadarha TPP (DB Power TPP)	D.B.Power co.Ltd	U-1	600	600	---	---	---
			U-2	600	600	---	---	---
	Balco TPP	Bharat Aluminium Co. Ltd	U-1	300	---	---	300	---
			U-2	300	---	---	300	---
	Bandakhari TPP	M/s Maurti Clean Coal & Power Ltd	U-1	300	---	---	300	---
	Binjkote TPP	M/s SKS Power Generation (Chhattisgarh) Ltd.	U-1	300	---	---	300	---
			U-2	300	---	---	300	---
			U-3	300	---	---	300	---
			U-4	300	---	---	300	---
	Lanco Amarkantak TPS-II	LAP Pvt. Ltd.	U-3	660	---	---	660	---
			U-4	660	---	---	660	---
	Raikheda TPP	GMR	U-1	685	---	---	---	685
			U-2	685	---	---	---	685
	Singhitarai TPP	Athena Chhattisgarh Power	U-1	600	---	---	600	---
			U-2	600	---	---	600	---
	Swastic TPP	M/s ACB	U-1	25	---	25	---	---
	Tamnar TPP (Raigarh)	O.P.Jindal	U-1	600	600	---	---	---
			U-2	600	600	---	---	---
	TRN Energy TPP	M/s TRN Energy Pvt. Ltd.	U-1	300	---	---	300	---
			U-2	300	---	---	300	---
	Uchpinda TPP	RKM Powergen Pvt. Ltd	U-1	360	---	---	360	---
			U-2	360	---	---	360	---
			U-3	360	---	---	360	---
			U-4	360	---	---	360	---

<i>State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>CAPACITY (MW)</i>	<i>BHEL Cap. (MW)</i>	<i>NON-BHEL (Indian) Cap.(MW)</i>	<i>CHINESE Cap. (MW)</i>	<i>OTHERS Cap. (MW)</i>
Chhattisgarh	Vandana Vidyut TPP- Chhattisgarh	M/s Vandana Vidyut	U-1	135	---	---	135	---
			U-2	135	---	---	135	---
Gujarat	Bhavnagar CFBC TPP	Bhavnagar Energy	U-1	250	250	---	---	---
			U-2	250	250	---	---	---
	Mundra UMTTP	Tata Power Co.	U-3	800	---	---	---	800
			U-4	800	---	---	---	800
			U-5	800	---	---	---	800
Jharkhand	Adhunik Power TPP	Adhunik Power Co.Ltd	U-1	270	270	---	---	---
			U-2	270	270	---	---	---
	Corporate Power Ltd -Ph-I (Matrishri Usha)	M/s Corporate Power Ltd	U-1	270	270	---	---	---
			U-2	270	270	---	---	---
Maharashtra	Amravati TPP Ph-I	India Bulls	U-1	270	270	---	---	---
			U-2	270	270	---	---	---
			U-3	270	270	---	---	---
			U-4	270	270	---	---	---
			U-5	270	270	---	---	---
	Amravati TPP Ph-II		U-1	270	270	---	---	---
			U-2	270	270	---	---	---
			U-3	270	270	---	---	---
			U-4	270	270	---	---	---
			U-5	270	270	---	---	---
	Bela TPP-I	IEPL	U-1	270	270	---	---	---
	Butibori TPP Ph-II	Vidarbha Industries Power	U-1	300	---	---	300	---
	Dhariwal Infracture TPP	Dhariwal Infracture (P) Ltd	U-1	300	---	---	300	---
			U-2	300	---	---	300	---
	EMCO Warora TPP	EMCO Energy Ltd.(GMR)	U-1	300	---	---	300	---
			U-2	300	---	---	300	---
	Lanco Vidarbha TPP	Lanco Vidarbha	U-1	660	---	---	660	---
			U-2	660	---	---	660	---

<i>State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>CAPACITY (MW)</i>	<i>BHEL Cap. (MW)</i>	<i>NON-BHEL (Indian) Cap.(MW)</i>	<i>CHINESE Cap. (MW)</i>	<i>OTHERS Cap. (MW)</i>
Maharashtra	Nasik TPP Ph-I	India Bulls	U-1	270	270	---	---	---
			U-2	270	270	---	---	---
			U-3	270	270	---	---	---
			U-4	270	270	---	---	---
			U-5	270	270	---	---	---
	Nasik TPP Ph-II		U-1	270	270	---	---	---
			U-2	270	270	---	---	---
			U-3	270	270	---	---	---
			U-4	270	270	---	---	---
			U-5	270	270	---	---	---
	Tirora TPP Ph-I	Adani Power Ltd	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
	Tirora TPP Ph-II		U-1	660	---	---	660	---
			U-2	660	---	---	660	---
			U-3	660	---	---	660	---
MP	Anuppur TPP Ph-I	MB Power MP	U-1	600	---	---	600	---
			U-2	600	---	---	600	---
	Bina TPP	Bina Power Supply Co. Ltd	U-1	250	250	---	---	---
			U-2	250	250	---	---	---
	Gorgi TPP (DB Power)	DB Power	U-1	660	660	---	---	---
	Mahan TPP	Essar Power MP Ltd	U-1	600	---	---	600	---
			U-2	600	---	---	600	---
	Nigri TPP	Jaiprakash Power Ventures Ltd	U-1	660	---	660	---	---
			U-2	660	---	660	---	---
	Sasan UMPP	Reliance Power Ltd.	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
			U-3	660	---	---	660	---
			U-4	660	---	---	660	---
			U-5	660	---	---	660	---
	Seioni TPP Ph-I	Jhabua Power Ltd	U-6	660	---	---	660	---
			U-1	600	600	---	---	---

<i>State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>CAPACITY (MW)</i>	<i>BHEL Cap. (MW)</i>	<i>NON-BHEL (Indian) Cap.(MW)</i>	<i>CHINESE Cap. (MW)</i>	<i>OTHERS Cap. (MW)</i>
Orissa	Derang TPP	JITPL	U-1	600	600	---	---	---
			U-2	600	600	---	---	---
	Ind Bharat TPP (Orissa)	Ind. Bharat	U-1	350	---	---	350	---
			U-2	350	---	---	350	---
	Kamalanga TPP	GMR	U-1	350	---	---	350	---
			U-2	350	---	---	350	---
			U-3	350	---	---	350	---
	KVK Nilanchal TPP	KVK Nilanchal	U-1	350	---	---	350	---
			U-2	350	---	---	350	---
			U-3	350	---	---	350	---
	Lanco Babandh TPP	Lanco Babandh Power Ltd	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
	Malibrahmani TPP (Monnet Ispat)	MPCL	U-1	525	525	---	---	---
			U-2	525	525	---	---	---
Punjab	Goindwal Sahib	GVK Power	U-1	270	270	---	---	---
			U-2	270	270	---	---	---
	Rajpura TPP (Nabha)	Nabha Power Ltd	U-1	700	---	700	---	---
			U-2	700	---	700	---	---
	Talwandi Sabo TPP	M/s Sterlite	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
			U-3	660	---	---	660	---
Rajasthan	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	U-5	135	---	---	135	---
			U-6	135	---	---	135	---
			U-7	135	---	---	135	---
			U-8	135	---	---	135	---
	Kawai TPP	Adani Power Ltd.	U-1	660	---	---	660	---
			U-2	660	---	---	660	---
	Melamaruthur TPP	Coastal Energen	U-1	600	---	---	600	---
			U-2	600	---	---	600	---
TN	Tuticorin TPP (Ind- Barath TPP)	IBPIL	U-1	660	---	---	660	---
UP	Bara TPP	J.P.Power	U-1	660	660	---	---	---
			U-2	660	660	---	---	---

<i>State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>CAPACITY (MW)</i>	<i>BHEL Cap. (MW)</i>	<i>NON-BHEL (Indian) Cap.(MW)</i>	<i>CHINESE Cap. (MW)</i>	<i>OTHERS Cap. (MW)</i>
UP	Bara TPP	J.P.Power	U-3	660	660	---	---	---
	Lalitpur TPP	Lalitpur Power Generation Co. Ltd.	U-1	660	660	---	---	---
			U-2	660	660	---	---	---
			U-3	660	660	---	---	---
WB	Haldia TPP-I	M/s Haldia Energy Ltd.	U-1	300	---	---	300	---
			U-2	300	---	---	300	---
			Sub-Total :	62485	19800	2745	36170	3770
			Total :	91884.6	40389.6	6325	39420	5750


8. Thermal Capacity Addition Target/Achievement for the year 2012-13								
S.No	Project Name	Impl Agency	Targeted Cap. (MW)	Q1	Q2	Q3	Q4	Cap. (MW) Achieved
	<u>CENTRAL SECTOR</u>							
1	Vindhyachal STPS-IV, U-11	NTPC	500		500			500
2	Rihand STPS- III, U-5	NTPC	500	500				500
3	Sipat-I, U-3	NTPC	660	660				660
4	Mouda TPP, U-1	NTPC	500		500			500
5	Indira Gandhi TPP, U-3	APCPL	500			500		
6	Vallur TPP Ph I U-2	NTECL	500				500	
7	Koderma TPP U-2	DVC	500			500		
8	Tripura Gas, Module-1	ONGC	363.3			363.3		
	Total -Central sector		4023.3	1160	1000	1363.3	500	2160
	<u>STATE SECTOR</u>							
9	Marwa TPP, U-1	CSEB	500				500	
10	Pragati CCGT - III , GT-3	PPCL	250		250			250
11	Pipavav CCP, Block-2	GSECL	351				351	
12	Ukai TPP Extn. U-6	GSECL	490			490		
13	Ramgarh GT,	RRVUNL	110				110	
14	Ramgarh ST	RRVUNL	50				50	
15	Satpura TPS Extn , U-10	MPPGCL	250				250	
16	North Chennai Extn, U-2	TNEB	600				600	
17	Mettur TPS Ext, U-1	TNEB	600	600				
18	Parichha Extn, U-5	UPRVUNL	250	250				250
19	Parichha Extn, U-6	UPRVUNL	250		250			
20	Harduaganj Ext, U-9	UPRVUNL	250	250				250
	Total -State sector		3951	1100	500	490	1861	750
	<u>PRIVATE SECTOR</u>							
21	Simhapuri Ph-I, U-2	Madhucon	150		150			150
22	Thamminapatnam TPP-I	Meenakshi	150		150			
23	Thamminapatnam TPP-I, U-2	Meenakshi	150			150		
24	Vandana Vidyut TPP, U-1	Vandana	135			135		
25	Kasaipalli TPP , U-2	ACB	135	135				135
26	Swastik Korba , U-1	ACB	25	25				
27	Mundra UMTTP, U-2	Tata Power	800			800		
28	Salaya TPP, U-2	Essar Power	600		600			600
29	Jajjar TPS (Mahatama Gandhi TPP) , U-2	CLP Power	660	660				660
30	Adhunik Power TPP, U-1	Adhunik Power	270		270			
31	Corporate Power Ltd -Ph-I (Maitrishi Usha), U-1	Corporate	270			270		
32	Butibori TPP Ph-II, U-1	RPL	300		300			
33	Bela TPP-I, U-1	IEPL	270		270			
34	EMCO Warora TPP, U-1	EMCO (GMR)	300			300		
35	Tirora TPP Ph-I, U-1	Adani Power	660		660			
36	Tirora TPP Ph-I, U-2	Adani Power	660			660		
37	Tirora TPP Ph-II, U-1	Adani Power	660				660	
38	Bina TPP, U-1	Bina Power	250		250			
39	Jallipa-Kapurdi TPP, U-5	Raj West	135				135	
40	Sterlite TPP, U-4	Sterlite	600	600				600
	Total -Private sector		7180	1420	2650	2315	795	2145
	Total		15154.3	3680	4150	4168.3	3156	5055
	Thermal		15154.3					
	Overall Central Sector		4023.3	1160	1000	1363.3	500	2160
	Overall State Sector		3951	1100	500	490	1861	750
	Overall Private Sector		7180	1420	2650	2315	795	2145
	Total Thermal		15154.3	3680	4150	4168.3	3156	5055
	Total Hydro		802	127	269	234	172	0
	Grand Total of 2012-13		15956.3	3807	4419	4402.3	3328	5055
	GEPL TPP, U-1(Not targeted in the year 2012-13)	GEPL						60

9. Thermal Power Projects visited during the Quarter (April-June, 12)

The following thermal power projects were visited by the officers of TPM Division to have on the spot assessment of the progress of construction activities going on at project sites.

1. Thammipatnam TPP (MEPL) , AP(2x150 MW+ 2x300 MW).
2. Simhapuri TPP, SEPL, Andhra Pradesh(4x150 MW)
3. Painampuram TPP, TPTCIL, AP (2x660 MW)
4. Marwa TPP, Korba , CSPGL, Chhattisgarh (1x500 MW)
5. Lanco Amarkantak TPS, LAPL, Chhattisgarh (2x660 MW)
6. Akaltara TPS, KSK Mahanadi, Chhattisgarh (2x600 MW)
7. Bandakhar TPP, Maruti Clean CCPL., Chhattisgarh (1x300 MW)
8. Chhuri-Salora TPP, Vandana Vidyut, Chhattisgarh (2x 135 MW)
9. Swastik TPP, ACB, Chhattisgarh (1x 25 MW)
10. Tirora TPP, Nagpur, Maharastra(2x660 MW)
11. Bela TPP-I, IEPL,(1x270 MW)
12. Butibori TPP-II, Vidharb I P, Maharastra(1x300 MW)
13. Dhariwal Infra TPP, DIPL, Maharastra (2x 300 MW)
14. Amravati TPP, Maharastra(5x270 MW)
15. EMCO Warora TPP, Maharastra(2x 300 MW)
16. Lanco Vidharbha TPP, Maharastra(2x 660 MW)
17. Agrigold TPP, Ramagundam, AP (1x480 MW)
18. Chhabra TPP, RRVUNL, Rajasthan , (2x 250 MW)
19. Kalisindh TPS, RRVUNL, Rajasthan , (1x 600 MW)
20. Kawai TPP, APL, Rajasthan , (2x 660 MW)
21. North Chennai TPS, TNEB, Tamilnadu (2x 600 MW)
22. Vallur TPP, NTECL, Tamilnadu (2x 500 MW)
23. Kamalanga TPP, GMR, Odisha(2x 350 MW)
24. Lanco Babandh TPP, LBPL, Odisha (2x 660 MW)
25. Malibrahmani TPP, MPCL, Odisha (1x 525 MW)
26. Derang TPP, JITPL, Odisha (2x 600 MW)
27. KVK Nilanchal TPP, KVKN, Odisha (2x 350 MW)


10. TREND OF CAPACITY ADDITION AS % OF TOTAL (Thermal,Hydro & Nuclear mix)

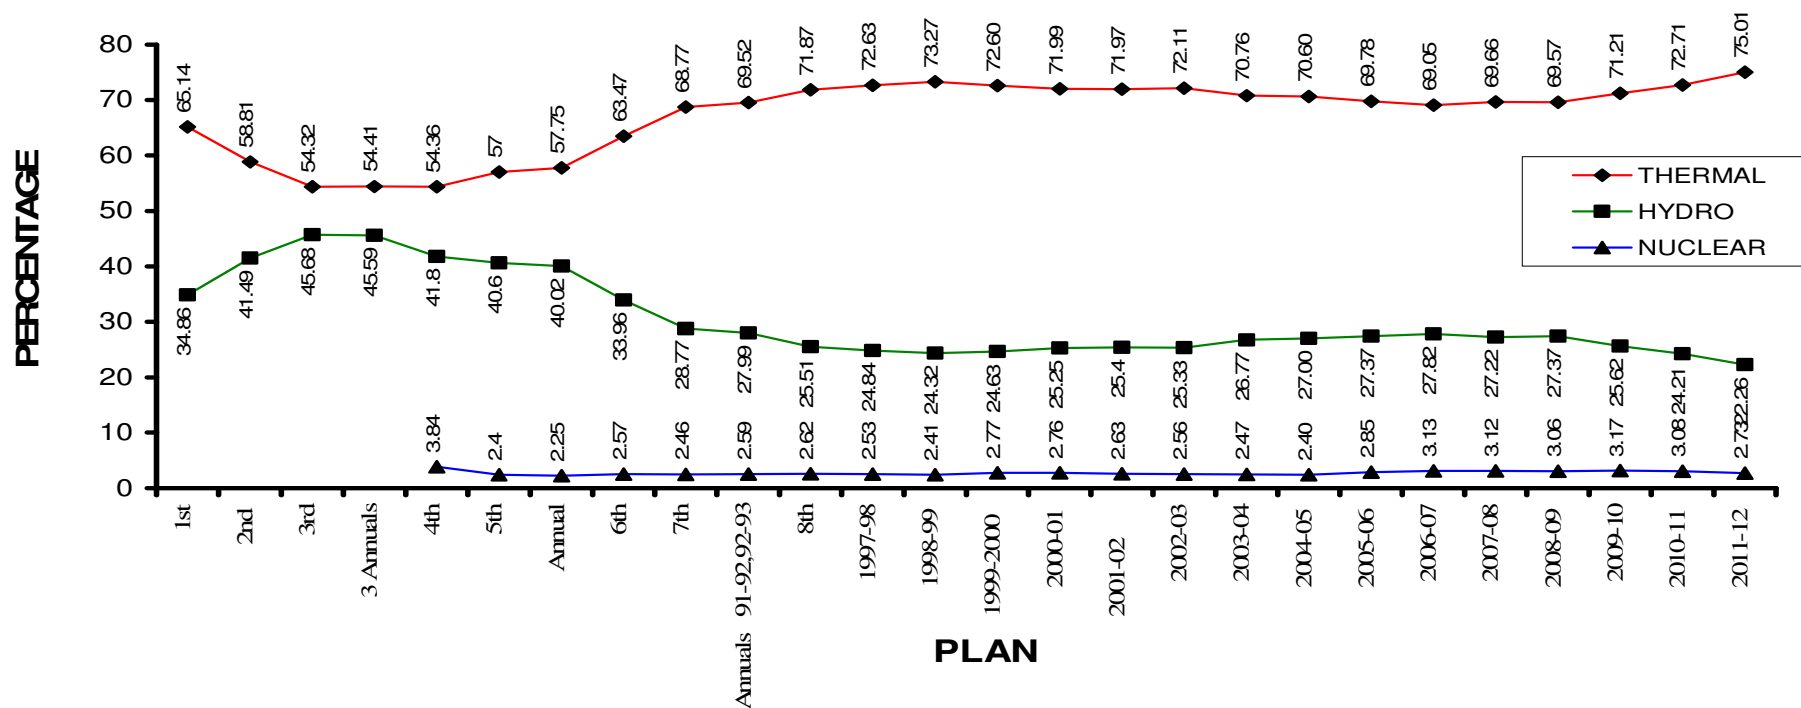

**11(a) Power Generating Capacity of Thermal Units in the country
since inception of 1st five year plan**

Plan/ Duration	Capacity Addition (MW)	Cumulative (MW)
1st Plan (1.1.51 to 31.3.56)	602.11	1755.34
2nd Plan (1956-61)	981.05	2736.39
3rd Plan (1961-66)	2166.89	4903.28
Annual Plan (1966-67)	431.67	5334.95
Annual Plan (1967-68)	1061.29	6396.24
Annual Plan (1968-69)	654.12	7050.36
4th Plan (1969-74)	2007.9	9058.26
5th Plan (1974-79)	6148.73	15206.99
Annual Plan (1979-80)	1216.87	16423.86
6th Plan (1980-85)	10898.00	27321.86
7th Plan (1985-90)	17093.3	44415.16
Annual Plan (1990-91)	2364.00	46779.16
Annual Plan (1991-92)	2370.50	49149.66
8th Plan (1992-97)	13554.82	62704.48
9th Plan (1997-2002)	13700.90	76405.38
10th Plan (2002-07)	12114.24	88519.62
11th Plan (2007-12)	48539.90	137059.52

11(a) Bar Chart representing Plan-Wise Growth of Thermal Installed Capacity

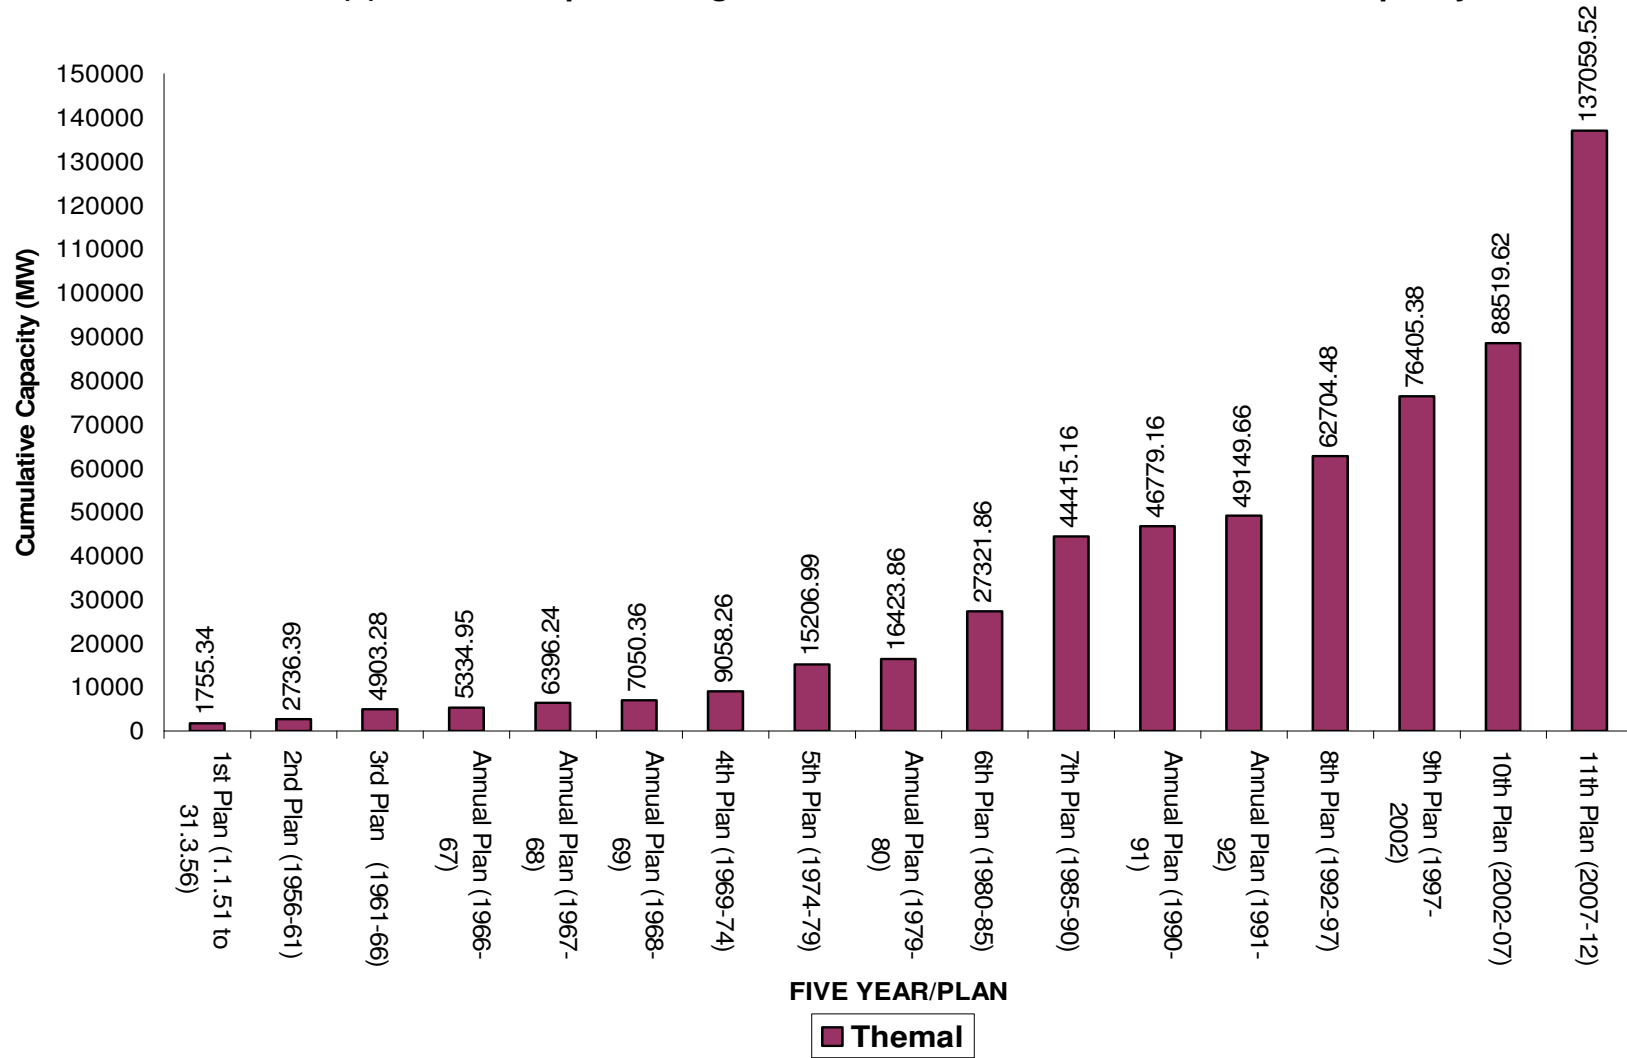

12. SUPERCRITICAL THERMAL POWER PROJECTS COMMISSIONED DURING 11TH PLAN

<i>Sector State</i>	<i>Project Name</i>	<i>Impl. Agency</i>	<i>Unit No.</i>	<i>Cap. (MW)</i>	<i>Actual. Comm. Date</i>
2010-11					
<u>PRIVATE SECTOR</u>					
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-1	660	26-12-10
2011-12					
<u>CENTRAL SECTOR</u>					
Chhattisgarh	Sipat-I	NTPC	U-1	660	28-06-11
			U-2	660	24-12-11
Sub Total :				1980	
<u>PRIVATE SECTOR</u>					
Gujarat	Mundra TPP Ph-II	Adani Power Ltd	U-2	660	20-07-11
	Mundra TPP Ph-III	Adani Power Ltd	U-1	660	07-11-11
			U-2	660	03-03-12
			U-3	660	09-03-12
Haryana	Mundra UMTTP	Tata Power Co.	U-1	800	25-02-12
	Jajjar TPP (Mahatama Gandhi	CLP Power India Pvt. Ltd	U-1	660	12-01-12
Sub Total :				4100	
Total (11thPlan):				6080	

13. Details of Expenditure of Thermal Power Projects Under Construction

State	Project Name	Impl Agency	Main Equipt. Supplier	Unit No	Cap. (MW)	Ant. Comm. Schedule	Total Exp incurred (Cr.)	Till (Month/Year)
	CENTRAL SECTOR							
Assam	Bongaigaon TPP	NTPC	BHEL	U-1	250	Aug-13	2861.00	2/12
Assam	Bongaigaon TPP	NTPC	BHEL	U-2	250	Jun-14		
Assam	Bongaigaon TPP	NTPC	BHEL	U-3	250	Nov-14		
Bihar	Barh STPP- I	NTPC	Others	U-1	660	Jul-14	6543.00	2/12
Bihar	Barh STPP- I	NTPC	Others	U-2	660	May-15		
Bihar	Barh STPP- I	NTPC	Others	U-3	660	Mar-16		
Bihar	Barh STPP-II	NTPC	BHEL	U-1	660	Aug-13	3595.00	2/12
Bihar	Barh STPP-II	NTPC	BHEL	U-2	660	Jun-14		
Bihar	Muzaffarpur TPP Exp	NTPC	BHEL	U-3	195	Jun-14	1.02	3/10
Bihar	Muzaffarpur TPP Exp	NTPC	BHEL	U-4	195	Sep-14		
Bihar	Nabi Nagar TPP	NTPC	BHEL	U-1	250	May-14	184.00	3/10
Bihar	Nabi Nagar TPP	NTPC	BHEL	U-2	250	Nov-14		
Bihar	Nabi Nagar TPP	NTPC	BHEL	U-3	250	May-15		
Bihar	Nabi Nagar TPP	NTPC	BHEL	U-4	250	Nov-15		
Haryana	Indira Gandhi TPP	APCPL	BHEL	U-3	500	Dec-12	5890.85	3/12
Jharkhand	BokaroTPS "A"Exp.	DVC	BHEL	U-1	500	Jun-14	991.91	2/12
Jharkhand	Kodarma TPP	DVC	BHEL	U-2	500	Nov-12	4848.09	2/12
Karnataka	Kudgi STPP Ph-I	NTPC	Others	U-1	800	Dec-15	Not Available	
Karnataka	Kudgi STPP Ph-I	NTPC	Others	U-2	800	Jun-16		
Karnataka	Kudgi STPP Ph-I	NTPC	Others	U-3	800	Dec-16		
Maharashtra	Mouda TPP	NTPC	BHEL	U-2	500	May-13	3575.00	2/12
MP	Vindhyachal TPP-IV	NTPC	BHEL	U-12	500	4/1/2013*	2965.00	1/12
TN	Neyveli TPS-II Exp.	NLC	BHEL	U-2	250	Feb-13	2154.25	3/11
TN	Tuticorin JV	NLC	BHEL	U-1	500	Dec-13	2362.39	12/11
TN	Tuticorin JV	NLC	BHEL	U-2	500	Mar-14		
TN	Vallur TPP Ph I	NTECL	BHEL	U-2	500	Feb-13	4614.34	12/11
TN	Vallur TPP-II	NTECL	BHEL	U-3	500	Sep-13	556.33	12/11
Tripura	Monarchak CCPP	NEEPCO	BHEL	GT+ST	101	Oct-13	79.60	1/11
Tripura	Tripura Gas	ONGC	BHEL	Module-1	363.3	Sep-12	2087.00	2/12
Tripura	Tripura Gas	ONGC	BHEL	Module-2	363.3	Dec-12		
UP	Rihand TPP- III	NTPC	BHEL	U-6	500	4/1/2013*	4487.00	2/12
WB	Raghunathpur TPP, Ph-I	DVC	Chinese	U-1	600	Apr-13	4468.49	2/12
WB	Raghunathpur TPP, Ph-I	DVC	Chinese	U-2	600	Jun-13		
Total Central Sector					15117.6			
	STATE SECTOR							
AP	Damodaram Sanjeevaiah TPS	APPDL	Non-BHEL	U-1	800	Oct-13	5195.03	1/12
AP	Damodaram Sanjeevaiah TPS	APPDL	Non-BHEL	U-2	800	Feb-14		
	Kakatiya TPP Extn	APGENCO	BHEL	U-1	600	May-14	478.41	3/11
	Rayalseema St-III U-6	BHEL	BHEL	U-6	600	Jul-14	10.58	3/11
Assam	Namrup CCGT	APGCL	BHEL	GT	70	Feb-13	57.97	12/10
Assam	Namrup CCGT	APGCL	BHEL	ST	30			
Chhattisgarh	Korba West St-III.	CSPGCL	BHEL	U-5	500	Jan-13	1909.44	2/12
Chhattisgarh	Marwa TPP	CSPGCL	BHEL	U-1	500	May-13	3128.02	2/12
Chhattisgarh	Marwa TPP	CSPGCL	BHEL	U-2	500	Jul-13		

Delhi	Pragati CCGT - III	PPCL	BHEL	GT-4	250	Dec-12	2408.89	3/11
Delhi	Pragati CCGT - III	PPCL	BHEL	ST-2	250	Feb-13		
Gujarat	Pipavav CCGP	GSECL	BHEL	Block-1	351	April,13	2547.38	3/12
Gujarat	Pipavav CCGP	GSECL	BHEL	Block-2	351	Feb,13		
Gujarat	Sikka TPP Extn.	GSECL	BHEL	U-3	250	April,14	1135.24	12/11
Gujarat	Sikka TPP Extn.	GSECL	BHEL	U-4	250	Jul-14		
Gujarat	Ukai TPP Extn.	GSECL	BHEL	U-6	490	Dec-12	1840.63	12/11
Karnataka	Yermarus TPP	KPCL		U-1	800	Mar,15 *	567.93	1/12
Karnataka	Yermarus TPP	KPCL		U-2	800	Jun,15 *		
Karnataka	Bellary TPP U-III	KPCL		U-3	700	Feb-15	1415.59	1/12
Maharashtra	Chandrapur TPS	MSPGCL	BHEL	U-8	500	Sep-13	2616.02	3/12
Maharashtra	Chandrapur TPS	MSPGCL	BHEL	U-9	500	Nov-13		
Maharashtra	Koradi TPP Expn.	MSPGCL	Non-BHEL	U-8	660	Dec-13	2037.50	3/12
Maharashtra	Koradi TPP Expn.	MSPGCL	Non-BHEL	U-9	660	Jun-14		
Maharashtra	Koradi TPP Expn.	MSPGCL	Non-BHEL	U-10	660	Dec-14		
Maharashtra	Parli TPP Expn.	MSPGCL	BHEL	U-8	250	Sep-13	985.62	3/12
MP	Malwa TPP (Shree Singati TPP)	MPGENCO	BHEL	U-1	600	Apr-13	3866.60	5/12
	Malwa TPP (Shree Singati TPP)	MPGENCO	BHEL	U-2	600	Jun-13		
MP	Satpura TPP Extn	MPPGCL	BHEL	U-10	250	May-13	1537.18	5/12
MP	Satpura TPP Extn	MPPGCL	BHEL	U-11	250	Oct-12		
Rajasthan	Chhabra TPP Extn.	RRVUNL	BHEL	U-3	250	Feb,13	1885.29	7/11
Rajasthan	Chhabra TPP Extn.	RRVUNL	BHEL	U-4	250	Jun-13		
Rajasthan	Kalisindh TPS	RRVUNL	Chinese	U-1	600	Mar,13	5015.32	4/12
Rajasthan	Kalisindh TPS	RRVUNL	Chinese	U-2	600	Aug-13		
Rajasthan	Ramgarh CCGP Extn. -III	RRVUNL	BHEL	GT	110	Oct-12	468.64	5/12
Rajasthan	Ramgarh CCGP Extn. -III	RRVUNL	BHEL	ST	50	Nov-12		
TN	Mettur TPP Ext	TNEB	Chinese	U-1	600	Aug-12	2408.51	3/12
TN	North Chennai Extn, U-1	TNEB	BHEL	U-1	600	May-13	1791.76	3/12
TN	North Chennai Extn, U-2	TNEB	BHEL	U-2	600	Nov,12		
UP	Anpara-D	UPRVUNL	BHEL	U- 6	500	Mar-13	3615.52	2/12
UP	Anpara-D	UPRVUNL	BHEL	U-7	500	Jun-13		
UP	Parichha Extn	UPRVUNL	BHEL	U-6	250	Sep-12	2274.6	3/12
WB	Durgapur TPS Extn	DPL	BHEL	U-8	250	Dec-13	215.00	7/11
WB	Sagardidhi TPP-2	WBPDCCL	BHEL	U-3	500	Feb,15	858.00	5/12
WB	Sagardidhi TPP-3	WBPDCCL	BHEL	U-4	500			
	Total State Sector				19982			
	PRIVATE SECTOR							
AP	Bhavanpadu TPP	M/s East Coast Energy Ltd.	Chinese	U-1	660	Nov-14	1114.92	7/11
AP	Bhavanpadu TPP	M/s East Coast Energy Ltd.	Chinese	U-2	660	Jan-15		
AP	NCC TPP	NCC Power Projects Ltd	Chinese	U-1	660		Not Available	
AP	NCC TPP	NCC Power Projects Ltd	Chinese	U-2	660			
AP	Painampuram TPP	Thermal Power Tech Corporation Ltd	Chinese	U-1	660	May-14	2199.00	10/11

AP	Painampuram TPP	Thermal Power Tech Corporation Ltd	Chinese	U-2	660	Aug-14		
AP	Simhapuri Energy Pvt Ltd Ph-II	Madhucon Projects Ltd.	Chinese	U-3	150	Sep-12	315.64	3/11
AP	Simhapuri Energy Pvt Ltd Ph-II	Madhucon Projects Ltd.	Chinese	U-4	150	Dec-12		
AP	Thamminapatnam TPP-I	Meenakshi Energy Pvt. Ltd	Chinese	U-1	150	Aug-12	1243.17	2/12
AP	Thamminapatnam TPP-I	Meenakshi Energy Pvt. Ltd	Chinese	U-2	150	Oct-12		
AP	Thamminapatnam TPP-II	Meenaksha Energy Ltd.	Chinese	U-3	350	May-13	885.88	2/12
AP	Thamminapatnam TPP-II	Meenaksha Energy Ltd.	Chinese	U-4	350	Aug-13		
AP	Vizag TPP	Hinduja National Power Corp. Ltd	BHEL	U-1	520	Jun-13	1674.18	2/12
AP	Vizag TPP	Hinduja National Power Corp. Ltd	BHEL	U-2	520	Sep-13		
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	Chinese	U-1	600	Jun-13	6164.33	11/11
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	Chinese	U-2	600	Oct-13		
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	Chinese	U-3	600	Feb,14		
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	Chinese	U-4	600	Jun-14		
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	Chinese	U-5	600	Nov-14		
Chhattisgarh	Akaltara (Naiyara) TPP	Wardha PCL (KSK)	Chinese	U-6	600	Mar,15 *		
Chhattisgarh	Avantha Bhandar TPS, U-1	Korba West Power Co. Ltd.	BHEL	U-1	600	Jul-13	1482.30	12/11
Chhattisgarh	Baradarha TPP (DB Power TPP)	D.B.Power co.Ltd	BHEL	U-1	600	Aug-13	2148.04	1/12
Chhattisgarh	Baradarha TPP (DB Power TPP)	D.B.Power co.Ltd	BHEL	U-2	600	Dec-13		
Chhattisgarh	Balco TPP	Bharat Aluminium Co. Ltd	Chinese	U-1	300	Dec-12	2636.09	3/10
Chhattisgarh	Balco TPP	Bharat Aluminium Co. Ltd	Chinese	U-2	300	Aug-12		
Chhattisgarh	Bandakhar TPP	M/s Maruti Clean Coal & Power Ltd	Chinese	U-1	300	Dec-13	170.00	12/11
Chhattisgarh	Binjkote TPP	M/s SKS Power Generation (Chhattisgarh) Ltd.	Chinese	U-1	300	Jun,14	856.60	7/11
Chhattisgarh	Binjkote TPP	M/s SKS Power Generation (Chhattisgarh) Ltd.	Chinese	U-2	300	Sep-12		

Chhattisgarh	Binjkote TPP	M/s SKS Power Generation (Chhattisgarh) Ltd.	Chinese	U-3	300	Dec,14		
Chhattisgarh	Binjkote TPP	M/s SKS Power Generation (Chhattisgarh) Ltd.	Chinese	U-4	300	Mar,15		
Chhattisgarh	Lanco Amarkantak TPS-II	LAP Pvt. Ltd.	Chinese	U-3	660	Aug-13	3256.44	9/11
Chhattisgarh	Lanco Amarkantak TPS-II	LAP Pvt. Ltd.	Chinese	U-4	660	Dec-13		
Chhattisgarh	Raikheda TPP	GMR	Others	U-1	685	Jun-14	Not Available	
Chhattisgarh	Raikheda TPP	GMR	Others	U-2	685	Nov-14		
Chhattisgarh	Ratija TPP	Spectrum Coal & Power Ltd	Chinese	U-1	50	Sep-12	270.00	12/11
Chhattisgarh	Singhitarai TPP	Athena Chhattisgarh Power Ltd.	Chinese	U-1	600	Oct-14	923.94	7/11
Chhattisgarh	Singhitarai TPP	Athena Chhattisgarh Power Ltd.	Chinese	U-2	600	Jan-15		
Chhattisgarh	Swastic TPP	M/s ACB	Non-BHEL	U-1	25	Oct-12	NA	
Chhattisgarh	Tamnar TPP (Raigarh)	O.P.Jindal	BHEL	U-1	600	Jan-14	NA	
Chhattisgarh	Tamnar TPP (Raigarh)	O.P.Jindal	BHEL	U-2	600	Apr-14		
Chhattisgarh	Tamnar TPP (Raigarh)	O.P.Jindal	BHEL	U-3	600	Dec,14		
Chhattisgarh	Tamnar TPP Raigarh)	O.P.Jindal	BHEL	U-4	600	Mar,15 *		
Chhattisgarh	TRN Energy TPP	M/s TRN Energy Pvt. Ltd.	Chinese	U-1	300	Mar-14	100.00	9/11
Chhattisgarh	TRN Energy TPP	M/s TRN Energy Pvt. Ltd.	Chinese	U-2	300	Jun-14		
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	Chinese	U-1	360	Oct-13	2409.19	1/12
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	Chinese	U-2	360	Jan-14		
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	Chinese	U-3	360	Apr-14		
Chhattisgarh	Uchpinda TPP	RKM Powergen Pvt. Ltd	Chinese	U-4	360	Jul-14		
Chhattisgarh	Vandana Vidyut TPP- Chhattisgarh	M/s Vandana Vidyut	Chinese	U-1	135	Oct-12	927.00	6/11
Chhattisgarh	Vandana Vidyut TPP- Chhattisgarh	M/s Vandana Vidyut	Chinese	U-2	135	Feb-13		
Gujarat	Bhavnagar CFBC TPP	Bhavnagar Energy	BHEL	U-1	250	Oct-13	NA	
Gujarat	Bhavnagar CFBC TPP	Bhavnagar Energy	BHEL	U-2	250	Dec-13		
Gujarat	Mundra UMTTP	Tata Power Co.	Others	U-3	800	May-13	13124.00	3/11
Gujarat	Mundra UMTTP	Tata Power Co.	Others	U-4	800	Aug-13		
Gujarat	Mundra UMTTP	Tata Power Co.	Others	U-5	800	Nov-13		

Jharkhand	Adhunik Power TPP	Adhunik Power Co.Ltd	BHEL	U-1	270	Nov-12	1300.00	6/11
Jharkhand	Adhunik Power TPP	Adhunik Power Co.Ltd	BHEL	U-2	270	Feb-13		
Jharkhand	Maitrishi Usha TPP-Ph-I	M/s Corporate Power Ltd	BHEL	U-1	270	Sep-12	NA	
Jharkhand	Maitrishi Usha TPP-Ph-I	M/s Corporate Power Ltd	BHEL	U-2	270	Dec-12		
Jharkhand	Maitrishi Usha TPP-Ph-II	Corporate Power Ltd	BHEL	U-3	270	Jun-13		
Jharkhand	Maitrishi Usha TPP-Ph-II	Corporate Power Ltd	BHEL	U-4	270	Sep-13		
Jharkhand	Tori TPP	Essar Power	Chinese	U-1	600			
Jharkhand	Tori TPP	Essar Power	Chinese	U-2	600		729.00	6/11
Maharashtra	Amravati TPP Ph-I	India Bulls	BHEL	U-1	270	Feb-13	1697.12	3/11
Maharashtra	Amravati TPP Ph-I	India Bulls	BHEL	U-2	270	Jul-13		
Maharashtra	Amravati TPP Ph-I	India Bulls	BHEL	U-3	270	Sep-13		
Maharashtra	Amravati TPP Ph-I	India Bulls	BHEL	U-4	270	Dec-13		
Maharashtra	Amravati TPP Ph-I	India Bulls	BHEL	U-5	270	Mar-14		
Maharashtra	Amravati TPP Ph-II	India Bulls	BHEL	U-1	270	Jul-14	165.55	7/11
Maharashtra	Amravati TPP Ph-II	India Bulls	BHEL	U-2	270	Sep-14		
Maharashtra	Amravati TPP Ph-II	India Bulls	BHEL	U-3	270	Nov-14		
Maharashtra	Amravati TPP Ph-II	India Bulls	BHEL	U-4	270	Jan-15		
Maharashtra	Amravati TPP Ph-II	India Bulls	BHEL	U-5	270	Mar-15		
Maharashtra	Bela TPP-I	IEPL	BHEL	U-1	270	Dec-12	1329.00	2/12
Maharashtra	Butibori TPP Ph-II	Vidarbha Industries Power	Chinese	U-1	300	Aug-12	313.80	6/11
Maharashtra	Dhariwal Infracture TPP	Dhariwal Infracture (P) Ltd	Chinese	U-1	300	Mar-13	1100.00	11/11
Maharashtra	Dhariwal Infracture TPP	Dhariwal Infracture (P) Ltd	Chinese	U-2	300	Sep-13		
Maharashtra	EMCO Warora TPP	EMCO Energy Ltd.(GMR)	Chinese	U-1	300	Nov-12	2183.00	12/11
Maharashtra	EMCO Warora TPP	EMCO Energy Ltd.(GMR)	Chinese	U-2	300	Jan-12		
Maharashtra	GEPL TPP	GEPL	Chinese	U-1	60	Sept-12	587.16	5/11
Maharashtra	Lanco Vidarbha TPP	Lanco Vidarbha	Chinese	U-1	660	April,14	1471.00	7/11
Maharashtra	Lanco Vidarbha TPP	Lanco Vidarbha	Chinese	U-2	660	Aug,14		
Maharashtra	Nasik TPP Ph-I	India Bulls	BHEL	U-1	270	Feb-13	1368.05	3/11
Maharashtra	Nasik TPP Ph-I	India Bulls	BHEL	U-2	270	Jul-13		
Maharashtra	Nasik TPP Ph-I	India Bulls	BHEL	U-3	270	Nov,14		
Maharashtra	Nasik TPP Ph-I	India Bulls	BHEL	U-4	270	Jan,14		
Maharashtra	Nasik TPP Ph-I	India Bulls	BHEL	U-5	270	Mar-15		
Maharashtra	Nasik TPP Ph-II	India Bulls	BHEL	U-1	270	Jul-14	123.02	6/11
Maharashtra	Nasik TPP Ph-II	India Bulls	BHEL	U-2	270	Sep-14		
Maharashtra	Nasik TPP Ph-II	India Bulls	BHEL	U-3	270	Nov-14		
Maharashtra	Nasik TPP Ph-II	India Bulls	BHEL	U-4	270	Jan-15		
Maharashtra	Nasik TPP Ph-II	India Bulls	BHEL	U-5	270	Mar-15		
Maharashtra	Tirora TPP Ph-I	Adani Power Ltd	Chinese	U-1	660	Aug-12	5454.58	6/11
Maharashtra	Tirora TPP Ph-I	Adani Power Ltd	Chinese	U-2	660	Nov-12		
Maharashtra	Tirora TPP Ph-II	Adani Power Ltd	Chinese	U-1	660	Dec-12	1846.28	7/11

Maharashtra	Tirora TPP Ph-II	Adani Power Ltd	Chinese	U-2	660	Aug-13		
Maharashtra	Tirora TPP Ph-II	Adani Power Ltd	Chinese	U-3	660	Nov-13		
MP	Anuppur TPP Ph-I	MB Power MP	Chinese	U-1	600	Dec,13	2600.00	3/12
MP	Anuppur TPP Ph-I	MB Power MP	Chinese	U-2	600	April,14		
MP	Bina TPP	Bina Power Supply Co. Ltd	BHEL	U-1	250	Aug-12	1474.00	1/11
MP	Bina TPP	Bina Power Supply Co. Ltd	BHEL	U-2	250	Jul-13		
MP	Gorgi TPP (DB Power)	DB Power	BHEL	U-1	660	Feb-15	335.18	1/12
MP	Mahan TPP	Essar Power MP Ltd	Chinese	U-1	600	Apr-13	5554.04	5/12
MP	Mahan TPP	Essar Power MP Ltd	Chinese	U-2	600	Jun-13		
MP	Nigri TPP	Jaiprakash Power Ventures Ltd	Non-BHEL	U-1	660	May-13	908.16	12/10
MP	Nigri TPP	Jaiprakash Power Ventures Ltd	Non-BHEL	U-2	660	Oct-13		
MP	Sasan UMPP	Reliance Power Ltd.	Chinese	U-1	660	Apr-13	3471.00	3/11
MP	Sasan UMPP	Reliance Power Ltd.	Chinese	U-2	660	Jul-13		
MP	Sasan UMPP	Reliance Power Ltd.	Chinese	U-3	660	Oct-13		
MP	Sasan UMPP	Reliance Power Ltd.	Chinese	U-4	660	Jan-14		
MP	Sasan UMPP	Reliance Power Ltd.	Chinese	U-5	660	May-14		
MP	Sasan UMPP	Reliance Power Ltd.	Chinese	U-6	660	Sep-14		
MP	Seioni TPP Ph-I	Jhabua Power Ltd	BHEL	U-1	600	Oct-13	1052	3/12
Orissa	Derang TPP	JITPL	BHEL	U-1	600	Sept,13	2000.00	12/11
Orissa	Derang TPP	JITPL	BHEL	U-2	600	Dec,13		
Orissa	Ind Barat TPP (Orissa)	Ind. Barat	Chinese	U-1	350	Jan.13	2200.00	1/12
Orissa	Ind Barat TPP (Orissa)	Ind. Barat	Chinese	U-2	350	Mar-13		
Orissa	Kamalanga TPP	GMR	Chinese	U-1	350	Nov-12	4054.80	11/11
Orissa	Kamalanga TPP	GMR	Chinese	U-2	350	Mar,13		
Orissa	Kamalanga TPP	GMR	Chinese	U-3	350	Jul-13		
Orissa	KVK Nilanchal TPP	KVK Nilanchal	Chinese	U-1	350	Feb-14	609.18	10/10
Orissa	KVK Nilanchal TPP	KVK Nilanchal	Chinese	U-2	350	Dec-14		
Orissa	KVK Nilanchal TPP	KVK Nilanchal	Chinese	U-3	350	Jan-15		
Orissa	Lanco Babandh TPP	Lanco Babandh Power Ltd	Chinese	U-1	660	Mar-12	3208.00	3/12
Orissa	Lanco Babandh TPP	Lanco Babandh Power Ltd	Chinese	U-2	660	July-14		
Orissa	Malibrahmani TPP (Monnet Ispat)	MPCL	BHEL	U-1	525	Oct-13	1415.92	3/12
Punjab	Goindwal Sahib	GVK Power	BHEL	U-1	270	Feb-13	2240.45	6/12
Punjab	Goindwal Sahib	GVK Power	BHEL	U-2	270	Aug,13		
Punjab	Rajpura TPP (Nabha)	Nabha Power Ltd	Non-BHEL	U-1	700	Jan-14	3050.00	5/12

<i>Punjab</i>	Rajpura TPP (Nabha)	Nabha Power Ltd	Non-BHEL	U-2	700	Mar-14		
<i>Punjab</i>	Talwandi Sabo TPP	M/s Sterlite	Chinese	U-1	660	Dec,13	5141.49	5/12
<i>Punjab</i>	Talwandi Sabo TPP	M/s Sterlite	Chinese	U-2	660	April,14		
<i>Punjab</i>	Talwandi Sabo TPP	M/s Sterlite	Chinese	U-3	660	Jun,14		
<i>Rajasthan</i>	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-5	135	Oct-12	6394.38	3/12
<i>Rajasthan</i>	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-6	135	Jan-13		
<i>Rajasthan</i>	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-7	135	Aug-13		
<i>Rajasthan</i>	Jallipa-Kapurdi TPP	Raj West Power Ltd.(JSW)	Chinese	U-8	135	Dec-13		
<i>Rajasthan</i>	Kawai TPP	Adani Power Ltd.	Chinese	U-1	660	Mar,13	6253.88	3/12
<i>Rajasthan</i>	Kawai TPP	Adani Power Ltd.	Chinese	U-2	660	May,13		
<i>TN</i>	Melamaruthur TPP	Coastal Energen	Chinese	U-1	600	Feb,13	3250.16	2/12
<i>TN</i>	Melamaruthur TPP	Coastal Energen	Chinese	U-2	600	May-12		
<i>TN</i>	Tuticorin TPP (Ind- Barath TPP)	IBPIL	Chinese	U-1	660	Jan-14	195.00	2/12
<i>UP</i>	Prayagraj (Bara) TPP	J.P.Power	BHEL	U-1	660	Feb-14	3168.34	6/12
<i>UP</i>	Prayagraj (Bara) TPP	J.P.Power	BHEL	U-2	660	Jul-14		
<i>UP</i>	Prayagraj (Bara) TPP	J.P.Power	BHEL	U-3	660	Dec-14		
<i>UP</i>	Lalitpur TPP	Bajaj Energy Pvt Ltd	BHEL	U-1	660	Sep-14	3103.99	3/12
<i>UP</i>	Lalitpur TPP	Bajaj Energy Pvt Ltd	BHEL	U-2	660	Dec-14		
<i>UP</i>	Lalitpur TPP	Bajaj Energy Pvt Ltd	BHEL	U-3	660	Mar,15 *		
<i>WB</i>	Haldia TPP-I	M/s Haldia Energy Ltd.	Chinese	U-1	300	Aug-14	442.48	5/12
<i>WB</i>	Haldia TPP-I	M/s Haldia Energy Ltd.	Chinese	U-2	300	Nov-14		
	Total Private Sector				67530			
	Grand Total				102630			
